

Fortnightly District Report

Kavrepalanchok

1 – 14 February 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint Monitoring Field Visit to Bethanchok Gaupalika	1 Feb 2019	2	1	reshma@hrrpnepal.org	Field Visit Section below
GMALI/HRRP Coordination Meeting	11 Feb 2019	9	1	reshma@hrrpnepal.org	Meeting Minutes
Joint Monitoring Field Visit to Dhulikhel Nagarpalika	12-14 Feb 2019	-	-	reshma@hrrpnepal.org	Field Visit Section below
Training Database Update	1-14 Feb 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Data Collection and Updating Palika Profiles in Municipal websites	1-14 Feb 2019	-	-	im.kavrepalanchok@hrrpnepal.org	NA
Housing Typology Update	14 Feb 2019	-	-	reshma@hrrpnepal.org	GD
Support to GMALI on grievance handling	1-14 Feb 2019	-	-	reshma@hrrpnepal.org	NA

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Field Visit to Namobuddha Municipality to update on the interaction and awareness program at the ward levels of the municipality	19 Feb 2019, 8:00 AM-5:00 PM, Namobuddha NP	HRRP	reshma@hrrpnepal.org
Joint Monitoring Field Visit to Temal Gaupalika	26-28 Feb 2019, 8:00 AM- 5:00 PM, Temal GP	HRRP	reshma@hrrpnepal.org

Tranche Status


Municipality	Banepa	Bethanchok	Bhumlu	ChauriDeurali	Dhulikhel	KhaniKhola	Mahabharat	MandanDeupur	NamoBuddha	Panchkhal	Panauti	Roshi	Temal
Total HHs Surveyed	-	-	-	-	-	-	-	-	-	-	-	-	-
Total HHs Eligible	7070	4377	6203	6411	5968	2842	2950	9195	7593	9937	9178	6262	4847
Total HHs Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
1 st Tranche	6364	3762	5820	5473	5088	2735	2874	8456	6153	8845	8010	5473	4147
2 nd Tranche	2786	2560	4761	3741	2481	2171	2369	6413	3101	5846	4204	3858	2816
3 rd Tranche	2132	1334	3481	1829	1596	545	1317	3852	1612	3472	2886	1832	1588
Total HH Constructed	-	-	-	-	-	-	-	-	-	-	-	-	-
Grievance Registered	2226	1202	1038	1578	2151	683	1075	2300	2814	3041	2874	2257	2101
Grievance Addressed	2031	1202	971	1517	1919	681	1055	1762	2296	2932	2851	2203	2069
RF HH Eligible	-	-	-	-	-	-	-	-	-	-	-	-	-
RF HH Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
RF 1 st Tranche	76	73	14	43	39	43	143	25	20	108	123	129	103
RF 2 nd Tranche	1	0	1	0	0	0	0	0	0	14	0	0	1
Non-Compliance Registered	-	-	-	-	-	-	-	-	-	-	-	-	-
Non-Compliance Addressed	-	-	-	-	-	-	-	-	-	-	-	-	-

Tranche Status

Reconstruction Tranche Status (14 Feb 2019)

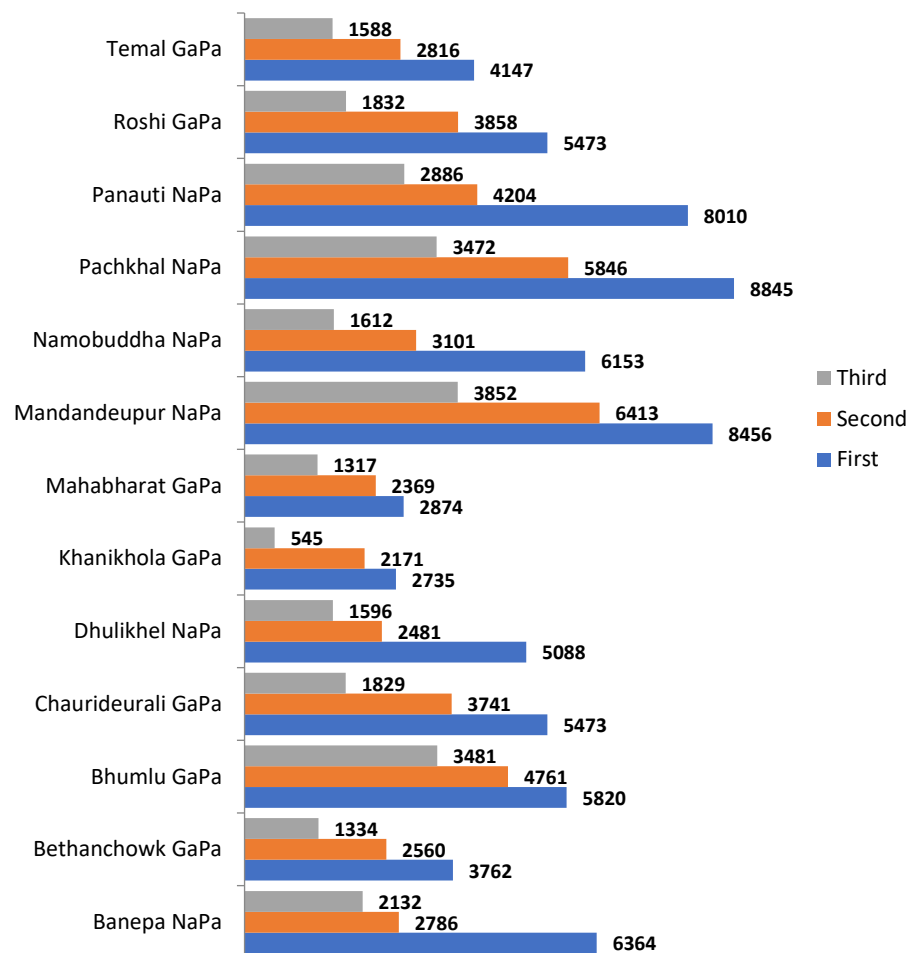

Grievance Addressal Status (14 Feb 2019)

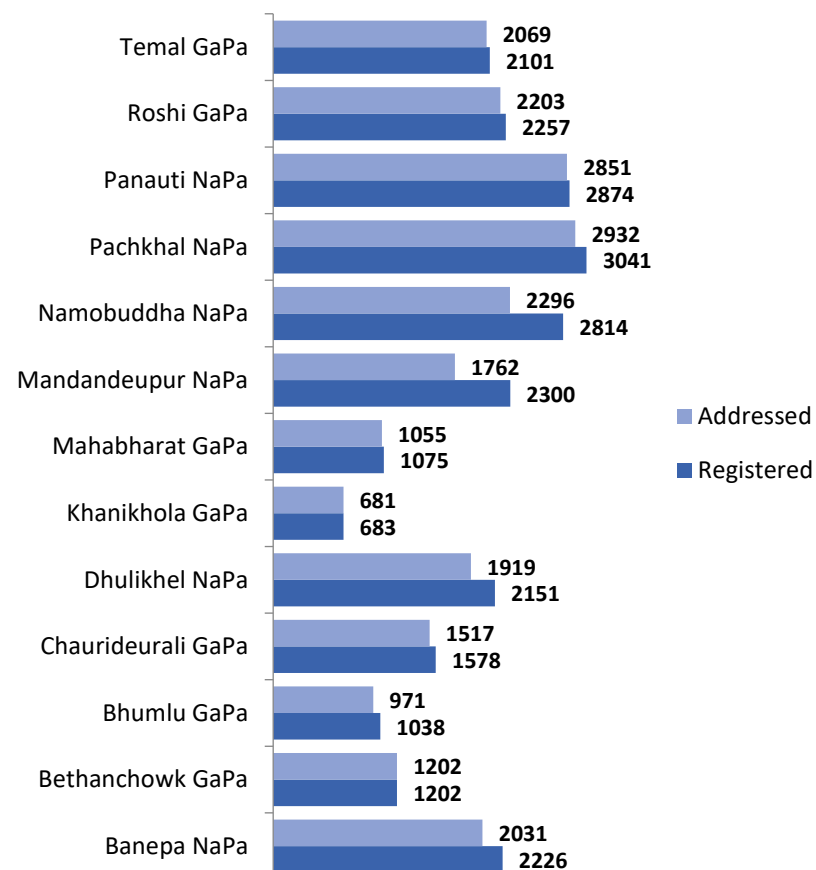

Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
1 Feb 2019	ChalalGanesthan, MahankalChaur, Bethanchok Gaupalika	• Roshan Kesari, M&E Consultant • Reshma Shrestha, HRRP Kavre • Ishor Neupane, HRRP Kavre

Objective(s)

- Meeting at ward level.
- Monitoring of technical team.
- Update on reconstruction status of each wards.
- Monitor main non-compliance issues.

Summary

During the visit, ward level meetings were conducted at Ward 4 and 6 of the Gaupalika. Retrofitting is the major challenge in both the wards. Though retrofitting awareness programs have been conducted at both the wards, beneficiaries are still reluctant for retrofitting their houses.

At Ward 4, out of 74 retrofit beneficiaries, only 3 have enrolled but none have withdrawn the first tranche from their accounts and none have move forth with retrofitting either. The ward is collecting applications for switching the retrofit beneficiaries to reconstruction beneficiaries. Of the total 893 beneficiaries, 852 have received the first tranche, 657 have received second tranche and 419 have received third tranche whereas of the 41 beneficiaries yet to enroll, 37 have land issues and 4 are landless.

At Ward 6, there are a total 239 retrofit beneficiaries, 44 have received first tranche and none have retrofitted. Almost all of the beneficiaries desire to build a new house but do not want to demolish the pre earthquake house either. Mass orientation and video awareness on retrofitting too have been conducted multiple times by UNOPS. The major reason for the continued reluctance to retrofit is the high transportation cost for cement and steel. Wood available in the ward is soft wood which cannot be used for the retrofit so the only option is retrofit using cement. The Ward Chief along with UNOPS team is planning to do a demo retrofit in his own damaged house where the material will be sufficed by the home owner and technical support will be provided by UNOPS team but there is only a faint hope that other beneficiaries will be motivated through the demo.

Photos



Sanu Kajo Kaji Thapa of Bethanchok 6 was the first beneficiary to complete his house and receive the third tranche at MahankalChaur.
Photograph By: Reshma Shrestha



The proposed retrofit demo house of the Ward Chief of MahankalChaur, Bethanchok 6.
Photograph By: Reshma Shrestha

Field Visit Report

Visit 2

Date	Location	Participants from HRRP and stakeholders
12-14 Feb 2019	Dhulikhel Nagarpalika	- Roshan Kesari, M&E Consultant - Reshma Shrestha, HRRP Kavre - Ishor Neupane, HRRP Kavre

Objective(s)

- Meeting at ward level.
- Monitoring of technical team.
- Update on reconstruction status of each wards.
- Monitor main non-compliance issues.

Summary

During the visit, ward level coordination meetings were held in Ward 9, 10 and 12 whereas technical coordination meeting was conducted in Ward 11. The visit at ward 12 was also accompanied by a donor visit team of Saudi Arab, GMALI/CLPIU and GMALI/DLPIU.

At Ward 9, the maximum beneficiaries who are yet to enroll have land issues. Compulsory municipal building permit also has discouraged beneficiaries to reconstruct. The major issue of the ward is that the technical persons deployed from NRA need to prepare all the site plans and location plans of the beneficiaries who are constructing houses using the DUDBC models. Most of the houses being constructed are load bearing structures with a very few RCC houses. Whilst the technical persons need to engage in drawing preparation, the inspection progress is lower. None of the houses have been final inspected and distributed with the completion certificate.

At Ward 11, of the 899 beneficiaries, 871 have received first tranche, 479 have received second tranche and 262 have received third tranche. Only 6 of the structures are non-complaint, the files have been forwarded for analysis to the DSE.

At Ward 10, the major issue is the coordination gap with the municipal engineers. There are some cases where the municipal drawings do not comply with the building codes and hence the structures are non-compliant. All the non-compliances though have been addressed by the DSE, beneficiaries are reluctant for corrections. As per the request from the ward, one day field visit of DSE was scheduled to oversee five major non-compliances of the ward.

At Ward 12, of the 631 beneficiaries, 461 have received first tranche, 121 have received second tranche and 102 have received third tranche. The rate of reconstruction is comparatively lower because most of the beneficiaries have temporarily migrated to Banepa and Kathmandu. During the visit, the Saudi Arab team was briefed about the tranche distribution process by the Ward Chief which was followed by interactions with beneficiaries.

Photos



Ward Chief of Dhulikhel-12 briefing about the tranche distribution process to the Saudi Arab visit team.
Photograph By: Reshma Shrestha



Khil Prasad Dhimal of Dhulikhel-10 though has received third tranche, his house misses the roof bands and will need to correct the bands to receive the completion certificate.
Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Bethanchok-4
Building Typology: Brick in Cement
Description: Thuli Maya Dong has received the third tranche of housing reconstruction grant.
Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-6
Building Typology: Stone in Mud
Description: Aaite Singh has received the third tranche of housing reconstruction grant.
Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-6
Building Typology: Brick in Cement
Description: Man Kumar Lama has received all three tranches of housing reconstruction grant.
Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-4
Building Typology: RCC
Description: This house has received all three tranches of housing reconstruction grant. Detailed analysis report had to be submitted due to the L shaped configuration.
Photographed By: Reshma Shrestha



<u>Address:</u> Kavrepalanchok, Dhulikhel-11 <u>Building Typology:</u> Brick in Cement <u>Description:</u> Keshav Badal has received third tranche of housing reconstruction grant. <u>Photographed By:</u> Reshma Shrestha	<u>Address:</u> Kavrepalanchok, Dhulikhel-11 <u>Building Typology:</u> RCC <u>Description:</u> Ram Sharan Badal has his house inspected for the second tranche. <u>Photographed By:</u> Reshma Shrestha
	
<u>Address:</u> Kavrepalanchok, Dhulikhel-9 <u>Building Typology:</u> RCC <u>Description:</u> Ram Chandra Humagain has received all three tranches of housing reconstruction grant. <u>Photographed By:</u> Reshma Shrestha	<u>Address:</u> Kavrepalanchok, Dhulikhel-12 <u>Building Typology:</u> Brick in Cement <u>Description:</u> Bishnu Maya Tamang has received all three tranches of housing reconstruction grant. <u>Photographed By:</u> Reshma Shrestha

Case Story

Technical Staff Feature

Binita Shrestha, Architect, Dhulikhel-9

Binita Shrestha, a resident of Chitwan was working as an architect in Bhaktapur Municipality. To lend her support as a technical person for the post-earthquake reconstruction, she joined NRA on 19th Asadh 2073 BS. She was deployed to Chatrabaj VDC, now Namobuddha Municipality-9 where she worked until Asadh 30 2075 BS and since then she has been stationed to Dhulikhel Municipality-9.

Both her work areas are earlier VDCs recently restructured to municipalities. The housing typologies of both the areas are dominated by load bearing structure of Brick Masonry in Cement Mortar and Stone Masonry in Mud Mortar with very few RCC buildings whereas compared to Namobuddha, houses at Dhulikhel are more clustered and hence traveling is a lot easier.

The major part of her job includes providing technical guidance to beneficiaries and inspecting houses. She also ensures all the inspected houses receive tranches timely by visiting and regularly communicating with the DLPIUs. For these, the trainings she has received on ToT, Correction and Exception Manual and Retrofitting has helped a lot. ToT has helped her understand the technical aspects of construction and building codes whereas Correction Manual has helped her suggest the correction measures for non-compliances. Retrofitting whereas, as is a very complex process, she has not been able to deliver the learnings from the training to the beneficiaries.

"Her regularity and positivity towards work reflects in the tranche progress of the ward. Eight months before, the overall reconstruction progress was 35% whereas now it is 60%", shares the Ward Chief, whereas according to her, the working environment of the ward office and support from beneficiaries has helped improve the tranche figures of the ward. The beneficiaries of the ward along with the masons easily take her advice and construct accordingly. She shares her first field experience as, "It was my first inspection of Brick Masonry in Cement Mortar. A group of untrained masons were constructing the house. They were laying the rods in the plinth beam with two rods tied twelve inches apart. I taught them the actual standards to use four rods and tie at four inches interval. They respected me as an engineer and took in the advice not only in that house but replicated it in every construction thereafter. I had never thought working can be as easy."

The positive aspect of reconstruction, as she shares, is the gradual shift from temporary shelters to safer houses. The policies/guidelines developed by NRA to support reconstruction, beneficiary awareness programs, mason trainings and technical persons mobilization has helped achieve the expected safer constructions whereas insufficient masons and less manpower at DLPIUs pose challenges to reconstruction progress. She also expresses her fear that in the name of safer construction, the traditional architecture and technology will be lost.



Different houses constructed with her technical supervision
