

District Report

Rasuwa

22 Nov to 6 Dec 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
The GPS location of all palikas offices has been submitted at national level. The GPS location of palikas (Latitude and Longitude) is as follows. Uttargaya RM = 27.991965° 85.182784° Kalika RM = 27.993787° 85.203422° Naukunda RM = 28.011519° 85.273886° Gosaikunda RM = 28.165339° 85.341672° Aama Chhindigmo RM= 28.170846° 85.316013°	26-Nov-2018	1		Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
On the request from National IMs the total beneficiary list of district was submitted at national level. HHs details with their PA number and tranche status of each HHs was submitted.	28-Nov,2018	1		Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
5 th Round of 5W was updated and uploaded on respective district google drive. The new event added/updated for this round is: 1. GoN housing tranche is updated in this round. 2. ASF activities was updated.	28-Nov,2018	1		Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
The meal data of district has been updated at national level.	6- Dec,2018	1		Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Rasuwa team conducted field visit at Gosaikunda RM ward number 1 (Thuman). HRRP team together with Building DLPIU team visited the place. The details information of this field visit is at field visit section.	29-Nov,2018	4	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	


Summary of events during this period

Discussion with the banks and uduhyog byawasi Sangh regarding the post-earthquake reconstruction and recovery.	23-Nov,2018	20	1	Techcord.rasuwa@hrrpnepal.org	
Collection of non-compliance data of five RM upto November 2018	Dec-5,2018			Techcord.rasuwa@hrrpnepal.org lm.rasuwa@hrrpnepal.org	
Update of Housing Typology of Naukunda RM ward no-5,Bhorley				Techcord.rasuwa@hrrpnepal.org lm.rasuwa@hrrpnepal.org	


Tranche Status

Rural /Municipality	Gosaikunda RM	Naukunda RM	Aama Chhodingmo RM	Kalika RM	Uttargaya RM
Total HHs Surveyed	1,979	3,349	1,963	2,569	2,630
Total HHs Eligible	1,979	3,349	1,963	2,569	2,630
Total HHs Enrolled	1,788	3,251	1,715	2,410	2,269
First Tranche	1,788	3,250	1,715	2,410	2,269
Second Tranche	1592	2960	1523	2241	1905
Third Tranche	1116	2657	1219	2040	1635
Total HH Constructed	1,116	2,657	1,219	2,040	1,635
Grievance Registered					
Grievance Addressed	257	237	238	277	245
RF HH Eligible	84	11	59	32	25
RF HH Enrolled	60	10	2	10	11
RF 1 st Tranche	60	10	2	10	11
RF 2 nd Tranche	0	0	0	0	0
Non-Compliance Registered	89	48	54	101	124
Non-Compliance Addressed	69	36	40	70	86


Graph of Tranche Status:

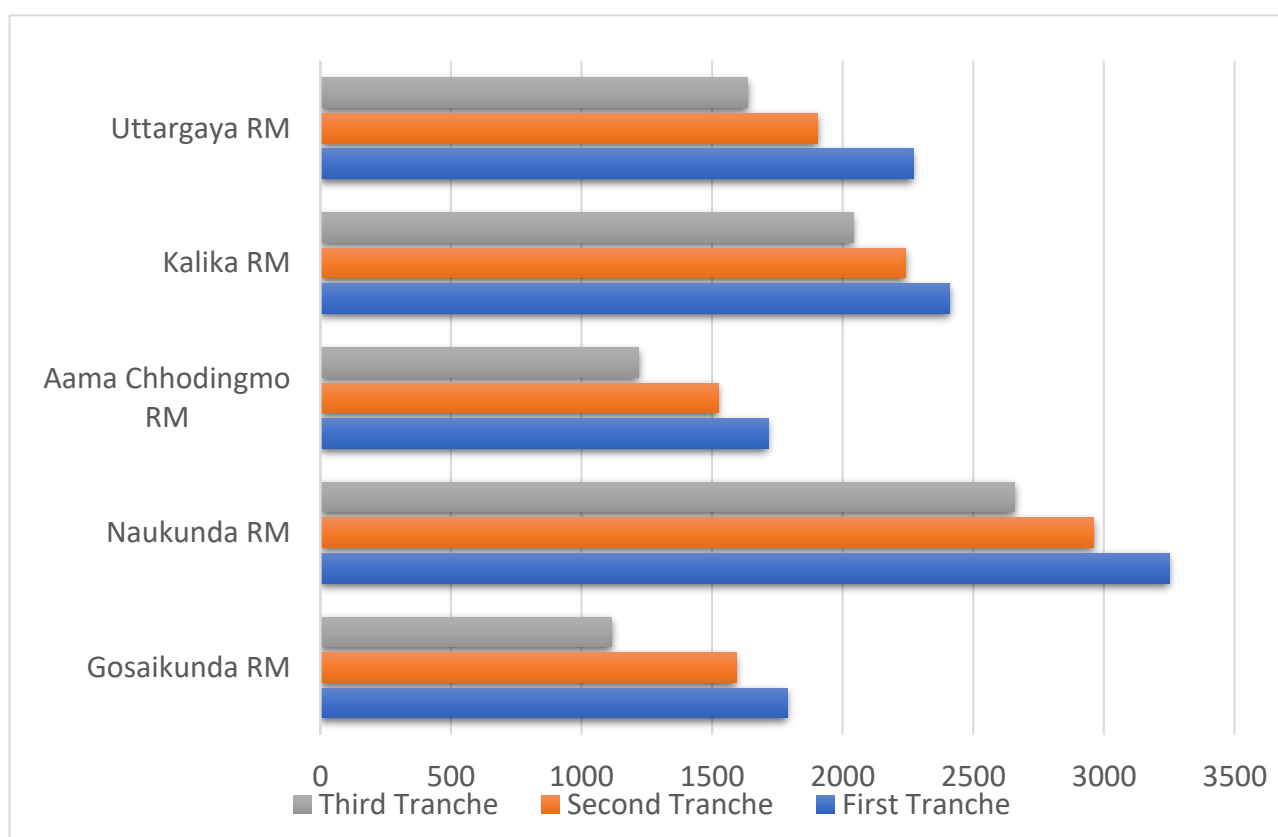

Graph for Retrofitting Status:

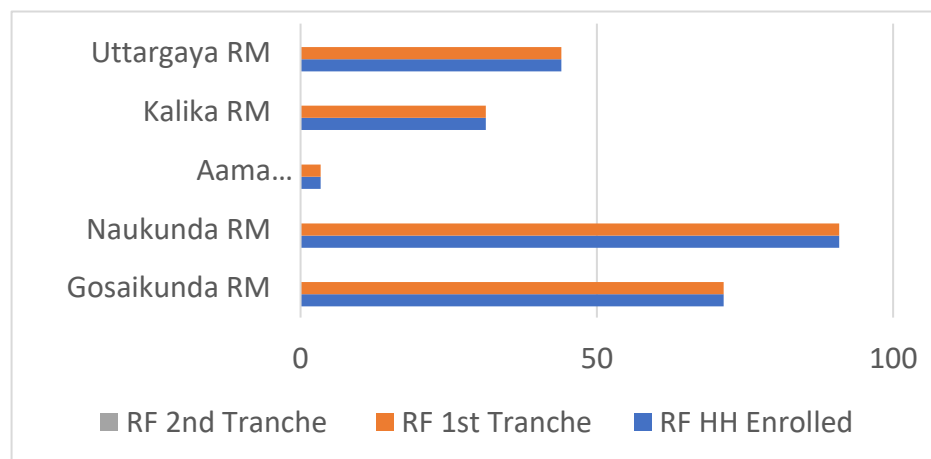

Graph for Grievance Status:

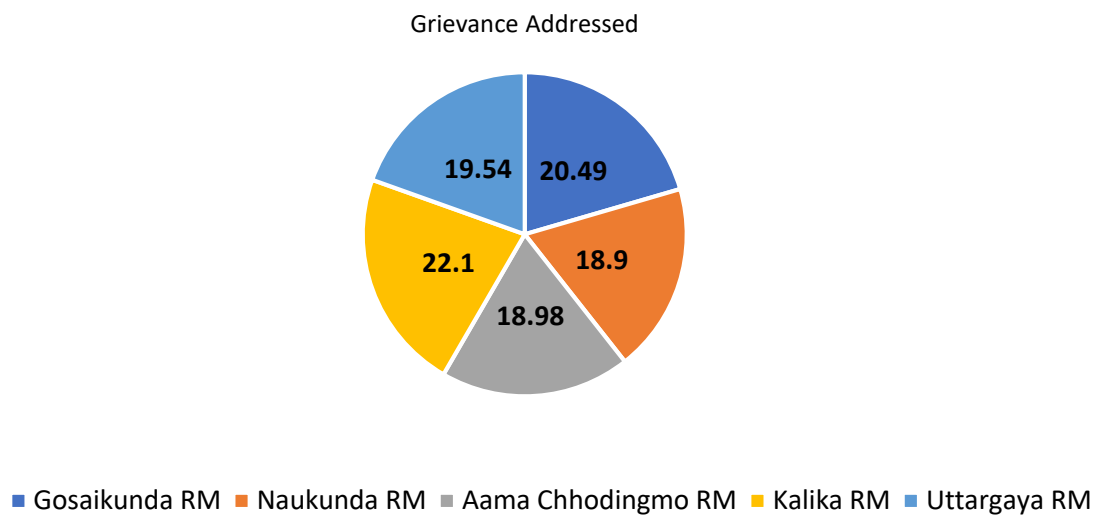

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders															
2018-Nov-29 to 2018-Nov-30	Gosaikunda RM ward number 1	- Rijan Gajurel - Biren Shah - Saroj Kumar Yadav - Arun															
Objective(s)	- To interact with local representative, engineers along with beneficiaries to know the reconstruction progress and challenges. - To monitor reconstruction status of ward 1 - To collect housing typologies. - To collect information on Status of timber structure and non-compliant issues.																
Summary	HRRP team together with Building DLPIU team conducted field visit at Gosaikunda RM ward number 1 (Thuman). The field visit was targeted in to collect the reconstruction status and challenging issues of the ward. The GMaLI tranche update of this ward is as follows:																
	<table><tr><td>Total Eligible HHs for housing grant</td><td>354</td></tr><tr><td>Total enrolled HHs for housing grant</td><td>341</td></tr><tr><td>First tranche received HHs</td><td>341</td></tr><tr><td>Secound tranche received HHs</td><td>297</td></tr><tr><td>Third Tranche received HHs</td><td>254</td></tr><tr><td>HHs Constructed</td><td>254</td></tr><tr><td>Total Eligible HHs for Retrofitting grant</td><td>0</td></tr></table>			Total Eligible HHs for housing grant	354	Total enrolled HHs for housing grant	341	First tranche received HHs	341	Secound tranche received HHs	297	Third Tranche received HHs	254	HHs Constructed	254	Total Eligible HHs for Retrofitting grant	0
	Total Eligible HHs for housing grant	354															
	Total enrolled HHs for housing grant	341															
	First tranche received HHs	341															
	Secound tranche received HHs	297															
	Third Tranche received HHs	254															
	HHs Constructed	254															
	Total Eligible HHs for Retrofitting grant	0															
Field visit team conducted a meeting with Ward president of ward 1. The key discussion point of that meeting is , grievances have been addressed and an additional 52 households have been identified as eligible for the housing reconstruction grant. The ward office has sent the list to DLPIU GMaLI for further processing. 12 houses have been left out during the resurvey and verification process and are not on the eligible list. The ward chairperson suggested that the process had been biased as a result of political pressure and reported that some households that were not eligible for the grant were included in the grievance list and submitted to NRA without his signature. Most of the houses are constructed using local materials which are easily available. It was also reported that technical persons are present in the area as well as the ward office to support on technical issues.																	
Challenges / Issues Identified	Action Required	Responsible	Timeframe														
There is no proper accessibility of road transportation due to which the hauling cost of construction material ultimately is high and therefore increased rate of construction materials after reaching the site.	Road accessibility, Support from the government and POs to start a storage center at ward level from where the people can buy materials at low cost.	Palika representatives, POs, GON	ASAP														

Photos



Caption: Gosaikunda RM, Ward no-1, Thuman
Beneficiary Name :-Phurpu Chiring
Tranche :- Second Tranche Received and third tranche is recommended
Housing Typolog :-Two storeyed hybrid structure with lower Stone Masonary In Cement Mortar with RC band and upper timber structure.



Caption: Gosaikunda RM, Ward no-1, Thuman
Beneficiary Name :-Bunima Tamang
Tranche :- Third Received
Housing Typolog :-Two storeyed hybrid structure with lower Stone Masonary In Cement Mortar with RC band and upper timber structure.

Housing Typology Report



Caption :Gosaikunda RM, Ward no-1, Thuman
Beneficiary Name :- Lakpa Bhoti Tamang
Tranche :- Second Tranche Received and Third not Recommended as the foundation wall settlement occurred after the construction of the house.
Housing Typolog :- Two storeyed timber structure with four rooms and light CGI flexible roof.



Caption:
Gosaikunda RM, Ward no-1, Thuman
Beneficiary Name :-Lakpa Gyaljen Ghale
Tranche :-Third Tranche Received
Housing Typolog :-Timber structure with two rooms and light CGI flexible roof

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When is the deadline for the second tranche for the beneficiaries who have received the first tranche?	Ward Chair-person	Those beneficiaries who have received the first tranche within the Ashar has the deadline of Poush month to receive the second tranche.
When is the deadline for the third tranche?	Beneficiary and ward-chairperson	Those beneficiaries who have received the second tranche within 2075 Poush will have the deadline of 2076 Baisakh for the third tranche.

Challenges and Way Forward

Challenge	Way Forward
Lack of information among the beneficiaries about the tranche deadline and the procedures related to get the tranche.	DLPIU Building , DLPIU GMaLI must conduct an orientation program about the deadline through the ward technicals.

Case Study

Thuman village is situated in Gosaikunda RM ward number 1. This village is highly affected by the Gorkha earthquake 2015.

All together 354 HHs are completely damaged by the earthquake but no any human casualty occurred by earthquake. Roads were not accessible on this place before, so transportation of construction materials is very hard. People used their local construction materials like stone and timber for construction. The houses were made by using dry stone and timber. So by the earthquake all the houses were damaged. Now the reconstruction status is satisfied in this place. The GMaLI tranche update of this place is as follows:

Total Eligible HHs for housing grant	354
Total enrolled HHs for housing grant	341
First tranche received HHs	341
Secound tranche received HHs	297
Third Tranche received HHs	254
HHs Constructed	254
Total Eligible HHs for Retrofitting grant	0



According to Ward president Mr. Phurpu sonam Tamang the reconstruction process is very complicated at first time. The design approved by NRA (design Catalog) was not accepted by community. Road is not accessible at that time and its very difficult to transport construction materials at village (Approximately 2 hours walk from Highway) . After the timber structure design approved by NRA then the process speed up at this place. We saw all the houses were constructed by using timber. People were very familiar with timber because we saw that big timbers were has been used on their old houses. One of the villagers shows us 50 years old timber column which was look new now also. Also the weather at this place is very cold near Langtang peak so the timber is environmental friendly also. Its not so much cold inside timber structure and also timber is not affected because of cold weather.

10 displaced HHs from this place has already taken the land grant from NRA and they have completed their house. They also received all the housing grant from GoN. The ward president Mr. Tamang share that 12 houses have been left out during the resurvey and verification process and are not on the eligible list.

The reconstruction status is satisfactory in this place but the challenges which we can see in other places i.e one room house problem is also the major problem in this area. Some people who have big structure had constructed one room in front .Some vulnerable HHs has constructed one room timber structure in front of their old EQ affected HHs . And they are living in same old house and use the new one room for kitchen. It seems that the social mobilization part is not effectively adopted same as other areas of district.

House construction ongoing on Right side and completed at left side by displaced HHs – Before and after photo

