


## FACTS AND FIGURES

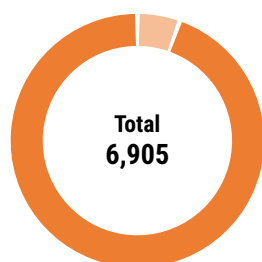

Damage Status - Private Structures

## MAJOR HOUSING TYPOLOGIES

| Typology                               | Municipal | District |
|----------------------------------------|-----------|----------|
| Stone and Mud Mortar Masonry           | 89.26%    | 89.07%   |
| Adobe Structures                       | 5.63%     | 4.25%    |
| Brick and Cement Mortar Masonry        | 1.87%     | 2.11%    |
| Reinforced Cement Concrete (RCC) Frame | 1.51%     | 3.05%    |
| Others                                 | 1.72%     | 1.52%    |

CBS damage assessment survey, 2015

## HOUSING RECONSTRUCTION & RETROFIT UPDATES

### Reconstruction Status

|                                    |       |
|------------------------------------|-------|
| Total Eligible HHs                 | 6,954 |
| PA Agreement                       | 6,472 |
| I <sup>st</sup> Tranche received   | 6,472 |
| II <sup>nd</sup> Tranche received  | 5,767 |
| III <sup>rd</sup> Tranche received | 3,823 |

### Houses

Under Construction: - Completed: 3,927

### Retrofitting Status

|                                   |     |
|-----------------------------------|-----|
| Total Eligible HHs                | 175 |
| PA Agreement                      | 49  |
| I <sup>st</sup> Tranche received  | 49  |
| II <sup>nd</sup> Tranche received | 175 |

### Grievances

Registered: 1,389  
Addressed: 759

### Non-compliances

Registered: -  
Addressed: -

Data Updated on: 2019-05-27 00:00:00

## P0 Presence

Active: No POs Reported

**Phased Out:** ACF (Shelter), ACF (Hygiene), GON-PAF (Shelter), MI (Health), NJSI (Education), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Hygiene), OXFAM-GB (Shelter), PA (Shelter), RoomTR (Education), RoundT-N (Education), SCI (Education), SCI (Shelter), SCI (Social Protection), SCI (Hygiene)

## OTHER SECTORS



### Schools

Damaged: 63  
Under Construction: 37  
Construction Completed: 37



### Health Posts

Damaged: -  
Under Construction: -  
Construction Completed: -

## STATUS OF CONSTRUCTION MATERIALS

| Materials    | Unit           | Req. Quantity* | Ava. | Cost (NRs.)** |
|--------------|----------------|----------------|------|---------------|
| Stone        | m <sup>3</sup> | 148,589        | Y    | 8,000         |
| Aggregate    | m <sup>3</sup> | 141,675        | N    | 12,000        |
| Sand         | m <sup>3</sup> | 15,765         | Y    | 7,000         |
| Timber       | cu. ft.        | 17,824         | Y    | 3,000         |
| Cement (PPC) | Sack           | -              | Y    | 950           |
| Cement (OPC) | Sack           | 470,922        | Y    | 1,050         |
| Rebars       | kgs.           | 1,626,558      | N    | 98            |
| Tin          | bundle         | 19,228         | -    | -             |
| Bricks       | pcs.           | 2,217,096      | Y    | 16            |

### Types of Workers

1. Skilled mason
2. Labourer

### Avg. daily wage (NRs.)

1,200 /-  
1,000 /-

## KEY CONTACTS

### Municipal Office

Man bahadur lama  
Mayor  
9851082727

### Municipal Office

Kishor Paudel  
Focal Person  
9842747770

### Municipal Office

Sita Lama  
Deputy Mayor  
9851254126

### GMaLI/NRA

Bickey Lakha  
NRA Chief-District  
9849179333


### Municipal Office

Santosh Kumar Dahal  
Administration Officer  
9841364307

### DLPIU-Building

Koshnath Adhikari  
DUDBC.DLPIU Chief  
98550465884

## HHs WITH LAND ISSUES




## STATUS OF TECHNICAL STAFF

| Staff               | Available Nos.            | Additional Req. Nos.      |
|---------------------|---------------------------|---------------------------|
| Engineers           | 1                         | 1                         |
| Sub-Engineers       | -                         | -                         |
| Asst. Sub-Engineers | -                         | -                         |
| Masons              | - (7 days)<br>- (50 days) | - (7 days)<br>- (50 days) |


Source: Municipal survey

## MASON TRAINING

**Trainings (# out of total required)**

Source: HRRP Analysis

## TA ACTIVITIES MAP

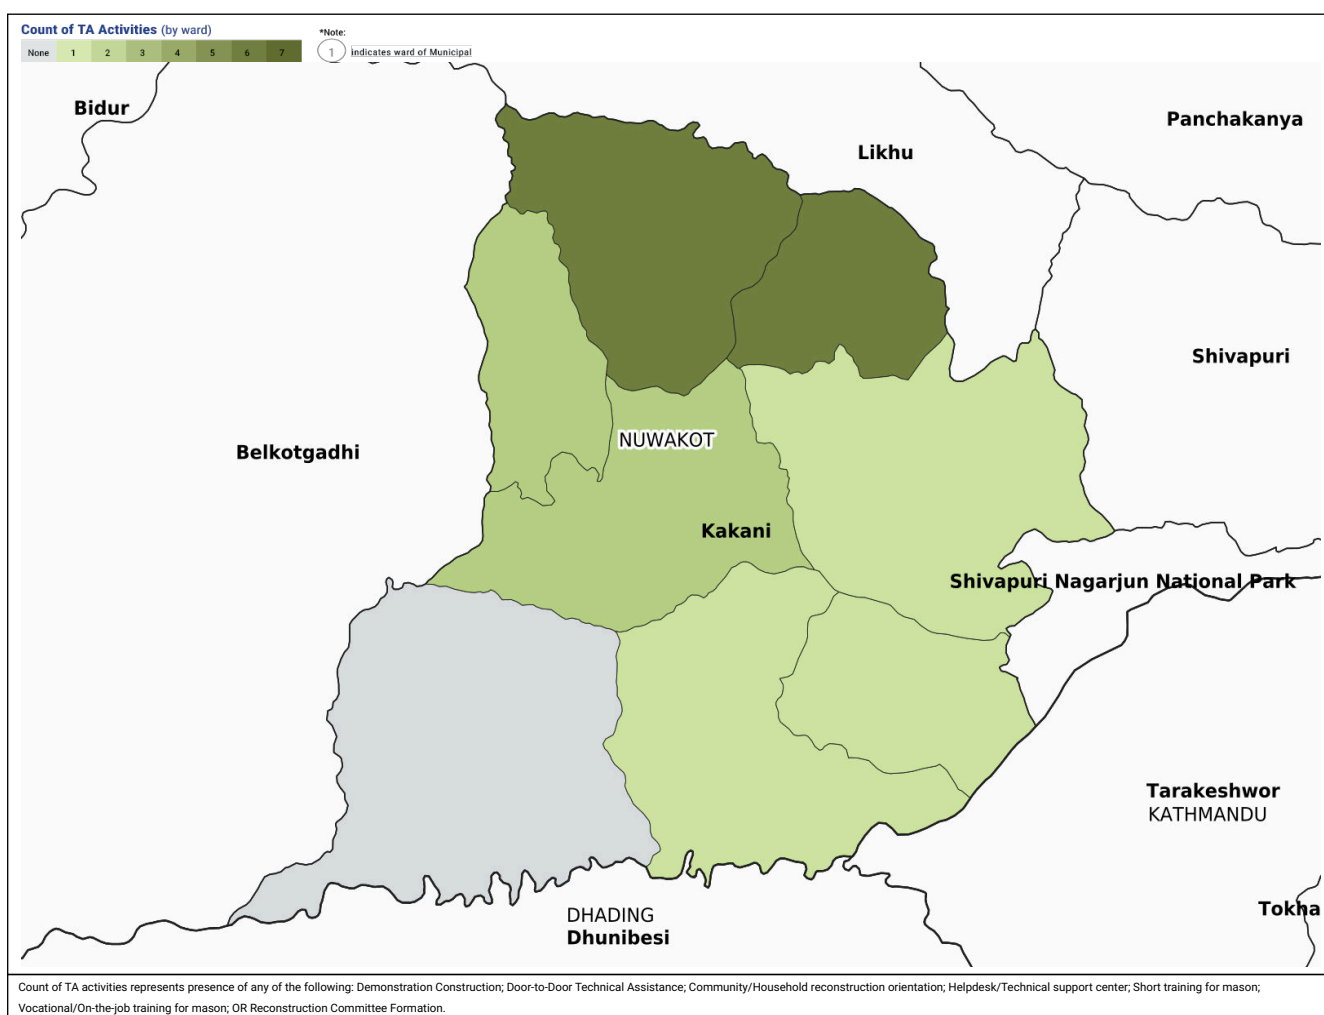

## FAQs

**Q: What documents are required for enrolment in the GoN housing reconstruction programme?**

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

**Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?**

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

**For further information** 1. Badri Pyakurel (District Coordinator) 9851154201 2. Sachin Sapkota (District Technical Officer) 9847621292 3. Manisha Rai (District Information Management Officer) 9842062006
