

District Report

Sindhuli

4 – 11 May 2018

Activity Summary

Activity	Contact Person	Reference Document
Info Pack, District Profile Distribution to Sunkoshi Rural Municipality and collection of Feedback.	techcord.sindhuli@hrrpnepal.org	
Conducted joint monitoring and field visit in sunkoshi Rural Municipality and respective wards and ward office from 8 th May 2018 to 12 th May 2018 in presence of M&E consultant from CLPIU and DLPIU Engineer.	techcord.sindhuli@hrrpnepal.org	

Upcoming Events & Meetings

	Date, Time, and Location	Contact Person
Planning to conduct Technical coordination meeting focusing on the agenda of design approval of Timber Structure and issues on non-compliance houses.	On 16 th May 2018, at NRA Meeting Hall, from 12:00 PM to 2:00 PM.	techcord.sindhuli@hrrpnepal.org

News & Updates

- Restructuring of NRA office in the district
- Change of NRA chief

Field Visit Reports

Date	Location	Participants
8 th May 2018 – 12 th May 2018	Sunkoshi Rural Municipality Sindhuli	• Er. Kiran Mahat (M&E) Consultant, Er. Lekhanath Paudel, Er. Sabal Bhandari (DLPIU)
Objective(s)	• Visit with Ward President and monitoring owner- driven households of Sunkoshi Rural Municipality. • Discussion about the problem related with reconstruction, tranche received by the beneficiaries, policies made by respective ward president, upcoming events by NRA, etc.	
Summary	The field visit was conducted by NRA/HRRP joint monitoring with M&E CLPIU Sindhuli from 8 th May 2018 to 12 th May 2018 in Sunkoshi Rural Municipality.	

- On 8th May 2018 we visited with the president, beneficiaries of ward no 7, Majhuwa, of Sunkoshi Rural Municipality and discussed on the problems and challenges in the reconstruction, most of the beneficiaries of ward no 7 were waiting for the government 2nd tranche, due that those houses were constructed recently after the Gorkha Earthquake and must be corrected.
- On 9th May 2018 we visited with the president, beneficiaries of ward no 1 & 2, Dumja, of Sunkoshi Rural Municipality and discussed on the problems and challenges in the reconstruction. Most of the houses had got government 2nd tranche. We found one critical case of Single widow woman who had not till started the construction.
- On 10th May 2018 we visited with the president, beneficiaries of ward no. 6 & 4, Sitalpati and Kotgaun, of Sunkoshi Rural Municipality and discussed on the issues and challenges regarding reconstruction. NRCS Sindhuli had given technical assistance in Sitalpati so about 70% of construction had completed on that area.
- On 11th May 2018 we visited with the president, beneficiaries of ward no 3 & 5, Gaikhora and Purano Jhangajholi, of Sunkoshi Rural Municipality and discussed on the issues and challenges regarding reconstruction. In ward no. 5 of Gaikhora we found one room building but had already received government 2nd tranche. In ward no. 3, Purano Jhangajholi there was one problem regarding DLPIU Engineer who had been away from field since 4 to 5 months.
- On 11th May 2018 we visited and conducted the Palika Level Meeting in Sunkoshi Rural Municipality in presence of Vice Chairperson Mr. Dirbu Singh Moktan. During meeting we discussed on the reconstruction challenges and asked for overall Rural municipality progress regarding reconstruction.

Reconstruction Progress Report of Sunkoshi Rural Municipality

S. N	Name of Ward	Total Beneficiaries	1 st Tranche Received	2 nd Tranche Received	3 rd Tranche Received	Remarks
1	Mahadev Danda	1024	876	691	217	
2	Pokhari	1178	1178	588	138	
3	Khola Gaun	1155	1153	1020	244	
4	Khangsang	880	805	742	423	
5	Solpa Thana	486	445	209	28	
	Total	4723	4457	3250	1050	

Source: Sunkoshi Rural Municipality Office, Ratmata 2075/01/28.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
➤ Non-compliant houses	Control over	DLPIU Engineers	As soon as possible
➤ Scarcity of Skilled mason	Mason Training	DUDBC, CLPIU, NRA	As soon as possible
➤ Unavailability of DLPIU Engineers	Regular Monitoring	DLPIU, CLPIU, NRA	Quick
➤ Problems regarding retrofitting houses	Retrofitting Training	NRA, DLPIU	As soon as possible

Photos



Caption: Stone Masonry building located in Majhuwa ward no – 07 of Sunkoshi Rural Municipality, Sindhuli district. This house was built recently after the Gorkha Earthquake, there is attic height problem. Due to non-compliance issue house owner hasn't received government 2nd tranche.



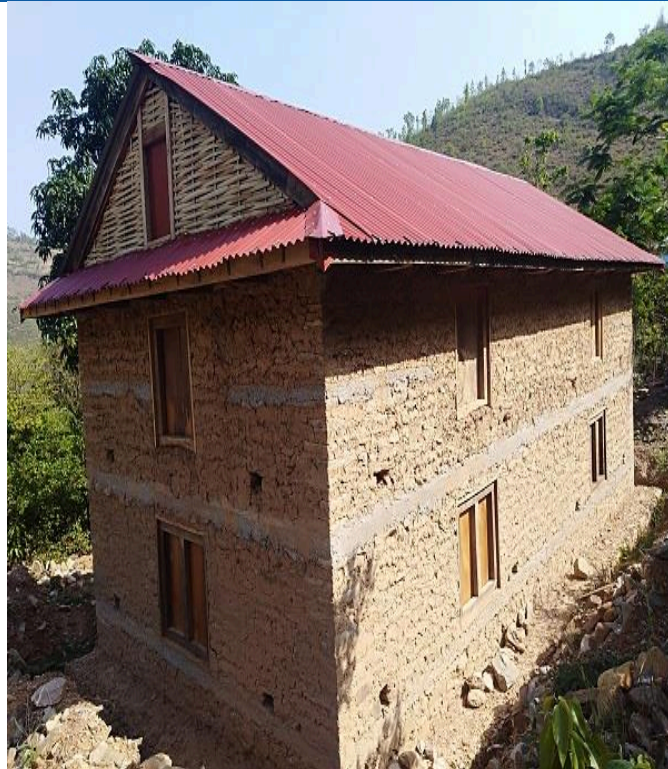
Caption: Stone Masonry building located in Tamling Ward no – 03 of Sunkoshi Rural Municipality, Sindhuli district. This house was built recently after the Gorkha Earthquake, before the deployment of DLPIU Engineers. The house is L-Shape with non-compliance issue, so that house owner hasn't yet received government 2nd tranche.



Caption: Stone Masonry building located in Majhuwa ward no – 07 of Sunkoshi Rural Municipality, Sindhuli district. This house was built recently after the Gorkha Earthquake, there is attic height problem. Due to non-compliance issue house owner hasn't received government 2nd tranche.



Caption: Stone Masonry building located in Amare Sitalpati ward no – 06 of Sunkoshi Rural Municipality, Sindhuli district. NRCS/ERO Sindhuli provided technical assistance to build houses in this area. The house was non-compliance so we provided some correction tips so

	that house owner could receive government 2 nd tranche.
	
Caption: Stone masonry building located in Gaikhora ward no – 05 of Sunkoshi Rural Municipality, Sindhuli district. The house was non-compliance due that there was no horizontal band below and top of the window. House owner has received government 2nd tranche and waiting for 3rd tranche.	Caption: Stone masonry building located in Gaikhora ward no – 05 of Sunkoshi Rural Municipality, Sindhuli district. Construction of this house is completed but there seems problem regarding that no adequate set back distance from the road but house owner has received government 2nd tranche.
