

Monthly District Report

Sindhupalchowk

27 September - 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Sindhupalchowk	Field visit with DLPIU GMaLI/ Building to To have Interaction with the elected officials on the progress of housing reconstruction and further planning to gear up the progress. - To discuss and get way forward with ward chairperson and Palika on being not completed the house (complete house) despite getting third tranche long ago. -Discuss on Retrofit with Palika and ward officials.	30 th Sept – 4 th Oct	Tripurasundari and Lisankhupakhar Rural Municipality	pradip.sharma@hrrpnepal.org	Field visit section below
	To inform that landless beneficiaries are beneficiaries;Chautara Mun, Indrawati Mun, Melamchi Mun To make landless and relocation beneficiaries oriented towards land purchaseIndrawati Mun ward no. 3,4,5 To prepare necessary documents for the purchase of land; Tripura Mun, Bhotekoshi Mun, Jugal Mun, Balephi Mun	13 th - 14 th Oct	GMaLI	pradip.sharma@hrrpnepal.org	N/A
	Field visit with DLPIU GMaLI/ Building to To have Interaction with the elected officials on the progress of housing reconstruction and further planning to gear up the progress. - To discuss and get way forward with ward chairperson and Palika on being not completed the house (complete house) despite getting third tranche long ago. -Discuss on Retrofit with Palika and ward officials.	16 th - 19 th Oct	Barhabise Municipality and Bhotekoshi Rural Municipality	pradip.sharma@hrrpnepal.org	Field visit section below
	Prepare District Report, Meeting minutes, meal report	21 th - 22 th Oct	N/A	pradip.sharma@hrrpnepal.org	GD

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
HRRP 4 orientation and Discussion Workshop	24 th to 25 th Oct 2019	HRRP Nepal	dmt@hrrpnepal.org

Tranche Status (Sindhupalchowk)


Table of Tranche Status: As of 16th October 2019

Municipality	Reconstruction				Retrofit		
	Eligible HHs	1st Tranche	2nd Tranche	3rd Tranche	Eligible HHs	1st Tranche	2nd Tranche
Balefi Gaunpalika	6241	5977	5879	5502	91	12	0
Barhabise Nagarpalika	7988	7902	7517	6678	27	16	0
Bhotekoshi Gaunpalika	4438	4152	3680	2431	69	15	0
Chautara SangachokGadhi Nagarpalika	14580	13784	13375	12761	97	32	0
Helambu Gaunpalika	5732	5232	4870	4407	52	8	0
Indrawati Gaunpalika	8569	8291	8065	7399	39	26	0
Jugal Gaunpalika	5660	5599	5428	5103	17	15	0
Lisangkhu Pakhar Gaunpalika	4873	4972	4466	3742	40	11	0
Melamchi Nagarpalika	13946	13192	12482	10845	123	9	0
Panchpokhari Thangpal Gaunpalika	6461	6922	6486	5496	20	8	0
Sunkoshi Gaunpalika	5608	5659	5427	5004	34	10	0
Tripurasundari Gaunpalika	4512	4489	4366	3965	19	5	0

Graph of Tranche Status: As of 31th August 2019

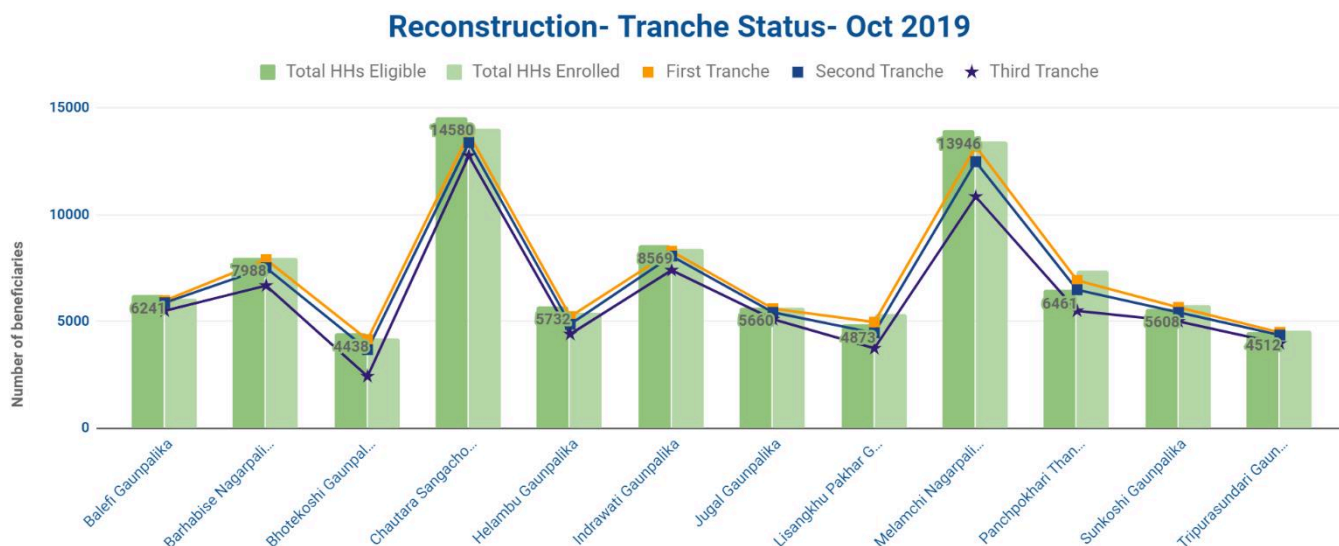

Graph for Retrofitting Status: As of 31th August 2019

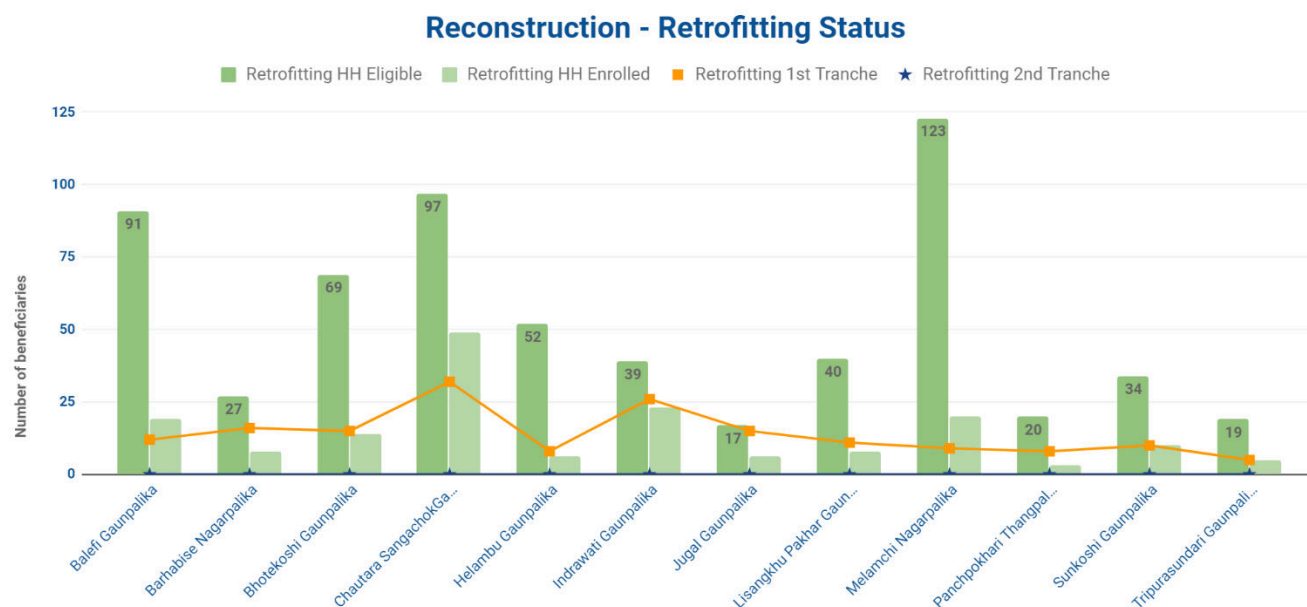

Field Visit Report (Sindhupalchowk)

Visit 1

Date	Location	Participants
30 th September to 4 th October, 2019	Tripurasundari and Lisankhupakhar Rural Municipality	Bishnu Paudel; Chief GMaLI, Pradip Sharma, HRRP, Sunita Shrestha DLPIU, Building and Palika/ward members
16 th to 19 th October, 2019	Barhabishe Municipality and Bhotekoshi Rural Municipality	Binod Sah, MIS Officer DLPIU, Building; Pradip Sharma, HRRP, Deepak Mahato and Youbaraj Khatri Engineer DLPIU Building and Palika/ward members
Objective(s) Tripura RM	- Regarding the reconstruction issue - Regarding the landless issue - Regarding Technician issue - Regarding the reconstruction issue - Regarding Completion certificate - others: Decisions: - Detailed details of how many landless beneficiaries and what the condition of their building is like were to be find out by the ward level. - In the past, the last day of the technical month used to come and prove their attendance sheet and return, but now some changes have come. - According to Palika Chairperson Mr. Bhupendra Shrestha, we will inform you soon about the status of the beneficiaries who did not own a home with fifty thousand. - Certificates of completion of the building have been distributed by some wards and the rest of the wards are also moving forward.	
Objective(s) Bhotekoshi Rural Municipality	- Review of last meeting/meeting minute - Review of last meeting/meeting minute - Discussion about retrofit - Discussion about the target - Discussion about CS entry - Discussion about final inspection - Regarding the Decisions: - According to the field engineer, thirty-six beneficiaries have to reconstruction from the retrofit beneficiary in ward number four, but as of now nothing is known about what happened, Seven beneficiaries have come up with the list on retrofit in ward number 1, but there are nothing to break it down but the technical said that we should send a technical report with the same photo of whatever is in their field. - According to the technician, the Dwarka Foundation has not built a one hundred fifty-six house without the target, so the target is not dated.	

	3. According to the technician, the file sent in the month of Bhadra has not been received yet and we have not been informed that there is no CS entry. 4. Jica EHRP's friends say that we had a problem with work being the focus too much on the completion Certificate of Enrichment, but let's say the technical first but we did the second and third inspections and only the last inspections. 5. Displaced beneficiaries were fifty-three and twenty beneficiary names came up list, but another beneficiaries list did not come as to what happened.
Objective(s) Barhabishe Municipality	• Review of last meeting/meeting minute • Regarding the reconstruction issue • Regarding the CS entry issue • Regarding the progress in reconstruction • others: <i>Decisions:</i> • According to the municipality chief Mr. Nim Funju Sherpa, the responsibility of rebuilding the ward chairperson has been reduced at the wider level. • According to the technician, the file sent in the month of Srawan has not been received yet and we have not been informed that there is no CS entry. • The ward chairperson asked why the twenty beneficiaries did not come tranche, the building informed that there was no stopping the beneficiary's structure report. • Field Technical says the building is not built in the village and how our target is reached • Due to the absence of some ward engineer reports, the chief of administrative officer of the municipality informed that the meeting could not be held at the next meeting.
Why was the visit carried out in this location?	
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'	
NA	
Summary	It is decided to collect the list of beneficiaries who have not yet reconstruction their first installment and submit it to all the field engineers in the municipality and take action from the municipality by letter from each ward office.

Field Visit:

- No. of HHs visited: 21
- No. of meetings with engineers:
- No. of meetings with local officials: 9

Meeting: NA

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe

Photos



Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Tripurasundari Rural Municipality



Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Bhotekoshi Rural Municipality



Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Barhabise Municipality



Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Barhabise Municipality

Photos



The house located in Bhotekoshi Rural Municipality ward no.1, the house owner name is Bhupendra bahadur Pradhan. he has received second tranche and third tranche from GoN. The house is brick and cement mortar with Reinforced Cement Concrete Framed Building (RCC)



The house located in Bhotekoshi Rural Municipality ward no.1, the house owner Name is Bikash BK has received second tranche and third tranche from GoN. The house Load Bearing Stone and Mud Mortar Masonry.

Housing Typology Report



The house located in Barhabise Municipality ward no.1, the house owner Name is Prem Bahadur Magar. He has received second tranche and third tranche from GoN. The house is Reinforced Cement Concrete Framed Building (RCC).



The house located in Barhabise Municipality ward no.4, the house owner Name is Urken Sherpa. He has received second tranche and third tranche from GoN. The house is Stone and Mud mortar with load bearing structure.

Housing Typology Report



The house located in Tripurasundari Rural Municipality ward no.2, the house owner Name is Jhule Thami. He has received second tranche from GoN. and third tranche is not processing. The house is Stone and Mud mortar with load bearing structure.



The house located in Tripurasundari Rural Municipality ward no.2, the house owner Nmae is Kushule Thami. He has received second tranche from GoN. and third tranche is not processing. The house is Stone and Mud mortar with load bearing structure.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)

Challenges and Way Forward

Challenge	Way Forward
Jica EHRP's friends say that we had a problem with work being the focus too much on the completion Certificate of Enrichment	First but we did the second and third inspections and only the last inspections.
