

District Report

Ramechhap

23 November - 6 December 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Ramechhap Team has successfully completed the General Coordination meeting at 27 th November 2018. The coordination meeting was chaired by Gmali Chief Mr. Krishna Lal piya. A total of 25 participants were take participate in the meeting program from Government office and partner organization. The meeting was facilitated by HRRP team all partner's organization presented their progress, issues and challenges. Likewise, DLPIU, DSE shared the reconstruction status and shared the noncompliance issue of the district. At the end of the meeting Gmali chief put his remarks to thank you all the partners organization providing their support on reconstruction and hopefully for further support to Ramechhap till the end.	27 th Nov 2018	23	2	Mr. Prakash Bishwakarma	Link report
Ramechhap team has successfully completed the joint monitoring visit to Dorumba RM starting from 5-8 th Dec 2018. During the visit Joint monitoring team had conducted ward level meeting at Thapagaun and Gausara. Similarly, team has observed the topology of house construction in the area. In the joint monitoring visit a total of 5 participants were participated from DLPIU/HELVATAS and HRRP.	5-8 th Dec 2018	5	0	Mr. Prakash Bishwakarma	Report
MEAL Data successfully updated and send to Kathmandu HRRP.	2 Dec 2018			Mohammad Jawed	Link


Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
General coordination meeting	11, Dec 2018, DTO, office meeting Hall, 11:00am onwards	GMali/ HRRP Ramechhap	Prakash Bishwakarma


Tranche Status

Rural/Municipality	Doramba	Gokulganga	KhadaDevi	Likhu	Manthali	Ramechhap	Sunapati	Umakunda
Total HHs Surveyed & GR	5085	6343	5210	5605	11103	6581	3669	4984
Total HHs Eligible	5085	6343	5210	5605	11103	6581	3669	4984
Total HHs Enrolled	4485	5356	4860	5225	10043	5940	3348	4296
First Tranche	4485	5356	4860	5225	10043	5941	3348	4296
Second Tranche	3508	4894	4463	4686	9104	5375	3044	3826
Third Tranche	2052	3664	3195	3532	6439	4151	1456	2145
Total HH Constructed								
Grievance Registered	2448	1031	2007	1562	2815	1841	1392	843
Grievance Addressed	2448	1031	2007	1562	2815	1841	1392	843
RF HH Eligible								
RF HH Enrolled								
RF 1st Tranche								
RF 2nd Tranche								
Non-Compliance Registered	31	57	7	69	78	26	7	2
Non-Compliance Addressed	31	57	7	69	78	26	7	2


Graph of Tranche Status:

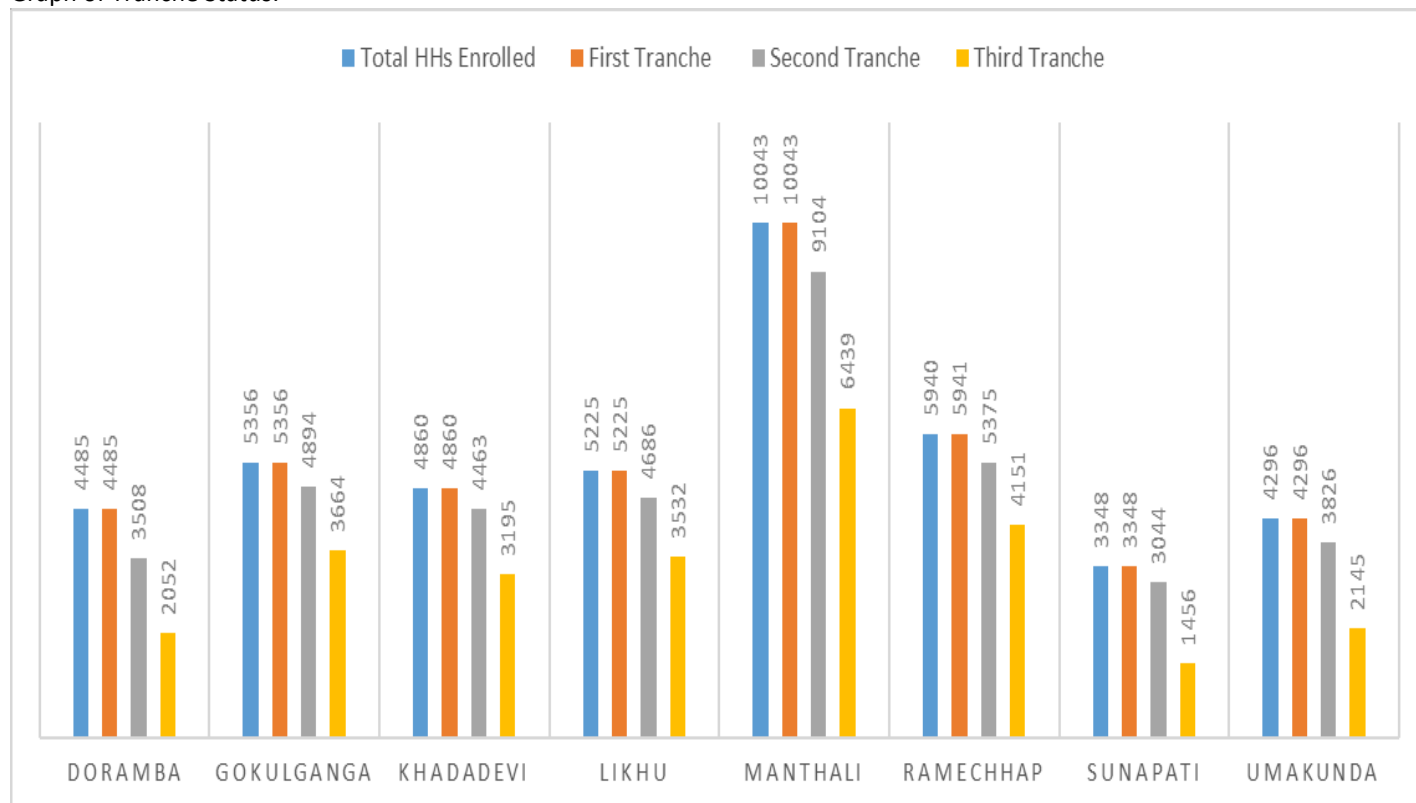

Graph for Retrofitting Status:

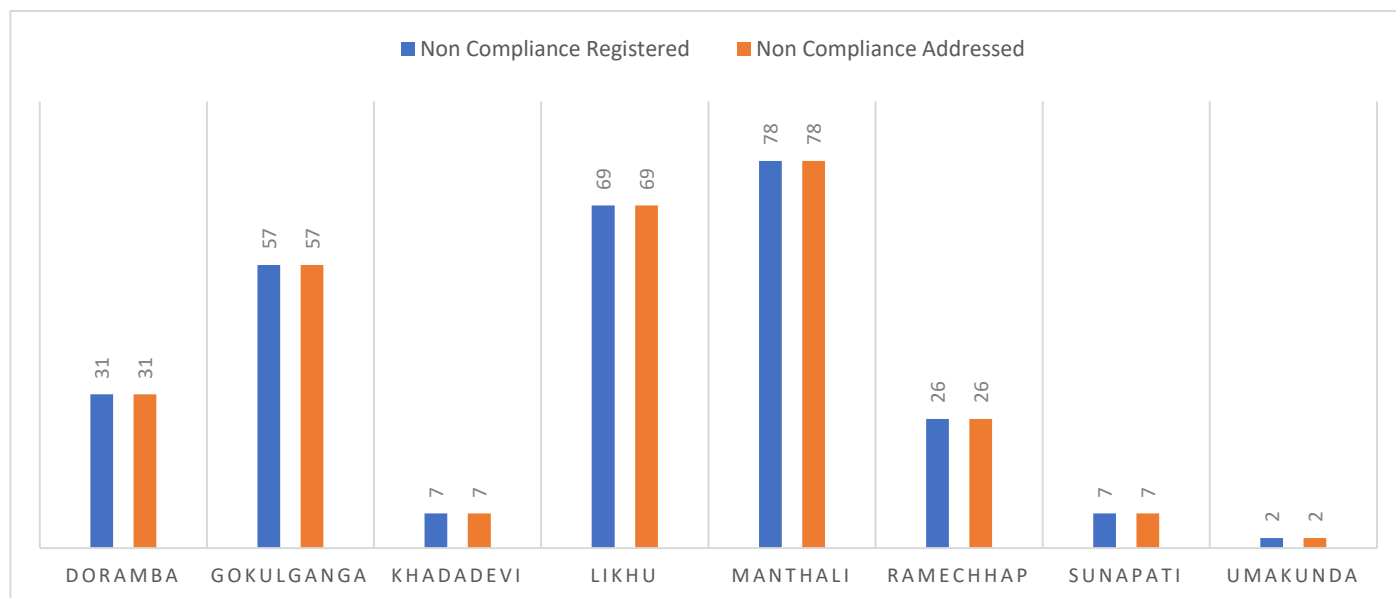

Graph for Grievance Status:

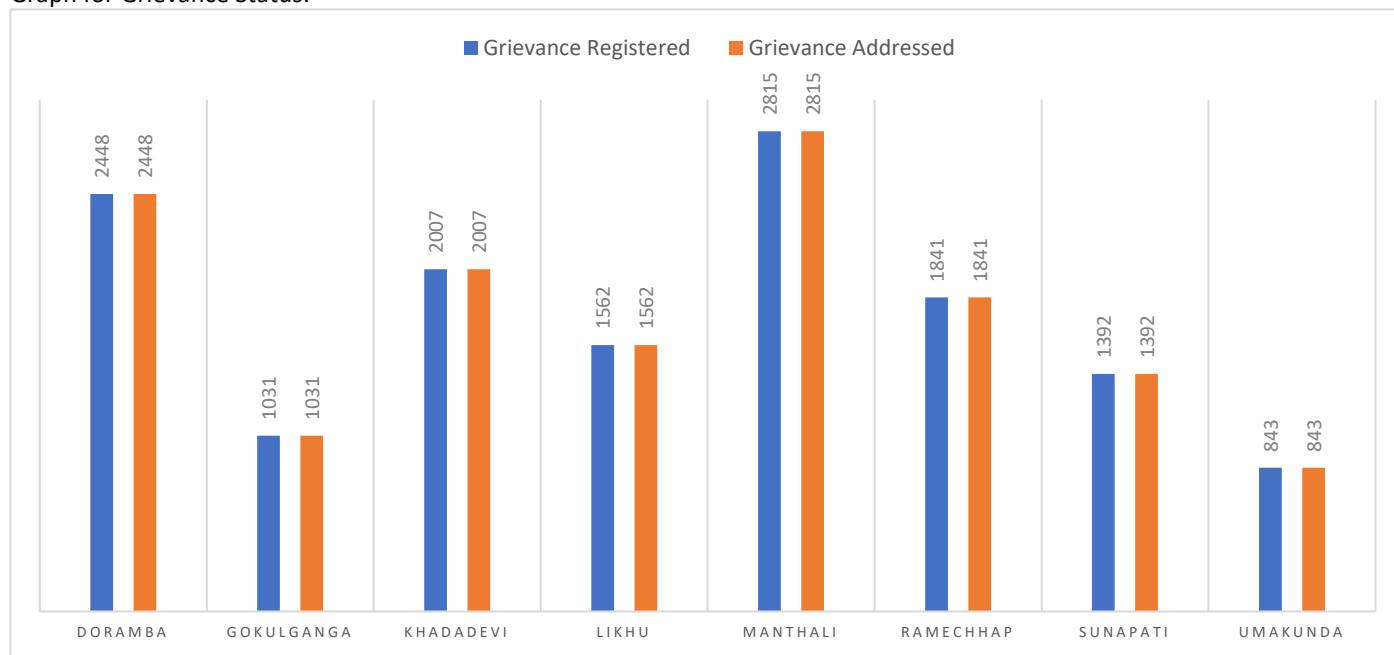

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
5-8 DEC 2018	Dorumba RM (Thapagaun and Gausara)	Prakash Bishwakarma (DC), Tulsi ram Lamichhane (TC), Ramesh Luitel (HELVATAS) and Jadhish Chanda (Engineer Focal Person DLPIU)
Objective(s)	- To observe the reconstruction status and interaction with reconstruction beneficiaries - Interaction and meeting with the local representatives' ward level.	
Summary	Housing Recovery and Reconstruction Platform (HRRP) is working in Nepal to support Government of Nepal (NRA, MOUD/DUDBC, MOFALD) in coordination, Strategic planning, facilitating cooperation with the national and international organizations, the private sector, and public associations involve in recovery and reconstruction. In this regards team Ramechhap has conducted and successfully completed the joint field monitoring visit to Dorumba Rural Municipality of Ramechhap District from 5 -8th Dec 2018. Objective of Field Visit: The main objectives of the field visit were as follows: - To observe the reconstruction status of the beneficiaries - To provide inputs to the beneficiaries in regards of housing reconstruction.	

- Interaction with the local representatives and beneficiaries to find the challenges and issues in the reconstruction.

Team Involved in the Joint Field Monitoring visit:

- Jadhish Chand, Focal Person Engineer, DLPIU, Ramechhap
- Ramesh Luitel, Engineer, HELVATAS
- Prakash Bishwakarma, District General Coordinator-HRRP
- Tulsi Ram Lamichhane, Technical Coordinator-HRRP

Key point of the visit at Ward-2, Dorumba

- A total of 302 houses are now actively construction that means 302 beneficiaries has now actively started to build their house in Ward-2, Dorumba.
- A total of 2-5 beneficiaries are started to discussion with the technical person of Ward-2, Dorumba for the provision and processes.
- A total of 50 beneficiaries had not done agreement due to land problem, Guthi Land and some have land on their relatives.
- Retrofitting beneficiaries are interested to transfer in the full construction beneficiaries.

Key point of the visit at Ward-7, Dorumba

- A total of 145 beneficiaries are in retrofitting beneficiaries and they are not interested do agreement in retrofitting beneficiaries due to thinking that with in only 1 lakh it is not enough for the house reconstruction.
- Some of the beneficiaries have not done agreement with government because of land problem i.e. argument with brother for house certificate (lalpurja)
- On the behalf of Ward office, the campaign was established to motivate beneficiaries to build the house with the guideline of government for earthquake resilience. Through the campaign lots of the beneficiaries start house construction who had received 1st and 2nd government tranche.
- Partner organization HELVATAS is working in the field for TA. Support of Community Resource person (CRP) is very crucial in the area to make beneficiaries motivation and technical support reported by government technical person. Throughout the mobilization of CRP from HELVATAS it is very positive and construction rate is increasing and support to the government technical person.
- Ward chairperson requested to the technical person and CRP to identify the beneficiaries those who are death, it will support to identify actual earthquake beneficiaries.
- 9 Household beneficiaries have taking suggestion to return the government grant but due to the campaign started by the ward office, regular visit and motivation from the CRP/Technical person now those beneficiaries have started the construction.
- Retrofitting beneficiaries were not interested to make agreement to the government because they are not secured about the grant will enough for the retrofitting.
- A total of 85 beneficiaries are interested and recommended to sift in full beneficiaries.
- Still ward chair person is not satisfaction with the earthquake beneficiaries list.
- With the recommendation of ward office some beneficiaries 3rd tranche had been stopped because they have not construction toilet.
- Ward chairperson thanks to all the NGOs and supporting hands in the reconstruction and looking forward for support till the end.

Key point of the visit at Ward-4, Dorumba, Gausara

- Due to the geography, scatter area and road condition of the area technical person and social mobilization movement is very low.
- HELVATAS as a partner organization is working in the area for technical assistant. Helvatas Community resource person now active and supporting to the government technical person.
- DLPIU/HELVATAS CRP should coordination and work together for better and smooth working environment.

- Ward chairperson not present is also one of the challenge to work smoothly in the area reported by technical person.
- 268 beneficiaries still not start construction their houses after receiving 1st tranche. They are still stay at their old house.
- 10-12 households are non-compliances in the area till date.
- The reconstruction status shows very slow in the area due to the other area but Helvatas CRP and government technical person effort 184 3rd tranche files were forwarded to the DLPIU district for further process.

Photos



House of Lothan Tamang at Dorumba ward-7, Thapagaun. The house owner has received 2nd tranche of government tranche



Meeting in ward office at Thapagaun with ward representative and technical person.



Meeting with the Technical person and CRP of Helvatas at Gausara village of Dorumba RM



House construction at Thapagaun at Dorumba-7. Mr. Hasta Bahadur Tamang is the owner of the house. Who received 2nd tranche and forwarded for 3rd tranche.

Housing Typology Report



The house of Bir Bahadur Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Nima Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Harta Bahadur Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Dhana Dorje Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using brick in cement mortar. RC bands has been provided in the house. The house owner has constructed a single way temporary roof. The house has been completed upto roof band. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Geet Bahadur Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed upto plinth level. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018. The house owner will continue the reconstruction after the transportation will be ease in the village.



The house of Buddhi Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using brick in cement mortar. Rc bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018. The house owner is one of the 1263 lying in vulnerable group.



The house of Tulka Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Sonam Kumar Moktan being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in cement mortar. RC bands has been provided in the house. It is a RC frame house and its construction has been completed. The rebars of 12mm dia has been provided in the column which do not comply with the building code. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.



The house of Lothan Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been



The house of Chandra Bahadur Tamang being constructed in formerly Lakhanpur VDC current Doramba Rural Municipality ward no 7. The house has been constructed using stone in mud mortar. RC bands has been provided in the house. It is a load bearing house and its construction has been completed. The house owner has received the second tranche of reconstruction tranche as of date 7th Dec 2018.

Challenges and Way Forward

Challenge	Way Forward
Retrofitting beneficiaries were not interested to make an agreement with the DLPIU because they are not secured about the grant will enough for the retrofitting	Technical personnel should motivation to the beneficiaries and make clearly understand about the grant provided by government that this is only the subsidy.
Some of the beneficiaries have not make agreement to the government even they are in the list of earthquake beneficiaries because of the land issue.	Ward office should make motivation and play important role to resolve the land issue.
The reconstruction status was very slow and till the date only 38 files was recommended for 3 rd tranche due to the technical person frequency and geography condition of the area.	Technical person should make coordination with the HELVATAS Community resource person and work together for the pace of the work.
