

Monthly District Report

Lamjung, Tanahun, Kaski, Syangja

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lamjung	Field Visit: HRRP team together with GMAI, Building and DSE have visited three Municipality (Rainash , SundarBazar and Madha Nepal)during these period. Main objective of Visit: - Palika level meeting with nagarpalika and ward stack holders. - Field inspection and information collection (Kobo app, Typology etc) - Interact with HHS regarding challenges faced during reconstruction process. - Non-Compliance houses visit.	27-May 29-may	Rainash NP office Sundar Bazar NP office Madha Nepal NP office	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Level Meeting: During this period HRRP district team have conducted palika level meeting at three Nagarpalika (Rainash , Sundarbazer and Madha Nepal) at nagarpalika offices. Participant from Nagarpalika offices , GMAI , Building , DSE , ward chairperson and technical person of ward and palika level participated at meeting. Major decision made during Palika level meeting: Rainash Nagarpalika: - Reconstruction update of Palika by both GMAI and Building. - Discussion of challenges faced by palika and ward level and way forward to speed up reconstruction process.	27 th May 28 th May	Rainash NP office Sundar Bazar NP office Madha Nepal NP office	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	For Meeting Minutes: Rainash Meeting Minute Sundarbazer Meeting Minute Madha Nepal Meeting minute

Summary of events during this period

	Sunder Bazar Nagarpalika: • Reconstruction update of palika by both GMaLI and Building. • Request on district facilitation committee to make some decision regarding those non-compliance houses which was constructed at initial stage after Gorkha earthquake during absence of technical person at field. • Some partners organization had conducted mason training at initial phase and teaches wrong methodology of construction, so that few houses holds were build as per their instruction which doesn't meet GON compliance. So, palika meeting requested district facilitation committee and other stack holders to coordinate with that partner and make punishment as per GoN guidelines. Madha Nepal Nagarpalika: • Reconstruction update of palika by both GMaLI and Building. • Request on district facilitation committee to make some decision regarding those non-compliance houses which was constructed at initial stage after Gorkha earthquake during absence of technical person at field.				
--	---	--	--	--	--

Summary of events during this period

	Request to district facilitation committee to coordinate with Banks for fast and easy process to transfer housing grant to EQ eligible victims.				
	Palika Profile: Data information of all palika of lamjung was updated and shared with national IM team.	25-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click Here)
	Contact List Update: Contact information of DCC staff, GMaLI staff, Building and ward/ Nagrapalika technical person, Palika leve authority and partners organization was updated and uploaded on respective district google drive.	25-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click here)
	Information Update: Reconstruction and Retrofitting households list, mason training participant details, palika level reconstruction staff, tranche details has been updated and uploaded on respective district google drive also shared with national team.	27-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click here)
	District facilitation meeting: Meeting was organized by GMaLI lamjung at DCC hall Bashishare Lamjung. Meeting was chaired by DCC chief Lok Raj Pandey and different GoN officers were participated meeting. Meeting was facilitated by HRRP district coordinator Mr.Rijan Gajurel. Decision made: Coordinate with all respective palika and ward to enroll all the eligible HHs which is left behind yet from housing grant enrollment process.	9-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	Meeting minute (Click Here)

Summary of events during this period

	- Start process to refund housing grant from those house holds who have received housing grant support both from Government and partners organization. - Responsible GMaLI, Building and HRRP. - Collect information regarding houses constructed by Gorkha Welfare and will present on next facilitation meeting – Responsible HRRP, GMaLI and Building. - Coordinate with respective palika and ward to start relocation process for all eligible displaced households which was listed by NRA as soon as possible. Also conduct field visit and report CDO and DCC chief about their present condition as soon as possible.- Responsible GMaLI, Building and GMaLI.				
	Internal planning meeting together with GMaLI, Building and HRRP to speed up reconstruction process of district. Major decision made: - Information collection of all back lock file which was approved by Building but stop at GMaLI or DCTO because of some information mistake to forward for correction. - Plan to conduct at least two or more field visit and palika level meeting every month. - Better information management and	27-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	circulation between two offices to speed up reconstruction.				
	5W Data collection: HRRP district team have communicated and coordinated with all working partners and requested them to submit updated NRA 5W. 5W collection is ongoing and HRRP district team has planed to update updated 5W from coming round onwards.	23-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Tanahau	Visited government offices of Tanahau district. HRRP district team visited government offices of GMaLI, Building and DCC. Team has conducted meeting with each offices and discussed about reconstruction process and shared their experiences to way forward for different reconstruction challenges.	31-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Contact List Update: Contact information of DCC staff, GMaLI staff, Building and ward/ Nagrapalika technical person, Palika leve authority was updated and uploaded on respective district google drive.	31-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click here)
	Information Update: Reconstruction and Retrofitting households list, mason training participant details, palika level reconstruction staff, tranche details has been updated and uploaded on respective district google drive also shared with national team.	30-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click Here)
	Palika Profile: Data information of all palika of lamjung was updated and shared with national IM team.	30-May		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click Here)
	Local level Staff status: Information regarding municipal level reconstruction staff status was collected and updated at national level.	13-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Field visit: HRRP team together with Dpiu building team conducted field visit at Bhanu Municipality. Key activities:	7-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	- Field inspection and information collection (Kobo app, Typology etc) - Interact with HHs regarding challenges faced during reconstruction process. - Non-Compliance houses visit.				
	District Facilitation Meeting: District facilitation meeting at Tanahau district was conducted on Jun,5 2019. Meeting was organized by GMaLI Tanahau and it was chaired by DCC chief Mr.Santi Ramada Wamlaa and all the members of district facilitation committee members were present at meeting. Key Decision made: - To complete resurvey and verification within given time committee decided to mobilized additional technical manpower at field level. Previously allocated manpower is not sufficient to accomplish resurvey and verification within given deadline. - One day orientation program for new deployed technical staff was scheduled for 7- Jun,2019 and DLPIU building is responsible to conducted orientation program and technical staff selection. - Municipality and ward are responsible for effective mobilization of technical person at field level for resurvey and verification. Also, to monitor this activities new	6-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	Meeting Minute(Click Here)

Summary of events during this period

	committee will be form at district level for effective mobilization and to accomplish this activities with in time.				
Kaski	Visited government offices: HRRP district team visited government offices of GMaLI, Building and DCC. Team has conducted meeting with each offices and discussed about reconstruction process and shared their experiences to way forward for different reconstruction challenges.	1 st Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Contact List Update: Contact information of DCC staff, GMaLI staff, Building and ward/ Nagrapalika technical person, Palika leve authority was updated and uploaded on respective district google drive.	3-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click Here)
	Palika Profile: Data information of all palika of kaski was updated and shared with national IM team.	3-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	(Click Here)
	Local level Staff status: Information regarding municipal level reconstruction staff status was collected and updated at national level.	12-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Public Hearing Program: HRRP district team had attended public hearing program organized by GMaLI Kaski at Annapurna RM office. Representative from GMaLI, Building, RM authority with ward chairpersons and local reconstruction beneficiary were presented at hearing program: Key discussion point: Non-compliance issues: Households which was built at initial phase after earthquake before presence of technical staff at field level. - Transformation process from	6-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	Meeting Minute (Click Here)

Summary of events during this period

	reconstruction to retrofitting and vice versa. • Technical and social mobilization at field. • Information circulation from RM and ward level to district level and vice versa.				
	Information Update: Reconstruction and Retrofitting households list, mason training participant details, palika level reconstruction staff, tranche details has been updated and uploaded on respective district google drive also shared with national team.	4-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	For information (Click Here)
Syangja	Visited government offices: HRRP district team visited government offices of GMAI, Building and DCC. Team has conducted meeting with each offices and discussed about reconstruction process and shared their experiences to way forward for different reconstruction challenges.	5-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika level meeting: Palika level meeting was conducted at Putali Bazar Nagrapalika. Meeting was chaired by mayor sima kumari chattri and representative from GMAI, Building and wards chairperson and technical person were presented at meeting. Key Decision made: • Effective mobilization of technical person for resurvey and verification at field level. • Request DFC and NRA for the suitable addressment of those houses which was build	6-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	For Meeting minute (Click Here)

Summary of events during this period

	at initial phase after earthquake before presence of technical staff at field. Deployed one focal person at Nagarpalika to coordinate with districts office and technical person and wards chairperson.				
	Contact List Update: Contact information of DCC staff, GMAII staff, Building and ward/ Nagrapalika technical person, Palika leve authority was updated and uploaded on respective district google drive.	6-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Local level Staff status: Information regarding municipal level reconstruction staff status was collected and updated at national level.	11-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Profile: Data information of all palika of lamjung was updated and shared with national IM team.	5-Jun		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Technical orientation for technical and non-technical staff of Tanahau district.	19-Jun-2019 District headquarter Tanahau (Damauli) Time: 9:30 AM	HRRP coordination with GMall and Building	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org
Technical orientation for technical and non-technical staff of Lamjung district	21-Jun,2019 District Headquarter Lamjung (Beshishar) Time: 9:30 AM	HRRP coordination with GMall and Building	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org
Technical orientation for technical and non-technical staff of Kaski district	Date will decide and circulate soon District Headquarter Kaski (Pokhara) Time: 9:30 AM	HRRP coordination with GMall and Building	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org
Technical orientation for technical and non-technical staff of Syangja district	Date will decide and circulate soon District Headquarter Syangja Time: 9:30 AM	HRRP coordination with GMall and Building	Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org

Upcoming Events & Meetings

News & Updates

- **Orientation for technical staff for resurvey and verification:** Orientation was conducted at Tanahu district. On the presence of GMaLI chief and building focal person orientation program was accomplished at district headquarter Damauli.
- **Orientation for technical staff for resurvey and verification :** Orientation was conducted at Lamjung district. Building focal person Mr. Sital Babu Lohane and DSE Umesh Dangol conducted orientation session for new technical staff at district headquarter Bashishar.
- **Public hearing program at Kaski:** Program was conducted by Kaski GMaLI office at Annapurna rural municipality. Representative from GMaLI, Building, RM authority with ward chairpersons and local reconstruction beneficiary were presented at hearing program:

Key discussion point:

1. **Non-compliance issues:** Households which was built at initial phase after earthquake before presence of technical staff at field level.
 2. Transformation process from reconstruction to retrofitting and vice versa.
 3. Technical and social mobilization at field.
 4. Information circulation from RM and ward level to district level and vice versa.
 5. Importance of focal person at rural municipality level to circulate reconstruction information at palika level and ward.
 6. Palika level reconstruction challenges.
- **District Facilitation meeting at Rasuwa:** Meeting was chaired by DCC chief Mr. Kul Parsad Bhatta and participant from different GoN organization and partners were participated meeting.

Important decision made:

1. DLPIUs (GMaLI and Building) has presented housing reconstruction update of district.
 2. To speed up private housing reconstruction process following decision were made regarding relocation process:
 3. Payment will make as soon as possible by GMaLI for land owners who have sold their lands for 14 HHs of Uttargay RM ward 5. Rural municipality, ward DCC and others responsible stack holders will coordination with host communities to manage Conflicts which was created by host communities for this relocation process.
 4. Request district reconstruction coordination committee and central NRA to re- relocate 24 HHs who have bought land under high tension transmission line to another safe space. This decision is made for only 24 HHs who have bought land at santibazzar, Nuwakot under high tension transmission line. Now discussion is ongoing to relocate those HHs on other land and to keep that land into government ownership.
 5. Start relocation process as soon as possible for all eligible displaced HHs those who are still staying at unsafe land to safer land.
- **District facilitation meeting at Lamjung:** Meeting was organized by GMaLI lamjung at DCC hall Bashishare Lamjung. Meeting was chaired by DCC chief Lok Raj Pandey and different GoN officers were participated meeting..

Important Decision made:

1. Coordinate with all respective palika and ward to enroll all the eligible HHs which is left behind yet from housing grant enrollment process.
2. Start process to refund housing grant from those house holds who have received housing grant support both from Government and partners organization. -Responsible GMaLI, Building and HRRP.
3. Collect information regarding houses constructed by Gorkha Welfare and will present on next facilitation meeting – Responsible HRRP, GMaLI and Building.
4. Coordinate with respective palika and ward to start relocation process for all eligible displaced households which was listed by NRA as soon as possible. Also conduct field visit and report CDO and DCC chief about their present condition as soon as possible. - Responsible GMaLI, Building and GMaLI.

Upcoming Events & Meetings

- **District Facilitation Meeting at Tanahau:** District facilitation meeting at Tanahau district was conducted on Jun,5 2019. Meeting was organized by GMaLI Tanahau and it was chaired by DCC chief Mr.Santi Ramada Wamlaa and all the members of district facilitation committee members were present at meeting.

Important decision made:


1. To complete resurvey and verification within given time committee decided to mobilized additional technical manpower at field level. Previously allocated manpower is not sufficient to accomplish resurvey and verification within given deadline.
2. One day orientation program for new deployed technical staff was scheduled for 7- Jun,2019 and DLPIU building is responsible to conducted orientation program and technical staff selection.
3. Municipality and ward are responsible for effective mobilization of technical person at field level for resurvey and verification. Also, to monitor this activities new committee will be form at district level for effective mobilization and to accomplish this activities with in time.

Tranche Status (Lamjung)


Tranche Status Table: 25-May,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Besishahar Nagarpalika	2851	1308	1257	1257	545	359	11	6	6	0
Dordi Gaunpalika	3375	2238	2206	2206	818	214	25	3	3	0
Dudhpokhari Gaunpalika	2667	2437	2361	2361	1812	355	6	4	4	0
Kwholasothar Gaunpalika	740	314	271	271	104	59	72	0	0	0
MadhyaNepal Nagarpalika	2346	1505	1448	1448	681	179	54	0	0	0
Marsyangdi Gaunpalika	1936	911	877	877	342	250	176	158	158	0
Rainas Nagarpalika	4362	2989	2947	2947	1970	653	105	99	99	0
Sundarbazar Nagarpalika	4084	2257	2157	2157	1334	762	90	19	19	0

Graph of Tranche Status:

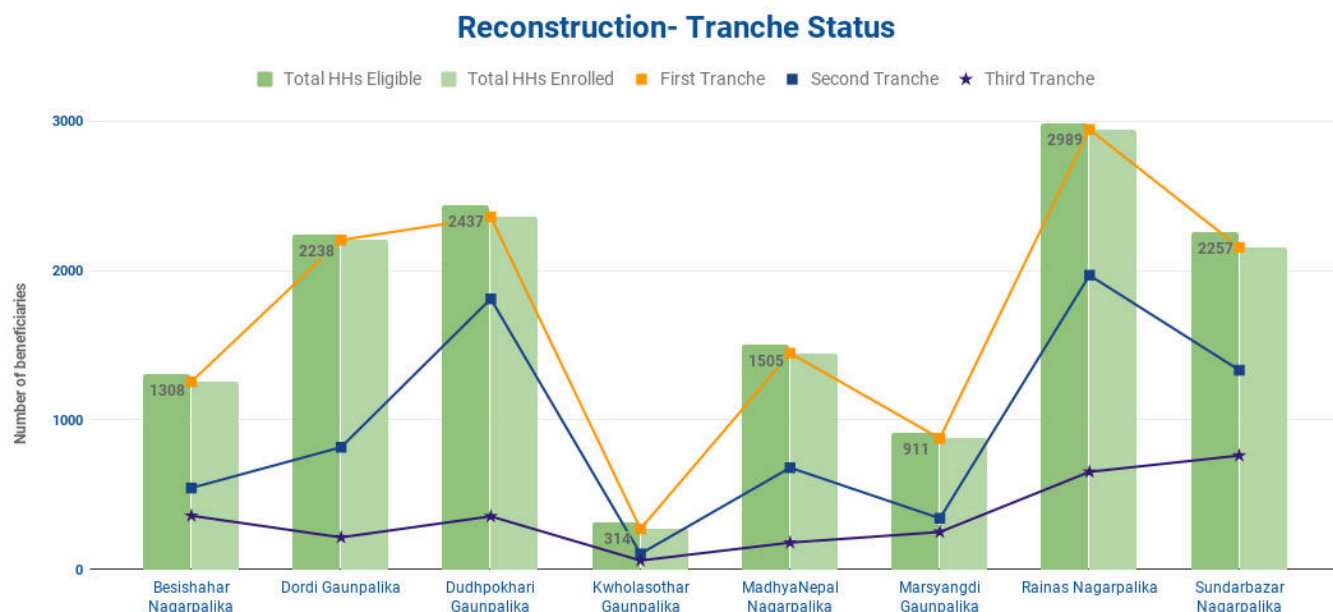

Graph for Retrofitting Status:

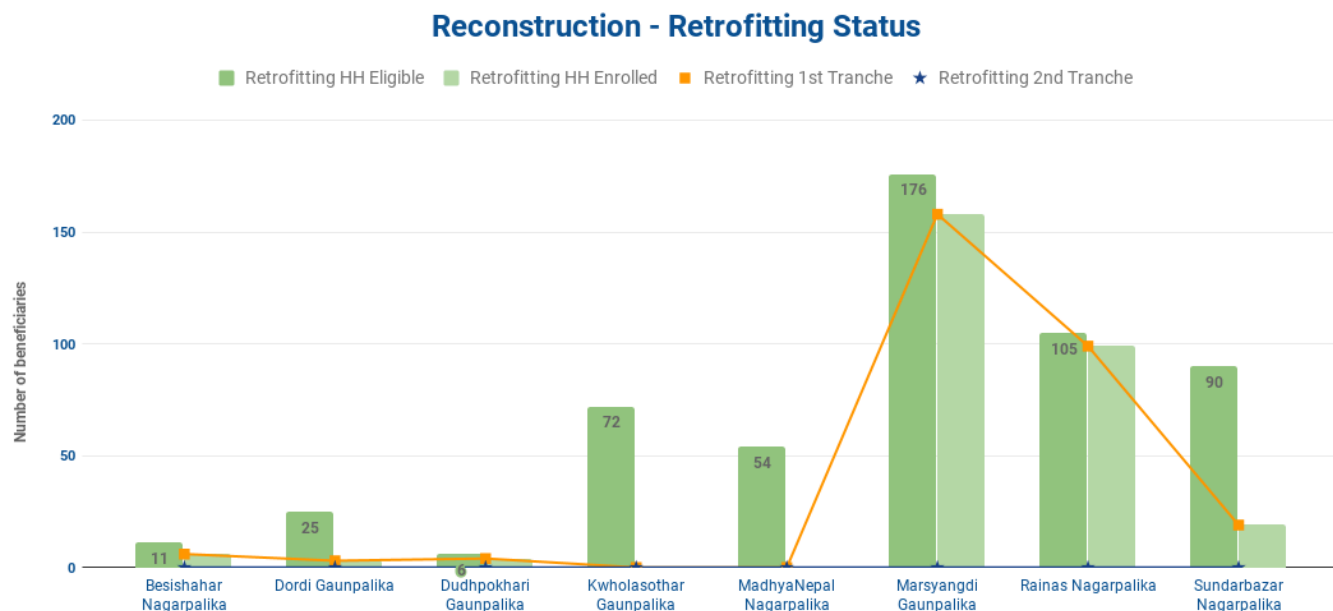


Tranche Status (Tanahun)

Graph of Tranche Status:

Tranche Status Table: 25th May-2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Anbukhaireni Gaunpalika	1050	710	705	705	470	370	21	5	5	0
Bandipur Gaunpalika	1226	609	1055	1055	628	317	33	32	32	0
Bhanu Nagarpalika	7540	4219	4147	4147	2342	1303	75	12	12	0
Bhimad Nagarpalika	2680	987	974	974	495	154	46	0	0	0
Byas Nagarpalika	4626	2486	1981	1981	1111	847	163	152	152	0
Devghat Gaunpalika	960	725	499	499	327	127	32	7	7	0
Ghiring Gaunpalika	969	254	232	232	120	80	0	0	0	0
Myagde Gaunpalika	1877	1292	1065	1065	604	338	38	33	33	0
Rhishing Gaunpalika	1771	680	473	473	278	142	34	0	0	0
Shuklagandaki Nagarpalika	2837	1859	1740	1740	941	457	24	1	1	0

Reconstruction- Tranche Status

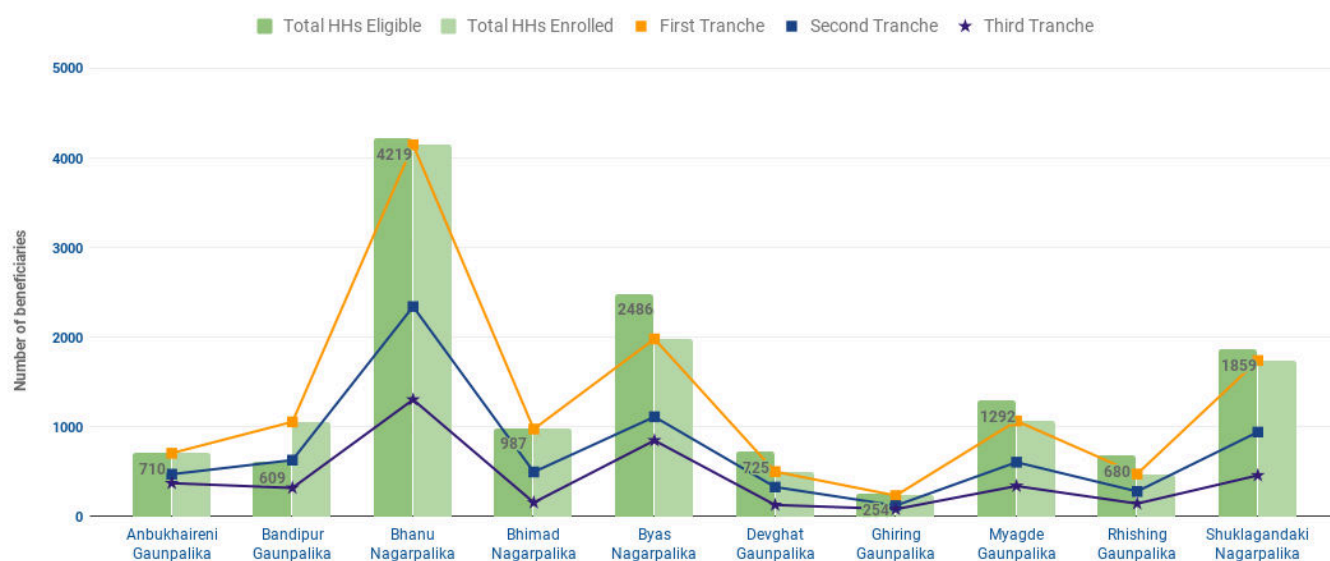


Tranche Status (Kaski)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Annapurna Gaunpalika	667	395	395	395	179	74	19	12	12	0
Machhapuchchhre Gaunpalika	781	427	427	427	265	34	30	5	5	0
Madi Gaunpalika	2296	1160	1160	1160	512	97	40	12	12	0
Pokhara Lekhnath Mahanagarपालिका	5276	2774	2421	2421	1153	281	111	84	84	0
Rupa Gaunpalika	2054	1270	1222	1222	455	238	42	26	26	0

Graph of Tranche Status:

Reconstruction - Retrofitting Status

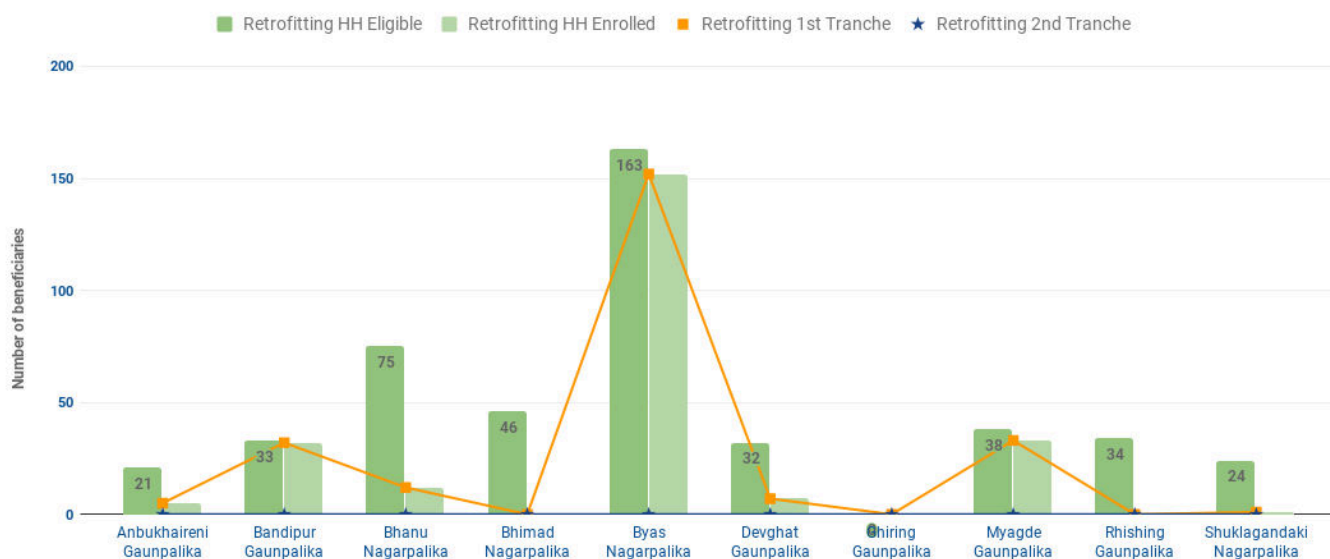


Reconstruction- Tranche Status

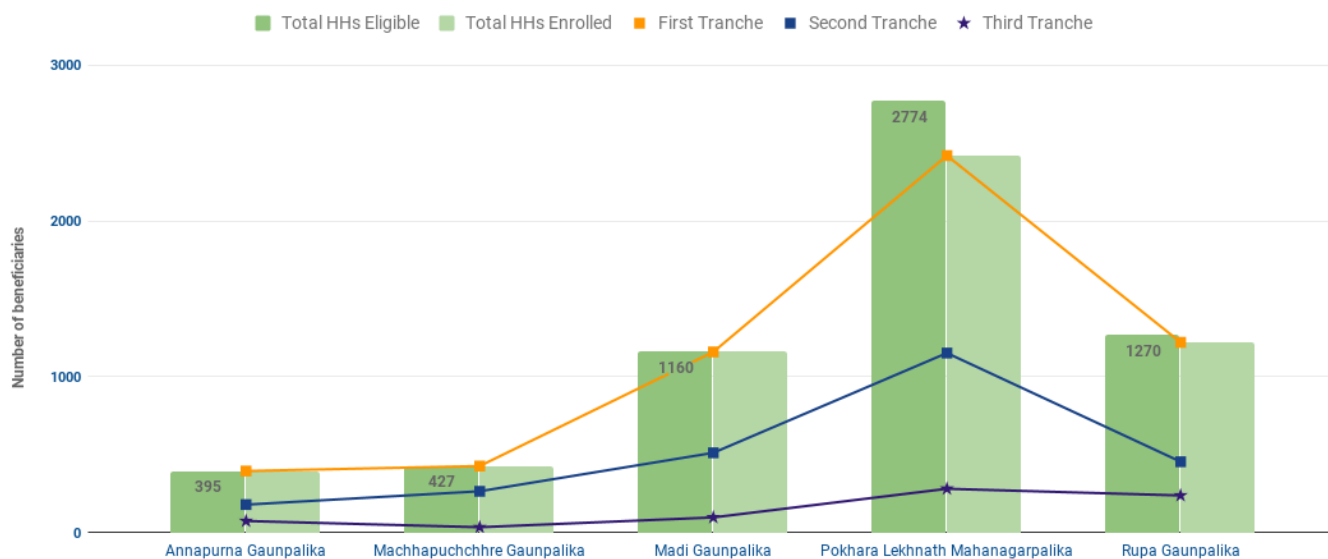

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

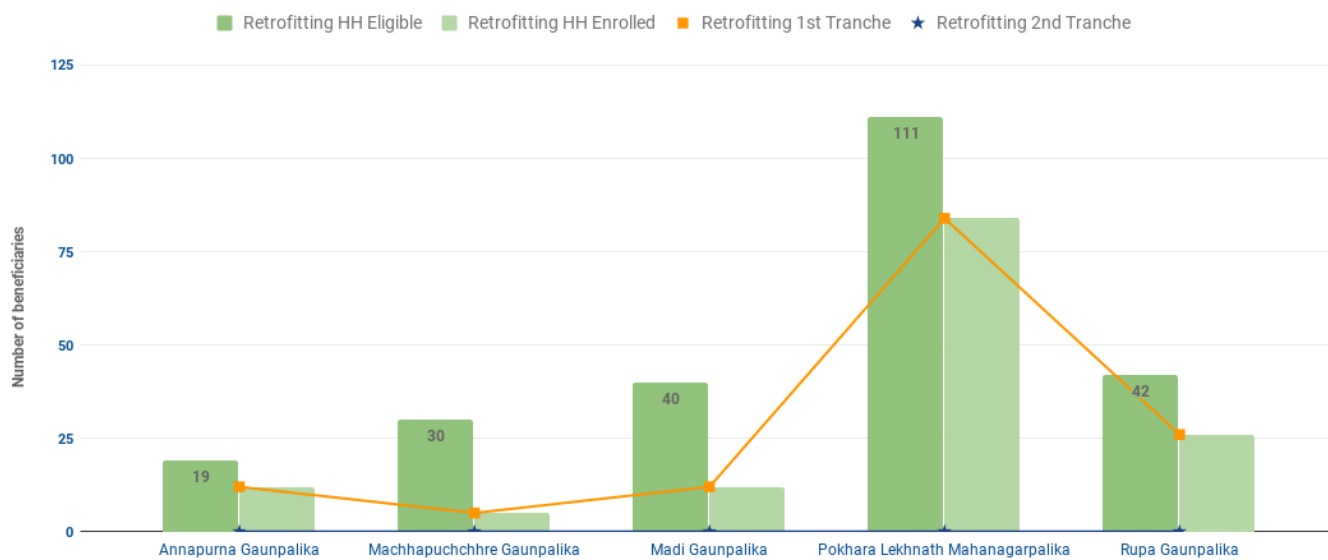


Tranche Status (Syangja)

Tranche Status Table:25-May,2019


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Aandhikhola Gaunpalika	1515	843	820	820	365	29	72	31	31	0
Arjunchaupari Gaunpalika	803	509	470	470	238	136	65	46	46	0
Bhirkot Nagarpalika	2099	1041	992	992	299	73	26	24	24	0
Biruwa Gaunpalika	1024	638	609	609	149	48	40	9	9	0
Chapakot Nagarpalika	1815	804	797	797	404	0	12	2	2	0
Galyang Nagarpalika	1294	634	621	621	311	42	101	99	99	0
Harinas Gaunpalika	912	435	396	396	157	32	1	0	0	0
Kaligandagi Gaunpalika	752	493	397	397	144	58	2	0	0	0
Phedikhola Gaunpalika	403	278	266	266	111	46	10	7	7	0
Putalibazar Nagarpalika	2798	1471	1458	1458	728	258	321	294	294	0
Waling Nagarpalika	2696	1671	1604	1604	679	89	54	32	32	0

Graph of Tranche Status:

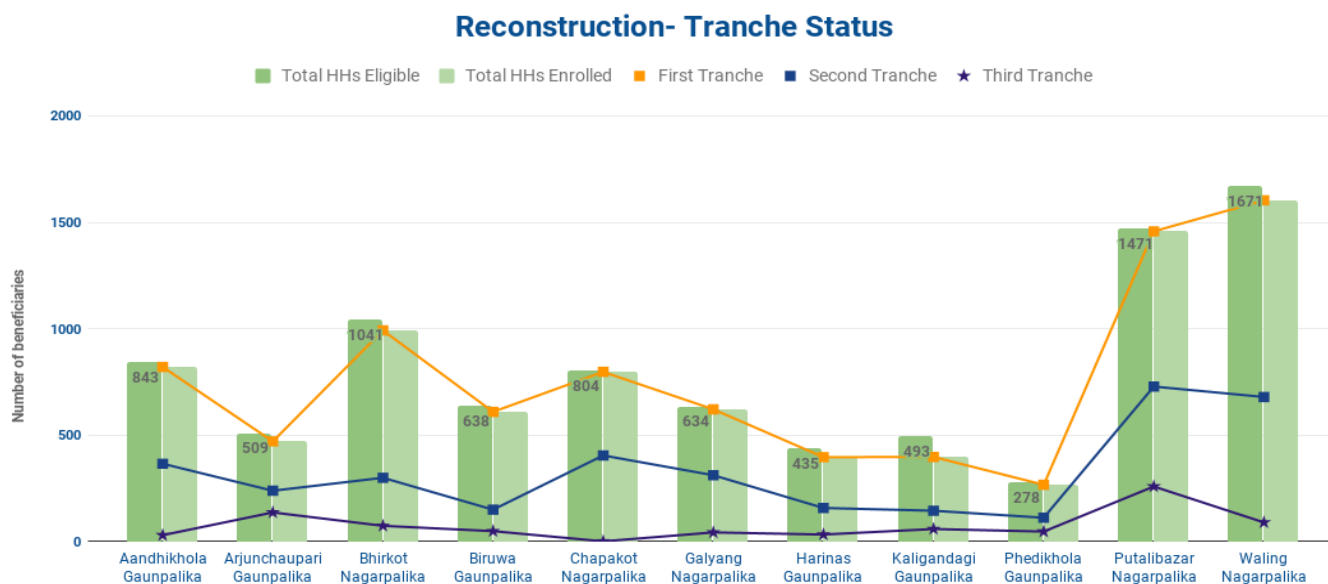

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

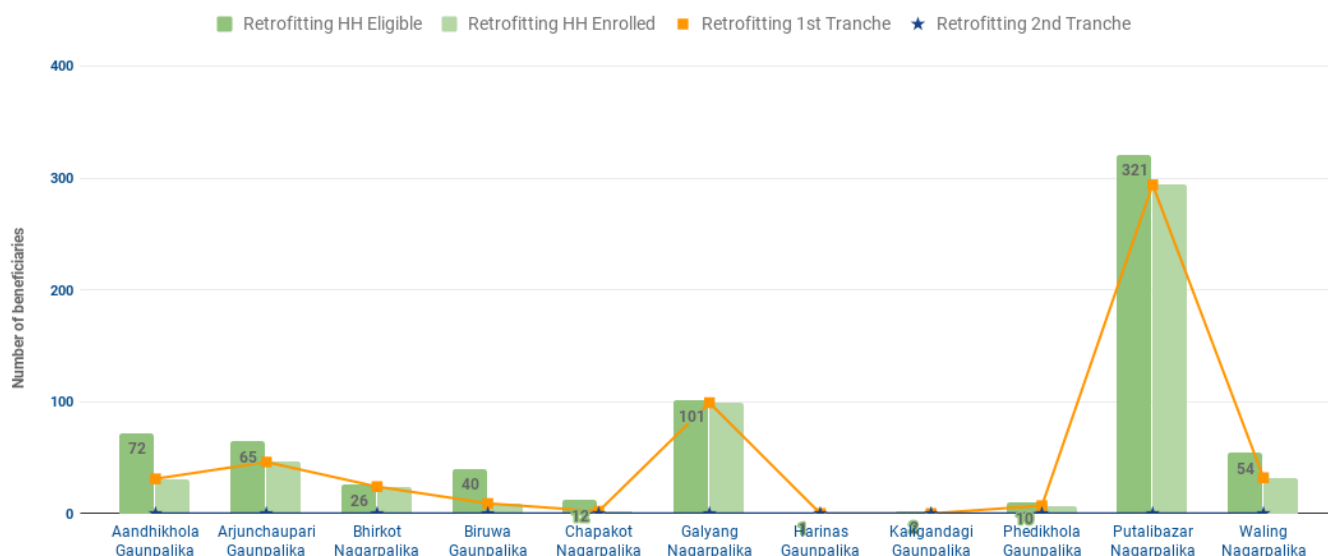

Field Visit Reports (Lamjung)

Visit 1

Date	Location	Participants
26-May,2019	Rainas Nagarpalika , ward no-5, Tinpile tole SundarBazer Nagarpalika	• Jagdish Mishra (GMAI chief) • Umesh Dangol (DSE, NRA) • Rijan Gajurel (DC, HRRP) • Biren Shah (DTC, HRRP) • Binayak Dawadi (GMAI) • Mayananda Chaudhary (Engineer, DLPIU Building) • Dinesh Achhami (Sub-Er, DLPIU Building)
Objective(s)	• To conduct Palika level meeting at Nagarpalika. • To conduct 3rd inspection of the houses that have been reconstructed. • To take building typology on KoBo Collect App. • To interact with beneficiaries and provide relevant suggestions further. • Update the reconstruction progress at Nagarpalika level. • Discuss the problems and issues faced by the Nagarpalika elected officials and Engineers regarding reconstruction. • Non-compliance issues of the Nagarpalika and Building code implementation scenario.	
Why was the visit carried out in this location?		
• Variation and complex Non-compliances resulting in backlog tranche progress. • Lack of information and update in Palika representatives regarding reconstruction progress and tranche update. • Housing Typology of this Nagarpalika has not been taken.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
First time visit.		
Summary		

Field Visit:

- No. of HHs visited:9
- No. of meetings with engineers:1
- No. of meetings with local officials:1

HRRP team together with GMaLI, Building and DSE has conducted field visit at Rainash municipality. During field visit. Team has conducted palika level meeting at municipal office and also conducted field monitoring visit. During field monitor we have Interact with affected HHs about the challenges faced by them during reconstruction process which is mention below table.As per GMaLI update tranche distribution update of this municipality is as follows:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
MadhyaNepal Nagarpalika	2346	1505	1448	1448	681	179	54	0	0	0

Palika Level Meeting at Rainash Nagarpalika: Palika level meeting was chaired by acting administrative chief officer Mr.Purna Nepali and different wards president, ward technical and representative of GMaLI , Building were presented at meeting. Objective and agendas of palika level meeting was first briefed by HRRP district coordinator Mr.Rijan Gajurel which is as follows:

- To Interact with local representative and to discuss about reconstruction challenges faced.
- To discuss about Reconstruction action plan and palika profile update and upload at website.
- To discuss about Non-compliance issues.
- Others

Following decision were made by this meeting:

- Reconstruction update of Palika by both GMaLI and Building.
- Discussion of challenges faced by palika and ward level and way forward to speed up reconstruction process.
- Request District facilitation coordination committee(DFC), District reconstruction coordination committee (DRCC) and Nepal reconstruction authority(NRA) to address those non-compliance houses which was constructed at initial phase after earthquake before presence of technical staff at field level.

Please ([Click here](#)) for meeting minute

HRRP team together with GMaLI, Building and DSE has conducted field visit at Sundarbazar municipality. During field visit. Team has conducted palika level meeting at municipal office and also conducted field monitoring visit. During field monitor we have Interact with affected HHs about the challenges faced by them during reconstruction process which is mention below table.As per GMaLI update tranche distribution update of this municipality is as follows:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
MadhyaNepal Nagarpalika	2346	1505	1448	1448	681	179	54	0	0	0

Palika Level Meeting at SundarBazar Nagarpalika:

Palika level meeting was chaired by Deputy Mayor Miss. Ganu Shah and together with palika administrative chief officer different wards president, ward technical and representative of GMaLI, Building were presented at meeting. Objective and agendas of palika level meeting was first briefed by HRRP district coordinator Mr.Rijan Gajurel which is as follows:

- To Interact with local representative and to discuss about reconstruction challenges faced.
- To discuss about Reconstruction action plan and palika profile update and upload at website.
- To discuss about Non-compliance issues.
- Others

Following decision were made by this meeting:

- Reconstruction update of palika by both GMaLI and Building.
- Request District facilitation coordination committee (DFC), District reconstruction coordination committee (DRCC) and Nepal reconstruction authority(NRA) to address those non-compliance houses which was constructed at initial phase after earthquake before presence of technical staff at field level.

- Some partners organization had conducted mason training at initial phase but they had teaches wrong methodology of construction during training, because of which few mason had constructed houses as per the training which doesn't meet GON compliance. So, palika meeting requested district facilitation committee and other stack holders to coordinate with that partner and make punishment as per GoN guidelines.

Please ([Click Here](#)) for meeting minute

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1st tranche from government.	Ward offices can play a vital role in motivating the beneficiaries to construct the houses as soon as possible. Also, the technicals deployed in the wards should provide technical assistance in rebuilding safe and compliant houses. If the beneficiaries are not interested in building houses, then the ward must take an action and lobby them to return the tranche.		Ward office, Municipality office, DLPIU Technicals	
Houses constructed after 2015 earthquake and before the recruitment of Technicals are non-compliant and the HHS are not likely to apply corrections.	Immediate correction must be applied under the supervision of DSE and in assistance of deployed technicals.		DLPIU Building, DSE	
There is likely of addition of storeys after beneficiaries receives 3rd tranche in face of risk towards houses constructed on small parcel land in core areas	Ward office along with municipality office should conduct appropriate monitoring so that addition of storeys will be reduced. Further, Ward office should inform beneficiaries about risk of adding storeys on houses that are constructed on small land		DLPIU Building, Ward office	
Lack of masons for implementing the correction and retrofitting.	Implementation of mason training regarding retrofit and correction measures.		CLPIU Building, Partner organization	
Bad practice and Lack of knowledge in the Nagarpalika Engineers regarding Building Code implementation.	Orientation to the Nagarpalikas technicals regarding technical support and training on Building code implementation.		CLPIU Building, Partner organization	
Lack of Reporting and information dissemination of ward Technicals to the elected officials regarding reconstruction progress , issues and challenges.	Tracking of ward technicals from the DLPIU building and orient them to disseminate information regarding reconstruction to the Palika Representatives. Also frequent or minimally monthly meeting from GMali and DLPIU Building to the Nagarpalika and Rural Municipalities regarding reconstruction update.		DLPIU Building , GMaLI	
Modification of houses after receiving the third tranche making the houses non-compliant.	Construction completion certificate distribution must be started inorder to track those houses and only after the correction of modification the		Ward level, DLPIU Building . Municipality	

	certificate should be distributed. Also proper information sharing and public hearing program should be conducted regarding the information dissemination for minimizing the modification.			

Photos



Beneficiary Name: Banik Raj Bhatta
Location: ward no- 5, Tinpile , Rainas Nagarpalika , Lamjung
Tranche Update: Second Received
Building Typology: It is a single storey, four rooms RCC structure with brick masonry with RC band as infill material with columns of size 12" x 12". The floor area is less than 1000 sq. feet and building size 27 x 23 feet. The cost of construction is NRPs 1700000.



Beneficiary Name: Kamal Kanta Bhatta
Location: ward no- 5, Tinpile , Rainas Nagarpalika , Lamjung
Tranche Update: Second Received
Building Typology: It is a single storey, four rooms RCC structure with brick masonry with RC band as infill material with columns of size 12" x 12". The floor area is less than 1000 sq. feet and building size 27 x 23 feet. The cost of construction is NRPs 1400000



Beneficiary Name: Ram Krishna Bogati
Location: ward no- 5, Tinpile , Rainas Nagarpalika , Lamjung
Tranche Update: Third Received
Building Typology: It is a single storey, four rooms RCC structure with brick masonry with RC band as infill material with columns of size 12" x 12". The floor area is less than 1000 sq. feet and building size 27 x 23 feet. The cost of construction is NRPs 2700000.



Beneficiary Name: Uday Raj Pokhrel
Location: ward no- 5, Tinpile , Rainas Nagarpalika , Lamjung
Tranche Update: Second Received
Building Typology: It is a two storey, six rooms RCC structure with brick masonry with RC band as infill material with floor area less than 1000 sq. feet and building size 30 x 30 feet. The cost of construction is NRPs 3500000.



Caption: Palika level meeting at Rainash NP office.
PC: Rijan Gajurel



Caption: Palika Level meeting at Sundarbazar NP.
PC: Biren Shah

Field Visit Reports (Lamjung)

Visit 1

Date	Location	Participants
28-May, 2019	Madhya Nepal Nagarpalika ward number-5, Borhetar	- Sheetal Babu Lohani (Focal Engineer , DLPIU Building) - Umesh Dangol (DSE, NRA) - Rijan Gajurel (DC ,HRRP) - Biren Shah (DTC, HRRP) - Binayak Dawadi (GMaLI) - Arjun Ranabhat (Engineer , DLPIU Building) - Bishwash Pande (Engineer ,DLPIU Building)
Objective(s)	- To conduct Palika level meeting. - To conduct 3rd inspection of the houses that have been reconstructed. - To take building typology on KoBo Collect App. - To interact with beneficiaries and provide relevant suggestions further. - Update the reconstruction progress at Nagarpalika level. - Discuss the problems and issues faced by the Nagarpalika elected officials and Engineers regarding reconstruction. - Non-compliance issues of the Nagarpalika and Building code implementation scenario.	

Why was the visit carried out in this location?

- Variation and complex Non-compliances resulting in backlog tranche progress.
- Lack of information and update in Palika representatives regarding reconstruction progress and tranche update.
- Housing Typology of this Nagarpalika has not been taken.
- To interact with local representative and other stakeholders.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

First Visit

Summary

Field Visit:

- No. of HHs visited:9
- No. of meetings with engineers:1
- No. of meetings with local officials:1

HRRP team together with GMaLI, Building and DSE has conducted field visit at Madhanepal municipality. During field visit Team has conducted palika level meeting at municipal office and also conducted field monitoring visit. During field monitor we have interact with affected HHs about the challenges faced by them during reconstruction process which is mentioned below table. As per GMaLI update tranche distribution update of this municipality is as follows:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
MadhyaNepal Nagarpalika	2346	1505	1448	1448	681	179	54	0	0	0

Palika Level Meeting at MadhaNepal Nagarpalika:

Palika level meeting was chaired by Mayor Mrs.Ramesh Kumar Pandey together with palika administrative chief officer different wards president, ward technical and representative of GMaLI, Building were presented at meeting. Objective and agendas of palika level meeting was first briefed by HRRP district coordinator Mr.Rijan Gajurel which is as follows:

- To Interact with local representative and to discuss about reconstruction challenges faced.
- To discuss about Reconstruction action plan and palika profile update and upload at website.
- To discuss about Non-compliance issues.
- Others

Important decision made by this meeting:

- Reconstruction update of palika by both GMaLI and Building.
- Request District facilitation coordination committee (DFC), District reconstruction coordination committee (DRCC) and Nepal reconstruction authority(NRA) to address those non-compliance houses which was constructed at initial phase after earthquake before presence of technical staff at field level.
- Request to district facilitation committee to coordinate with Banks for fast and easy process to transfer housing grant to EQ eligible victims.

Please ([Click Here](#)) for Meeting Minute

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1st tranche from government.	Ward offices can play a vital role in motivating the beneficiaries to construct the houses as soon as possible. Also the technicals deployed in the wards should provide technical assistance in rebuilding safe and compliant houses. If the beneficiaries are not interested in building houses, then the ward must take an action and lobby them to return the tranche.		Ward office , Municipality office , DLPIU Technicals	
Houses constructed after 2015 earthquake and before the recruitment of Technicals are non-compliant and the HHS are not likely to apply corrections.	Immediate correction must be applied under the supervision of DSE and in assistance of deployed technicals.		DLPIU Building, DSE	
There is likely of addition of storeys after beneficiaries receives 3rd tranche in face of risk towards houses constructed on small parcel land in core areas	Ward office along with municipality office should conduct appropriate monitoring so that addition of storeys will be reduced. Further, Ward office should inform beneficiaries about risk of adding storeys on houses that are constructed on small land		DLPIU Building, Ward office	
Lack of masons for implementing the correction and retrofitting.	Implementation of mason training regarding retrofit and correction measures.		CLPIU Building, Partner organization	
Bad practice and Lack of knowledge in the Nagarpalika Engineers regarding Building Code implementation.	Orientation to the Nagarpalikas technicals regarding technical support		CLPIU Building, Partner organization	

	and training on Building code implementation.			
Lack of Reporting and information dissemination of ward Technicals to the elected officials regarding reconstruction progress , issues and challenges.	Tracking of ward technicals from the DLPIU building and orient them to disseminate information regarding reconstruction to the Palika Representatives. Also frequent or minimally monthly meeting from GMali and DLPIU Building to the Nagarpalika and Rural Municipalities regarding reconstruction update.		DLPIU Building , GMali	
Modification of houses after receiving the third tranche making the houses non-compliant.	Construction completion certificate distribution must be started inorder to track those houses and only after the correction of modification the certificate should be distributed. Also, proper information sharing and public hearing program should be conducted regarding the information dissemination for minimizing the modification.		Ward level, DLPIU Building , Municipality	

Photos



Beneficiary Name: San Bahadur Ale Magar
Location: ward no- 5, Parajuli Besi , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Second Received
Building Typology: It is a single storey, five rooms house made of interlocking brick masonry with floor area less than 1000 sq. feet and building size 25 x 18 feet. The cost of construction is NRPs 5,50,000.

Beneficiary Name: Pabitra Devi Poudel
Location: ward no- 5, Parajuli Besi , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Second Received
House status: Non- compliant
Building Typology: It is a single storey, three rooms Brick Masonary in Cement Mortar structure with floor area less than 1000 sq. feet and building size 24 x 15 feet. The cost of construction is NRPs 12,00,000.
The span and size of one room is more than minimum requirement so the house has been recommended for correction (addition of buttress wall).



Beneficiary Name: Radha Kunwar.
Location: ward no- 6, Rani Pani , Madhya Nepal Nagarpalika , Lamjung.
Tranche Update: First Received.
House Status: Compliant.
Building Typology: It is a two storey, seven rooms RCC structure with brick Masonary with RC band as infill material and columns of size 12" x 12". The floor area less than 1000 sq. feet and building size 30 x 26 feet. The cost of construction is NRPs 35,00,000.



Beneficiary Name: Mani Ram Ghimire
Location: ward no- 5, Borletar , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Second Received
House status: Non-compliant
Building Typology: It is a two storey, eight rooms RCC structure with brick masonry with RC band as infill material with floor area less than 1000 sq. feet and building size 28 x 24 feet. The cost of construction is NRPs 40,00,000. The size of columns is 9" x 9" resulting the structure to be non-compliant.



Beneficiary Name: Shree Prasad Regmi
Location: ward no- 6, Borletar , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: First Received
Building Typology: It is a three storey, sixteen rooms RCC structure with brick masonry with RC band as infill material with floor area more than 1000 sq. feet and building size 40 x 32 feet. The cost of construction is NRPs 1,00,00,000.
House Status: Non-Compliant
Columns are missing in grids due to which after structural analysis the structural failed to be earthquake resilient.



Beneficiary Name: Ram Krishna Ghimire
Location: ward no- 6, Borletar , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Third Received
Building Typology: It is a two storey plus staircase cover, nine rooms RCC structure with brick masonry and RC band as infill material with floor area less than 1000 sq. feet and building size 30 x 30 feet. The cost of construction is NRPs 45,00,000.



Beneficiary Name: Arjun Parajuli Thapa
Location: ward no- 6, Rani Pani , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Second Received
House Status: Non - compliant
Building Typology: It is a two storey, ten rooms RCC structure with brick masonry with RC band as infill material with floor area less than 1000 sq. feet and building size 30 x 26 feet. The cost of construction is NRPs 65,00,000.
The structure has stepped footing with addition of first floor after receiving the second tranche.

Caption: Palika level meeting at Madhanepal Nagarpalika.
PC: Rijan Gajurel

Field Visit Reports (Tanahun)

Visit 1

Date	Location	Participants
6-June, 2019	Bhanu Nagarpalika , ward no -2, Ananda Tole	Biren Shah (DTC, HRRP) Rijan Gajurel (DC ,HRRP) Meera Shrestha (DSE ,NRA) Bipin Shrestha (Focal Engineer , DLPIU Building)
Objective(s)	• To conduct 3rd inspection of the houses that have been reconstructed. • To take building typology on KoBo Collect App. • To interact with beneficiaries and provide relevant suggestions further. • Non-compliance issues of the Nagarpalika.	
Why was the visit carried out in this location?		
• Variation and comlex Non-compliances resulting in backlog tranche progress. • Housing Typology of this Nagarpalika has not been taken.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
First time.		
Summary		

Field Visit:

- No. of HHs visited:7
- No. of meetings with engineers:0
- No. of meetings with local officials:0

HRRP district team together with building focal person, DSE and ward technical person conducted field visit at Bhanu municipality ward number 2. Team has visited different houses and interact with individual beneficiary about challenges they have faced during reconstruction. As per GMaLI record the tranche distribution update is as follows:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhanu Nagarpalika	7540	4219	4147	4147	2342	1303	75	12	12	0

Note: Team has previously plan to conduct meeting at nagarpalika but because of busy scheduled of palika stack holders meeting was postpone for next month.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Lack of proper information regarding NRA technical manuals and guidelines in the field technicals as maximum of the technicals are recruited newly.	TOT program to be conducted as soon as possible		GMaLI , Building and HTRRP	
Houses constructed after 2015 earthquake and before the recruitment of Technicals are non-compliant and the HHS are not likely to apply corrections.	Immediate correction must be applied under the supervision of DSE and in assistance of deployed technicals.		NRA	
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1st tranche from government.	Ward offices can play a vital role in motivating the beneficiaries to construct the houses as soon as possible. Also the technicals deployed in the wards should provide technical assistance in rebuilding safe and compliant houses. If the beneficiaries are not interested in building houses, then the ward must take an action and lobby them to return the tranche.		Ward technical person, ward, Municipality, building and GMaLI.	
There is likely of addition of storeys after beneficiaries receives 3rd tranche in face of risk towards houses constructed on small parcel land in core areas	Ward office along with municipality office should conduct appropriate monitoring so that addition of storeys will be reduced. Further, Ward office should inform beneficiaries about risk of adding storeys on houses that are constructed on small land		Ward technical person, Municipality, Building.	
Modification of houses after receiving the third tranche making the houses non-compliant.	Construction completion certificate distribution must be started in order to track those houses and only after the correction of modification the certificate should be distributed. Also proper information sharing and public hearing program should be conducted regarding the		Municipality, ward	

	information dissemination for minimizing the modification.			
Lack of masons for implementing the correction and retrofitting.	Implementation of mason training regarding retrofit and correction measures.		GMail, NRA and partners	

Photos



Beneficiary Name: Meena Kumal
Location: ward no- 2, Ananda Tole, Bhanu Nagarpalika , Tanahun
Tranche Update: First Received
Building Typology: It is a single storey, two rooms Brick Masonary in Cement Mortar with RC band and floor area less than 1000 sq. feet and building size 26 x 12 feet. The cost of construction is NRPs 5,00,000.
House Status: Non-compliant
During the construction of vertical bands at the openings brick was laid instead of concrete casting therefore the structure is under correction and will be forwarded after the correction.

Beneficiary Name: Rishi Bahadur Baral Chhetri
Location: ward no- 2, Bhanu Chowk, Bhanu Nagarpalika , Tanahun
Tranche Update: Third Received
Building Typology: It is a single storey, two rooms Brick Masonary in Cement Mortar with RC band and floor area less than 1000 sq. feet and building size 24 x 12 feet. The cost of construction is NRPs 5,50,000.

Housing Typology Report

Photo



Photo



Beneficiary Name: Babu Ram B.K.
Location: ward no- 2, Ananda Tole, Bhanu Nagarpalika , Tanahun
Tranche Update: Third Received
Building Typology: It is a single storey, three rooms RCC structure with brick masonry with RC band as infill material with columns of size 12" x 12". The floor area is less than 1000 sq. feet and building size 28 x 24 feet. The cost of construction is NRPs 45,00,000.

Photo



Beneficiary Name: Tek Nath Poudel
Location: ward no- 2, Syano Bagaicha, Bhanu Nagarpalika , Tanahun
Tranche Update: Second Received
Building Typology: It is a single storey, two rooms Brick Masonry in Mud Mortar with timber band and floor area less than 1000 sq. feet and building size 28 x 12 feet. The cost of construction is nearly 1,00,000.
House Status: Non-Compliant
The house owner has used bricks of the Earthquake damaged house and local unskilled masons due to which there is no proper and continuous bands at different levels .There is no DPC as well in the house.

Photo



Beneficiary Name: Radha Kunwar.
Location: ward no- 6, Rani Pani , Madhya Nepal Nagarpalika , Lamjung.
Tranche Update: First Received.
House Status: Compliant.
Building Typology: It is a two storey, seven rooms RCC structure with brick Masonry with RC band as infill material and columns of size 12" x 12". The floor area less than 1000 sq. feet and building size 30 x 26 feet. The cost of construction is NRPs 35,00,000.



Beneficiary Name: San Bahadur Ale Magar
Location: ward no- 5, Parajuli Besi , Madhya Nepal Nagarpalika , Lamjung
Tranche Update: Second Received
Building Typology: It is a single storey, five rooms house made of interlocking brick masonry with floor area less than 1000 sq. feet and building size 25 x 18 feet. The cost of construction is NRPs 5,50,000.



Beneficiary Name: Meena Kumal
Location: ward no- 2, Ananda Tole, Bhanu Nagarpalika , Tanahun
Tranche Update: First Received
Building Typology: It is a single storey, two rooms Brick Masonry in Cement Mortar with RC band and floor area less

Beneficiary Name: Rishi Bahadur Baral Chhetri
Location: ward no- 2, Bhanu Chowk, Bhanu Nagarpalika , Tanahun
Tranche Update: Third Received
Building Typology: It is a single storey, two rooms Brick Masonry in Cement Mortar with RC band and floor area less

than 1000 sq. feet and building size 26 x 12 feet. The cost of

than 1000 sq. feet and building size 24 x 12 feet. The cost of

Challenges and Way Forward

Challenge	Way Forward
Most of the houses are constructed using traditional structure such as mud-brick and wood, which are not earthquake resistant. The correction measures are not being implemented in a timely manner, leading to increasing the non-compliance cases.	Such houses must be suggested to apply the correction measures. For the houses which are not addressed by the correction measures, number of such houses must be collected, and NRA should make a policy to address such cases.
There is no proper and systematic implementation of Building codes in Nagarpalikas .	Technical support and training on Building code implementation must be organized.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
What is the process of beneficiary amends during the death of the actual beneficiary?	Beneficiary	The nominee of the beneficiary can request beneficiary amendment at GMALI office. After the beneficiary name is changed, the nominee will be the beneficiary in place of the previous beneficiary. (HRRP)

Case Study



- Interlocking Brick Masonry Quality Test:
- Beneficiary Name: San Bahadur Ale Magar
- Location: ward no- 5, Parajuli Besi , Madhya Nepal Nagarpalika , Lamjung
- Tranche Update: Second Received
- Building Typology: It is a single storey, five rooms house made of interlocking brick masonry with floor area less than 1000 sq. feet and building size 25 x 18 feet. The cost of construction is NRPs 5,50,000.

Quality of Construction Materials:

The key reliable construction is technique, technology but most importantly building materials used. Building materials include cement, aggregate, brick, rebar, blocks etc. Quality assurance of construction materials is important to ensure strength, durability and cost effectiveness. As we all are aware that quality of building materials effects overall quality of building. After gorkha earthquake 2015, demand of construction materials increased intensely because large number of construction is ongoing over 32 district. As demand increased the cost of materials increased dramatically but its quality goes on downwards pattern. To increase entrepreneurship at local level and to fulfill gap between demand and supply government is encouraging local community for production of alternative construction materials. However, because of less knowledge and working experience community are producing less quality materials and using them to construct earthquake safer house which may caused devastating effect in near future.

During our field visit at households level we found some of houses are using very less quality interlocking brick at Madhanepal municipality, Lamjung. We saw their walls are getting crack in newly constructed houses also physical quality test of interlocking block was conducted with 5 blocks and the test specimen were of poor quality. The compressive strength of interlocking brick masonry was found to be less than 3.5 MPA since while the specimen were thrown from the chest height it broke down into several pieces as shown in the picture.

.We asked house owners why they bought such less quality materials then they answered we have no idea about quality of such brick. This is new technology now we are using and we thought that made our house more durable. We also asked technical person why he did not suggested them to not use such quality less materials at initial phase then one of ward technical person answered our role is just to ensure minimum compliance in overall building about quality of materials we have no idea. As that houses got only second tranche from reconstruction grant so visiting team decided to not process them further grant. This is an example which we found in field but might be this kinds of negligence is ongoing over all part. Its time to focus on quality parallely with techniques and technology so, we should be more aware about the quality and government much should give training and provide other knowledge to both small entrepreneur and at community level to accomplish BUILD BACK BETTER goal .

“Interlock Brick Technology consists of specially designed unburnt bricks with tongue and groove features that allows bricks to interlock each other in masonry and thereby reduces mortar usage. Construction with interlocking brick is economical, quick and environment friendly. Special design of interlocking bricks allows for vertical reinforcement bars in strategic locations of buildings.”
