


FACTS AND FIGURES

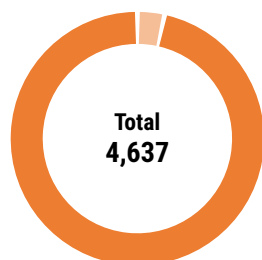

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	95.44%	89.07%
Reinforced Cement Concrete (RCC) Frame	2.01%	3.05%
Stone and Cement Mortar Masonry	1.01%	0.64%
Brick and Cement Mortar Masonry	0.63%	2.11%
Others	0.90%	5.13%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	4,737
PA Agreement	4,387
I st Tranche received	4,387
II nd Tranche received	4,142
III rd Tranche received	3,765

Houses

Under Construction: - Completed: 3,801

Retrofitting Status

Total Eligible HHs	51
PA Agreement	1
I st Tranche received	1
II nd Tranche received	-

Grievances

Registered: 809
Addressed: 553

Non-compliances

Registered: -
Addressed: -

Data Updated on: 2019-06-24 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: ACF (Agriculture), ACF (DRM), ACF (Health), ACF (Hygiene), BC (Education), BC (Shelter), GIZ (Health), GON-PAF (Shelter), HFH (DRM), HFH (Shelter), HFN (Shelter), IMC (Health), MI (Health), NR (Education), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), PA (Shelter), WR (Agriculture), WR (Education), WR (Livelihood), WR (Health), WR (Shelter), WR (Hygiene)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	42,164	Y	7,000
Aggregate	m ³	41,123	Y	16,000
Sand	m ³	4,483	N	12,000
Timber	cu. ft.	5,102	Y	2,500
Cement (PPC)	Sack	-	Y	950
Cement (OPC)	Sack	136,996	Y	1,050
Rebars	kgs.	460,783	Y	95
Tin	bundle	5,598	-	-
Bricks	pcs.	632,375	Y	17

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,500 /-
1,000 /-

OTHER SECTORS



Schools

Damaged: 31
Under Construction: 13
Construction Completed: 13



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

KEY CONTACTS

Municipal Office

Chhatra Bahadur Lama
Mayor
9851173433

Municipal Office

Govinda Pandey
Focal Person
9844894370

Municipal Office

Maya Devi Neupane
Deputy Mayor
9851132976

GMAI/NRA

Sambhu Kumar Shah
NRA Chief-District
9847068897

Municipal Office

Krishna Raj Joshi
Administration Officer
9860361546

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
98550465884

HHs WITH LAND ISSUES




STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)



Source: HRRP Analysis

TA ACTIVITIES MAP

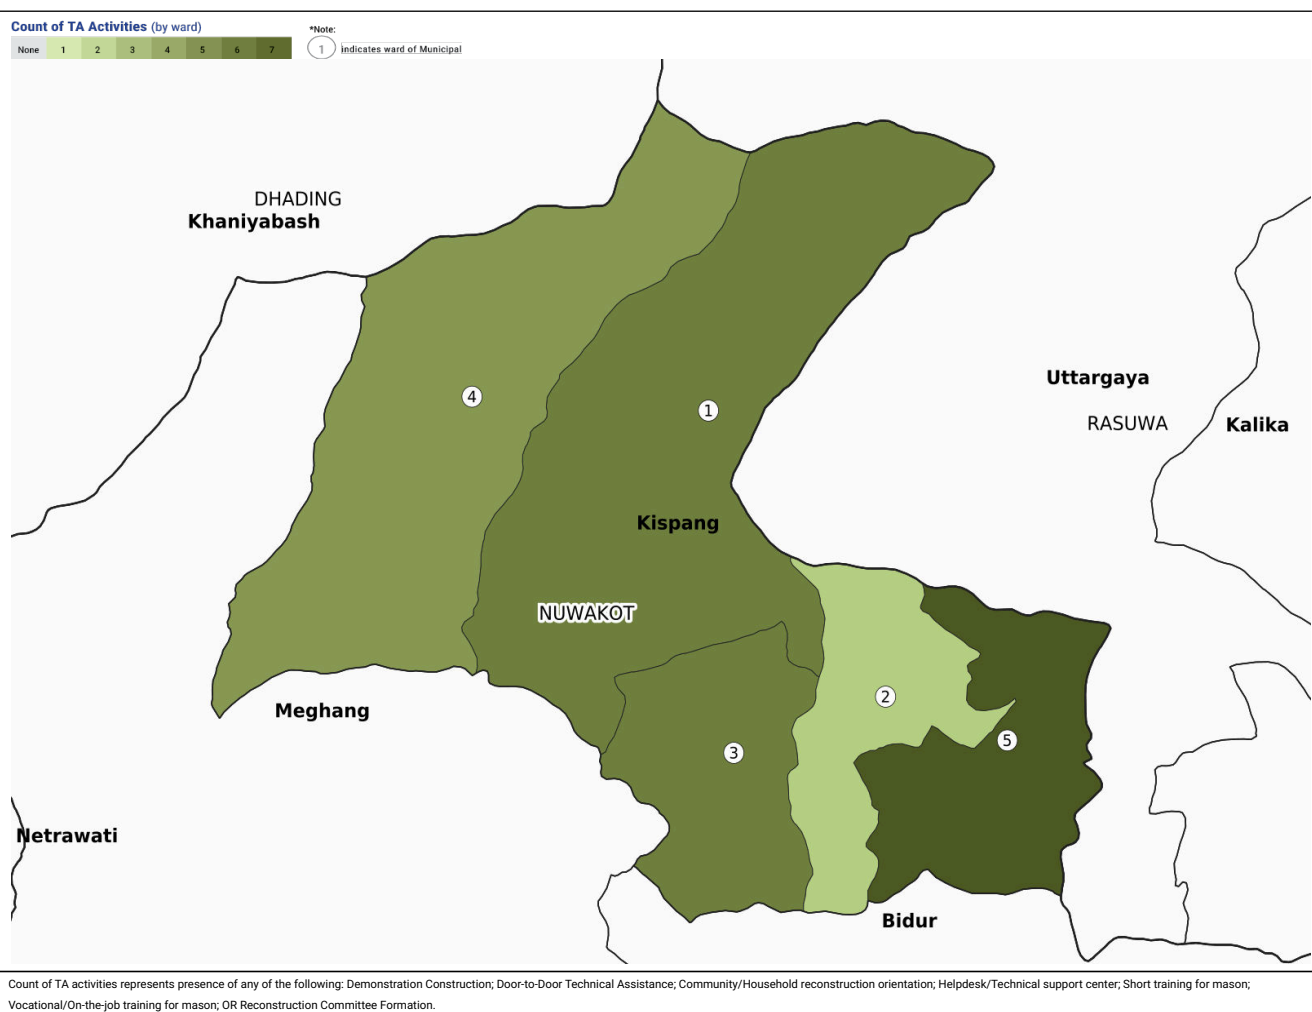

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Badri Pyakurel (District Coordinator) 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer)
9851154201 9842062006
