

District Report

Makwanpur

23 November – 6 December 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		M	F		
<u>Joint Field Monitoring visits (M& E CLPIU, Specialist, DSEs, HRRP):</u> Date: 29 th December, 2018 Time: 10:00AM onwards Location: Makwanpur Gadhi Rural Municipality(Budhichaur VDC) Participants: M&E CLPIU Specialist, DSEs, Local Government, HRRP, NRA technicians and Beneficiaries. Date: 30 th December, 2018 Time: 10:00AM onwards Location: Makwanpur Gadhi Rural Municipality (Makwanpur Gadhi VDC) Participants: M&E CLPIU Specialist, DSEs, Local Government, HRRP, NRA technicians and Beneficiaries.	29 th & 30 th December, 2018			teammakwanpur@hrrpnepal.org	Report & Photos
<u>Training Participated:</u> HRRP District Technical Coordinator has participated as an Instructor on “Earthquake Resilient Building Construction” training organized in Gorkha district. The event was organized by UNDP/DLPIU Gorkha and the technical assistance provided by DLPIU, NSET, UNDP and HRRP.	26 th Nov to 2 nd Dec, 2018			teammakwanpur@hrrpnepal.org	
<u>Palika Level ESMP Meetings, Orientation on Grievance Re-appealing Process and Public Hearing Program</u> Participants: - Local Body Members (Chair, Vice-chair, Ward-chair, Palika/Ward Staffs, Technicians and beneficiaries) - Chief and Staffs of DLPIU-GMaLI - HRRP District Coordinator Venue/Location: 2nd Dec: Thaha Municipality 3rd Dec: Kailash Rural Municipality 4th Dec: Bhimfedi Rural Municipality 5th Dec: Bagmati Rural Municipality Outcomes: - Palika level Environmental and Social Safeguard Management Plans formulated. - Local bodies and beneficiaries were well-oriented on grievance re-appealing process. - Through the public hearing program, voices, issues and complaints of beneficiaries and local bodies were heard and addressed.	2 nd to 5 th December, 2018			teammakwanpur@hrrpnepal.org	Report under preparation

Summary of events during this period

District Coordination Meeting (Meeting of DRFC) Participants: - Members of DRFC - Staffs of DLPIU-Building - Staffs of DLPIU-GMaLI - HRRP Team <i>(see in meeting minute)</i> Agenda: - Reconstruction progress review in line with the decisions of last meeting - AoB Decisions: Based on the progress updates on post-earthquake reconstruction shared by DLPIUs (Building, Education and GMaLI), the meeting concluded the following points:- - Reconstruction of structures planned under DLPIU-Building have been completed and progress achieved in reconstruction of school facilities planned under DLPIU-Education is satisfactory. - In response to the complaints from different rural municipalities, such as, Bhimfedi and Raksirang, regarding the difficulties in approval of inspection/tranche request forms caused by absence or unavailability of Engineers in Municipal and Ward level, the meeting decided to urge relevant agency to take necessary action to overcome the situation. - In line with the decisions of previous meeting, today's meeting has decided to make a fruitful and meaningful discussion/coordination with NRA during the upcoming district level review workshop of NRA (first week of Poush, 2075) to take appropriate action to address the issues of Landlessness and Retrofitting.	6 th Dec 2018	27	5	dc.makwanpur@hrrpnepal.org , techcord.makwanpur@hrrpnepal.org , im.makwanpur@hrrpnepal.org	Meeting Minute available at the below link- https://drive.google.com/drive/u/0/folders/0B1qABhotx8FSc0xLZEhoUUxajA
---	--------------------------	----	---	--	--


Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
ESMP Consultation, Orientation on Grievance Re-appealing Process and Public Hearing	10 Dec, 2018 Bakaiya	DLPIU-GMaLI and HRRP Makwanpur	dc.makwanpur@hrrpnepal.org , techcord.makwanpur@hrrpnepal.org im.makwanpur@hrrpnepal.org


Tranche Status

Rural /Municipality	Bagmati	Bakaiya	Bhimfedi	Hetauda	Indrasarowar	Kailash	M'Gadhi	Manahari	Raksirang	Thaha
Total HHs Surveyed	3454	2384	1056	1636	599	1095	2029	2322	968	1596
Total HHs Eligible	2467	3990	2696	6324	2921	2609	2209	2321	1710	6727
Total HHs Enrolled	1634	2292	2047	522	2437	1962	1581	1158	1482	5868
First Tranche	1742	2224	2089	4624	2398	1997	1631	1220	1507	5950
2 nd Tranche	1247	1485	1738	2508	1720	1616	1272	990	1382	4674
3 rd Tranche	713	548	1518	2370	1007	1172	808	773	913	2791
Total HH Constructed	442	313	943	1557	737	725	435	571	608	2020
Grievance Registered	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658
Grievance Addressed	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658
RF HH Eligible	1941	1616	929	1881	245	606	1372	1330	537	1178
RF HH Enrolled	254	358	365	995	159	185	170	410	302	414
RF 1 st Tranche	228	203	351	995	144	177	170	401	302	414
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	79	304	188	636	24	115	682	489	54	225
Non-Compliance Addressed	0	3	0	0	0	0	6	2	0	0


Tranche updates

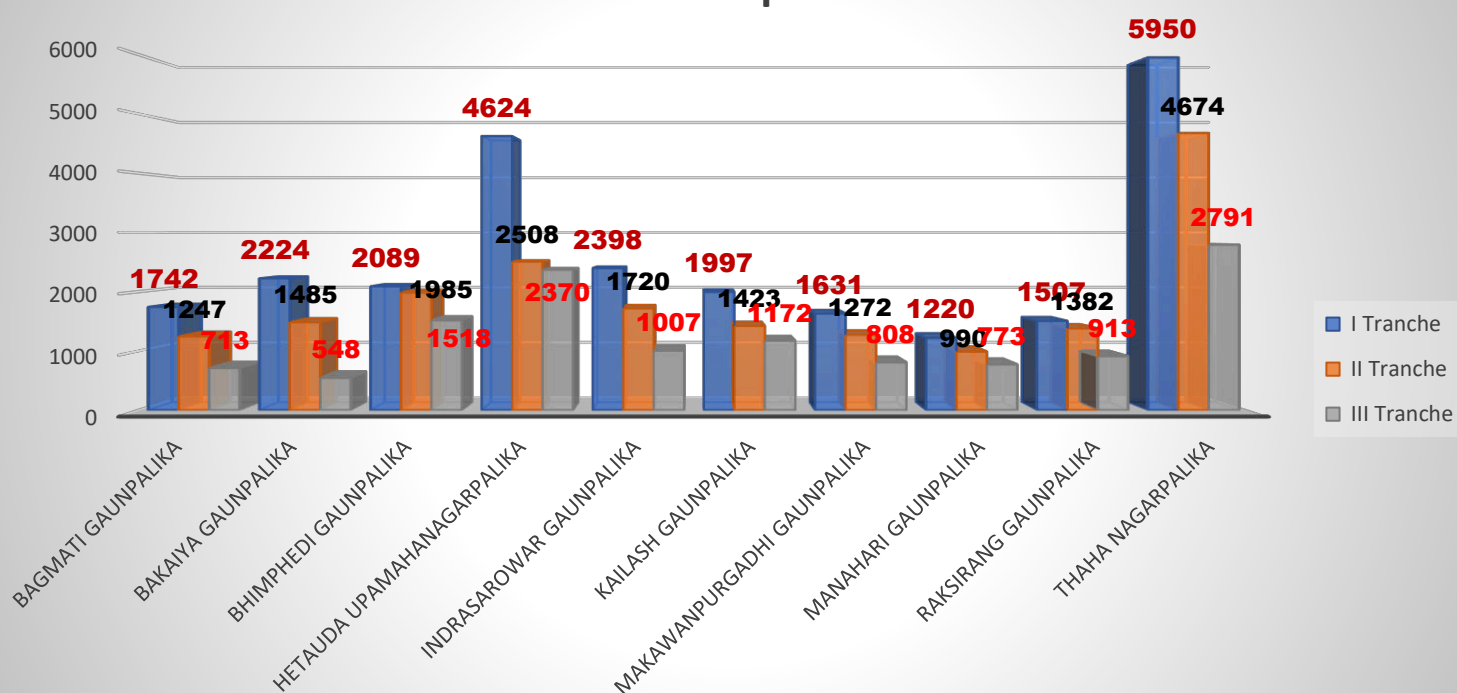

Retrofitting status

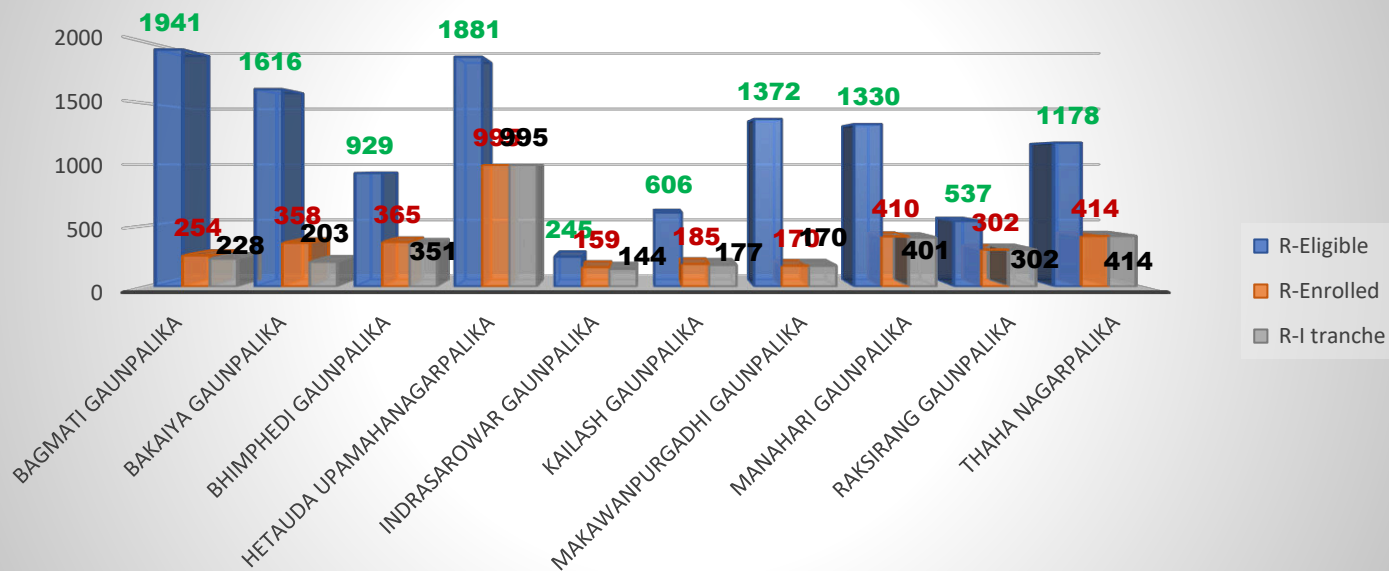

Grivance Status

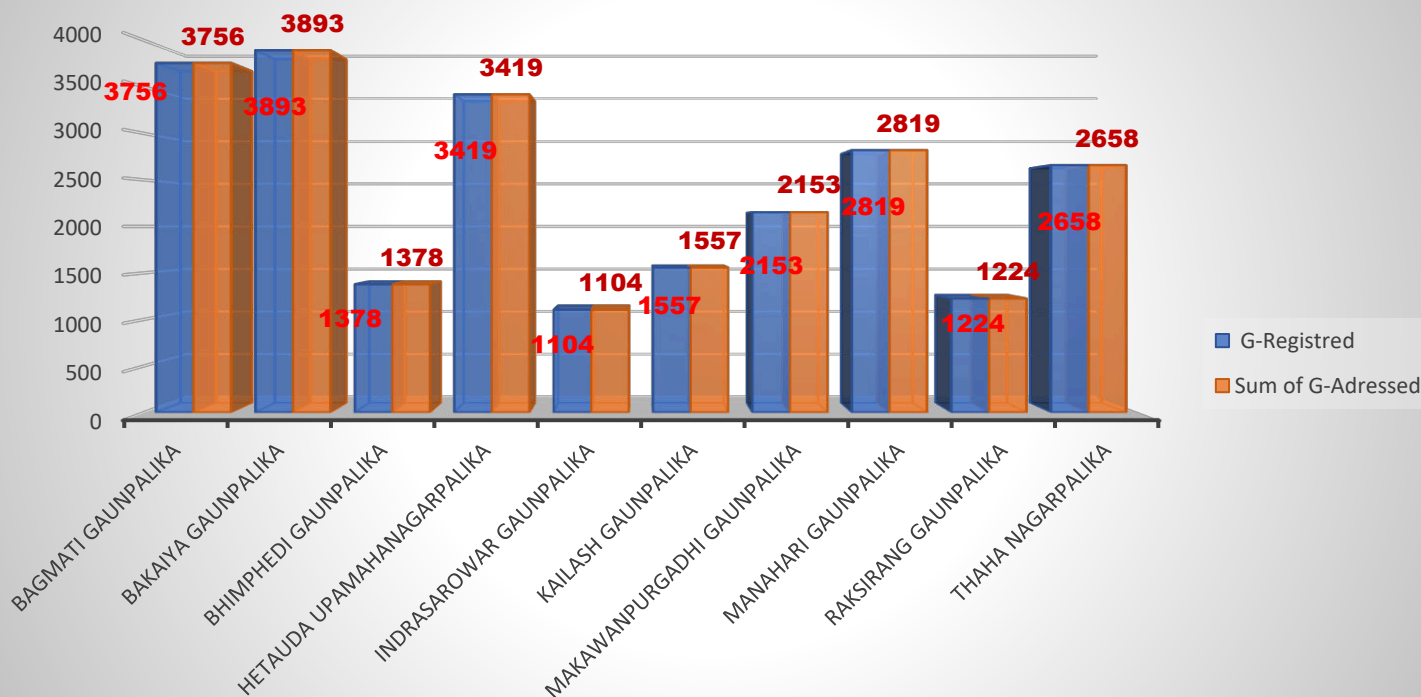

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Visit 1								
Date	Location	Participants from HRRP and stakeholders						
29 th & 30 th Nov, 2018	Makwanpur Gadhi Rural Municipality (Budhichau and Makwanpur Gadhi VDCs)	Joint Monitoring Visits; M&E CLPIU Specialist, DSEs, local government, ward engineers and HRRP team.						
Objective(s)	- To organize technical coordination meeting and separate interaction with ward technicians and beneficiaries. Known the present scenarios of reconstruction in those areas as well as collection of housing typology. - Monitoring in non-compliance issues. - Observe the overall reconstruction status, final inspection status with CS entry, gap between inspection and supervision.							
Summary	The main objectives of the visit were how to solve noncompliance issues like as self-constructed houses before deploying the government engineers and just after earthquake. During the visit first of all we have organized technical coordination meeting in ward offices. The main agendas were how to finalize the reconstructions processes who have received the first tranche, inspection and supervision gap, status in final inspection and CS entry. Conclusion of meeting; To start final inspection who have completed the houses and distribution to completion certificate for completed houses. Maintain the GAP between supervision and inspection and completely minimize the non-compliance issues rather self-constructed houses just after Gorkha earthquake with absent of technical manpower. Regular supervision on correction process when DSEs recommendation it. Monitoring on non-compliance issues; During the visit, we have collected, observed and recommended best solution for self-constructed houses before deploying the government engineers. Most that types of structure became non-compliance issues. We recommended for some correction for those types of structures. During visits also we have collected the different types of construction. There were almost stone in mud with RCC band and timber band, brick in cement mortar, block houses, hybrid structure and frame structures. We discussed further planning of reconstruction and meet to government time frame and complete all housing reconstruction in this fiscal year. <u>Latest reconstruction progress of Makwanpur Gadhi Rural Municipality;</u> The latest reconstruction rate is here in tabular form. <table><tr><th>Makwanpur Gadhi RM</th></tr><tr><td>Total Beneficiaries- 2059; Agreement Beneficiaries- 1668</td></tr><tr><td>First tranche received HHs- 1943; Construction Started HHs- 1785</td></tr><tr><td>Verified for second tranche- 1215; Second tranche received HHs- 1185</td></tr><tr><td>Verified for third tranche- 765; Third tranche received HHs- 730</td></tr><tr><td>Total construction Completed houses HHs- 800; Certificate received HHs- 0</td></tr></table>		Makwanpur Gadhi RM	Total Beneficiaries- 2059; Agreement Beneficiaries- 1668	First tranche received HHs- 1943; Construction Started HHs- 1785	Verified for second tranche- 1215; Second tranche received HHs- 1185	Verified for third tranche- 765; Third tranche received HHs- 730	Total construction Completed houses HHs- 800; Certificate received HHs- 0
Makwanpur Gadhi RM								
Total Beneficiaries- 2059; Agreement Beneficiaries- 1668								
First tranche received HHs- 1943; Construction Started HHs- 1785								
Verified for second tranche- 1215; Second tranche received HHs- 1185								
Verified for third tranche- 765; Third tranche received HHs- 730								
Total construction Completed houses HHs- 800; Certificate received HHs- 0								

Challenges / Issues Identified	Action Required	Responsible	Timeframe
- Buildings where there is a presence of RCC slab in stone in mud as well as wooden slab. - Block masonry structure with an attic height and hybrid structure / mixed design have not properly addressed by owners. - Noncompliance issues in self-constructed houses after just earthquake and before deploying government engineers.	- Regular supervision and inspection on time - Early, noncompliance file submit to DSE for further analysis of structures. - Block guide line is publishing and help to for block structures. - Regularly supervision for correction after DSEs recommendation it.	DSEs, ward engineers.	Regular

Photos



Figure 1: Technical coordination meeting has been organized in MakwanpurGadhi Rural Municipality; the agendas were how to finalize the reconstructions who have received the first tranche, inspection and supervision gap, status in final inspection and CS entry.



Figure 2: Technical interaction program has been organized in Makwanpur Gadhi Rural Municipality-02; discussed on noncompliance issues, final inspection of completed houses, CS entry process and process of certificate distribution to completed houses.

Housing Typology Report



Figure 3: House owner; Narayan Prasad Dhungana, Makwanpur Gadhi RuralMunicipality-03, he is a retrofitting beneficiary and received first tranche but he doesn't agree for correction and he has apply for beneficiaries change process retrofitting to reconstruction. But still from technical view point this house may eligible for government tranche after some earthquake seismic resistant elements provided.



Figure 4: House owner; Durga Prasad Dhungana, Makwanpur Gadhi RuralMunicipality-03, also he is a retrofitting beneficiary and received first tranche and he has apply for beneficiaries change process retrofitting to reconstruction. And result couldn't publish till to date but he started own house for reconstruction. Generally we provide 3'*3' size of foundation but still not provided sufficient size. We suggested for some correction of foundation.



Figure 5: House owner; Tara Nath Sapkota, Makwanpur Gadhi RuralMunicipality-03, he is a reconstruction beneficiary and he constructed own house before deploying the government engineer. Now this house has not eligible for government grants because of he has not provided seismic resistant elements like as vertical post, horizontal bands, too thing etc. He used block material with two stories. DSEs recommended for correction but also he does not agree for correction. It is an example of issues almost in Makwanpur district these types of problems have faced by government engineers.



Figure 6: House owner; Khadak Prasad Lamsal, Makwanpur Gadhi RuralMunicipality-03, he is a reconstruction beneficiary and he constructed own house before deploying the government engineer. Now this house has not eligible for government grants because of he has not provided seismic resistant elements like as vertical post, horizontal bands, too thing etc. He used block material with two stories with huge opening. DSEs recommended for correction but also he does not agree for correction.

Challenges and Way Forward

Challenge	Way Forward
- Noncompliance issues in self-constructed houses after just earthquake and before deploying government engineers. - Final inspection of completed houses and CS entry.	- Regularly supervision for correction after DSEs recommendation it. Also, We are planning to frequently field visit in those types of structures and give solution for correction. - It is a duty of engineers but it has not started yet so engineers should be starting it. And also we are carrying regular field visit and suggest for final inspection and CS entry and also distribution of certificate for completed houses.
