

## Fortnightly District Report

### Rasuwa

18 – 31 January 2019

#### Summary of events during this period

| Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                                                            | Event date | Participants summary |        | Contact Person                                                                                                                                           | Reference Document |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|----------------------|--------|----------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |            | Male                 | Female |                                                                                                                                                          |                    |
| The MoU signed between NRA and local bodies was completed on 21 <sup>st</sup> Jan 2019 at Rasuwa District. Whole day session was conducted in which different GoN stakeholders : GMAII, Building DLPIU, School-DLPIU and HRRP presented their achievement which district have accomplished in sector of public building, GoN building and in school construction. Presentation had carried out in terms of grand management , resettlement process for displaced by Gon person came from central. |            |                      |        | <a href="mailto:Im.rasuwa@hrrpnepal.org">Im.rasuwa@hrrpnepal.org</a><br><a href="mailto:Techcord.rasuwa@hrrpnepal.org">Techcord.rasuwa@hrrpnepal.org</a> |                    |
| The contact list of all palikas focal person was updated at national level in addition also requested them to upload action plan and palika profile in their respective Palikas website. During our last phone conversation with them, They showed their interest to upload the provided documents in website.                                                                                                                                                                                    |            |                      |        | <a href="mailto:Im.rasuwa@hrrpnepal.org">Im.rasuwa@hrrpnepal.org</a><br><a href="mailto:Techcord.rasuwa@hrrpnepal.org">Techcord.rasuwa@hrrpnepal.org</a> |                    |
| Followed up with partners , GoN stakeholders, donors for the feedback on district HRRP had requested them to filled the partners Satisfaction survey. By which 22 different stakeholders including GON , Donors and partners organization provided feedback on PSS .                                                                                                                                                                                                                              |            |                      |        | <a href="mailto:Im.rasuwa@hrrpnepal.org">Im.rasuwa@hrrpnepal.org</a><br><a href="mailto:Techcord.rasuwa@hrrpnepal.org">Techcord.rasuwa@hrrpnepal.org</a> |                    |
| . 5W for the month of January was updated and uploaded on district folder.                                                                                                                                                                                                                                                                                                                                                                                                                        |            |                      |        | <a href="mailto:Im.rasuwa@hrrpnepal.org">Im.rasuwa@hrrpnepal.org</a><br><a href="mailto:Techcord.rasuwa@hrrpnepal.org">Techcord.rasuwa@hrrpnepal.org</a> |                    |

## Summary of events during this period


Field visit was conducted at Gosaikunda RM ward number 6-Dhunche. HRRP team together with M&E specialist for Rasuwa and Nuwakot Mr.Prabu Ram Pokheral , Building DLPIU focal person Mr. Saroj Kumar Yadav and district support engineer Mr. Projwal KC visited ward 6 to monitor the ongoing construction. In addition to ward number 6, on the recommendation made by DLPIU chief monitoring team also visited ward number 1 of same palika on same day.

[Im.rasuwa@hrrpnepal.org](mailto:Im.rasuwa@hrrpnepal.org)  
[Techcord.rasuwa@hrrpnepal.org](mailto:Techcord.rasuwa@hrrpnepal.org)


## Tranche Status

| Rural /Municipality        | Gosaikunda RM | Kalika RM | Naukunda RM | Aamo Chhindigmo RM | Uttargaya RM |
|----------------------------|---------------|-----------|-------------|--------------------|--------------|
| Total HHs Surveyed         | 1979          | 2569      | 3349        | 1964               | 2631         |
| Total HHs Eligible         | 1979          | 2569      | 3349        | 1964               | 2631         |
| Total HHs Enrolled         | 1836          | 2456      | 3291        | 1802               | 2274         |
| First Tranche              | 1836          | 2456      | 3291        | 1802               | 2274         |
| Second Tranche             | 1649          | 2308      | 3038        | 1560               | 1958         |
| Third Tranche              | 1248          | 2121      | 2758        | 1273               | 1725         |
| Total HH Constructed       | 1248          | 2121      | 2758        | 1273               | 1725         |
| Grievance Registered       |               |           |             |                    |              |
| Grievance Addressed        | 257           | 277       | 246         | 237                | 239          |
| RF HH Eligible             | 84            | 11        | 59          | 32                 | 25           |
| RF HH Enrolled             | 60            | 10        | 2           | 10                 | 11           |
| RF 1 <sup>st</sup> Tranche | 60            | 10        | 2           | 10                 | 11           |
| RF 2 <sup>nd</sup> Tranche | 0             | 0         | 0           | 0                  | 0            |
| Non-Compliance Registered  | 89            | 48        | 54          | 101                | 124          |
| Non-Compliance Addressed   | 69            | 36        | 40          | 70                 | 86           |


Graph of Tranche Status:

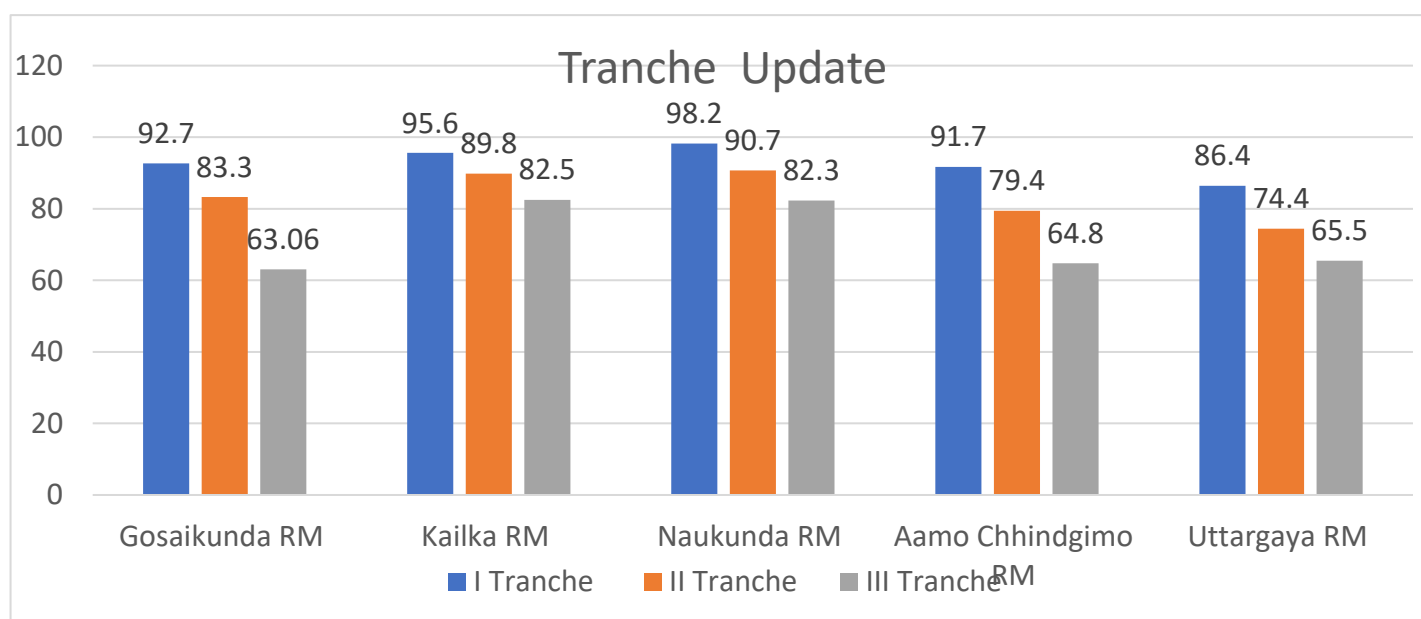

Graph for Retrofitting Status:

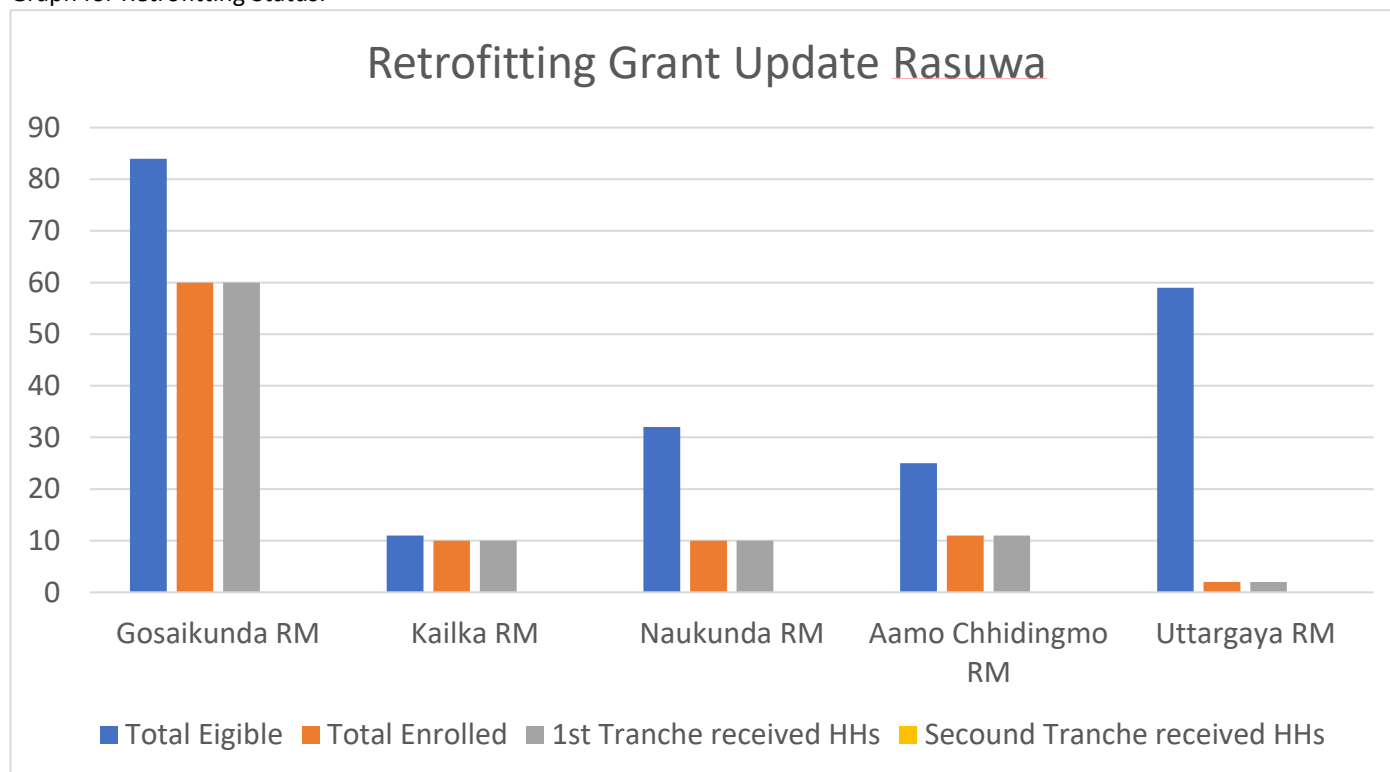

Graph for Grievance Status:

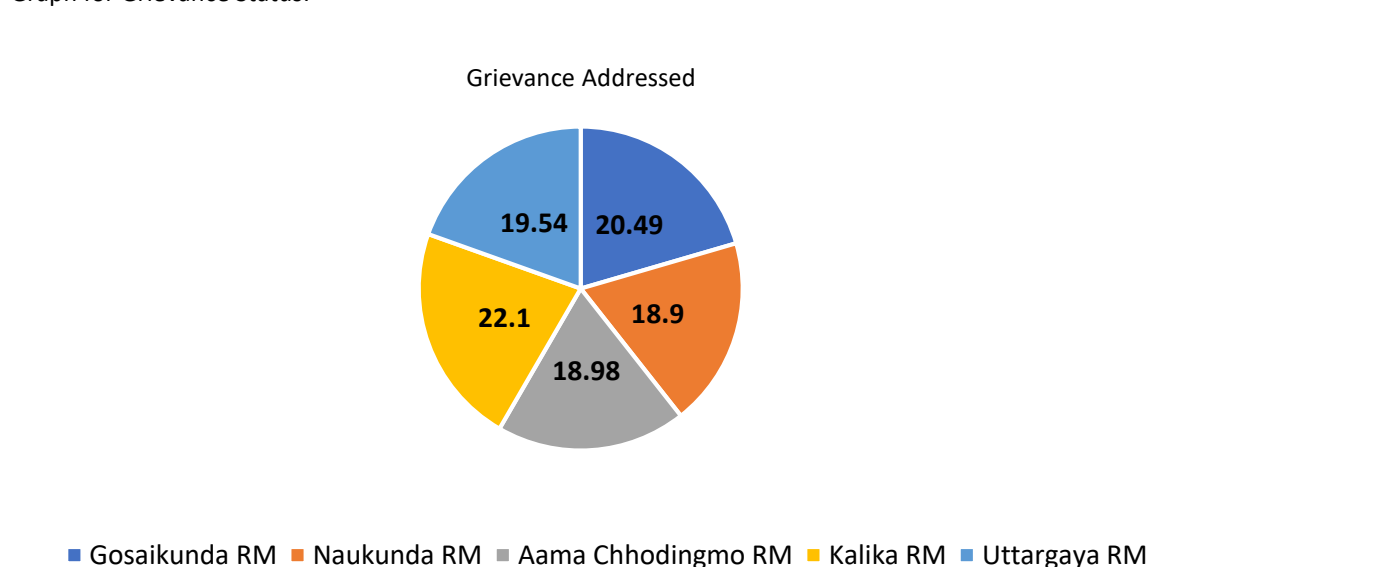

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 1

| Date                                                                                                                                                                        | Location                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | Participants from HRRP and stakeholders                                                                                                                                                                                                                      |           |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|
| Jan22,2019                                                                                                                                                                  | Gosaikunda RM, Ward no-6                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | <ul style="list-style-type: none"><li>Biren Shah, DTC, HRRP</li><li>Prabhu Pokhrel, M &amp; E Expert</li><li>Rijan Gajurel, DC, HRRP</li><li>Prajwal K.C., DSE, NRA</li><li>Saroj Kumar Yadav, DLPIU Building</li><li>Bhim Bahadur Bohara,ward sub</li></ul> |           |
|                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |                                                                                                                                                                                                                                                              |           |
| Objective(s)                                                                                                                                                                | <ol style="list-style-type: none"><li>To interact with local representatives, engineers along with beneficiaries to know the reconstruction progress and challenges.</li><li>To monitor reconstruction status of the ward</li><li>To collect housing typologies.</li><li>To collect information on Status of timber structure and non-compliant issues.</li></ol>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                              |           |
| •                                                                                                                                                                           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |                                                                                                                                                                                                                                                              |           |
| Summary                                                                                                                                                                     | <p>Number of beneficiaries after survey = 507<br/>Beneficiary after Grievance = 106<br/>Total Beneficiary=613<br/>First Tranche =563<br/>Second Tranche=518<br/>Third Tranche=323<br/>No. of houses constructed=323<br/>Retrofitting Beneficiaries=12<br/>First Tranche=8<br/>Second Tranche=0</p> <p>The field visit was targeted in Gosaikunda RM, ward-6, Dhunche to collect the reconstruction status and challenging issues of the ward. There are total 613 total numbers of beneficiaries of which 563 has received the first tranche, 518 have received the second tranche and 323 have received the third tranche. The reconstruction of this RM is lagging as compared to the other RM of Rasuwa district. There are 12 beneficiaries listed in the retrofitting list but the process for the second tranche has not been started due to the unavailability of technical. Even the technicals have no idea about the process and the methods that will be applied for retrofit.</p> |                                                                                                                                                                                                                                                              |           |
| •                                                                                                                                                                           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |                                                                                                                                                                                                                                                              |           |
| Challenges / Issues Identified                                                                                                                                              | Action Required                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Responsible                                                                                                                                                                                                                                                  | Timeframe |
| No involvement of the beneficiaries in construction of houses after receiving the first tranche.                                                                            | Follow-up by the ward and dissemination of information of returning the tranche for un-interested beneficiaries getting involved in construction.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             | DLPIU GMAI, Palika and ward                                                                                                                                                                                                                                  | ASAP      |
| Building with structural span more than 4.5-meter, panel area more than 13.5 sq. m. The slab with loner span is found which can undergo deflection and are thus vulnerable. | Structure analysis of the building /significant correction measures.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | DSE/DLPIU Building                                                                                                                                                                                                                                           | ASAP      |

|                                                                                                                      |                                                                                      |                                            |      |
|----------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|--------------------------------------------|------|
| Some of the beneficiaries have constructed one room up to DPC level and are not looking up for further construction. | Follow up from DLPIU-Building, DLPIU -GMAI about the deadline and blacklist process. | DLPIU GMAI/DLPIU Building, Palika and ward | ASAP |
|----------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|--------------------------------------------|------|

#### Photos



**Ward NO.6, Gosaikunda RM, Rasuwa**

**Name of Beneficiary: Suman Tamang**

**Tranche Update: First Received**

**Housing Typology:** RCC framed one storeyed four rooms house.

The house has three bays in x-direction and two bays in Y-direction.

The distance of bay in x-direction are:

X1=13 feet, x2=13 feet and x3=12'8" and similarly the distance of bays in Y-directions are:

Y1=16' and Y2=11'.

The house was forwarded for non-compliance as the maximum size of the room was 208 square feet (19.28 sq m.) which did not comply with the standard requirement which is 13.5 sq m.

**Ward NO.6, Gosaikunda RM, Rasuwa**

**Name of Beneficiary: Ramesh Ghale**

**Tranche Update: Third Received**

**Housing Typology:** Load bearing Brick Masonary in cement mortar, three rooms house.

## Housing Typology Report

Photo



**Ward NO.6, Gosaikunda RM, Rasuwa**

**Name of Beneficiary: Lama Tenjing Ghale**

Photo



**Ward NO.6, Gosaikunda RM, Rasuwa**

**Name of Beneficiary: Memba Gyalbo Ghale**



|                                                                                                                                                                                                                                                                                                                                                            |                                                                                                                                                                                                  |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <p><b>Tranche: Received Third tranche</b><br/><b>Housing Typology:</b> Load bearing Brick Masonary in cement mortar, three rooms house. The construction of the house is completed.</p>                                                                                                                                                                    | <p><b>Tranche: Second Received</b><br/>The house belongs to a single woman<br/><b>Housing Typology:</b> One room house. Stone used up to DPC level and rebar at the corners and mid-section.</p> |
| <p>Photo</p>                                                                                                                                                                                                                                                              | <p>Photo</p>                                                                                                                                                                                     |
| <p><b>Ward NO.6, Gosaikunda RM, Rasuwa</b><br/><b>Name of Beneficiary:</b> Snig Ghale<br/><b>Tranche: Received Third tranche</b><br/><b>Housing Typology:</b> Hybrid structure with lower load bearing stone Masonary in cement mortar and upper Timber structure. There are altogether three rooms in the house – one room lower and two rooms upper.</p> |                                                                                                                                                                                                  |



## Questions Collected

| Question                                                    | Who Asked the Question? | Response Provided (By Whom)                                                                           |
|-------------------------------------------------------------|-------------------------|-------------------------------------------------------------------------------------------------------|
| When will the construction completion certificate be given? | Beneficiaries           | (The distribution of completion certificate is started in other wards like Kalika-5 and will be soon) |
| What is the deadline of the third tranche?                  | Beneficiaries           | Biren Shah                                                                                            |
| Will there be additional top-up for us??                    | Beneficiaries           | There is top up only for of 50k Rs for people who have been listed in vulnerable groups.              |

## Challenges and Way Forward

| Challenge                                                                                                                                                                    | Way Forward                                                                                        |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------|
| Building with structural span more than 4.5-meter, panel area more than 13.5 sq. m. The slab with longer span is found which can undergo deflection and are thus vulnerable. | Increase thickness of slab or provide secondary beam in the longer direction. (Recommended by DSE) |
| Some of the beneficiaries have constructed one room up to DPC level and are not looking up for further construction.                                                         | Follow up from DLPIU-Building, DLPIU -GMaI about the deadline and blacklist process.               |
