


FACTS AND FIGURES

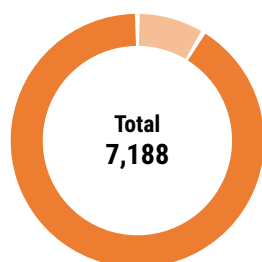

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	91.73%	82.76%
Reinforced Cement Concrete (RCC) Frame	4.65%	3.23%
Brick and Cement Mortar Masonry	1.36%	2.57%
Timber Frame Structure	1.05%	0.88%
Others	1.23%	10.57%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	6,924
PA Agreement	6,655
I st Tranche received	6,655
II nd Tranche received	6,270
III rd Tranche received	5,494

Houses

Under Construction: 776

Completed: 5,494

Retrofitting Status

Total Eligible HHs	177
PA Agreement	31
I st Tranche received	32
II nd Tranche received	0

Grievances

Registered: 967

Addressed: 318

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: UNDP (Shelter)

Phased Out: CRS (Agriculture), CRS (Livelihood), CRS (Shelter), FCA (Education), GNI (Education), GNI (Health), HELVETAS (Shelter), INF (Livelihood), LIONS (Education), SAHAS (Shelter), SCI (Education), SCI (Health), SCI (Shelter), SCI (Social Protection), UNDP (Shelter)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	166,542	Y	1,800
Aggregate	m ³	141,795	-	8,000
Sand	m ³	17,506	-	7,000
Timber	cu. ft.	19,190	-	-
Cement (PPC)	Sack	-	Y	1,000
Cement (OPC)	Sack	470,708	N	1,200
Rebars	kgs.	1,843,877	-	-
Tin	bundle	19,171	-	-
Bricks	pcs.	3,186,234	-	20

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,500 /-
900 /-

OTHER SECTORS



Schools

Damaged: 44
Under Construction: 25
Construction Completed: 25



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

KEY CONTACTS

Municipal Office

Purna Bahadur Dahal
Chairman
9846543034

Municipal Office

Nabaraj Khanal
Focal Person
9860841586

Municipal Office

Kalpna Nepali
Deputy Chairman
9846075455

GMAI/NRA

Ram Sharan Acharya
NRA Chief-District
9856042637

Municipal Office

Eak Dev Khannal
Chief Administration Officer
9856010044

DLPIU-Building

Sunita Shrestha
DUDBC.DLPIU Chief
9841632087

HHs WITH LAND ISSUES



STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	7	-
Sub-Engineers	14	-
Asst. Sub-Engineers	7	-
Masons	1,016 (7 days) 574 (50 days)	1,500 (7 days) 1,000 (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)

7 days Training




50 days Vocational Training



Source: HRRP Analysis

TA ACTIVITIES MAP

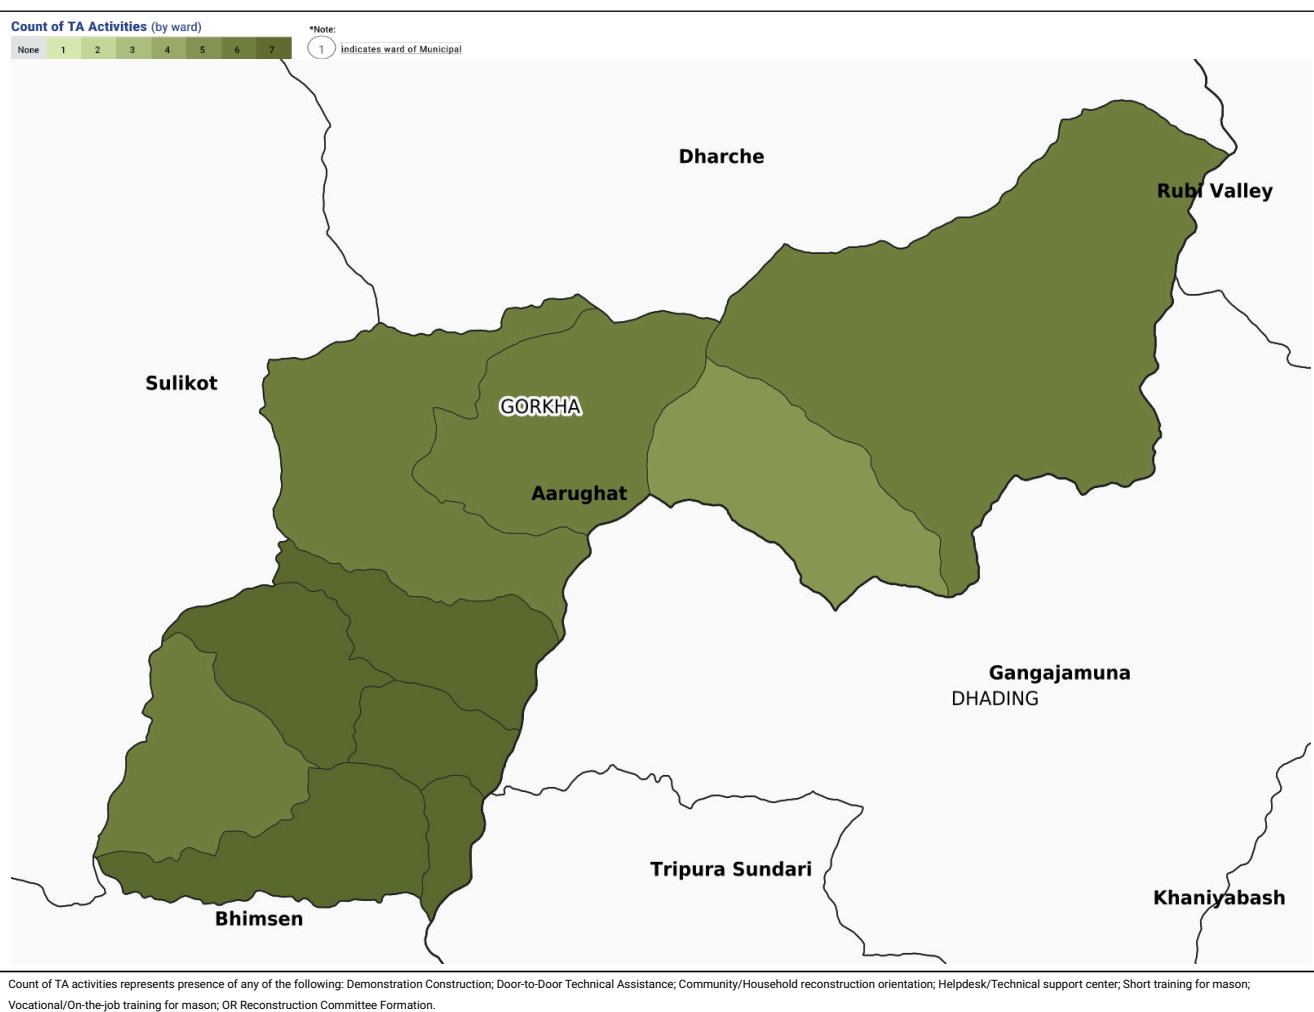

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Chandra Gurung (District Coordinator) 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer)
9841478742 9842062006
