

Monthly District Report

Dolakha, Ramechhap, Sindhuli

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	Palika level reconstruction coordination meeting	9-May-2019	Shailung Gaupalika	prabin.gautam@hrrpnepal.org	Refer to Field visit section
	Palika level reconstruction coordination meeting	20-May-2019	Tamakoshi Gaupalika	prabin.gautam@hrrpnepal.org	Refer to Field visit section
	GMaLI/HRRP district coordination meeting with POs.	22-May-2019	GMaLI office, Dolakha.	prabin.gautam@hrrpnepal.org	Document Here
	Reconstruction coordination meeting	23-May-2019	Baiteshwor Gaupalika	prabin.gautam@hrrpnepal.org	Refer to Field visit section
	District Reconstruction Facilitation/Coordination Meetings at DCC office where DCC chief Mr. Double Pandey was the chairperson.	28-May-2019	DCC office, Dolakha.	prabin.gautam@hrrpnepal.org	Document Here
	Ward level reconstruction coordination meeting	29-May-2019	Bhimeshwor ward no.: 1	prabin.gautam@hrrpnepal.org	Refer to Field visit section
	Palika and ward level reconstruction coordination meeting at municipality office.	30-May-2019	Jiri Municipality and ward no.: 4 & 5	prabin.gautam@hrrpnepal.org	Refer to Field visit section
	Preparation of district report and municipal experience sharing report.	10- 13 June-2019		prabin.gautam@hrrpnepal.org	
	Prepared Dolakha MEAL report for the month of May 2019 and submit to HRRP	5-June-2019		prabin.gautam@hrrpnepal.org	
Ramechhap	Palika Level Coordination Meeting	12-May-2019	Ramechhap, Khadadevi RM	Pranjal Bhandari	Meeting Minutes
	Palika Level Coordination meeting	13-May-2019	Ramechhap, Doramba RM	Pranjal Bhandari	Meeting Minutes
	Palika Level Coordination Meeting	15-May-2019	Ramechhap, Sunapati RM	Pranjal Bhandari	Meeting Minutes
	Ward Level Coordination Meeting	3 rd -Jun-2019	Ramechhap, Gokulganga RM-4	Pranjal Bhandari	Meeting Highlights
	Palika Level Coordination Meeting	6 th -Jun-2019	Ramechhap Umakunda RM	Pranjal Bhandari	Meeting Highlights
Sindhuli	Palika Level Coordination meeting	15 th May 2019	Sunkoshi Gaupalika	tulashi.lamichhane@hrrpnepal.org	Click Here for Report
	Ward Level Coordination Meeting	29 th May 2019	Ghyanglekh Gaupalika	tulashi.lamichhane@hrrpnepal.org	Click Here for Minutes
	District Level Coordination Meeting	11 th May 2019	DCC Chief office	tulashi.lamichhane@hrrpnepal.org	Click Here for Minutes

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
NSET day celebration	18 th June 2019 at Charikot, Dolakha.	NSET-Dolakha	pranavdahal@nset.org.np
Joint monitoring field visit with GMAI, DLPIU/Building and CLPIU-M&E	24-28 June 2019 at Gaurisankar RM and Kalinchowk RM.	HRRP-Dolakha	prabin.gautam@hrrpnepal.org
Joint Monitoring field visit and Palika level Coordination Meeting	Ramechhap, Ramechhap Municipality	HRRP, DLPIU Building	Pranjal Bhandari
Palika Level Coordination Meeting	Fikkal Gaupalika, 14 th May 2019	HRRP and GMAI	Tulasi Ram Lamichhane sindhuli@hrrpnepal.org

News & Updates

Dolakha NSET/Baliyo Ghar conducted two days training on Disaster Risk Reduction Management at Simpani Hall, Charikot and Virkot village, Tamakoshi RM from 11 to 12 June 2019.



Photo: Retrofit and DRR training at Charikot, Simpani Hall, Dolakha.

- The program was focused on disaster risk reduction and prolonged reconstruction for local representatives.
- Building code implementation and process of approval for house designs.
- Observation of retrofit techniques at field visit.



Photo: Retrofitted beneficiary house at Tamakoshi RM, Virkot village, Dolakha.

Sindhuli District

- Skills for Safe Reconstruction Project (SSRP) of Swiss Contact in Sindhuli district has conducted 7 day's skills upgrading training on earthquake resilient timber frame building construction techniques to 120 construction carpenters involved in the reconstruction works. The training was conducted in Kamalamai Municipality and Marin Rural Municipality comprising of 80 and 60 trainees respectively. SSRP developed 7 days training curriculum for carpentry training that incorporated structural principles as specified for earthquake resiliency and further approved by CLPIU. The need of this training was identified by SSRP in collaboration with National Reconstruction Authority (NRA), Sindhuli. It was realized that house owners were facing problems to build timber houses for shortage of skilled workers and there were number of noncompliance issues.

- SERVE project conducted by Mercy Corps Nepal has been providing Socio Technical Support to the vulnerable groups of the vulnerable list provided by NRA. Out of 119 vulnerable group beneficiaries, others except 35 have completed the construction of house before the introduction of the SERVE Project. SERVE has been providing STA to the 35 Households among which 33 have completed their houses and remaining two are in the roof band and intermediate band level respectively.


The Solution to the landless issues has been provided via a meeting conducted in the presence of Member of Parliament (Haribol Gajurel and Ganesh Pahadi), CDO (Janardan Gautam), DCC Chief (Shankar Raj Barma Tiwari), DCO (Dik Bahadur Karki) and Act. GMALI Chief (Surya Prakash Bista). The program was organized by GMALI.

Tranche Status (Dolakha)


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8198	7726	7229	6764	342	6	6	0
Bhimeshwor Nagarpalika	10796	12525	11117	11029	8484	6894	353	110	110	0
Bigu Gaunpalika	5758	6733	6327	6228	5813	5150	35	6	6	0
Gaurishankar Gaunpalika	5405	6876	6571	6491	5919	5725	134	38	38	0
Jiri Nagarpalika	4764	5850	5634	5022	4234	3395	171	31	31	0
Kalinchok Gaunpalika	7527	8916	8457	8449	8115	7779	32	19	19	0
Melung Gaunpalika	7006	7685	6965	6583	6345	5525	476	30	30	0
Sailung Gaunpalika	6800	8424	6975	6949	6118	4946	918	50	50	0
Tamakoshi Gaunpalika	6191	7461	6873	6872	6481	5735	115	9	9	0

Graph of Tranche Status:

Reconstruction - Retrofitting Status

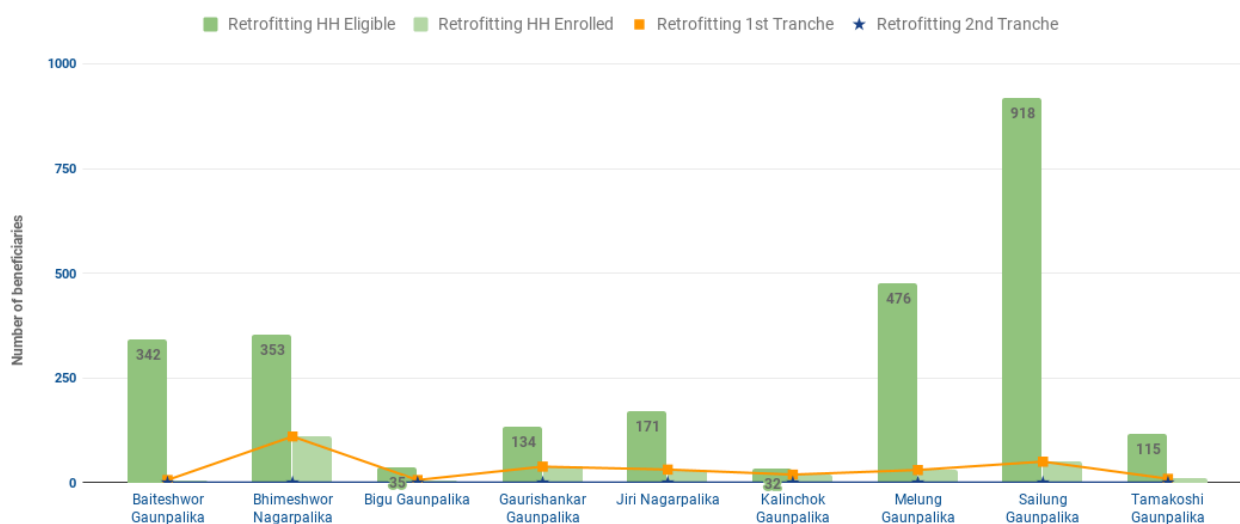

Reconstruction- Tranche Status

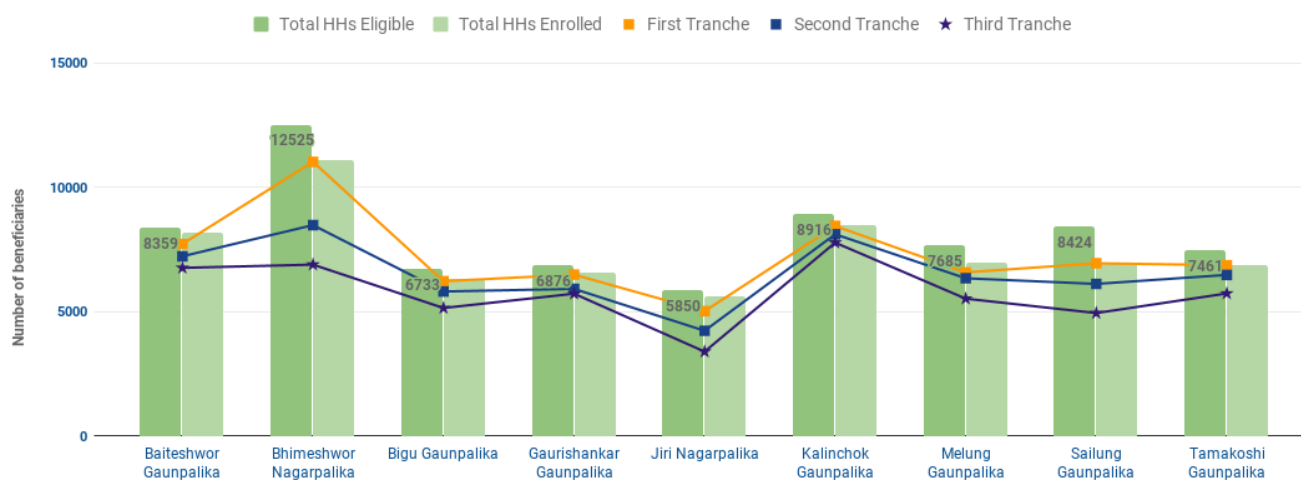


Tranche Status (Sindhuli)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5179	4692	4692	2275	842	3531		804	0
Ghanglekh Gaunpalika	3032	2244	2139	2139	1662	1148	530		118	0
Golanjor Gaunpalika	4835	3231	2992	2992	2372	1774	667		97	0
Hariharpurgadhi Gaunpalika	5176	2601	2296	2296	1746	326	1538		0	0
Kamalamai Nagarpalika	15659	8537	7799	7799	4528	2610	1788		376	0
Marin Gaunpalika	5717	3720	3192	3192	2084	830	1266		138	0
Phikkal Gaunpalika	4072	2666	2171	2171	2005	1699	932		8	0
Sunkoshi Gaunpalika	6393	5032	4858	4858	3554	1685	327		0	0
Tinpatan Gaunpalika	8863	4701	4671	4671	3986	3234	2499		543	0


Graph of Tranche Status:

Reconstruction- Tranche Status

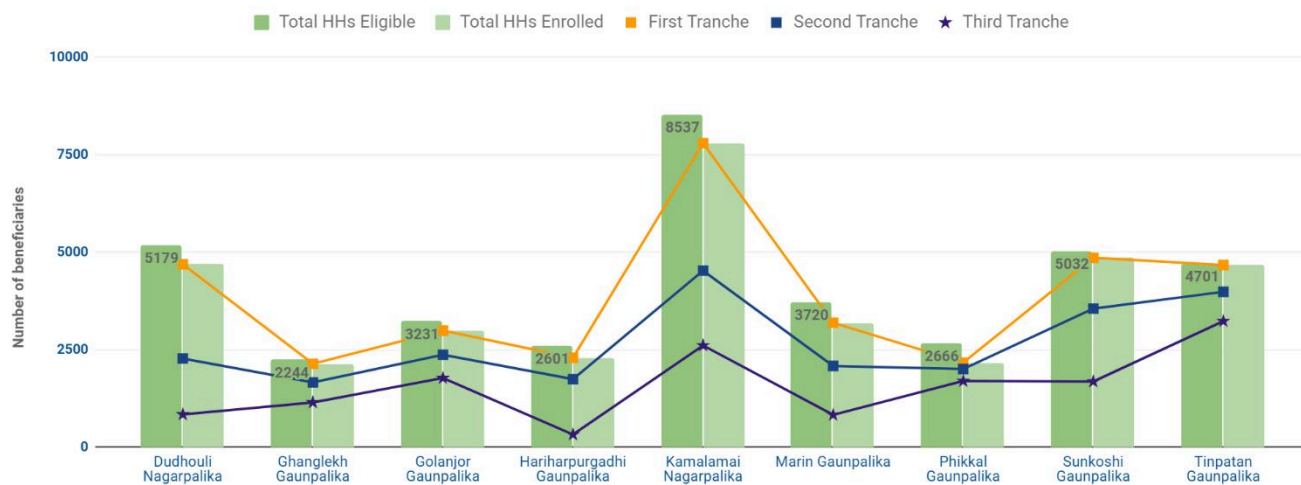

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

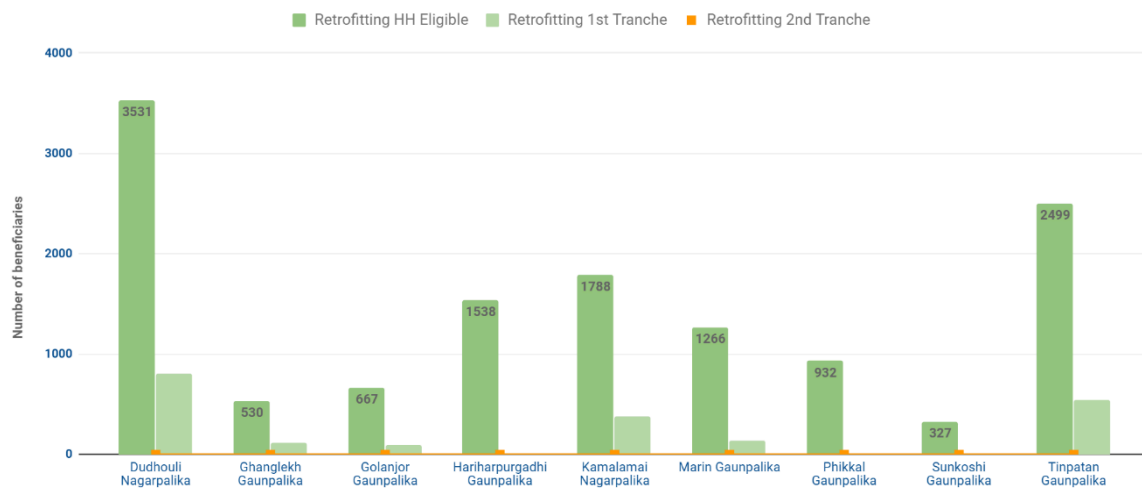


Tranche Status (Ramechhap)


Tranche Status Table:

Palika Name	Eligible HHs	PA Agreement Signed	Tranche I	Tranche II	Tranche III	Eligible HHs RF	PA Agreement RF	Tranche I RF	Tranche II RF
Doramba Gaunpalika	5252	4716	4708	3968	2932	1076	47	47	0
Gokulganga Gaunpalika	6343	6075	6066	5203	4294	347	1	1	0
Khadadevi Gaunpalika	5212	5215	5121	4769	4105	1317	222	222	0
Likhu Gaunpalika	5686	5545	5544	5123	4494	1010	16	16	0
Manthali Nagarpalika	11077	10758	10756	9700	8170	1271	39	39	0
Ramechhap Nagarpalika	6554	6416	6412	5708	5131	960	6	6	0
Sunapati Gaunpalika	3671	3555	3550	3148	2240	821	20	20	0
Umakunda Gaunpalika	4984	4566	4566	4087	2858	343	5	5	0

Graph of Tranche Status:

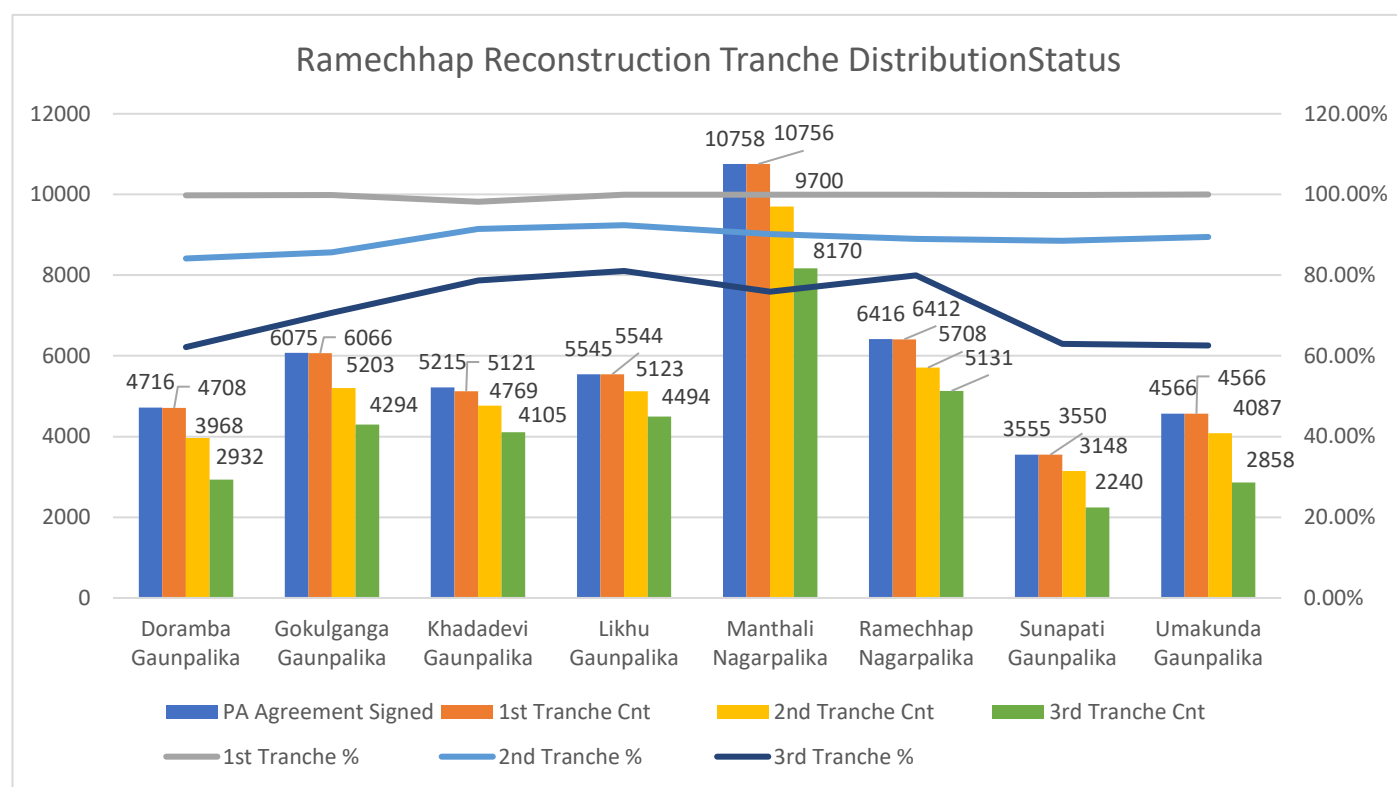

Graph for Retrofitting Status:

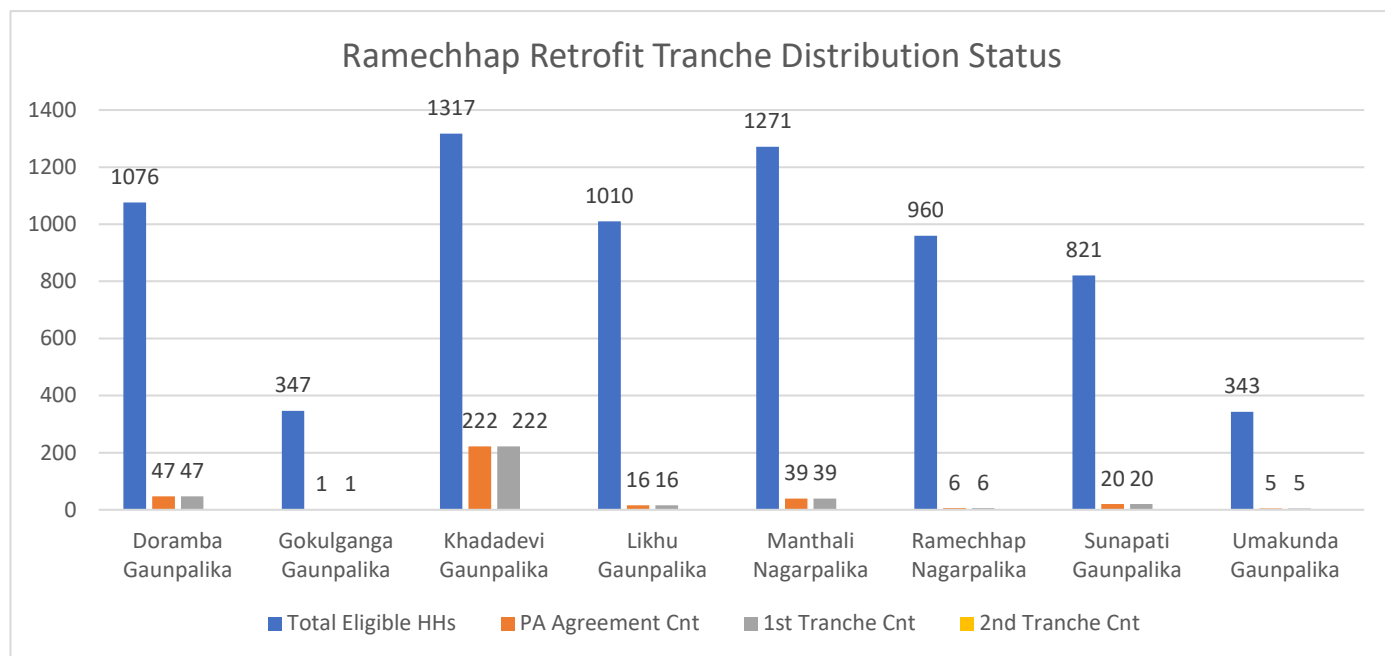

Field Visit Reports (Dolakha)

Visit 1

Date	Location	Participants
(6 – 10) May 2019	Dolakha district, Sailung rural municipality.	- Bhogendra Sha (DLPIU/building-Focal person) - Janak Raj Joshi (MoUD/CLPIU-M&E) - Prabin Gautam (Cluster-10, DC) - Ananta Poudel (Palika focal Er.) - Bikash Khattri (DLPIU-Er.)
Objective(s)	- Discussing the situation of the construction of private housing with local public representatives. - Resolve duplication of beneficiary at field level. - Regarding issue due to approval of tranches by NRA engineers before the start of construction of house.	

Why was the visit carried out in this location?

The field visit was conducted to find out the current situation of reconstruction at palika level. To support DLPIU/building engineers for final inspection process.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- 5 Households were visited at Sailung rural municipality
- Palika level meeting was conducted at palika office of Sailung rural municipality where two engineers attended it along with the local officials.

A close discussion was conducted with representatives of palika, technical staffs of DLPIU/building and ward chiefs at Sailung rural municipalities. The main agenda of the meeting/discussion were as follows:

- Convene and support retrofit beneficiaries for repair and retrofit of houses within deadline.
- Beneficiaries from all wards who have received 3rd tranche to be inspected for certificate of completion. A case load is prepared by DLPIU/building-Dolakha and on the basis of it, the last inspection needs to be completed on time.
- During the last inspection, technical support will be provided through DLPIU/building in coordination with ward office in order to conduct last inspection of “non-compliance and incomplete roofings” will not be carried out. If the beneficiary house construction is not completed at all, the PA number with the reason for the incompleteness need to be submitted at DLPIU/building office.
- After the 1st and 2nd inspection digitalization is completed then only 3rd inspection need to be checked and uploaded at EHRP portal.

Meeting: Meeting minute [Here](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
RM officers have less understandings with NRA engineers and did not respond positively with the team.	Common understanding is required from both sides.	--	NRA engineers and Palika officials	
Palika focused on providing all grant supports to those beneficiaries who have not followed NRA guidelines and built non-compliance houses.	Prolicy level orientation needed for palika officials.	--	NRA engineers and Palika officials	

Beneficiaries claim that they have registered grievance more than two times but, yet no result/solutions have come out.	Reapply on resurvey and reverification process.	--	Beneficiaries, local officials and NRA engineers	
---	---	----	--	--

Photos



Photo: Palika level meeting at Sailung RM



Photo: Ongoing retrofit construction at Sailung RM

Field Visit Reports (Dolakha)

Visit 2

Date	Location	Participants
(20 – 24) May 2019	Tamakoshi and Baiteshwor rural municipality.	- Bhogendra Sha (DLPIU/building-Focal person) - Janak Raj Joshi (MoUD/CLPIU-M&E) - Prabin Gautam (Cluster-10, DC) - Nirodh Pudasaini (DLPIU-DSE) - Sujit K. Gareri (DLPIU-Er.)

Objective(s)

- Housing Typology HRRP Survey collection.
- Discussing the situation of the construction of private housing with local public representatives.
- Palika level coordination meetings and Ward level reconstruction coordination meetings.

Why was the visit carried out in this location?

The field visit was conducted to find out the current situation of reconstruction at palika level. To support DLPIU/building engineers for final inspection process.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- 8 Households were visited at Tamakoshi rural municipality.
- Palika level meetings were conducted at Tamakoshi and Baiteshwor rural municipality respectively on 20th May and 23rd May 2019 where DLPIU engineers and local officials attended the meeting.

A close discussion was conducted with representatives of palika, technical staffs of DLPIU/building and ward chiefs at Tamakoshi RM and Baiteshwor rural municipalities. The main agenda of the meeting/discussion were as follows:

- Beneficiaries from all wards who have received 3rd tranche will be inspected for certificate of completion. A case load is prepared by DLPIU/building-Dolakha and on the basis of it, the last inspection needs to be completed on time.

- f. During the last inspection, technical support will be provided through DLPIU/building in coordination with ward office in order to conduct last inspection of “non-compliance and incomplete roofings” will not be carried out. If the beneficiary house construction is not completed at all, the PA number with the reason for the incompleteness need to be submitted at DLPIU/building office.
- g. After the 1st and 2nd inspection digitalization is completed then only 3rd inspection need to be checked and uploaded at EHRP portal.
- h. NRA technical staffs need to resolve digitized duplication, date and photo issue through login into ehrrpinspection.nra.gov.np
- i. Issues related with Engineers will be resolved by MIS officer at DLPIU/Building office.
- j. Remaining PA digitization must be done and for this purpose DLPIU/Building will provide a list of those missing records.

Meeting: Meeting minute [Here](#)
And [here](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe

Photos



Photo: Palika level meeting at Baiteshwor RM



Photo: Palika level meeting at Tamakoshi RM

Field Visit Reports (Dolakha)

Visit 3

Date	Location	Participants
(28 - 31) May 2019	Bhimeshwor Municipality, ward no.: 1. and Jiri municipality, wards 4 & 5.	• Ganesh Aryal (GMAI-Chief) • Rita Lamsal (GMAI-Officer) • Paban Devkota (GMAI-M&E) • Tika Joshi (GMAI) • Prabin Gautam (HRRP, Cluster-10, DC) • Bhogendra sha (DLPIU/building- District focal Er.)

Objective(s)

- Discuss the situation of the construction of private housing with local representatives and examine the area of unified settlement.
- Palika level coordination meetings and ward level reconstruction coordination meetings

Why was the visit carried out in this location?

An arial damage was reported at temporary shelter of Bhimeshwor municipality, ward no.:1 of Panipokari village. The field visit was conducted to find out the current situation of reconstruction at palika level. To support DLPIU/building engineers for final inspection process.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- 3 Households were visited at Bhimeswor municipality, ward no.: 1 and 7 households were visited at Jiri municipality, ward no.: 4 and 5.
- Palika level meeting was conducted at palika office of Jiri municipality where two engineers and one sub-engineer were met at ward no.: 4 and 5 respectively along with the local officials

A close discussion was conducted with ward chief Bir Bahadur Thami, women member Gauri Thami, Ward Secretary Ganesh Khadka, and **Bhimeswor Municipality ward No. 1** along with the beneficiaries.

1. A discussion was done to organize the reconstruction work at the locality in a proper way through systematically arrangement of reconstruction work, development of unified settlement of Panipokhari village and the construction of water drainage system to protect lower settlement areas within the village. During the meeting, it was found that some of the beneficiaries took third tranche without building their houses.



Photo: Water drain management at settlement area

2. At Panipokhari village, temporary settlement area of vulnerable beneficiaries was observed, and their situation was worsened due to strong wind. Aerial damage was found on temporary shelters. Different options for water management of settlement area was discussed with construction entrepreneurs, local residents and technical staffs. DLPIU/building is looking after the construction work for new settlement of these vulnerable households.



Photo: Temporary shelter of Panipokhari village, Bhimeswor municipality, ward no.: 1

3. Beneficiaries were found to take all tranches without building a complete house. Following beneficiaries were found:

<u>Name</u>	<u>PA number</u>
a) Raju Thami/Manbir Thami	G-22-50-8-0-016
b) Nawaraj Shiwakoti	22-50-9-0-114
c) Ramhari Shiwakoti	G-22-2-2-0112
d) Krishna Bahadur Shiwakoti	22-50-7-0-108

At Jiri municipality, an inhouse discussion was carried out regarding current reconstruction processes, issues and challenges. During the meeting, GMaLI and HRRP gave way forwards on some the issues that were bothering was the absence of NRA engineers at field. The last chance for bringing left behind beneficiaries though resurvey and reverification is at pace and have brought huge number from most of the wards. Issues here is regarding recently marries couples, separated family by law in 2073-2074 B.S. request for registration for resurvey and reverification and municipality cannot say no to those.

- Beneficiaries have taken government grant amount without completion of house.
- Engineers selectively (biasedly) process beneficiary files for tranche release which another big issue while bank also delays payment.

During the ward level meeting at Jiri municipality, ward no.: 4 and 5, NRA engineers put queries on inspection forms, household last survey for distributing completion certificate. A local beneficiary rushing for enquiry on receiving her 2nd and 3rd tranche said that many of the neighbors have taken all tranches without completion of house construction, Thus, she was wondering if that is the same case for her to quickly receive remaining tranches. It seems that beneficiaries were misguided on how government tranches. Ward offices haven't enough database of reconstruction.

Meeting: Minute not taken during meetings.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiary took all tranches of government grant support before constructing their house.	Either he/she needs to build house within deadline or return money.	Beneficiary.	Beneficiary, engineers and ward office.	
Arial damage in temporary shelter.	Support these vulnerable HHs for safe shelter.			
Delay in construction of new settlement area at Panipokhari village, Bhimeshwar municipality ward no.: 1,			DLPIU/building	

Photos



Photo: Ward level meeting at Bimeswar UM, ward no.: 1



Photo: Jiri municipality meeting with the Mayor Tanka Jirel.



Photo: Ward level meeting at Jiri – 5



Photo: Ward level meeting at Jiri - 4

Field Visit Reports (Ramechhap)

Visit 1

Visit 1		
Date	Location	Participants
12-May-2019	Khadadevi RM	Pranjal Bhandari (HRRP), Janak Raj Joshi (M&E, CLPIU Building), Keshav Raj Pandey (DSE, DLPIU Building), Nabin Sharma (MIS Officer, DLPIU Building), Jagadish Chand (Focal Person, DLPIU Building)
13-May-2019	Doramba RM	Pranjal Bhandari (HRRP), Janak Raj Joshi (M&E, CLPIU Building), Keshav Raj Pandey (DSE, DLPIU Building), Nabin Sharma (MIS Officer, DLPIU Building), Jagadish Chand (Focal Person, DLPIU Building)
14 to 15-May-2019	Sunapati RM	Pranjal Bhandari (HRRP), Janak Raj Joshi (M&E, CLPIU Building), Keshav Raj Pandey (DSE, DLPIU Building), Nabin Sharma (MIS Officer, DLPIU Building), Jagadish Chand (Focal Person, DLPIU Building)
Objective(s)	- To understand the status of reconstruction, to solve the non-compliance issues at the field level, to interact with the field engineers - To orient the ward officials regarding the resurvey and reverification	
Why was the visit carried out in this location?		
The understanding of the ward chiefs regarding the resurvey and reverification process was poor due to which the orientation was felt necessary. Also, there were several non-compliant issues reported in the location.		
If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
Summary		

Field Visit:

- No. of HHs visited:20
- No. of meetings with engineers:3
- No. of meetings with local officials:3

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

[Meeting Minute Palika Level Coordination Meeting, Khadadevi RM](#)

[Meeting Minute Palika Level Coordination Meeting, Doramba RM](#)

[Meeting Minutes Palika Level Coordination Meeting Sunapati RM](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The monitoring of the presence of the engineers in the wards are limited	Maintain attendance registers at each ward	--	Ward chiefs	Continuous
The final inspection is steady	Set the target and monitor	--	Ward chiefs and field engineers	Continuous

Photos



Palika Level Cordination Meeting ongoing at Khadadevi RM



Field engineers in interaction with an elderly beneficiary at Doramba RM



Palika Level Coordination Meeting ongoing at Doramba RM



Palika level coordination Meeting at Sunapati RM

Field Visit Reports (Ramechhap)

Visit 2

Date	Location	Participants
3-4 June, 2019	Gokulganga RM	Pranjal Bhandari (HRRP), Janak Raj Joshi (M&E, CLPIU Building), Keshav Raj Pandey (DSE, DLPIU Building), Nabin Sharma (MIS Officer, DLPIU Building), Jeevesh Karn (Scott Wilson Nepal)
5-7 June, 2019	Umakunda RM	Pranjal Bhandari (HRRP), Janak Raj Joshi (M&E, CLPIU Building), Keshav Raj Pandey (DSE, DLPIU Building), Nabin Sharma (MIS Officer, DLPIU Building), Jeevesh Karn (Scott Wilson Nepal)

Objective(s)	- To monitor the presence of the field engineers - To monitor the non-compliant houses
---------------------	---

Why was the visit carried out in this location?

- The Palikas are rural-most of the district where there were complaints of the field engineers not being present.
- There has been large number of houses built immediately after the earthquake and prior to the deployment of the engineers. To understand the issue of such households and suggest correction measures is possible.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited: 20
- No. of meetings with engineers: 4
- No. of meetings with local officials: 2

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

[Meeting Highlights Ward Level Meeting, Gokulganga-4](#)

[Meeting Highlights Palika Level Meeting Minutes, Umakunda RM](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Huge number of non-compliant houses were constructed immediately after earthquake who haven't been able to receive the tranches	The data regarding such houses are being collected from the ward levels	--	Ward Chiefs, Field Engineers	20-Jun-2019
The engineers deployed for resurvey and reverification did not reach 4 wards of Umakunda RM citing the deadline for resurvey has expired	The NRA should be informed and the deadline should be extended	--	NRA	ASAP

Photos



Ward Level Coordination Meeting at Gokulganga-4



Ward Level Coordination Meeting at Umakunda RM

Field Visit Reports (Sindhuli)

Visit 1

Date	Location	Participants
15 th May 2019	Sunkoshi Gaupalika	• Prabhakar Lal Karn (Project Chief DLPIU Building) • Pramod Kumar Sah (Focal Person DLPIU Building) • Kiran Mahat (M&E Consultant) • Dinesh Sanjel (DSE) • Tulasi Ram Lamichhane (DTC HRRP)
Objective(s)	• To observe the reconstruction status of the Rural Municipality • To interact with the local authorities regarding the reconstruction • To discuss regarding the pending caseload • To appoint the focal person of the Rural Municipality • To discuss regarding the resurvey and reverification • To collect housing typology	
Why was the visit carried out in this location?		
• To appoint focal person in the Gaupalika • To settle the issues regarding the reconstruction • To settle the issue of reconstruction in the Commission for the Investigation of Abuse of Authority (CIAA).		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
N/A		
Summary		
Field Visit:		
• No. of HHs visited: 6 • No. of meetings with engineers: 1 • No. of meetings with local officials: 1		
The field visit to Sunkoshi Gaupalika was organized in 15th May 2019 to identify the status of reconstruction, issues and challenges of reconstruction, interaction with the ward chairpersons, Palika chief and Pos regarding private housing reconstruction. The meeting was conducted in the meeting hall of the Rural Municipality. The meeting was chaired by the Chairperson of the Rural Municipality Ms Dipa Bohora. The program was facilitated by focal person of DLPIU Building Mr. Pramod Kumar Sah. The program started with the introduction of the participants. After then the issues were discussed on the ward level. The ward chairperson and the ward representatives talked about the status of their respective wards.		
Ward No. 1:		
• The genuine beneficiaries are still missing in the beneficiaries list. • Very few grievances have been addressed • The previous grievances are still not still solved.		
Ward No. 2:		
• 2 Households were constructed before the arrival of the technical persons • Still the process for conversion to beneficiaries from retrofitting has not been solved despite of sending the letter for central NRA long time past.		
Ward No. 3:		
• 25 Households were constructed before arrival of the technical persons • Houses expanded in height after receiving the third tranche • Confusion in the right of way allocated by Rural Municipality and the Nepal Government. • With same typologies one is provided with tranche and next is not. • Updates regarding the reconstruction must be provided on timely basis.		

Ward No. 4:

- 2 houses constructed before arrival of technical persons
- 2 houses with excess attic height
- Vulnerable houses have been constructed by Mercy Corps
- 2 house owners have died before receiving the 3rd tranche whose nominees are in beneficiaries list.
- 2 house owners have migrated from neighboring districts but the gaupalikas are attached with sunkoshi gaupalika. They are the beneficairees of the previous gaupalika and want to reconstruct in sunkoshi gaupalika

Ward No. 5:

- 38 real beneficiaries missing in the beneficiaries list
- 3 retrofitting beneficiaries have applied for beneficiary's conversion

Ward No. 6:

- NRCS have provided STA and financial support in the reconstruction
- 9 households have not received the tranche due to right of way
- 4 house owners have applied for appellate against the decision of having another house
- No proper correction provided to the 5 households
- Tranche of Bhakta Bahadur Karki has been halted due to the excess opening

Ward No. 7:

- No detail information regarding the new grievance has been provided via radio

Discussion of resurvey and Reverification

- The house owners who have been involved in previous grievances are not eligible for this resurvey and reverification
- This will be the final round of resurvey and reverification
- The number of engineers involved in the resurvey and reverification is limited by resources and persons which is difficult to conduct. So, the resource and number of engineers must be added.

Case Load

- The project Chief of DLPIU directed the engineers no to hold the case load and process them as soon as possible. The DLPIU Building will provide necessary action for the case load support if required.

Focal Person Assignment

- Pujan Raj Shrestha has been assigned as the focal person for the Sunkoshi Gaupalika.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held) [Click Here for Report](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
As the number of grievances is higher, the number of engineers assigned for the resurvey and reverification process is too low so that the resurvey and reverification will not be completed in allocated time.	Request for addition of engineers	DLPIU Building Chief	NRA	ASAP
The conflict between Central Government and local government regarding the right of way of BP highway is prevailed. The National government has allocated 25 meters right of way from center while the local government has decided it to be 15 meters from center and forwarded those houses for construction.	N/A	N/A	Central Govt	

Photos



Meeting being conducted in the premises of Sunkoshi Rural Municipality



Project Chief of DLPIU Building addressing the questionnaires raised by the ward chairperson.

Visit 2

Date	Location	Participants
28-30 May 2019	Ghyanglekh Gaupalika ward no 5	- Kiran Mahat (M&E Consultant) - Dinesh Sanjel (DSE) - Tulasi Ram Lamichhane(DTC HRRP)
Objective(s)	- To observe the reconstruction status of the Rural Municipality - To interact with the local authorities regarding the reconstruction - To discuss regarding the pending caseload - To discuss regarding the resurvey and reverification - To collect housing typology	

Why was the visit carried out in this location?

- To sort out the issues between the engineer and ward chairperson.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

- No. of HHs visited: 11
- No. of meetings with engineers: 2
- No. of meetings with local officials: 1

The visit to Ghyanglekh gaupalika ward no.5 Shanteswari was made on 28-30 May 2019 to observe the reconstruction status and interact with the ward representatives. The meeting was conducted in the ward office. In the meeting the reconstruction status of the ward was discussed. Besides this the status of the resurvey and reverification was discussed which was not started till the date of meeting because of the limited manpower which were involved in the same in other wards. Also the process for the beneficiaries conversion was oriented to the newly joined technical persons. The manual of hollow concrete block was shared with the technical persons for the correction of the constructed houses using the same technology. Also the ward chairperson was requested to revise the vulnerable group list and send to the palika office for verification. Besides this the technical persons were directed to continue the CS Entry.

Total Beneficiaries	1 st Tranche	2 nd Tranche	3 rd Tranche
405+38(RS/RV)	387	373	246


Meeting: put a link to meeting minute (if Municipal/Ward level meetings held) [Click Here for Minutes](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
No tabs were available for the technical persons	Arrangement of new tab	Kiran Mahat M&E Consultant	DLPIU Building	ASAP

Photos



Ward level Meeting at Ghyanglekh Gaupalika ward no 5



Minutes of Ward Level Coordination meeting

Housing Typology Report



The house of Dirgha Raj Puri, resident of Sunkoshi Rural Municipality-3, Jhangajhuli has constructed his house. The house is constructed using brick in cement mortar. The RC bands have been provided to the house. The RC slab has been provided to the house. There are two rooms in the house. The house has been constructed under the technical support of SERVE project of Mercy Corps. The house owner has received second tranche of reconstruction grant. The house owner is one of the beneficiaries of vulnerable group.



Name: - Tej Bahadur Jirel
Location: - Jiri Municipality, ward no.: 5, Dolakha.
It is single storey special moment resisting structure. The construction of house was supported by British Gorkha Welfare with construction cost of 6 Lakhs. The beneficiary has received all tranche of government grants.



Name: - Harka Bahadur Jirel
Location: - Jiri Municipality, ward no.: 4, Dolakha.
It is two storey load bearing structure with brick in cement mortar. The beneficiary has received 2nd tranche of government grants.



Name: - Man Bahadur Thami
Location: - Bhimeswor Municipality, ward no.: 1, Dolakha.
It is a one storey block in cement mortar load bearing structure. Its floor area is less than 1000 sqft. The beneficiary has received 3rd tranche of government grants.

Case Study



Nabin Kumar Yadav (Engineer, Umakunda
RM, Gumdel)

Place Photo here

Nabin hails from Bariyarpatti, Siraha Municipality-5 and has been working in Gumdel since the past 11 months. It was a challenging initial few months shares Nabin. The culture was different, the geography was different, and the language was different. He was selected by the NRA and was deployed to Umakunda RM a few months after completion of his Engineering. Furthermore, he was deployed alone in the ward and without any training by the DLPIU. He continued to work despite any training. He would fill the forms but a lot of them would be returned due to his mistakes he shares.

Occasionally, he would come across aggressive beneficiaries who would use threatening languages to make him do their work which made it very difficult for him to work particularly when the ward chief was not around. Matters became easier when he began living in the house of a local hotelier and political activist named Jhappar Karki. Jhappar helped him adapt to the local environment and helped deal with difficult beneficiaries.

Gumdel is the most rural area of the district and has the most difficult topography characterized by very high hills and thin, scattered settlement. Due to the remoteness of the area, the engineers' turnover was high. For a man who was raised in the plains of Terai and with no habit of walking for long, it was a very difficult scenario. Things became easier for him when a sub engineer was deployed three months after he began working in Gumdel. The two would divide the working areas amongst themselves and walked for inspection. During the initial phases, the presence of the engineers was limited due to which there were a lot of non-compliant houses but in coordination with the ward and frequent field visits by the engineers, corrections have been made to most of them but for the few remaining, it has been a difficult prospect to convince them to apply corrections due to the high cost of materials. Also, there are a lot of SMM houses which are more than one story. These houses were built immediately after the earthquake and they lack the horizontal bands which make applying corrections to them impossible. Despite the collection of data about such houses, their issues have not been resolved yet. During the inspection visits, it is the issue that keeps popping up. He hopes, the issue would be addressed by the NRA soon. Nabin's experience in the reconstruction of the ward has been very positive. He shares that he was a shy, introvert person when he joined but a year in the reconstruction has changed him a lot. He is now more outgoing and confident in dealing with the people. He is happy to see the people are now aware about the safer reconstruction practices and are being applied even at the remote places even though the costs are higher.
