


FACTS AND FIGURES

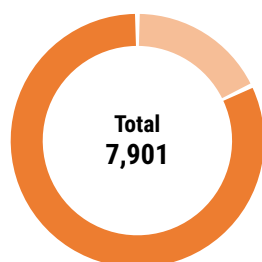

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	92.11%	82.76%
Brick and Cement Mortar Masonry	2.19%	2.57%
Reinforced Cement Concrete (RCC) Frame	1.76%	3.23%
Adobe Structures	1.13%	1.79%
Others	2.81%	9.66%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	7,065
PA Agreement	6,087
I st Tranche received	6,087
II nd Tranche received	5,474
III rd Tranche received	4,681

Houses

Under Construction: 793

Completed: 4,681

Retrofitting Status

Total Eligible HHs	836
PA Agreement	28
I st Tranche received	31
II nd Tranche received	0

Grievances

Registered: 2,283

Addressed: 212

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: CA (Shelter), CA (Hygiene), COSAN (Education), CRS (Agriculture), CRS (Livelihood), CRS (Shelter), GON-PAF (Shelter), IOM (Shelter), JICA (Shelter), LIONS (Education), NRA (Shelter), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), OXFAM-GB (Shelter), ROTARY (Shelter), UNDP (Shelter), UNWOMEN (Shelter)

OTHER SECTORS



Schools

Damaged: 79
Under Construction: 51
Construction Completed: 51



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	126,056	-	-
Aggregate	m ³	118,434	-	-
Sand	m ³	13,367	-	-
Timber	cu. ft.	15,084	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	400,561	-	-
Rebars	kgs.	1,391,367	-	-
Tin	bundle	16,392	-	-
Bricks	pcs.	3,018,414	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

KEY CONTACTS

Municipal Office

Ramesh Thapa Magar
Chairman
9856040375

Municipal Office

Sanu Kaji Basnet
Focal Person
9846075365

Municipal Office

Indira Tiwari
Deputy Chairman
9846433515

GMA/INRA

Ram Sharan Acharya
NRA Chief-District
9856042637

Municipal Office

Jivan Ale Magar
Chief Administration Officer
9856010533

DLPIU-Building

Sunita Shrestha
DUDBC.DLPIU Chief
9841632087

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING

Trainings (# out of total required)


7 days Training



610

Reached

50 days Vocational Training




320

378

Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

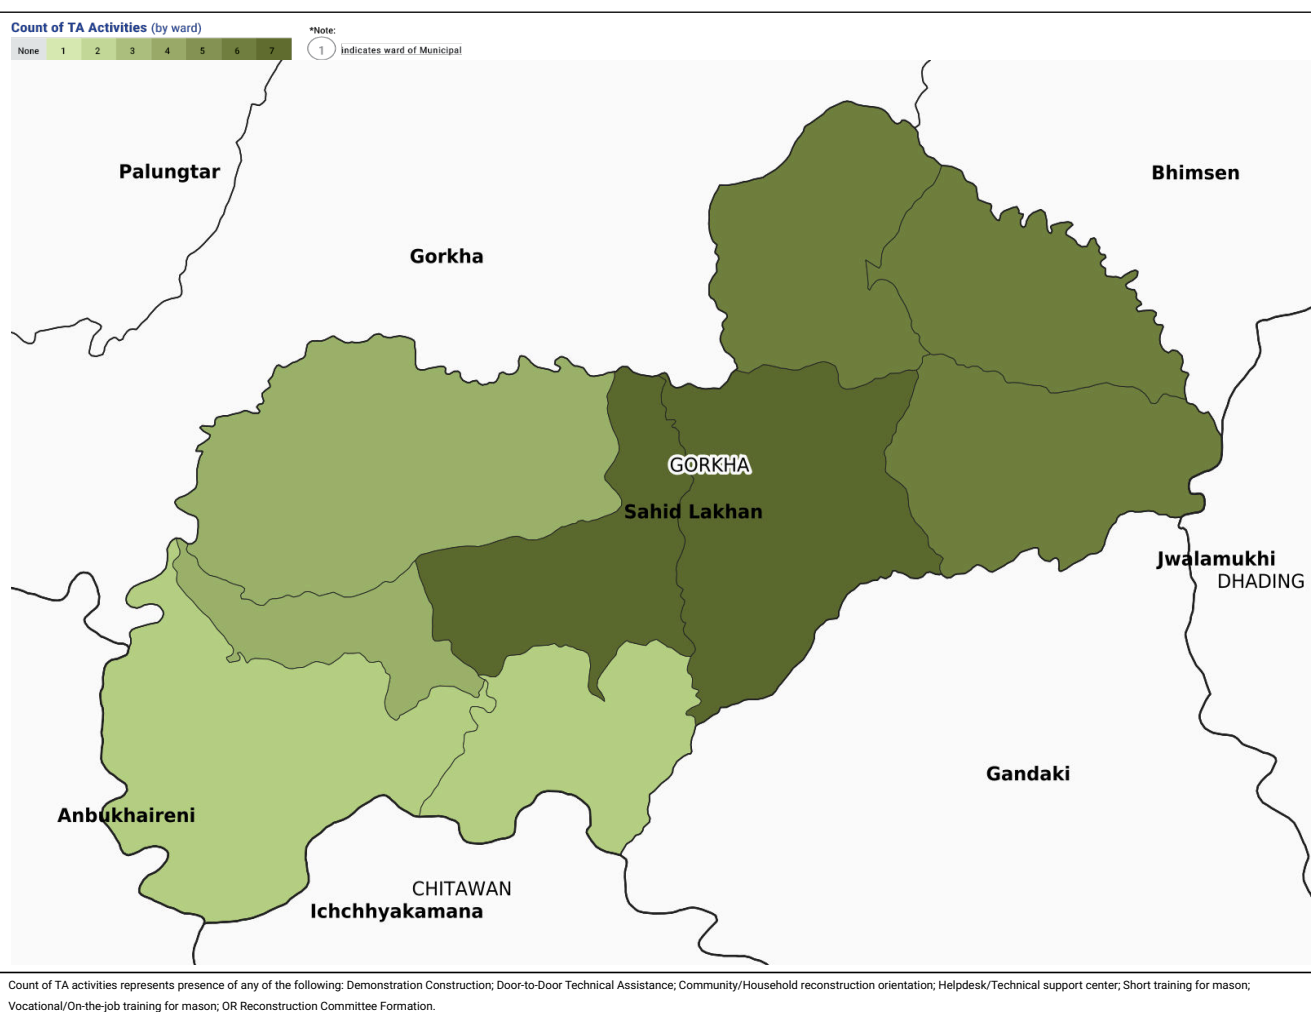

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Chandra Gurung (District Coordinator) 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer)
9841478742 9842062006
