

District Report

Rasuwa

4 - 17 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
District meal data for the month of December was updated to DMT. Summary of activities achieved in Dec,2018: Meetings : District General coordination meeting - 1 Ward level coordination meeting - 3 (Gosaikunda-5, Uttargaya - 2, 3) Field visit : At Gosaikunda ward-5 At Uttargaya ward -2 At Uttargaya ward -3	5-Jan,2019	1	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Initial plan prepare by district to for collection of rooms information of all over district is prepared and shared at district management team.	7-Jan,2019	2	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
District team conducted a joint monitoring visit at Kalika rural municipality ward number 5 (Jibjibea) on 4- Jan,2019. HRRP district team together with building dliu focal person Mr. Saroj Kumar Yadav and district support engineer Mr. Projwal KC were the main visitors from district level and ward chairperson Mr. Ram Hari Devokata , ward technical person Mr.Govenda Dhala from ward number 5 has conducted the visit. Firstly, we had conducted a ward level meeting at ward office where the reconstruction process and its challenges of wards were discussed also some non compliances issues were discussed. Secondly, All the team member both district level and ward level stockholders jointly visited a newly constructed houses. The details of field visit is	4-jan,2019	6	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	

Summary of events during this period

mentation in below field visit section.					
21 st earthquake safety day program was conducted on 15-Jan,2019. As like as in others district DAO office Rasuwa has organized the program where people from different partners organization, government stockholders , Nepal Police, Armed police force , Nepal Army and journalist were participated the program. The program was started with short relay from dhunche welcome gate to district coordination committee office and then after a formal program was arranged where Asst. CDO took chaired the official program and GMaLI and HRRP made short speech by remaining earthquakes which was happened on different time and the negative affect which Nepali by the destruction.	15-Jan,2018			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
For the preparation of palika profile of all five local level of district the information has updated on system by closely coordination with national information management officer Mr. Yubraj Bhandari. As per the recommendation of Mr. Bhandari all the necessary information was updated. HRRP Nepal is working for the preparation of local level reconstruction profile where tranche update of each palika, materials availability and its cost , number of technical staff required vs presence , Number of trained mason (both 7 days and 50 days) required vs presence, contact details of all relative stockholders and more other information like school and health sector reconstruction status , displaced status is place on single page. HRRP is aiming to provide that profile at local level website so every one would be able to access the information from wards website and the data in profile is going to be update on 25 th of each months.	17-jan,2019	1	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	

Summary of events during this period

Housing typology upload: The housing typology was uploaded in the google drive and also set to DMT via mail.	Jan -6, 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Teechnical case study on non-compliance house which was collected during the field visit in Kalika RM ward no-5 was updated to DMT.	Jan-7, 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
NRA is going to organized a handover of reconstruction process to local level.	21-Jan, 2019 : District coordination committee office Dhunge, Rasuwa	NRA : GMaLI : Building (DLPIU)	Im.rasuwa@hrrpnepal.org

News & Updates

21st earthquake safety day program was conducted on 15-Jan, 2019. The Program was organized in the of memory of great Nepal – Bihar earthquake, the District Administrator Office Rasuwa has organized the program where people from different partners organization, government stockholders, Nepal Police, Armed police force, Nepal Army and journalist participated which was held in 17-Jan, 2018. The program was started with short relay from dhunche welcome gate to district coordination committee office and then after a formal program was arranged. Asst. CDO Mr. Dhabersi Devkota took chairmanship of the official program.

The Grand Management and local infrastructure (GMAI) division chief Mr. Krishna Kant Upadheya made short speech by remembering the earthquakes which was simultaneously happened on Nepal in different times interval and the negative affect which was faced by all Nepalis citizens. He also recalled the devastating Nepal earthquake 2015 in result 8,857 people dead and 21,952 were injured where 3.5 people became homeless. He updated the latest reconstruction status of district and also presented the strongest and weakest parts of reconstruction and recover, as the reconstruction of public housing is speed up where the settlement for displaced peoples becoming more challenges in the district. He added because of less availability of safe land within district, another side the desires of displaced people who wants to stay at market or urban areas creating more problems and the absence of technical person specially a geologist at district level is another challenges. At the end he closed his speech by thanking all the governments and others helping hands those who are continuously supporting the victims.

After then HRRP district coordinator Mr. Rijan Gajurel shared the importance of the event , as this types of program always recalls us the disaster which we had faced more then 3 times from last 70 years and also courage us to work for the better reconstruction of our's homes and property. He also describe the destruction which country, district and the people faced by the quake 2015 and how Nepal government and public society motivated for the better reconstruction to make our community safe and sound in terms of earthquake. He also described how Japan had worked for the prevention for earthquake by saying the words prevention is more better then that of care and the beautiful part is our country is moving on the same track with the support form different international and national expertise.


The closing speech of the program was given by Asst. CDO Mr. Dhabersi Devkota , he thanked all the participant for their active participation in order to make the program more successful. He said Nepal lies in high tectonic active zone and fault plane due to which it is very prone to quakes. He focused on preparedness rather then post assessment to minimize the catastrophic effect. However, GoN has formed NRA to adopt the new technology in housing construction so if there will any quake in future then there will be a minimum affect. He also requested local levels and others relative stockholders to make our country at least this district as a earthquake resilient district mainly on public housing sectors.




Tranche Status

Rural /Municipality	Gosaikunda RM	Kalika RM	Naukunda RM	Aamo Chhindigmo RM	Uttargaya RM
Total HHs Surveyed	1979	2569	3349	1964	2631
Total HHs Eligible	1979	2569	3349	1964	2631
Total HHs Enrolled	1836	2456	3291	1802	2274
First Tranche	1836	2456	3291	1802	2274
Second Tranche	1649	2308	3038	1560	1958
Third Tranche	1248	2121	2758	1273	1725
Total HH Constructed	1248	2121	2758	1273	1725
Grievance Registered					
Grievance Addressed	257	277	246	237	239
RF HH Eligible	84	11	59	32	25
RF HH Enrolled	60	10	2	10	11
RF 1 st Tranche	60	10	2	10	11
RF 2 nd Tranche	0	0	0	0	0
Non-Compliance Registered	89	48	54	101	124
Non-Compliance Addressed	69	36	40	70	86

Graph of Tranche Status:

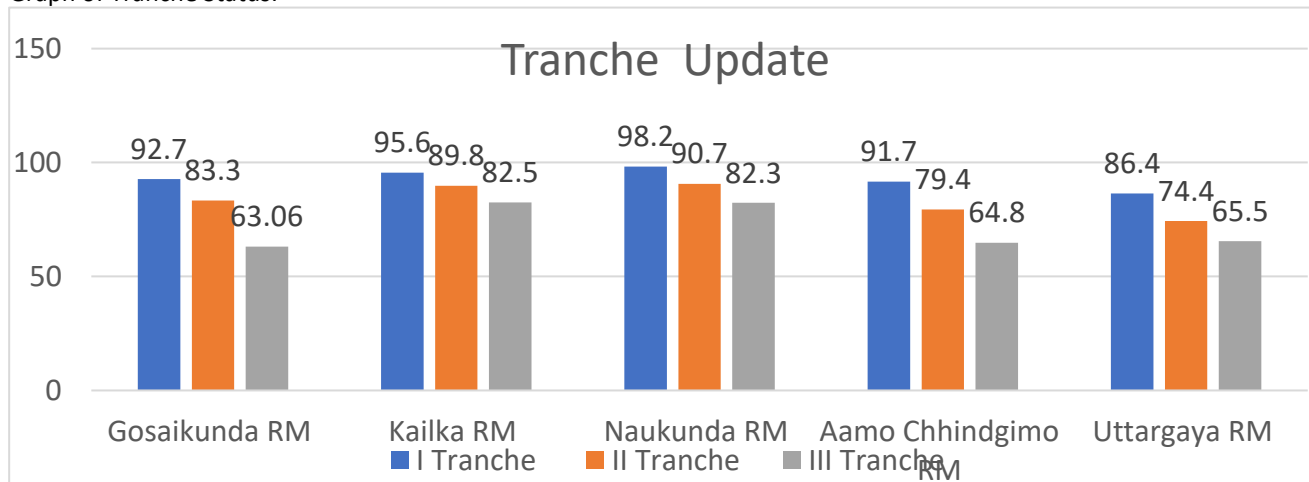

Graph for Grievance Status:

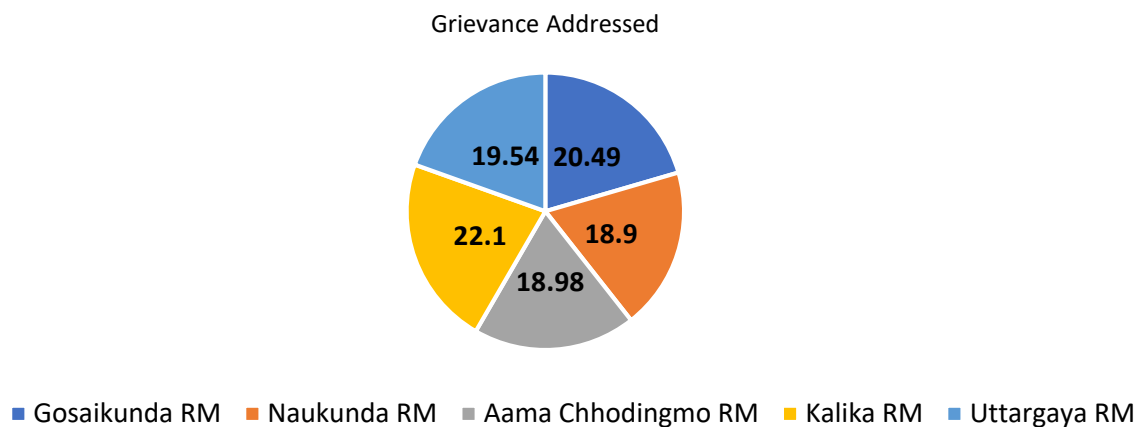

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders	
Dec 11,2018	Kalika RM ,Ward no-5,jibjibe	- Biren Shah, DTC, HRRP - Rijan Gajurel, DC, HRRP - Prajwal K.C., DSE, NRA - Saroj Kumar Yadav,DLPIU Building	
Objective(s)	- To interact with local representatives, engineers along with beneficiaries to know the reconstruction progress and challenges. - To monitor reconstruction status of the ward - To collect housing typologies. - To collect information on Status of timber structure and non-compliant issues		
Summary	Number of beneficiaries after survey = 445 Beneficiary after Grievance = 40 Total Beneficiary=485 First Tranche =427 Second Tranche=412 Third Tranche=380 No. of houses constructed=380 Retrofitting Beneficiaries=5 First Tranche=0 Second Tranche=0 The field visit was targeted in Kalika RM, ward-5, jibjibe to collect the reconstruction status and challenging issues of the ward. Technical Discussion: The technical discussion was themed with the technical issues and challenges residing in the ward. One engineer and one sub-engineers are deployed in the ward. During the field visit various technical challenges and problems regarding reconstruction were seen. The major issues seen in the ward are described below: <u>Problems in BMC / SMM /SMC structures</u> - Attic of CGI Sheet more than 5 feet. - The houses missing roof band. - Two storey structure in 9" wall. - Two beneficiary's homes with single roofing. - Addition of storey after receiving the third tranche. <u>Problems in RCC Structures</u> - Rcc structure with 9"X12" Size column, one-bay and two storey. - Flat slab structure i.e. a reinforced slab, built monolithically with the supporting columns and is reinforced in two or more directions, without any provision of beam. The major problem in this ward is modification of structure after receiving the third tranche.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
No involvement of the beneficiaries in construction of houses after receiving the first tranche.	Follow-up by the ward and dissemination of information of returning the tranche for un-interested beneficiaries getting involved in construction.	DLPIU GMAli, Palika and ward	ASAP

Modification of structure after receiving the third tranche.	Structure analysis of the building /significant correction measures.	DSE/DLPIU Building	ASAP
Monolithically constructed CGI sheet Or casted slab roofing for two or more houses of beneficiaries after receiving the third tranche making the structure as one can be the major problem during the distribution of Completion Certificate.	Timely dissemination of information about the procedures of getting completion certificate along with the awareness program and technical support.	DLPIU Building, DLPIU GMaLI, Palika and ward	ASAP

Photos



Caption: **Ward NO.5, Kalika RM, Rasuwa**
Name of Beneficiary: Netra Prasad Poudel
Tranche Update: Third Tranche Received

The home owner has already received the third tranche of the GoN housing grant and then built the first floor after receiving the third tranche. In order to receive the third tranche, the house had to be analyzed by the District Support Engineer (DSE) as the columns in the ground floor are 9"x12" which does not meet the required standards. Altogether there are 6 columns in the house and the walls are 9". The DSE recommended use of light CGI roofing, and construction of an interior partition wall, as the room sizes also did not meet the required standards. After completion of the structure up to the roof band the house was approved for the third tranche. After receiving the third tranche the owner constructed the two room, 4" masonry wall system structure as the first floor, and now the whole structure is more vulnerable. The distribution of construction completion certificates has begun in this area, but the home owner will not be able to receive the certificate without making significant corrections to the structure.

Caption: **Ward NO.5, Kalika RM, Rasuwa**
Name of Beneficiary: Bhawanath Poudel
Tranche Update: Second Received

Housing Typology: Load bearing Brick Masonary in cement mortar house with 9" wall consisting of 14" Copla and rigid slab roofing resting in beam.


Housing Typology Report



Caption Ward NO.5, Kalika RM, Rasuwa
Name of Beneficiary: Ram Prasad Poudel
Tranche: Received Third tranche
Housing Typology: RCC four rooms structure with passage in between. The structure consists of all the bands at different levels. There are 15 columns (12"x 12") in the structure, each column consists of 8 rebars of which 4 nos. @12mm and 4 nos. @16mm. The construction of the house is completed.



Caption: Ward NO.5, Kalika RM, Rasuwa
Name of Beneficiary: Arjun Poudel
Tranche: First Received
Housing Typology: Hybrid structure with lower as load bearing Stone Masonary in mud mortar and upper storey CGI sheet structure. The lower structure is two room house and upper storey is one room.

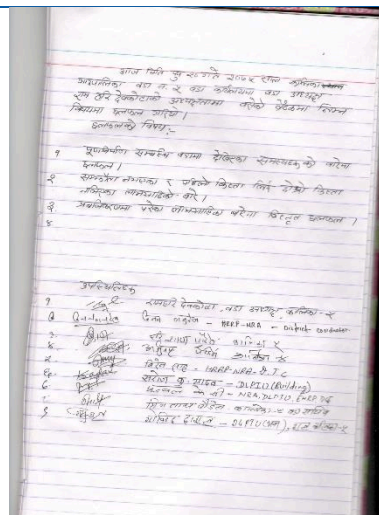

Caption:
Meeting Minute of ward level meeting at kalika RM ward number 5.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will the construction completion certificate be given?	Beneficiaries	The distribution of completion certificate is started in other wards like Kalika-5 and will be soon
What is the deadline of the third tranche?	Beneficiaries	Biren Shah
Can we get the third tranche if our houses consists of uni-directional roofing	Beneficiaries	Biren Shah
