

District Report

Okhaldhunga

4 – 17 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint Monitoring with CLPIU Monitoring, Expert Okhaldhunga DSE and HRRP Okhaldhunga has been successfully organised at Siddhicharan Municipality ward-1 & 2 to inspect the reconstruction progress. The main mission of this visit was to conduct ward level meeting and to check the noncompliance as well as compliance houses of this ward During this field we found that some of the houses are corrected only to show the correction actually the corrected house did not have any bars on corrected horizontal bands .DSE and DLPIU engineers threats them to correct again as per the standards and norms without it the tranche will paused at bank.	9 th January 2019	11	3	Prakash Basnet prakash@hrrpnepal.cog	See the field report below
Ward level coordination meeting has also been conducted at Chisankhugadi Rural Municipality ward-5 where 99% of beneficiaries has received their third tranches and are on the process of getting completion certificate during the mitting Ward chief express his happiness for those technician who has worked hard in the ward level to get his result he also said that now onwards all the houses will be build safer following the rules	10 th January ,2019	8	1	Prakash Basnet prakash@hrrpnepal.cog	no any formal minute had raised.

Summary of events during this period

of earthquake safety which they have learned from the Reconstruction.


Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
General District Coordination Meeting	23 th February 2019	HRRP Okhaldhunga	Prakash Basnet prakash@hrrpnepal.org
Joint monitoring Khijidemba Rural Municipality and Palika Level Meeting	5 th to 13 th of February 2019	HRRP Okhaldhunga	Sagar Chandra Adhikari techrd.okh@hrrpnepal.org
	To include details of upcoming events and meetings in the next bulletin, please share details with prakash@hrrpnepal.org by COB Wednesday of each week.		


Tranche Status

Rural /Municipality	Champha devi RM	Chishankhu Gadhi RM	Khijidemba RM	Likhu RM	Maney bhyanjang RM	Molung RM	Soddhicharam UM	Sunkoshi RM
Total HHs Surveyed								
Total HHs Eligible	3341	1063	2914	2914	3258	1663	2660	3268
Total HHs Enrolled	3050	961	2780	3090	1518	2737	2401	2997
First Tranche	3049	961	2778	3087	1517	2726	2394	2994
Second Tranche	2908	888	2643	2916	1192	1971	1859	2876
Third Tranche	2450	733	2170	2472	778	1980	1249	2283
Total HH Constructed								
Grievance Registered								
Grievance Addressed								
RF HH Eligible	513	228	218	200	441	365	573	330
RF HH Enrolled	443	151	196	114	373	219	317	46
RF 1 st Tranche	111	140	196	67	373	98	299	44
RF 2 nd Tranche	0	0	0	0	0	0	0	0
Non-Compliance Registered								
Non-Compliance Addressed								

Graph of Tranche Status:

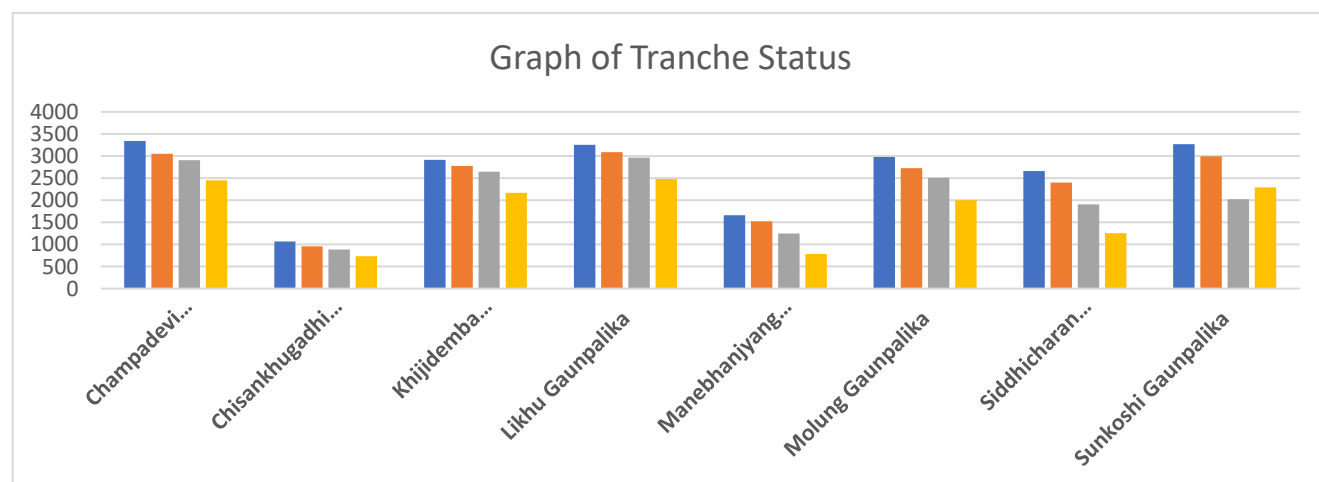

Graph for Retrofitting Status

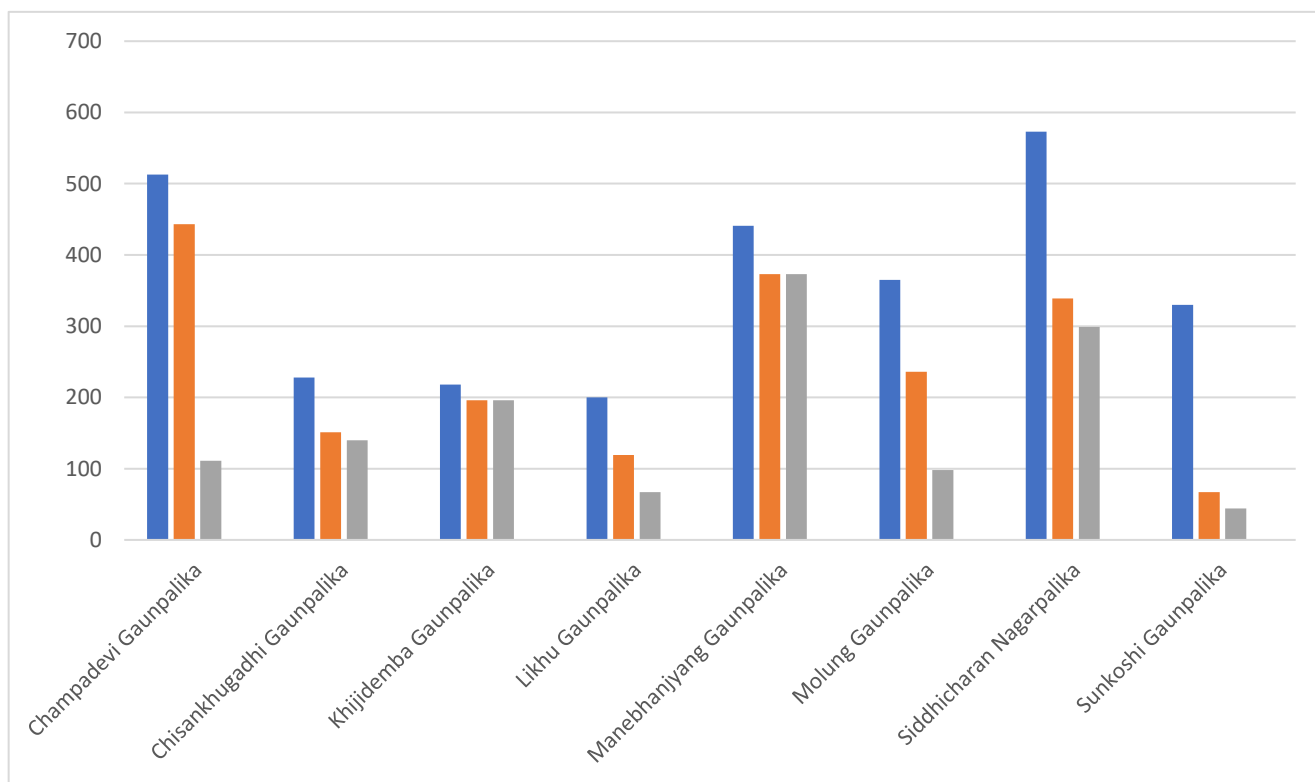

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
9 th and 10 th of January 2019	Ward no 1 and 2 of Siddhicharan Municipality and ward no 5 of Chisankhugadi Rural Municipality	NRA-CLPIU M&E (Kiran Kumar Mahat), DSE Prakash Paudel, DLPIU-Building Engineer Sanjib Yadav , Prakash Basnet DC HRRP Uttam Parajuli IMO HRRP

Objective(s)

Reconstruction Update/ Housing Reconstruction Challenges

Interaction between government agencies, implementing partners and local people

Collection of Typologies of Houses

Summary

Joint visit was conducted by HRRP Okhaldhunga along with NRA-CLPIU M&E (Kiran Kumar Mahat), DSE Prakash Paudel, DLPIU-Building Field Engineers and HRRP Team Okhaldhunga. Along with Ward level meeting at ward no 1 and 2 of Siddhicharan Municipality and ward no 5 of Chisankhugadi Rural Municipality

The field visit gave an opportunity to NRA-CLPIU/DLPIU and HRRP to observe, supervise and monitor ongoing construction of Houses (Compliance & Non-Compliance houses) at wards 1 and 2 of Siddhicharan Municipality After visiting those houses DSE had advised DLPIU Engineers for the inspection of those completed houses for releasing 3rd tranche.

Almost houses of Siddhicharan Municipality ward no 1 and 2 are stone in mud mortar with RCC and wooden bands.

Whereas at ward no 5 of Chisankhugadi Rural Municipality almost reconstruction has been completed 99% of the houses have received their third tranches and waiting for the certificates of completion.

Some of the Key points that made compliant houses in the ward 1 and 2 of Siddhicharan Municipality and ward no 5 of Chisankhugadi Rural Municipality are

1. Availability of trained mason in every ward no 5 of chisankhugadi Rural Municipality
2. Awareness of beneficiaries about the earthquake resilient housing construction.
3. Use of local materials for the reconstruction (timber, stone, mud, aggregate etc.)
4. Good technical assistance of DLPIU Engineers.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Some of the houses in the ward no 1 and 2 of Siddhicharan Municipality which were built before the arrival of guidelines and engineers are non-compliant and the beneficiary are not ready to do correction.	Bring those beneficiary in the mainstream of the correction	GMaLI	ASAP

Photos



**Figure 1 Meeting with ward leader at Siddhicharan Municipality
ward no 1 Taluwa**



**Figure 2 Discussion with ward leader of Serna Ward no 5, of
Chisankhugadi
Rural Municipality**

Housing Typology Report



Figure 3 House of Kedar Prashad Ojha Siddhicharan Municipality Ward no 1 Tinpile Taluwa

Beneficiary has received first tranches only and has not get any house has four room this house was constructed immediately after the earthquake asper the beneficiary he has spent about 20 lakhs for the house and has taken loan in 5% interest. The beneficiary is not interested in the correction since he doesn't believe in correction. **Picture Credit:** Prakash Basnet DC HRRP



Figure 4 House of Bamila Pariyar Ward no 5 of Chisankhugadi Rural Municipality Serna

House is compliance with stone in mud mortar with wooden bands bands provided properly and has received first and second tranche of the government and third tranche has been recommended by the engineer.

Picture Credit: Prakash Basnet DC HRRP



Figure 5 House of Debika Shrestha Siddhicharan Municipality ward no 1

The house was noncompliance exceeding attic height and bands were provided in 3 feet house was made with stone in mud mortar. Correction was made as per the suggestion of District support engineers by providing the wooden bands and corner stich bands and the beneficiary has received all three tranches from the government.

Picture Credit: Sanjib Yadav NRA Engineer



Figure 6 House of Yek bahadur Pariya Siddhicharan Municipality ward no 1 Taluwa

The beneficiary has received first and second tranches and has been recommended for the third tranches the house was noncompliance since it missed some of the bands after the correction was made by providing the missing bands as per the suggestion of DSE the house was made compliance

Picture Credit: Sanjib Yadav NRA Engineer



Figure 7 Kumar Prashad Bhattari Serna ward no 5 of Chisankhugadi Rural Municipality



Figure 8 House of Jit Bahadur Shrestha Siddhicharan Municipality ward

no 1 Taluwa

Only One house of Serna which has not got the second and third tranches at serna, house is missing the plinth band and the other band are provided in 3 feet gap the house is made up of stone in mud mortar. DSE has suggested correction for the house for the second and third tranches.

Picture Credit: Prakash Basnet DC HRRP

House made with stone in mud mortar with wooden bands

Provided at appropriate place. The beneficiary has received first and second tranches from the government and third tranches

has been recommended by the field engineer.

Picture Credit: Prakash Basnet DC HRRP

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will get the full authority for the reconstruction	Ward leader of ward no 1 of Siddhicharan Municipality	M&E CIPIU Expert

Challenges and Way Forward

Challenge	Way Forward
Most of the Houses which were built before the arrival of NRA Guidelines and technicians in the wards are non-compliant and those beneficiaries are not ready for correction and they want their tranches.	They should be provided extra amounts for the correction from the governments. Either they should be provided trained manpower for the correction from the Gov.
