

District Report

Dolakha

15 March – 11 April 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Resurvey & reverification training concluded: Resurvey and reverification training concluded in district to the Technicians and local bodies' officials. The training was for two days to technicians and one day to local body officials which aim to include all genuine earthquake victims who left to be enlisted as earthquake beneficiaries. After the training, the technicians will be deployed to the local palikas. The training was organized by NRA.	25-27 March	M: 57	F: 20	Mr Bhogendra Sah, Information Officer, DLPIU(Building), Dolakha Cell: 9854045341 Email: mouddlpiu.dolkha@gmail.com	
DGCM concluded in district: District General Coordination Meeting (DGCM) concluded in district. The key decision taken in the meeting was that GOs and NGOs working in district on reconstruction will speed up to declare settlement reconstruction completion to reach reconstruction completion goal.	26 March	M: 13	F: 2	Ms Rita Lamsal, Section Officer, GMaLI,Dolakha Cell: 9846075504 Email: lamsalrita@mail.co.m	

News & Updates

March 21, 2019 (Chaitra 7, 2075) Arthik Abhiyan National Daily: 47,000 private houses constructed after earthquake

भूकम्पपछिको पुनर्निर्माण दोलखामा ४७ हजार घर बने

तबराज शिवाकोटी
दोलखा

दोलखाको उत्तरी सिंगटी बजारबाट भूकम्प पीडितको निजी आवास पुनर्निर्माण शुरू भएको ३ वर्ष पूरा भएको छ । यो अवधिमा जिल्लामा करीव ४६ हजार ७४५ घरको निर्माण सम्पन्न भएको राष्ट्रिय पुनर्निर्माण प्राधिकरण, दोलखाका प्रमुख निर्मलदर्शन आचार्यले बताए ।

फागुन २९ गतेसम्म दोलखाको निजी आवास पुनर्निर्माणको काम ७० प्रतिशत सम्पन्न भएको छ । प्राधिकरणको तथ्यांकअनुसार सरकारको तर्फबाट ४४ हजार ६९३ र गैरसरकारी संस्थाको तर्फबाट २ हजार २९ घरको पुनर्निर्माण भएको छ । दोस्रो किस्ता लिनेले तेस्रो किस्ता पनि प्राप्त गर्ने भएकाले घर निर्माण हुनेको संख्या अबको ३ महिनामा करीव ९० प्रतिशत पुग्ने प्राधिकरण दोलखाको प्रक्षेपण छ ।

सर्वेक्षण, गुनासो फछ्छ्योट र प्रवलीकरणसहित दोलखाको कुल ७२ हजार २२० लाभग्राहीमध्ये ९३ प्रतिशत अर्थात् ६७ हजार १५१ जनासँग सम्झौता भएको छ । यस्तै ६४ हजार ९५४ ले पहिलो किस्ता र ५४ हजार ३८७ ले दोस्रो किस्ता लिइसकेका छन् ।

प्रवलीकरण गर्ने लाभग्राहीतर्फ सबैभन्दा न्यून प्रगति ९ प्रतिशत मात्र भएको छ । कुल २ हजार २ लाभग्राहीमध्ये २१० जनाले मात्र पहिलो किस्ताका लागि सम्झौता गरेका छन् । तर पहिले नै घर प्रवलीकरण गरिसकेका लाभग्राहीले भने कागजी प्रक्रिया पूरा गर्न कठिन भएकाले अनुदान पाउन नसकेको गुनासो गरेका छन् । जिल्लावाहेक अन्यत्र पनि वस्तुयोग्य घर भएको कारण देखाउँदै ९ जना भूकम्पपीडितले पहिलो किस्तावापतको रकम फिर्ता गरेको कार्यालय प्रमुख आचार्यले जानकारी दिए ।

विपद् जोखिम न्यूनीकरण कार्यक्रम

जिरी समाचारदाता

घरकोट (दोलखा), चैत ८ गते । दोलखाको कालिञ्चोक गाउँपालिकाको उत्तरी विपद् गाउँहरूमा सञ्चालित बाल केन्द्रित विपद् जोखिम न्यूनीकरण कार्यक्रमका योजना सम्पन्न भएका छन् ।

करिब २७ लाखको लागतमा गाउँपालिकाको विभिन्न वडाका चालू ६० हजारदेखि तीन लाख ररियनसम्मको १४ वटा योजना सम्पन्न भएको हो । बालबालिका अध्ययनरत विद्यालयहरूको आवश्यकता अध्ययन गरी विद्यालयमा धाना, शौचालय, ग्याबियन बाल, स्कूल कम्पाउण्ड, ह्युमपाइप, कक्षा कोठा ढलान र बाटोघाटो निर्माणलगायतका कार्य भइरहेको थियो ।

२०१७ सेप्टेम्बरदेखि १५ पहिनाका लागि शुरू भएको कार्यक्रम लगभग सकिएको कालिञ्चोक गाउँपालिकाको नाम तथा बाल केन्द्रित विपद् जोखिम न्यूनीकरण कार्यक्रमका संयोजक राम ओलीले जानकारी दिनुभयो ।

गाउँपालिकाको सम्पन्ध र युनिसेफको आर्थिक तथा प्राविधिक सहयोगमा सञ्चालित बाल केन्द्रित विपद् जोखिम न्यूनीकरण कार्यक्रमको जिसस प्रमुख डबल पाण्डे, गाउँपालिका अध्यक्ष विनकुमार थापा, वडा अध्यक्षहरू तथा गाउँपालिका गठित स्थानीय विपद् जोखिम न्यूनीकरण व्यवस्थापन समितिले



कालिञ्चोक गाउँपालिका ३ लाईपिर्डाइस्थित भगवती प्राथमिक विद्यालयमा बनाएको बाटो अवलोकन गर्दै जिसस प्रमुखसहितको अनुगमन टोली ।

तस्विर : कैलाश तामा

संयुक्त रूपमा बिहीबार अनुगम गरिएको छ ।


अनुगमनको क्रममा विभिन्न वडाका विद्यालयमा पाँचवटा स्थानीय धाना, एउटा शौचालय, दुईवटा स्कूल कम्पाउण्ड, एउटा बाटो, एउटा भुईँ ढलान, दुईवटा ग्याबियन बाल र दुईवटा खोलापा ह्युमपाइप राखिएको पाइएको गाउँपालिका अध्यक्ष विनकुमार थापाले जनाउनुभयो ।

Gorkhapatra national daily, 23 March, 2019


Tranche Status

Rural /Municipality	Baiteshwor	Bhimeshwor	Bigu	Gaurishankar	Jiri	Kalinchowk	Melung	Sailung	Tamakoshi
Total HHs Surveyed	8550	13693	6799	6656	5991	9062	8067	8524	7537
Total HHs Eligible	8339	12503	6731	6767	5807	8914	7607	8119	7433
Total HHs Enrolled	8204	11198	6324	6583	5663	8431	6954	6998	6869
First Tranche	7717	11072	6221	6497	5029	8429	6562	6939	6868
Second Tranche	6962	8167	5454	5401	4007	7685	5857	5612	6137
Third Tranche	6212	6491	4785	5044	3164	7114	4913	4283	5444
Total HH Constructed	6226	6501	4790	5051	3173	7120	4927	4294	5458
Grievance Registered	248	546	132	123	222	378	1191	226	84
Grievance Addressed	1795	2235	719	760	961	1238	1100	1257	828
RF HH Eligible	339	348	34	74	153	32	402	746	110
RF HH Enrolled	4	103	5	26	31	19	9	41	9
RF 1 st Tranche	4	103	5	26	31	19	9	41	9
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	1925 (9 Palikas in total)								
Non-Compliance Addressed	1581 (9 Palikas in total)								


Graph of Tranche Status:

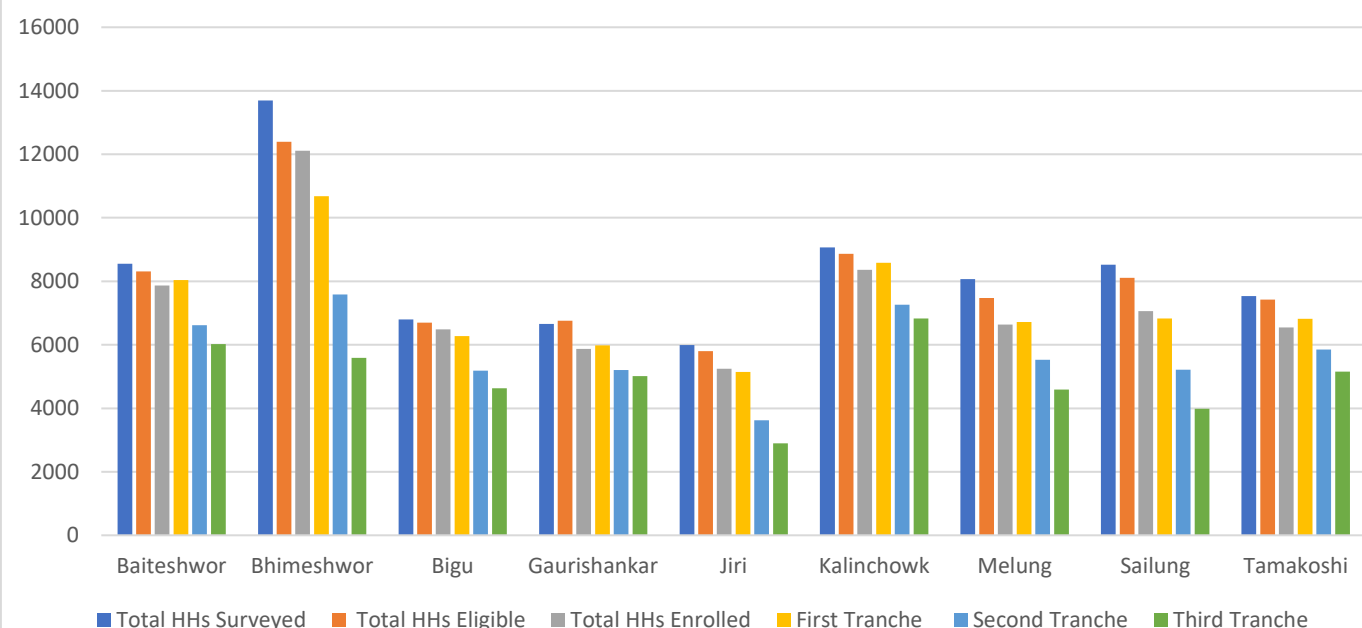

Graph for Retrofitting Status:

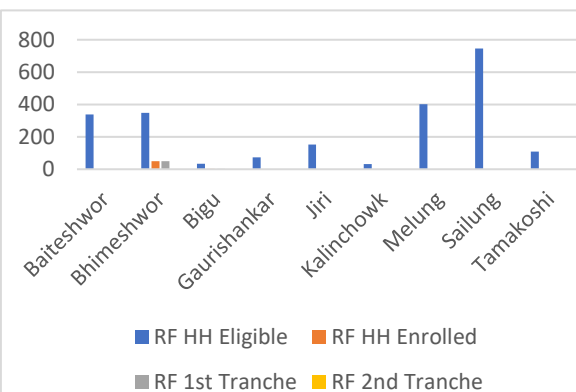

Graph for Grievance Status:

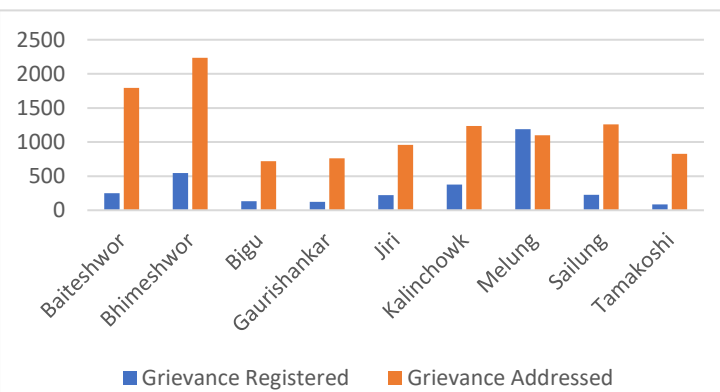

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
26 th March 2019	Kalinchowk Rural Municipality-5,6,8,9 Dolakha	- Kamal B Mahat - Pavan R Devkota, M&E Specialist, GMAI - Chandra Prakash Niroula, Social Development Specialist

Objective(s)
- To conduct ward level coordination meeting - To sort out reconstruction issues - To collect housing typology

Summary


Meetings in ward offices was mainly focused on vulnerable households i.e. above 65-year single women, above 70-year senior citizen, below 16year orphan children, People with disabled who have received red and blue cards from Nepal government who have not started to construct private houses yet. Further, we discussed about settlement, landless, ward completion of reconstruction declaration; re survey, let out beneficiaries; fake beneficiaries.

The gap between ward offices and Palika office were found in letter circulation, directives, reconstruction provisions and in other reconstruction issues. was mainly aimed to discuss and visit non-compliance issues in Sundrawati. Further, ward offices haven't enough database of reconstruction. Some households were in India so they were unable to begin the reconstruction process yet. In ward 5 Mr. Purna Man Thami is landless(he needs psycho social support). From that ward 5 people recommened for debt purpose to Rastriya Baniya Bank but unable to receive loan yet. In ward 5, households grievance that in the first time, nepotism was dominant to collect in beneficiaries list collection. Moreover, Kalinchowk-8 ward chair Mr. Nabaraj Siwakoti had query that one grandma late Mrs. Sunrekha Damai's grandson care her and Mrs Damai filled her grandson as *Ichhayaiko* (heir) person but after her untimely death he was unable to receive the grants. We discussed on improved cook stoves, NGOs working in their areas. During the field visit houses photos were collected for the housing typology purpose.

Photos



Caption: Ward level meeting at Kalinchowk RM-05

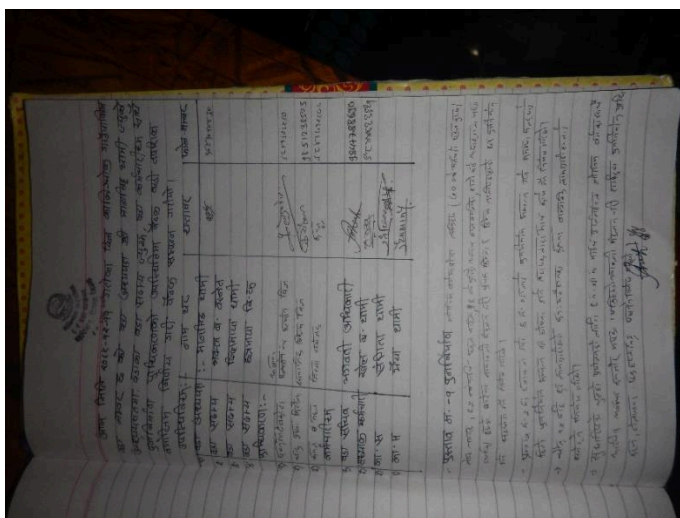

Meeting minute of KalinchowkRM-6

Housing Typology Report

Photo



Caption: SMM building has been constructed in Kalinchowk RM-06. House owner name is Mr. Indra B Shrestha who has received third tranche received Pic: Kamal B Mahat

Photo



Caption: Hybrid (SMM and Light timber frame) building has been constructed in Kalinchowk RM -06. House owner name is Mr. Birkha B Shrestha who has received third tranche. Pic: Kamal B Mahat

Photo



Caption: SMM building has been constructed in kalinchowk RM-06. Mr. Gopinath Thami is the name of house owner and he has received third tranche. Pic: Kamal B Mahat

Photo



Caption: Hybrid (SMM and Light timber frame) building has been constructed in Kalinchowk RM -06. Mr. Dhruba Pradhan is the name of the house owner and he has received third tranche. Pic: Kamal B Mahat

Photo



Caption: SMM building has been constructed in Kalinchowk RM -06. Mr. Chitra B Shrestha is the house owner and he has received third tranche till date. Pic: Kamal B Mahat

Photo



Caption: Building made up of interlocking block has been constructed in Kalinchowk RM-06, Mr. Maiyaram Thami is the name of houseowner and he has received second tranche till date. Pic: Kamal B Mahat



Caption: Hybrid (SMM and Light timber frame) building has been constructed in Kalinchowk RM-06, Mr. Subash Thami is the name of houseowner and he has received third tranche till date. Pic: Kamal B Mahat



Caption: Hybrid (SMM and Light timber frame) building has been constructed in Kalinchowk RM-06, Mr. Tilak Shrestha is the name of the house owner and he has received third tranche. Pic: Kamal B Mahat
