

District Report

Makwanpur

4 to 10 May, 2018

Summary of Activities		
Activity	Contact Person	Reference Document
<u>Meeting of District Reconstruction Facilitation Committee (District General Coordination Meeting):</u> Date: 8th May, 2018 Time: 11:00AM onwards Location: DCC, Makwanpur Chaired by: Mr. Raghunath Khulal, Chief, DCC Key Participants: <i>(Included in Attached meeting minute)</i> • Mr. Chakra Bdr. Budha, Chief District Officer • Chiefs/Heads of District Forest/Land Revenues/Survey Offices • Chiefs/Heads of DLPIUs • Engineers and other officials from DLPIUs • PIN/CSRC Team • HRRP Team Decisions: 1. To expedite housing grants delivery process and ask DLPIUs to present specific plan and target of reconstruction of private shelters at the next meeting of the committee. 2. To take immediate action on the applications of landless beneficiaries who've planned to purchase land with additional grant of Rs. 200,000.00 3. To ask Palikas and Wards to submit the detailed list of beneficiaries who are being unable to sign the housing grants agreement due to lack of land title documents (landlessness). 4. To formally request NRA in written to immediately address the issue of Grievances collected within the last timeline (End of Mangsir, 2074) given to the people.	dc.makwanpur@hrrpnepal.org	Scanned copies of meeting minute.
<u>Technical Coordination Meeting and Joint(GMLI/HRRP) Field Monitoring Visit:</u> Date: 9th May, 2018 Time: 7:00AM onwards Location: Thaha Municipality -9 (Previously Chitlang VDC) Participants: GMLI Makwanpur, MoUD CLPIU Specialist, local bodies, NRA technicians & Beneficiaries.	techcord.makwanpur@hrrpnepal.org	Field report and photo
<u>On-site inspection and meeting with landless beneficiaries:</u> Date and Locations: 9th May, 2018: Gadhi R. Municipality-4, Kalikhola; Hetauda-13, Padampokhari 10th May, 2018: Thaha Municipality-7, Agra Participants: GMLI: Sujan Lamichhane-Sub-Engineer HRRP: Hari Thalang, Nirmal Nepali PIN/CSRC: Fulmaya Tamang, Upahar Rai, Ran Subba Gurung Outcomes of the visits: 1. At Gadhi -4, Kalikhola, the team met with landless beneficiary Mr. Bir Bahadur Pakhrin and his counterpart (land seller) Mr. Lal Bahadur Ghising; and, inspection of land they've planned to	dc.makwanpur@hrrpnepal.org	

purchase done. <i>The team concluded to forward the process of this beneficiary.</i> 2. The team, then met with the 3 landless beneficiaries (buyers) of Bhimpheedi Rural Municipality who've accomplished almost whole process of purchase of land in Hetauda-13, Padampokhari; but, at the end, the proposed landowner is hesitating to sell his land to those beneficiaries. After dense discussion, <i>the team suggested all of them to go back to Ward Office and talk to them to solve their dispute.</i> 3. The team met Mr. Indra Lohani, another landless beneficiary of Thaha-7, Agra who've planned to purchase the land of local resident Mr. Dharam Bahadur Magar. After on-site inspection of the proposed land and meeting with the both of buyer and seller, <i>the team concluded to proceed the process of this beneficiary.</i>		
---	--	--

Upcoming Events		
Event	Date, Time and Venue	Contact Person
Technical Coordination Meeting and Joint (GMLI/MoUD Specialist/HRRP) Field Monitoring Visit in Kailash Rural Municipality and Thaha Municipality.	17 th May, 2018 - Gogane meeting and field visit. 18 th May, 2018 - Agra meeting and field visit.	techcord.makwanpur@hrrpnepal.org
Joint monitoring of private shelters constructed in Aliani Lands in Dhiyal, Chhatiwan, Raigaun and Bakaiya.	17 th May, 2018 – Bagmati RM 18 th May, 2018 – Bakaiya RM	dc.makwanpur@hrrpnepal.org

Field Visit Reports		
Date	Location	Participants
26 th April, 2018	Technical Coordination Meeting with Joint Field Visit in Indrasarowar Rural Municipality (Previous Marphu VDC)	NRA Chief, MoUD M&E Specialist, HRRP DTC, Local Bodies, NRA Technicians and Beneficiaries. (Total 13 participants)
Objective (s)	- Overall status of housing reconstruction and POs activities in their respective areas. - Separate interaction with NRA local based technicians and beneficiaries. - Find out the key issues and challenges for delay in reconstruction at local level. If any major issues include in district level general coordination meeting otherwise solve in local level. - Gap maintain between tranches distribution. - Observations of housing reconstruction including other activities related with reconstruction.	
Summary	We have conducted technical coordination meeting with VDC level and separate interaction with NRA field base technicians and also beneficiaries. Also we have observed different typology to construction of housing, POs activities if any their areas. Under construction school buildings, fund supported by Plan International Nepal and implementing partner is RADO Nepal. After completed 588 HHs, RADO Nepal also supporting in school buildings as a technical assistance.	



Figure 1: Indrasarowar Rural Municipality -05, Mahachuli Higher secondary school, under construction school building, fund supported by Plan International Nepal and implementing partner is RADO Nepal. Total 8rooms, two story with rigid roof. Reinforcement bar layout with first floor for 4rooms.

We briefed discussed about the agendas of overall reconstruction status, major key issues and challenges, POs activities, coordination between beneficiaries and technicians, role of ward members in their locally level.

We found out some issues like as shortage of skilled manpower, water problem in some places, payment rate is high for skilled manpower etc. Mobilization of technicians, inspection rate is good in now days. The concluded point after meeting is inspection file submit within 7days, if beneficiaries completed to roof band level and repaired/constructed toilet work early inspection and maintain to tranches gap and at ending of month, reconstruction meeting conduct in ward office with present of technicians and ward members.

Current reconstruction rate is here, Indrasarowar Rural Municipality.

Name of VDCs	Agreement HHs	Reconstruction Started	Verified for Second Tranche	Verified for Third tranche	Total completed house
Marphu	378	215	204	72	96
Phakhel	800	371	352	131	116
Kulekhan i	535	215	191	22	57
Sisneri	469	201	184	48	68

Field Visit Reports

Date	Location	Participants
9 th May, 2018	Technical Coordination Meeting with Joint Field Visit in Thaha Municipality -9 (Previous Chitalng VDC)	GMLI, HRRP DTC, Local Bodies, NRA Technicians and Beneficiaries. (Total 14 participants)
Objective (s)	- Conduct technical coordination meeting in local level, overall reconstruction status in housing reconstruction and POs activities in their respective areas. - Separate interaction with NRA local based technicians and beneficiaries. - To find out the key issues and challenges for delay in reconstruction at local level. If any major issues include in district level general coordination meeting otherwise solve in local level. - Gap maintain between tranches distribution. - Observations of housing reconstruction including other activities related with reconstruction.	

Summary

We have conducted technical coordination meeting with participate of LUMANTI Nepal and separate interaction with NRA field base technicians and also beneficiaries. Also we have observed different typology to construction of housing, POs activities if any their areas.

LUMANTI Nepal, under Community Managed Post- Earthquake Reconstruction in Urban Poor Communities in Nepal program 125HHs enrolled among them 81HHs have received second tranche, 58HHs received third tranche and 74HHs completed their houses as well.

We briefed discussed about the agendas of overall reconstruction status, major key issues and challenges, POs activities, coordination between beneficiaries and technicians, role of ward members in their locally level.

We found out some issues like as 23HHs don't enroll till to the date from side of LUMANTI Nepal. From government side, inspection not conducted on time and files submit. The concluded point after meeting is inspection file submit within 7days, if beneficiaries completed to roof band level and repaired/constructed toilet work early inspection and maintain to tranches gap.

Current reconstruction rate is here, Thaha Municipality.

Name of Rural/ Municipality	Agreement HHs	Reconstruction Started	Verified for Second Tranche	Verified for Third tranche	Total completed house
Thaha	2858	1171	1131	30	113
Agra	1539	1300	1288	678	652
Tistung	963	615	611	374	401
Chitlang	459	190	173	137	148

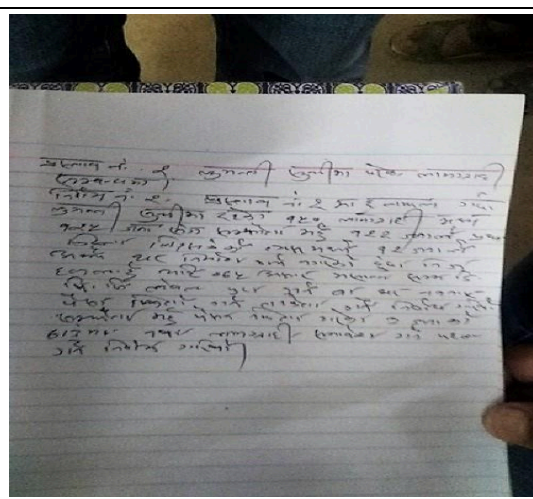
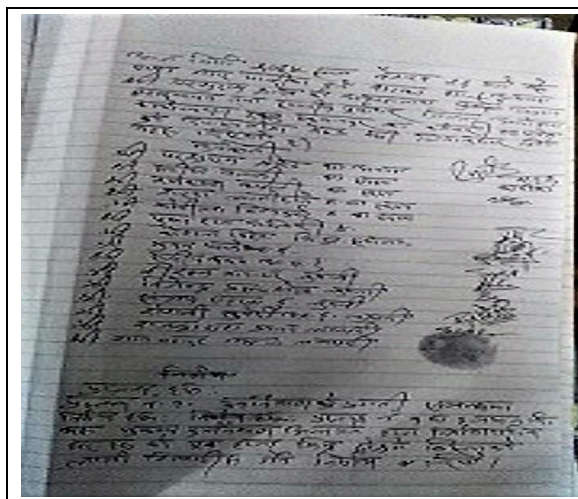


Fig: Meeting minute of technical coordination meeting in VDC level, the minute taken by ward office, Thaha Municipality-09.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Gap between tranches distribution	After meeting, we concluded if beneficiaries completed to DPC band level for second tranche and to roof band level, toilet constructed for third tranche till to meeting date, still technician inspection and submit file to DLPIU in the district with in 7days.	NRA technicians, Local Government	7days
Mobilization of technicians	It should be necessary for mobilization of technicians in timely for inspection and submit inspection file with in period of weekly. We all are aware	Local Government NRA Makwanpur	

	about mobilization of technicians under local government.		
--	---	--	--

Photos



Figure 2: Technical Coordination Meeting in VDC level Thaha Municipality-09 (Previous Chitalng VDC). There were 14 participants from Local Representatives, local government bodies, GMLI Makwanpur, HRRP-DTC, NRA Technicians and Beneficiaries.



Figure 3: Thaha Municipality-10, house owner Purna Kumari Nepali. She has not received any tranches from government grants because of her house built in government land but permission approved by local government. She has been living this land since 32 years.



Figure 3: House owner: Nani Maya Basnet, Thaha Municipality-10 (previous chitalng VDC). Brick in cement mortar with all vertical and horizontal bands provided. Under construction house, technical and financial support provided by LUMANTI Nepal. She has been received all tranches.



Figure 4: House owner: Bhuwan Magar, Thaha Municipality-10, Brick in cement mortar with all vertical and horizontal bands provided. Under construction house, he received second tranche.



Figure 4: Technical Coordination Meeting in VDC level Indrasarowar Rural Municipality-01 (Previous Marphu VDC). There were 13 participants from Local Representatives, local government bodies, NRA Makwanpur, MoUD M&E Specialist, HRRP-DTC, NRA Technicians and Beneficiaries.



Figure 5: Indrasarowar Rural Municipality-01, house owner Nar Bahadur Bist. Stone in mud mortar with timber band and flexible roof. He has received all tranches of government grant. The tentative construction cost of this building is 5lakh.



Figure 3: Indrasarowar-01, house owner: Govind Bahadur Bist, under construction brick in cement mortar with RCC band with vertical and horizontal elements. Verified for second tranche by NRA engineer.



Figure 4: RCC frame structure with meet all mandatory requirement Thumb rule. His house verified for second tranche and the location of building is Indrasarowar-01, house owner name is Ram Sharan Bist.

Questions Collected

Question of the week	Who Asked the Question?	Response Provided (By Whom)
Why delay in tranches released?	Beneficiary	Now, we have compiled the tranches received beneficiaries name list and publish to DLPIU field base engineer and respective ward office and no any file jam in GMLI-DLPIU. Hope, it should be released on time for further days.
Why doesn't implement the retrofitting issue for second tranche.	Ward member	Now, we have successfully completed the 2batch retrofitting training for engineers. According to the beneficiary application, engineer guided for construction with retrofitting methodology and after completed engineer inspected for second tranche.
Our house has been completed to roof band level and we have already repaired toilet with meet MRT, can we receive the third tranche?	Beneficiary and ward president	If the construction of the house meets all requirement of earthquake resistant as set out in the inspection checklist, then the engineer will be verified for third tranche. (M& E Specialist)
Why delay in tranches released?	Beneficiary	Tranches released process is already long and after few days, all CLPIU-DLPIU will be work under NRA. It is on processing. Hope, it will see positive result in overall reconstruction. Also, we are aware in this case and follow up in district.
