

Monthly District Report

Makwanpur, Chitwan, Nawalparasi

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	GMaLI meeting with involvement of NRA-CLPIU-GMaLI Chief and all staffs	15 th Nov, 2019	GMaLI office, Hetauda	makwanpur@hrrpnepal.org	Meeting minute click here
	Joint Monitoring Visit <u>Participants:</u> GMaLI MIS Specialist, Social development specialist, HRRP District Technical Coordinator, Ward technicians	21 th -22 th Nov, 2019	Raksirang Rural Municipality-6,7,8 (Previous Kakda VDC)	makwanpur@hrrpnepal.org	Report and photo here Below
	Update Palika Profile data of Makwanpur	14 th Nov, 2019		makwanpur@hrrpnepal.org	Palika Profile data
	Contact list updated in GD	20 th Nov, 2019		makwanpur@hrrpnepal.org	Contact List
Chitwan	Contact list updated in GD	20 th Oct, 2019		chitwan@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	27 th Sep, 2019		chitwan@hrrpnepal.org	Palika Profile Data
Nawalparasi	Contact list updated in GD	20 th Oct, 2019		nawalparasi@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	25 th Nov, 2019		nawalparasi@hrrpnepal.org	Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation Meeting	Tentative 29 th Nov, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLI/HRRP	makwanpur@hrrpnepal.org
Joint Monitoring visit, To prepare action plan in ward level (cover Previous VDC), follow up district made action plan, status of retrofitting.	2 th Dec to 5 th Dec, 2019	GMaLI/Building/HRRP	makwanpur@hrrpnepal.org

Upcoming Events & Meetings

News & Updates

NRA-CLPIU-GMaLI Chief has been visited in Makwanpur district. DLPIU-GMaLI has organized a meeting in that period at DLPIU-GMaLI office. The main agendas were; present status of reconstruction in the district, follow up action plan, field visit smoothly done or not and AoB. In the meeting, DLPIU chief has presented the overall reconstruction progress and its strategic. The CLPIU-GMaLI chief suggested and directed to us about reconstruction progress and how to meet the time line of NRA. So, for this purpose it should be given priority of tasks and smoothly implementation it. Like as prepare an action plan in ward level and strongly implement it. Also increasing the field visit from the district to ward level.



Figure 1: NRA-CLPIU-GMaLI Chief directed to all the DLPIU GMaLI staffs about the reconstruction progress and its speedup. On 15th November, 2019 at DLPIU-GMaLI office Hetauda, Makwanpur.



Figure 2: Group photo after completed the meeting.

Meeting minute is given below with link;

[Meeting minute click here.....](#)

Upcoming Events & Meetings


Tranche Status (Makwanpur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2330	2318	2033	1310	2176	1527	1491	0
Bakaiya Gaunpalika	8593	4019	2818	2817	2073	1333	1960	794	794	0
Bhimphedi Gaunpalika	5236	2698	2230	2227	2009	1806	932	633	608	0
Hetauda Upamahanagarpalika	32696	6363	4707	4706	2983	2670	2024	1089	1079	0
Indrasarowar Gaunpalika	3726	2923	2591	2581	2148	1674	254	166	166	0
Kailash Gaunpalika	4737	2614	2160	2159	1931	1641	731	400	389	0
Makawanpurgadhi Gaunpalika	5516	2216	1844	1840	1495	1197	1437	967	952	0
Manahari Gaunpalika	8841	2337	1295	1292	1141	996	1487	747	733	0
Raksirang Gaunpalika	5091	1715	1585	1584	1478	1210	576	481	466	0
Thaha Nagarpalika	10519	6919	6220	6207	5081	4145	1369	707	693	0


Graph of Tranche Status:

Reconstruction- Tranche Status

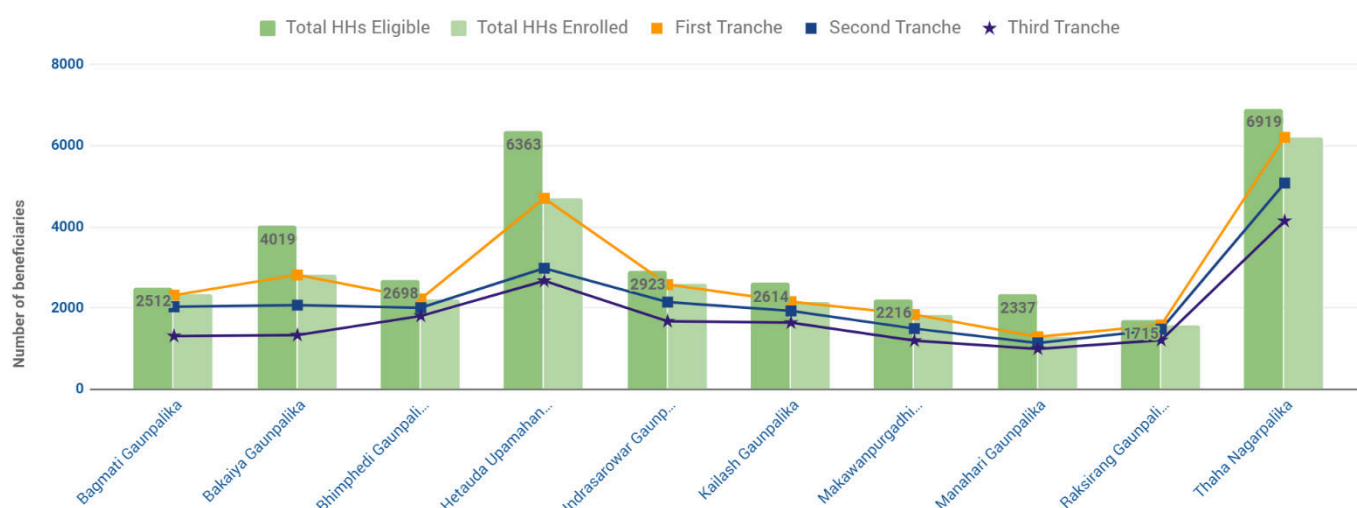

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

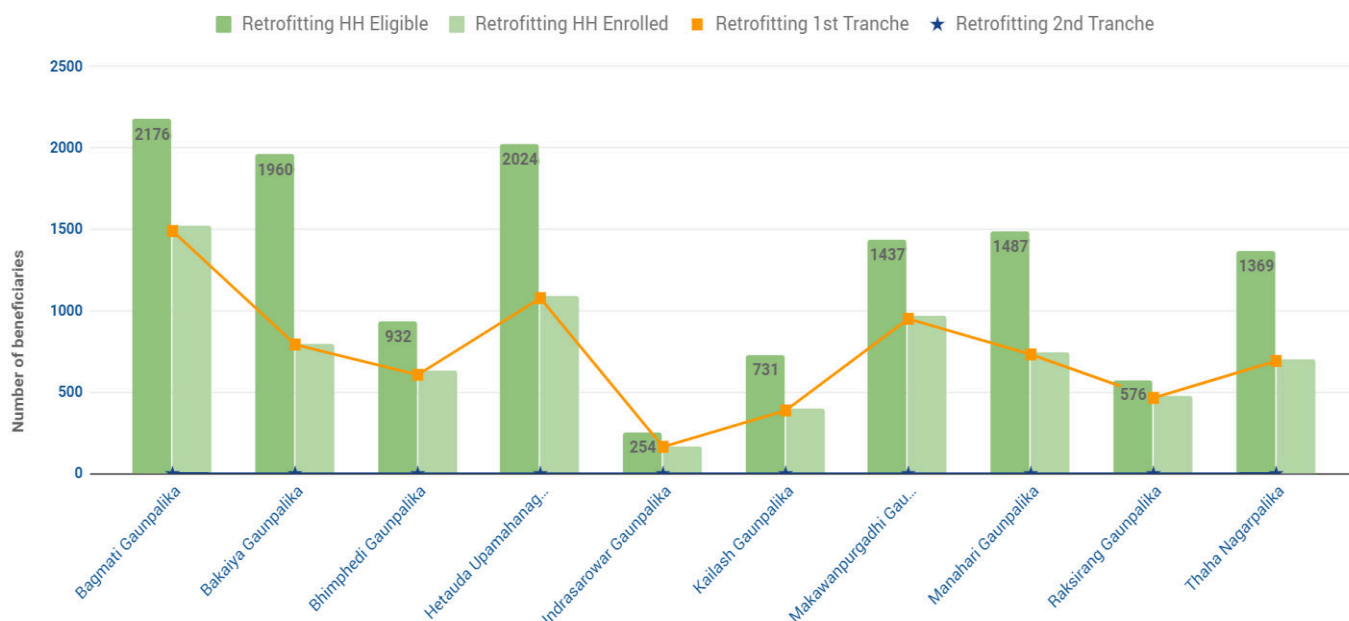


Tranche Status (Chitwan)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarpalika	2087	710	660	660	387	156	38	9	9	0
Ichchhyakamana Gaunpalika	3571	2353	2106	2106	1854	1366	248	196	196	0
Kalika Nagarpalika	2565	916	792	792	447	227	42	27	27	0
Khairahani Nagarpalika	1566	559	529	529	273	251	4	4	4	0
Madi Nagarpalika	123	23	23	23	21	16	15	13	13	0
Rapti Nagarpalika	3594	2043	1862	1862	898	578	71	18	18	0
Ratnanagar Nagarpalika	1763	731	657	657	425	381	175	164	164	0


Graph of Tranche Status:

Reconstruction- Tranche Status

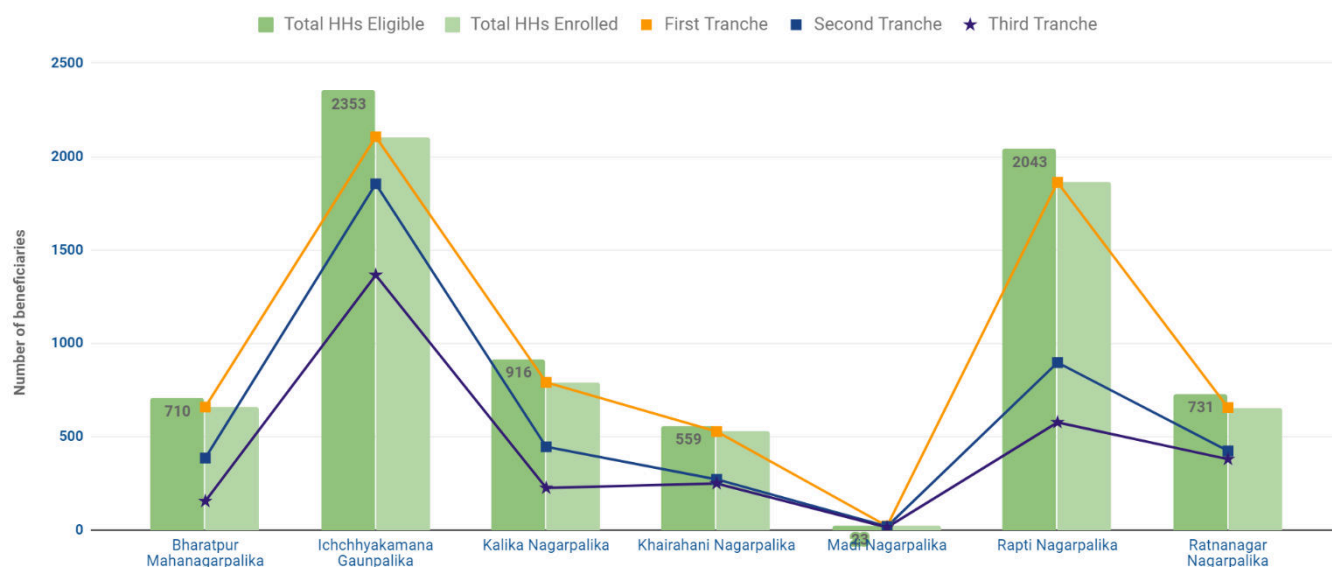

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

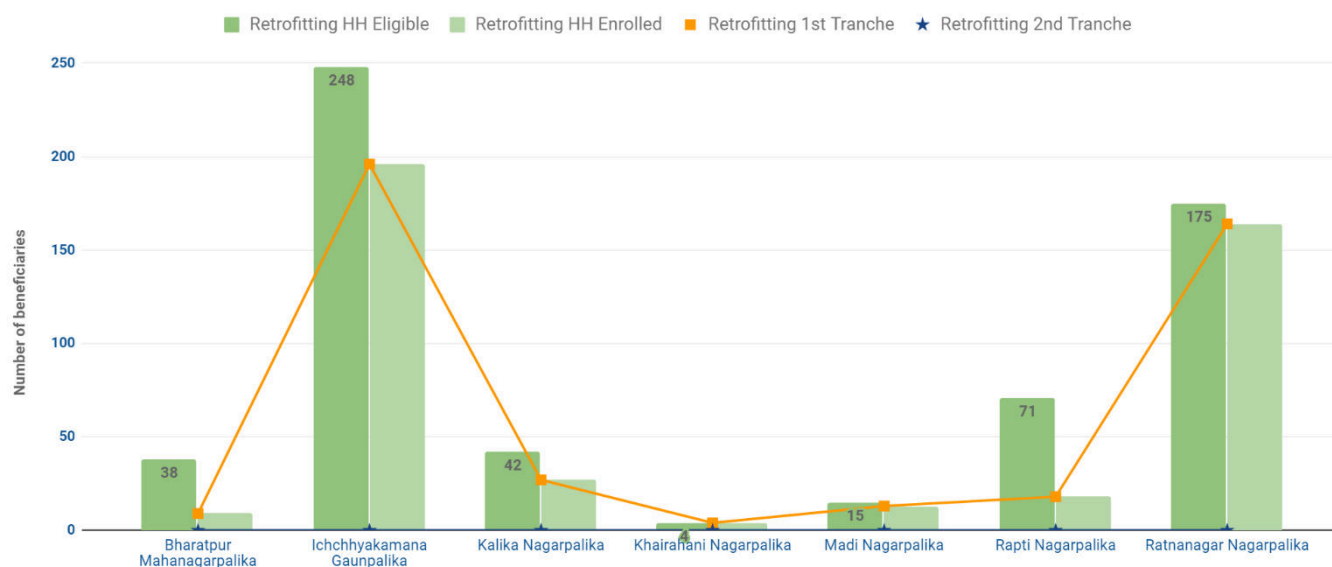


Tranche Status (Nawalparasi)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	4	3	0			
Binayee Tribeni Gaunpalika	70	70	69	69	65	60	2			
Bulingtar Gaunpalika	280	260	260	260	259	249	5	3	3	
Bungdikali Gaunpalika	133	72	72	72	68	68	1	1	1	
Devchuli Nagarpalika	177	177	177	177	172	165	1			
Gaidakot Nagarpalika	103	49	49	49	43	43	0			
Hupsekot Gaunpalika	155	139	139	139	134	121	2			
Kawasoti Nagarpalika	4	4	4	4	4	3	0			
Madhyabindu Nagarpalika	41	81	81	81	82	73	3			
Palhi Nandan Gaunpalika	1	4	4	4	4	3	0			
Pratapppur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	4	3	3	3	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	3	2	0			

Graph of Tranche Status:

Reconstruction- Tranche Status

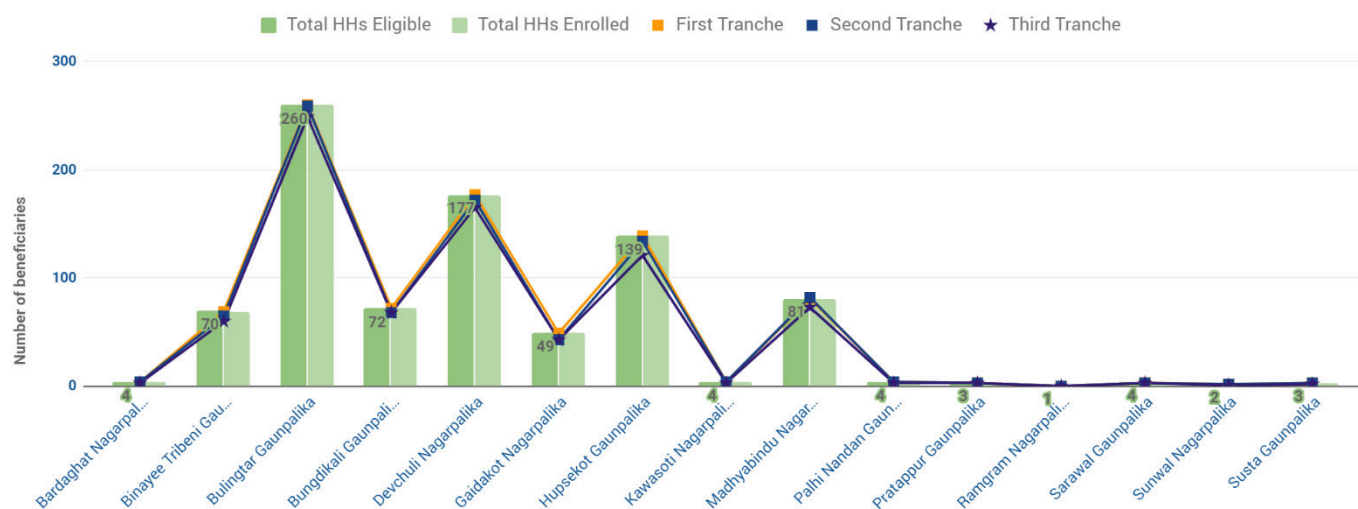

Graph for Retrofitting Status:

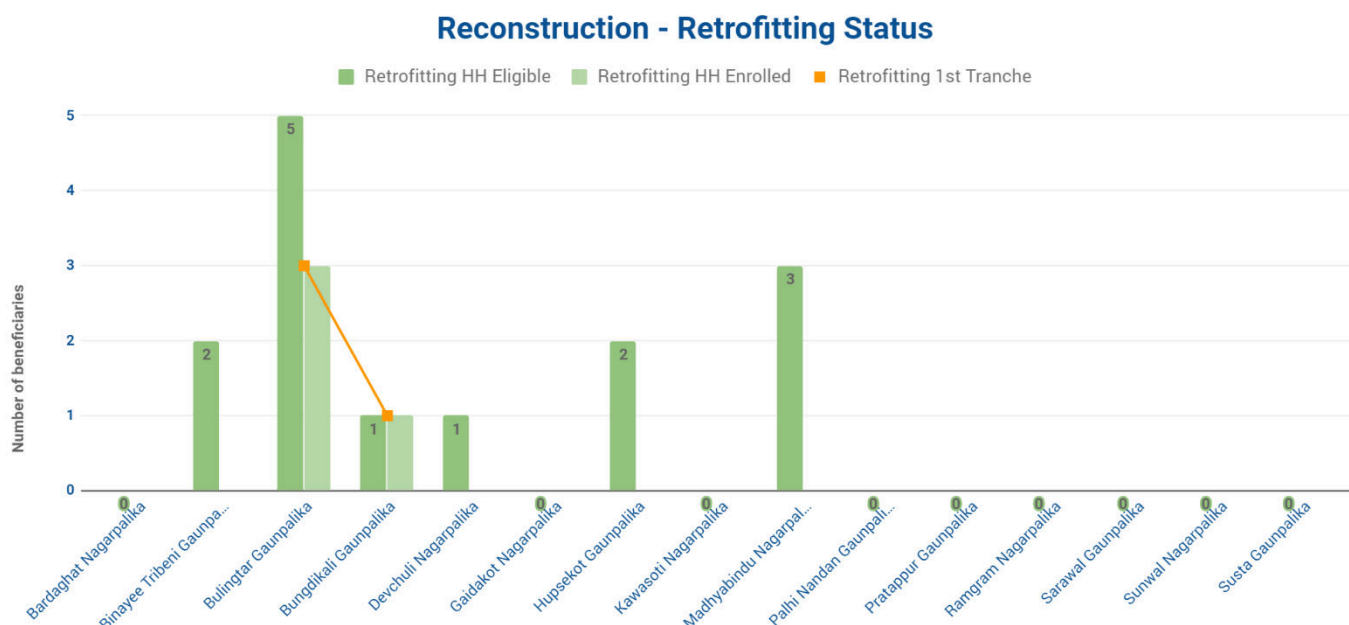

Field Visit Reports (Makwanpur)

Visit 1

Date	Location	Participants
21 th to 22 th Nov,2019	Raksirang Rural Municipality-6,7,8 (Previous Kakda VDC)	DLPIU-GMaLI MIS specialist, Social Development Specialist, HRRP and Ward level technicians and Beneficiaries
Objective(s)	- To conduct the Coordination meeting and prepare the reconstruction action plan at ward level and also its implementation. - To carryout the field monitoring visit; sharing the overall reconstruction progress of Raksirang Rural Municipality data as per MIS system and know the latest reconstruction update and to collect the housing typology with updated ODK Version.	
Why was the visit carried out in this location? Priority wise, Write any other reason		
Now at that place around 97% received the 2nd tranche as well around 82% received 3rd tranche with 40% received completion certificate. From one side need to be complete the re-construction and from another side starting the challenges work; retrofit. So, for this purpose we were carriedout field visit.		
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.		
- CS entry and distribution of completion certificate - Non-compliance issues after received the 3rd tranche.		- Non compliance issues after received the 3rd tranche and before to receive the completion certificate. - Difficult to convince them about retrofit and its implementation like as economically, financially and technically etc.

Summary

Field Visit:

We have organized the coordination meeting at Raksirang Rural Municipality-06 and in the meeting all wards 6,7,8 (Previous Kakda VDC) technicians were participated in the meeting and also from the wards representatives.

The meeting agendas were;

- To share the present status of reconstruction as per MIS data and know the current updated data of reconstruction at field level.
- To follow up the implementation of district action plan and prepare the reconstruction plan at ward level 6,7,8 (Covered Previous Kakda VDC) and also properly its implementation.
- Planning to finalise the reconstruction with CS entry, completion certificate distribution and starting of retrofit.

Decision Made;

- The current status of reconstruction is in final stage at ward nos. 6,7,8 (Previous Kakda VDC) further more to complete it on time strongly implementation an action plan.
- To complete the reconstruction before time line of NRA, make the reconstruction action plan and effectively its implementation and to complete all the reconstruction works at time.
- Till to date around 40% received the completion certificate for further more complete to all the works with CS entry doing according to action plan.

क.सं.	माइलस्टोन	२०७५ हात सम्पन्न प्रगती प्रतिशत	२०७५ मंसिर सम्पन्न प्रगती प्रतिशत	२०७५ पौष सम्पन्न प्रगती प्रतिशत	२०७५ फागुन सम्पन्न प्रगती प्रतिशत	२०७५ बैशाख सम्पन्न प्रगती प्रतिशत	२०७५ जेठ सम्पन्न प्रगती प्रतिशत
१	पहिलो किस्ता	१००					
२	दोश्रो किस्ता	०	४५	२०	४५	१००	
३	निर्माण सम्पन्न	०	१	१५	४५	१०	१००

Figure 3: Reconstruction action plan of Retrofit;

क.सं.	माइलस्टोन	२०७५ हात सम्पन्न प्रगती प्रतिशत	२०७५ मंसिर सम्पन्न प्रगती प्रतिशत	२०७५ पौष सम्पन्न प्रगती प्रतिशत	२०७५ फागुन सम्पन्न प्रगती प्रतिशत	२०७५ बैशाख सम्पन्न प्रगती प्रतिशत	२०७५ जेठ सम्पन्न प्रगती प्रतिशत
१	अनुदान सम्झौता / पहिलो किस्ता	०	०	४०	१००		
२	दोश्रो किस्ता	०	०	१०	२०	४०	१०
३	तेस्रो किस्ता	०	०	०	१०	२०	४०
४	निर्माण सम्पन्न	०	०	०	१०	२०	४०

Figure 4: Reconstruction action plan of Grievance;

The meeting minute is given below with link;

[Coordination Meeting Minute click here...](#)

After that, we carried out field visit and collected the housing typology. We saw the non compliance issues in after the third tranche received and before the completion certificate received like as modified the existing structure them selves.

Challenges/Issues identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Non compliance issues in after received the final tranche and before the completion certificate received like as after roof level completed, they are modified their house.	We have suggested to beneficiaries but they don't have convince in this issues because they have faced to the conjusted space for big family.	Now around 40% distribution the completion certificate for completed houses so completion certificate distribution with CS entry at timely and	Ward technicians and Local government.	According to action plan/Regular

		regular follow up done by local government		
Implementation of Reconstruction action plan, CS entry and certificate distribution	We have prepared a reconstruction action plan at the meeting and finally we are agreed to implementation it. After final inspection and CS entry, planning to distribution the completion certificate to completed HHs.	Coordination is necessary for that work. There are not problem in reconstruction because of it is in final stage insted of some rare issues like as file hold in DIPIU Building, modified of houses etc. Next to necessary publish the grievance registered issues in timely.	Local Government, Ward technicians	Action Plan/Regular

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

Retrofit, we are serious in this task and now we are collecting the data of retrofit. We found that different types of building typology. In case of Makwanpur, almost we found stone in mud mortar, hybrid structure and timber structure. We are planning to construct the model house with participate to Beneficiaries and ward level technicians. In case of Timber structure we strickly follow the hybrid structure manual and light timber manual for correction.

The our data collection is in final stage and hope the training pacakages for masons, SMs as well technicains announced by NRA-CLPIUs early.

 National Reconstruction Authority(NRA) District level Project implementation Unit (DLPIU), Building Makwanpur District					
SN	Municipality/ Rural Municipality	Agreement Signed	First Tranche received	Data Collected	%
1	Manahari	733	733	733	100
2	Kailash	379	379	379	100
7	Thaha	693	693	693	100
3	Bhimfedi	727	727	707	97
9	Bagmati	1490	1490	1260	85
6	Indrasarowar	208	208	176	85
5	Makwanpurgadhi	1037	1037	870	84
4	Bakaiya	673	673	476	71
10	Raksirang	477	477	320	67
8	Hetauda	1078	1078	426	40
	Total	7495	7495	6040	81

Figure 5: Latest collected retrofit data of Makwanpur district .

Summary of Retrofitting Status	
1 District Name	Makwanpur
2 Total No of Retrofit Beneficiary	12946 out of which 7495 has signed agreement and received first tranche
3 Technically retrofit unfeasible number	862
4 Technically retrofit feasible number	4777 (Remaining has either constructed new building or damaged building)
5 Major Reasons for Technical unfeasibility	Construction of building in different methodology than covered in documents such as: wooden log wall building (कतुरले बारेको), Straw wall(फरालले बारेको), Bamboo wall(बाँसले बारेको) without proper structural system
6	Building is in severely damaged condition such as: Cracks in all walls; Building is in tilting condition with leaning posts, fully collapsed and partially collapse
7	Site has been cleared
8	Foundation of building is not sufficient and is severely damaged
9	landslide and flooding vulnerability
10	
11 Design not covered by existing documents number	319
12 Interested no. of Houseowner in retrofitting	3659
13 not interested no of Houseowner in retrofitting	1841
14 Major reason for not interest	Poor economic condition: Higher cost is required for retrofitting
15	Building is already retrofitted
16	House owner wants to construct a new house instead of retrofitting
17	New building is already constructed by owner
18	Building is in tilting condition, fully damaged
19	Minor repair is done by house owner himself

Figure 6: Status of retrofitting like as technically unfeasible number, feasible number an dits reasons and also major reasons for not interest.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Almost issues have been addressed by NRA and local authorities such as landless issues, road access, MAP register systems etc. In case of Makwanpur they have planning of construction structure them selves. The estimated cost of structure is mostly high in urban areas and shortage of local materials like as aggregate sand etc. In case of block materials used houses, completed their reconstruction after some correction and finally received the all tranches of government reconstruction grant.

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

CCDN have been working in vulnerable reconstruction at Thaha Municipality and Kailash rural Municipality. The progress of vulnerable housings are satisfied results.

Photos



Figure 7: Ward level coordination meeting has been organized at Raksirang Rural Municipality-6 on 21st November, 2019.

अनुगमन दुव

क्र.सं.	माइलस्टोन	२०७५ हात्त सम्मको प्रगती प्रतिशत	२०७६ भर्तिर सम्म प्रगती प्रतिशत	२०७६ पाँच सम्म प्रगती प्रतिशत	२०७६ फागुन सम्म प्रगती प्रतिशत	२०७७ बैशाख सम्म प्रगती प्रतिशत	२०७७ असार सम्म प्रगती प्रतिशत
प्रबलिकरण लाभग्राही							
१	पहिलो किस्ता	१००					
२	दोश्रो किस्ता	०	*	२०	४५	१००	
३	निर्माण सम्पन्न	०	१	१५	४५	१०	१००

(Handwritten signatures and notes are present at the bottom of the table.)

Figure 8: From the ward level coordination meeting, we prepared a reconstruction action plan of Raksirang RM-6,7,8 (Previous Kakda VDC).

Housing Typology Report



Figure 9: House owner; Dev Bahadur Thing, the location of house is Raksirang Rural Municipality-06. He received all tranches of government reconstruction grant. He does not receive the completion certificate because his house modified after the third tranche received. Next 1 floor addition after the 3rd tranche received. But the best practice is to provide all seismic reinforcements, same location of openings, light gable wall and roofs.



Figure 10: House owner; Chatra Bdr. Thing, the location of house is Raksirang Rural Municipality-06. Load bearing structure stone in mud mortar with RCC band (Vertical reinforcement and Horizontal seismic resistant members); used light gable wall and light CGI roof sheet. He received all tranches of government reconstruction grant. The construction cost was around 6 lakh. This house model is copied from design catalogue I. Now, there is small family; 3 members. Sufficient living space so it became true design for small family.



Figure 11: House owner; Suk Maya Thing, the location of house is Raksirang Rural Municipality-06. Load bearing stone in mud mortar with two room; all reinforcement members; light gable wall with light CGI roof sheet. She received the all tranches of government reconstruction grant. The construction cost was around 5.5 lakh.



Figure 12: House owner; Aayt Singh Muktan, the location of house is Raksirang Rural Municipality-06. Load bearing stone in mud mortar. Almost houses constructed with stone in mud mortar so no different typology. The tentative construction cost was around 9 lakh. Now, this house is for totally living purpose, existing house was demolished. He received all tranches of government grant.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
We sent the around 35 nos. of files for third tranche at DLPIU building, now time became around 2 months but HHs could not receive the tranche, when to release the file and receive the tranche?	Ward technicians, ward no. 7	We faced the tranche released problems at district level for some times due to replacement of GMaLI chief but last time it is continuously ongoing. If that is issue in Building we coordinate in DLPIU Building and informed to ward level.

Challenges and Way Forward

Challenge	Way Forward
Implementation of Reconstruction action plan, CS entry and certificate distribution	Coordination is necessary for that work. There are not problem in reconstruction because of it is in final stage insted of some rare issues like as file hold in DIPIU Building, modified of houses etc. Next to necessary publish the grievance registered issues in timely.
Startup retrofit	Before recuirted the masons and mobilization, technicians should convince to the beneficiaries about retrofit and its benefits, required materials, construction cost etc. organize retrofit orientation at tole level according to retrofitting manual, which document was published in 2017.
Annouces the reconstruction complete ward (previous Ward) of Makwanpur district.	Strickly implementation the reconstruction action plan, done CS entry and distribution complete certificate and properly keep record who has not constructed their houses with NRA time line.
