

Makwanpur

4 – 17 January 2019

Summary of events during this period

Name of activity/event	Event date & Venue	Participant Summary		Contact Person	Reference Document
		M	F		
<u>Support to NRA Orientation and Review Workshop on Private Shelters Reconstruction in Chitwan and Nawalparasi Districts</u> Participants: - Hon'ble members of provincial and federal parliaments representing from Chitwan and Nawalparasi. - High level officials from NRA and CLPIUs - Chairs/Mayors, CA Officers and Focal Engineers of local bodies - Chief and Staffs of DLPIU-GMaLI Outcomes: - In-depth interaction on key issues and concerns of private shelter reconstruction done. - Agreement between NRA and Local Bodies on handover of private shelter reconstruction done.	Chitwan: 7 th & 8 th Jan, 2019 Day I: DCC Hall, Bharatpur Day II: Hotel Nawalparasi 9 th & 10 th Jan, 2019 Sitara Resort, Nawalparasi.			teammakwanpur@hrrp.nepal.org	Event participation report available at: https://drive.google.com/drive/u/0/folders/123NC30C558sDgfN-QJ5kxd9BkLoMT928
<u>District General Coordination Meeting:</u> Chaired & Facilitated by: Chief, DCC Participants: M&E Specialist, CLPIU-Building, DSEs, Ward Chair and Ward Secretary, HRRP DCT and local engineers Minute Prepared by: DC, HRRP. Agenda: - Reconstruction progress review - Earthquake Safety Day 2075 - AoB Decisions: Decision 1: Based on the progress updates presented on behalf of DLPIU-GMaLI, it is observed that increase in numbers of first tranche, second tranche and reconstructed started (houses under construction) are 432, 640 and 573 respectively, a nominal progress in reconstruction. However, as the issues and problems related to Grievances, Landlessness and Soft-loan and bank-related other issues have not been properly addressed, the meeting has decided to urge respective authorities/offices to take immediate necessary action to:- - Address all sorts of issues and problems associated with Grievances. - Deal with relevant authorities/level for policy review and/or reform for the resolution of issues of landless/beneficiaries not having land title documents (laalpurja).	10 th January, 2019 2:00PM onwards Chamber of Chief of DCC	24	8	dc.makwanpur@hrrpnepal.org	Meeting Minute available at: https://drive.google.com/drive/u/0/folders/11rd24F3dYrmcg7-bG1oTOmVkrOwVVw3P

Summary of events during this period

c. Organize an interaction meeting with local banks on 21st January, 2019 (7th Magh, 2075) to discuss on and make necessary decisions to resolve issues related to banks and their service delivery. Decision 2: The meeting decided to organize earthquake safety day ceremony at erstwhile DDC Hall (Complex of Chief Minister's Office, Hetauda) at 7:00am on 16th January, 2019 (2nd Magh, 2075) and assign the whole managerial tasks to DLPIU-GMaLI, Makwanpur. Decision 3: The meeting also decided to urge relevant offices to collect from Wards and Municipalities the details of beneficiaries who've not signed PAs, who have received the first tranche of housing grants but not started construction of their houses or left them incomplete.					
Interaction with Partner Organizations: Participants: - DLPIU-GMaLI Chief and staffs - Representatives of Different POs - HRRP District Team - DCC Press coordinator Objectives: - To share latest progress on reconstruction. - To collect details of reconstruction related activities of different POs. Key Activities and Outputs: - Introduction Round conducted to make participants familiar with each other. - Organization-wise sharing conducted to collect detailed information about the activities being carried out by different partner organizations. Agreed to send activity details to DLPIU-GMaLI. - Question-Answer session conducted to discuss on key issues and challenges of reconstruction being faced by different partner organizations.	10th Jan, 2019 8:30AM onwards Hotel Oshin, Hetauda	14	1	dc.makwanpur@hrrpnepal.org	Event Report available at: https://drive.google.com/drive/u/0/folders/123NC30C558sDgfN-QJ5kxd9BkLoMT928
Palika Level Technical Coordination Meeting at Manahari - 6: Chaired by: Mr. Gopi Lal Muktan, Ward Chairperson, Manahari RM Ward No. 6 Participants: Ward Members, DSEs, HRRP Technical Coordinator, Engineers and few beneficiaries. Minute Prepared by: Kauasal Bist, Technical Coordinator, HRRP. Agenda: - Present scenarios of reconstruction, presented by ward engineer. - Final inspection of completed houses, CS entry	14th Jan, 2019 11:00AM onwards Ward Office, Manahari-6	10	3		Meeting Minute available at: https://drive.google.com/drive/u/0/folders/12Uf7vZvxGYgNSQ6-umEvLOCeyk5fX_EZ

Summary of events during this period

and plan to distribute the completion certificate. 3. Non-compliance issues. Decisions: □ The present scenarios of reconstruction is very poor around 80% HHs don't have PA sign due to land less issues. Only 20% HHs signed, among them only few HHs received third tranche. They had constructed their houses before deployed the government engineer. The meeting concluded in agenda one, proper keep the record of housing reconstruction. During meeting we could not see any record of completed HHs and many more. □ The meeting concluded to accomplish final inspection of houses and immediately complete CS Entry. For those whose CS entry has completed would be further processed and coordinated for certification from relevant authority. □ During visit we recommended around 8nos of houses for correction and it will eligible for third tranche. From meeting day, proper supervision of reconstruction for under construction houses and regular supervision for correction.					
<u>Joint Field Monitoring Visit:</u> Joint monitoring visit has been accomplished at Ward No. 6 and 7 of Manahari Rural Municipality. Participants: ☞ DSE, ☞ Local Government, ☞ HRRP DTC, ☞ NRA technicians ☞ Beneficiaries.	14th Jan 2018 9:00AM onwards Manhari Rural Municipality-6	10	3	techcord.makwanpur@hrrpnepal.org	Report & Photos
<u>21st Earthquake Safety Day Celebration:</u> Key Organizer: District Administration Office Co-Organizers: DCC, DLPIUs and HRRP Key Participants: ☞ Chiefs of DCC ☞ Chief Secretary of Provincial Gov't, Province 3 ☞ CDO, ☞ Chiefs of Army and Security Forces ☞ DLPIUs ☞ Chiefs and staffs of different government offices ☞ Journalists and Media . ☞ HRRP ☞ POs. Major Activities: ☞ Presentation from DLPIU-GMaLI. ☞ Distribution of Building Completion Reports to the respective schools ☞ Speech: ▪ Chief Secretary of Province 3 ▪ Chief of DCC ▪ Chief District Officer – vote of thanks and adjourn of the ceremony.	16th Jan, 2019 7:00 AM Old DCC Hall, Hetauda	41	11	dc.makwanpur@hrrpnepal.org	Event Report available on: https://drive.google.com/drive/u/0/folders/123NC30C558sDgfN-QJ5kxd9BkLoMT928


Upcoming Events and Meetings

Name of Event/Activity	Date, Time and Location	Organizer	Contact Person
Interaction with Banks	21 st January, 2018 2:00PM DCC Hall, Hetauda	DRFC/DLPIU-GMaLI and HRRP	dc.makwanpur@hrrpnepal.org
Palika/Ward Meeting & Joint Monitoring Visit	23 rd & 24 th Jan, 2019 Kankada and Khairang of Raksirang RM	DLPIUs and HRRP	techcord.makwanpur@hrrpnepal.org


Tranche Status

Municipality	Bagmati	Bakaiya	Bhimfedi	Hetauda	Indrasarowar	Kailash	M'Gadhi	Manahari	Raksirang	Thaha	Total
Total HHs Surveyed	3454	2384	1056	1636	599	1095	2029	2322	968	1596	17139
Total HHs Eligible	2467	3990	2696	6324	2921	2609	2209	2321	1710	6727	33974
Total HHs Enrolled	1880	2393	2114	5284	2485	2005	1677	1248	1528	6017	26631
First Tranche	1877	2310	2099	4641	2428	2005	1667	1246	1517	6007	25797
Second Tranche	1403	1648	2033	2575	1772	1458	1289	1024	1403	4825	19430
Third Tranche	859	693	1633	2469	1106	1222	858	814	940	3131	13725
Total HH Constructed	610	405	1410	2010	950	1010	655	625	750	2650	11075
Grievance Registered	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
Grievance Addressed	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
RF HH Eligible	1941	1616	929	1881	245	606	1372	1330	537	1178	11635
RF HH Enrolled	532	404	397	1013	167	185	277	494	358	612	4439
RF 1 st Tranche	511	254	383	1013	152	177	277	489	359	612	4227
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	79	334	190	661	49	90	294	489	54	273	2513
Non-Compliance Addressed	71	328	187	635	49	85	286	464	54	248	2407


TRANCHE UPDATES

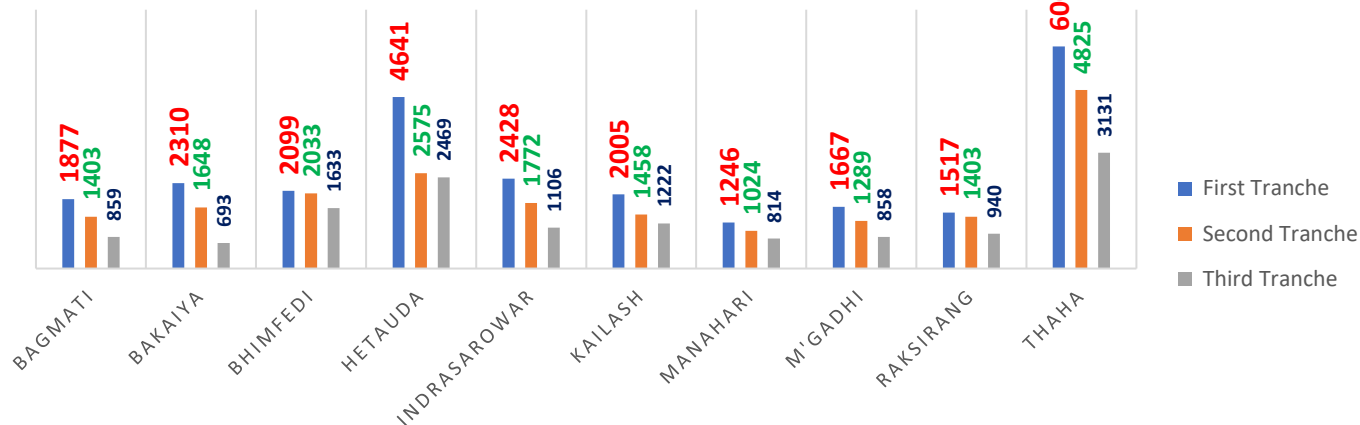

RETROFITTING UPDATES

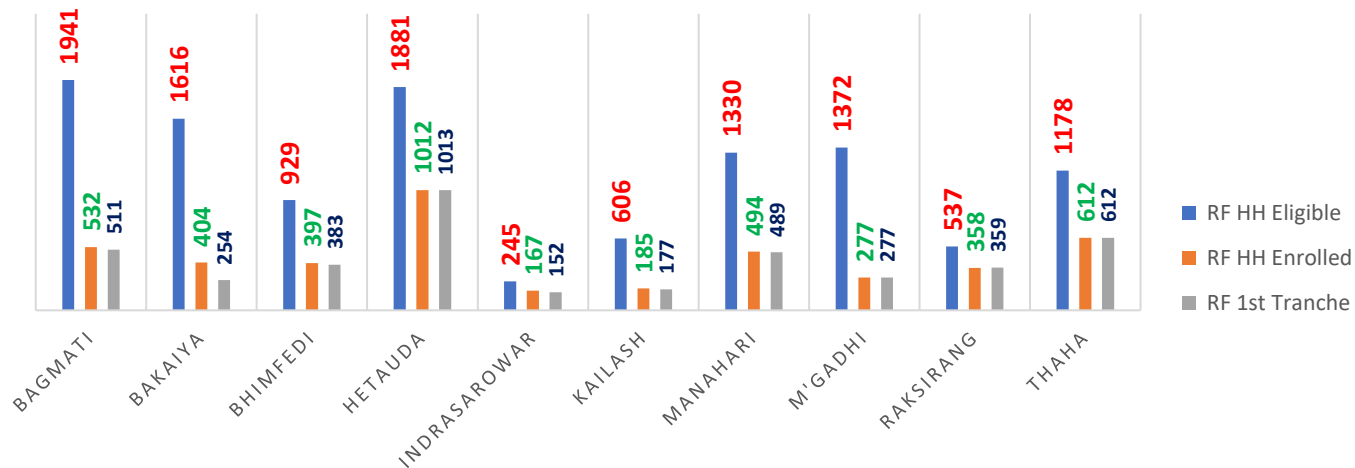

GRIVANCE STATUS

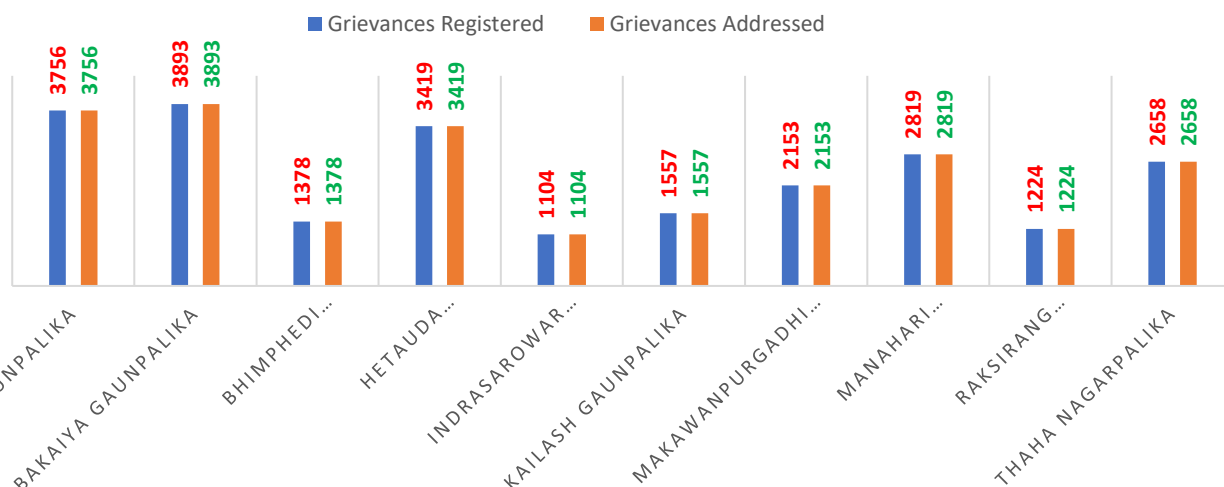

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
14 th Jan, 2019	Manhari Rural Municipality-06 & 07	Joint Monitoring Visit; DSE, local government, ward engineers, beneficiaries and HRRP district technical coordinator.

Objective(s)

- To organize technical coordination meeting and carry out field visit; to collect measure issues, housing typology.
- Promote to early final inspection for completed HHs and CS entry.
- Monitoring to noncompliance issues and recommended for correction.

Summary

We have successfully organized technical coordination meeting in ward level and carried out field visit in ward nos. 6 and 7. During the visit we suggested for correction and to collect construction typology and also to promote finalize the reconstruction work, final inspection and CS entry.

The agendas of meeting were;

- Present scenarios of reconstruction, presented by ward engineer.
- Final inspection of completed houses, CS entry and plan to distribute the completion certificate.
- Non-compliance issues and retrofitting issues.

We briefly discussed in agendas of current status of reconstruction, the following data has been found;

First tranche received HHs	Second tranche received HHs	Third tranche received HHs	Completed HHs	Remarks
520	355	263	300	Previous Manhari VDC

Decision Made of the meeting

- The present scenarios of reconstruction is very poor around 80% HHs don't have PA sign due to land less issues. Only 20% HHs signed, among them only few HHs received third tranche. They had constructed their houses before deployed the government engineer. The meeting concluded in agenda one, proper keep the record of housing reconstruction. During meeting we could not see any record of completed HHs and many more.
- The meeting concluded to accomplish final inspection of houses and immediately complete CS Entry. For those whose CS entry has completed would be further processed and coordinated for certification from relevant authority.
- During visit we recommended around 8nos of houses for correction and it will eligible for third

tranche. From meeting day, proper supervision of reconstruction for under construction houses and regular supervision for correction.

Non-compliance issues and retrofitting issues

In every field visit, we faced retrofitting issues; we could not organize any awareness program about lack of information between retrofitting and repairs. Our technicians don't apply his training skills. They had received 4days training of retrofitting for mud mortar houses before 4month ago but till to the date, we could not see any retrofitting done houses. So, it is vital and serious problem in field. Early it should be solve in field level. We don't have skilled manpower in field for retrofitting. So, quickly organize the OJT type training with including some technicians. For sample, in each rural municipality, it should be happen. From another way, we are far slow in final inspection and CS entry and we couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, in every visit, we delivered the message to technicians done for final inspection, CS entry and distribute the certificate but it couldn't happen rapidly.

During visit also we have collected the different types of construction housing typology. There were almost brick in cement mortar, RCC frame structure, hybrid structure and block houses.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
- Landless issues. - Retrofitting issues and noncompliance issues in self-constructed houses before deployed the technicians. - CS entry and final inspection.	- To organize awareness program about lack of information between retrofitting and repairs. - Required OJT type training with including some technicians in field level. For sample, in each rural municipality, it should be happen. - Refer correction manual. - Landless issues should be addressing by central level and local government as per early. - We couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, should do inspection, CS entry and distribute the completion certificate.	NRA, Local government, Ward technicians	Regular

Photos



Figure 1: Technical coordination meeting has been organized in Manhari Rural Municipality-06; the agendas were present scenarios of reconstruction, final inspection of completed houses, CS entry and plan to distribute the completion certificate, non-compliance issues and AoB.



Figure 2: Manhari Rural Municipality-06, house owner- Khadak Man Sherstha, RCC frame structure, received second tranche and verified for third tranche. Almost houses are constructing with hollow concrete block masonry in Manhari Rural Municipality. In some places of Manhari RM, also RCC frame structure constructed. In this case of house, 12'x12" pillar size provided but he doesn't provide sufficient rod like as 8nos. of rod, after analysis done by DSE, this house was eligible for third tranche.

Housing Typology Report



Figure 3: House owner; Laxmi Adhikari, Manhari Rural Municipality-6, load bearing brick masonry materials used in this house, second tranche received by house owner but for third tranche, required some correction. We can see in plan view, this house look like as L-shaped but in actually in field connected by wall in middle portion, we judged during field visit, 3rooms, used brick materials, all seismic resistant components provided, light roof, strongly truss connected with wall and one storey. We suggested for third tranche after that ward engineer planning to submit the file for third tranche.



Figure 4: House owner; Dul Kumar Rijal, Manhari Rural Municipality-06, Load bearing brick in cement mortar used and 4nos. of rooms with flexible roof. All seismic resistant elements were provided and he received all three tranches of government reconstruction grant. The total tentative cost of this is house is around 15lakh.



Figure 5: House owner; Rajendra Rimal, Manhari Rural Municipality-06, two types of materials used, block masonry and brick in cement mortar. In outer portion brick masonry used and in partition wall, hollow concrete block used, according to house owner. First of all this house had constructed before deployed the government technicians. Now, we could not prove it, how types of material used, provide or does not provided bands. But we believe the house owner and we (DSE) recommended used some correction. Like as wall tightening with horizontal and vertical bands and meet to compliance and strong and finally earthquake resistant structure. Always we suggested to beneficiaries in field level in simple way. In case of this house, we recommended for collection materials like as Gabion wire, chicken wire mesh (kukhure Jali), drill machine, hammer, nail etc. similarly, remove the plaster for existing portion and in every 30cm interval of wall from the some below of GL, create hole by drill machine after put the chicken wire mesh for stronger. In every hole tight by GI wire mesh with Chicken wire mesh. Finally we can do it and make partition wall strong connected with outer portion of vertical post. Sometimes in field level, we said to technicians used jacketing method.



*Figure 6: House owner; Lila Ram Karki, Manhari Rural Municipality-06, RCC frame structure, during joint monitoring, our technicians never carry the engineers tools; like as tape, diary etc. it is a truth. In case of this building. Technicians were conformed for huge opening. But actually in filed we measure the span to span length of pillar and it doesn't exceed 4.5*4.5 (in m). We strongly advised to technicians, sure confidence before work done and finally this house became (eligible) for third tranche.*

Challenges and Way Forward

Challenge	Way Forward
- Landless issues. - Retrofitting issues and noncompliance issues in self-constructed houses before deployed the technicians.	- To organize awareness program about lack of information between retrofitting and repairs. - Required OJT type training with including some technicians in field level. For sample, in each rural municipality, it should be happen. - Refer correction manual. - Landless issues should be addressing by central level and local government as per early.
