

District Report

Kavrepalanchok

15 March – 11 April 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint Monitoring Field Visit to Banepa Nagarpalika	27 & 29 Mar 2019	2	1	reshma@hrrpnepal.org	Field Visit Section below
Joint Monitoring Field Visit to Panchkhal Nagarpalika	28 Mar 2019	2	1	reshma@hrrpnepal.org	Field Visit Section below
Orientation on Hollow Concrete Block Manual	2-5 Apr 2019	136	50	reshma@hrrpnepal.org	Report
Training Database Update	25 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
5W Update	25 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Housing Typology Update	11 Apr 2019	-	-	reshma@hrrpnepal.org	GD
Collection of stories for experiences on reconstruction	10 -12 Apr 2019	-	-	reshma@hrrpnepal.org	GD
Tranche Return Update	11 Apr 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Meal Reporting	4 Apr 2019	-	-	reshma@hrrpnepal.org	GD
Support to GMALI on grievance handling	15 Mar-11 Apr 2019	-	-	reshma@hrrpnepal.org	NA
DLPIU Technical persons Contact List update	25-26 Mar 2019	-	-	reshma@hrrpnepal.org	GD

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Commencement Ceremony of Model Retrofit House at Namobuddha	12 April 2019, 11:00 AM- 3:30 PM, Namobuddha-5	UNOPS	NA
GMALI/HRRP Coordination Meeting	22 April 2019, 11:00 AM, GMALI Hall, Dhulikhel	HRRP	reshma@hrrpnepal.org
Joint Monitoring Field Visit to Temal Gaupalika	17-19 April 2019, 8:00 AM- 5:00 PM, Temal GP	HRRP	reshma@hrrpnepal.org
Joint Monitoring Field Visit to Roshi Gaupalika	26-30 April 2019, 8:00 AM- 5:00 PM, Roshi GP	HRRP	reshma@hrrpnepal.org

Tranche Status


Municipality	Banepa	Bethanchok	Bhumlu	ChauriDeurali	Dhulikhel	KhaniKhola	Mahabharat	MandanDeupur	NamoBuddha	Panchkhal	Panauti	Roshi	Temal
Total HHs Surveyed	-	-	-	-	-	-	-	-	-	-	-	-	-
Total HHs Eligible	7078	4377	6206	6412	5995	2846	2951	9221	7637	9948	9188	6374	4848
Total HHs Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
1 st Tranche	6371	3775	5842	5558	5233	2740	2875	8531	6324	8978	8108	5480	4176
2 nd Tranche	3260	2893	4932	4224	2914	2238	2420	6897	3494	6383	4646	4162	3118
3 rd Tranche	2341	1666	3919	2359	1843	842	1501	4515	2101	4011	2836	2447	1852
Total HH Constructed	-	-	-	-	-	-	-	-	-	-	-	-	-
Grievance Registered	2226	1202	1038	1578	2151	683	1075	2300	2814	3041	2874	2257	2101
Grievance Addressed	2031	1202	971	1517	1919	681	1055	1762	2296	2932	2851	2203	2069
RF HH Eligible	-	-	-	-	-	-	-	-	-	-	-	-	-
RF HH Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
RF 1 st Tranche	77	73	14	46	40	43	143	25	20	110	128	129	106
RF 2 nd Tranche	2	0	1	0	0	0	0	0	0	14	0	0	2
Non-Compliance Registered	-	-	-	-	-	-	-	-	-	-	-	-	-
Non-Compliance Addressed	-	-	-	-	-	-	-	-	-	-	-	-	-

Tranche Status

Reconstruction Tranche Status (10 April 2019)

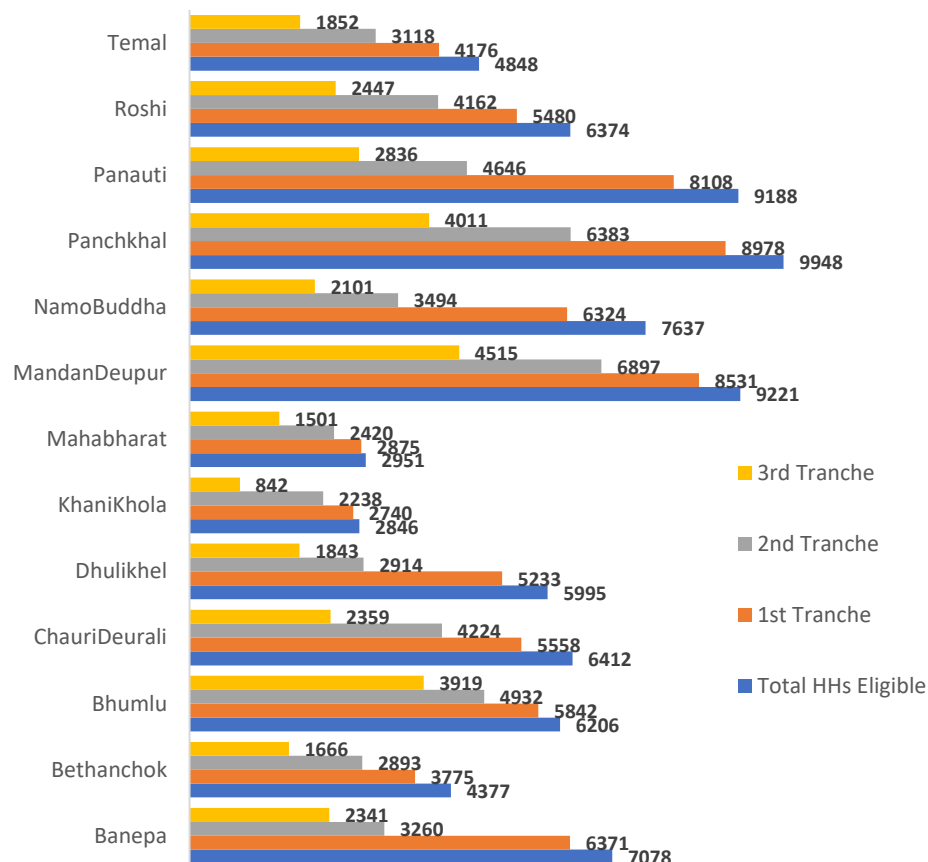

Grievance Addressal Status (10 April 2019)

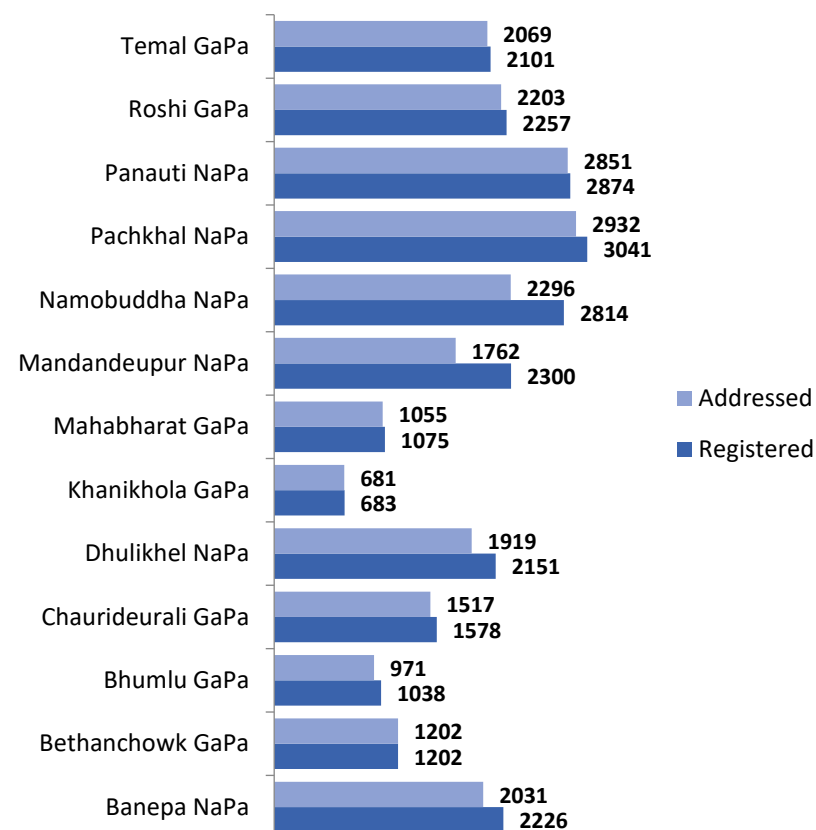

Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders																																													
27 & 29 March 2019	Banepa 2,3,5,6,7,8,9,10,11	• Roshan Kesari, M&E DLPIU • Arun Adhikari, DLPIU MIS Officer • Reshma Shrestha, HRRP																																													
Objective(s)	• Conduct Ward level meetings • Update the reconstruction progress at ward levels • Orient technical persons on third inspection and completion certificate • Orient technical persons on MIS and CS Entry																																														
Summary	During the field visit, Ward no 2, 3, 5, 6, 7, 8, 9, 10 and 11 were visited. Ward level coordination meeting was conducted in wards 2, 9, 10 and 11 whereas orientation to technical persons on third inspection and CS Entry was conducted in wards 2, 3, 5, 6, 7, 8, 9, 10 and 11. Also all the ward chiefs were requested to support data collection and verification of houses constructed immediately after the earthquake and before the mobilization of technical persons. The reconstruction progress of the wards is: <table><tr><th>Ward</th><th>Total Beneficiary</th><th>First Tranche</th><th>Second Tranche</th><th>Third Tranche</th></tr><tr><td>2</td><td>580</td><td>535</td><td>318</td><td>260</td></tr><tr><td>3</td><td>-</td><td>570</td><td>370</td><td>316</td></tr><tr><td>5</td><td>288</td><td>237</td><td>73</td><td>60</td></tr><tr><td>6</td><td>356</td><td>356</td><td>233</td><td>171</td></tr><tr><td>7</td><td>193</td><td>193</td><td>82</td><td>60</td></tr><tr><td>8</td><td>207</td><td>207</td><td>25</td><td>25</td></tr><tr><td>9</td><td>355</td><td>222</td><td>70</td><td>65</td></tr><tr><td>10,11</td><td>745</td><td>732</td><td>352</td><td>283</td></tr></table>		Ward	Total Beneficiary	First Tranche	Second Tranche	Third Tranche	2	580	535	318	260	3	-	570	370	316	5	288	237	73	60	6	356	356	233	171	7	193	193	82	60	8	207	207	25	25	9	355	222	70	65	10,11	745	732	352	283
	Ward	Total Beneficiary	First Tranche	Second Tranche	Third Tranche																																										
	2	580	535	318	260																																										
	3	-	570	370	316																																										
	5	288	237	73	60																																										
	6	356	356	233	171																																										
	7	193	193	82	60																																										
	8	207	207	25	25																																										
	9	355	222	70	65																																										
	10,11	745	732	352	283																																										
The common points discussed in the meeting were: ▪ Delay in tranche release and files missing at DLPIUs. ▪ Non-compliance cases; most of them constructed immediately after earthquake and difficulty in encouraging the beneficiaries to carry on the correction measures as suggested by DSE. ▪ Very slow rate of reconstruction in the core areas. ▪ Very high rate of migration from different palikas of the district in all the wards.																																															

Photos



Tanka Prasad Gautam of Banepa-2 recently received the first tranche after being listed as a beneficiary from the latest grievance addressal. Though unsure about him being listed as a beneficiary, he took the advantage of technical persons at his ward and under their continuous guidance reconstructed his house in a total worth of NPRs. 47 lakhs.
Photograph By: Reshma Shrestha



These houses belong to two families at Banepa-6 who wanted to construct adjoined house with combined column and beams. Taking the technical advice from the ward engineer, they re-casted the formwork separately and built two different structures. As the site is a slope land, the families were suggested to construct a retaining wall and leave some space from the wall which the families ignored. As the inspection for the second tranche was halted by the engineers, the house owners are now stabilizing the slope

for construction of retaining wall.
Photograph By: Reshma Shrestha

Field Visit Report

Visit 2

Date	Location	Participants from HRRP and stakeholders
28 March 2019	Ward 2, 3, 4, 5, 7 Panchkhal Nagarpalika	• Roshan Kesari, M&E DLPIU • Arun Adhikari, DLPIU MIS Officer • Reshma Shrestha, HRRP

Objective(s)

- Conduct ward level meetings
- Update the reconstruction progress at ward levels
- Orient technical persons on third inspection and completion certificate
- Orient technical persons on MIS and CS Entry

Summary

During the field visit, ward 2, 3, 4, 5 and 7 were visited. Ward level meeting was conducted in ward 5 whereas an orientation on third inspection and CS entry was conducted in all the wards to the technical persons. The main points from the coordination meeting at ward 5 were:

- 50 new grievances have been filed. Request was made to the ward chief to ask the beneficiaries who had already done reverification earlier to go through the appellate process rather than filing new grievances.
- There are about 25 land issues at a settlement Ryale where the beneficiaries do not want to resettle in new areas. The recent minute of NRA meeting regarding land issues was shared with the ward chief.
- A record of 5 houses constructing houses before the mobilization of technical persons has been prepared which will be sent to the DLPIU shortly.

Photos



Ram Bahadur Tamang of Panchkhal-7 has received all three tranches of housing reconstruction grant. He constructed his house at the peak hour of reconstruction, so had much difficulty in availing the masons. The reconstruction of his house had to be halted for more than four months as the masons had contracted many other houses.
Photograph By: Reshma Shrestha



Radhika Thapa of Panchkhal-7 has received all three tranches of housing reconstruction grant. As the house has no roof band and properly connected roof, the house needs some correction before the third inspection. The house owner whereas had no idea about the third inspection and completion certificate.
Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Banepa-2

Building Typology: RCC

Description: Laxmi Tamangni has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Banepa-11

Building Typology: Brick in Cement

Description: This house of Ramesh Deuja earlier was an L shaped house and non-compliant for further tranches. As per the suggestions from ward engineer, the house owner constructed a wall and connected the house as a rectangular structure. The house now has been inspected for the third tranche.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Panchkhal-2

Building Typology: RCC

Description: This house belongs to two beneficiaries, father and son both of who have received second tranche. As there is only one main door and one staircase, the engineers have not inspected the house for the third tranche.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Panchkhal-7

Building Typology: Brick in Cement

Description: Gore Thapa has received the third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Panchkhal-2

Building Typology: RCC

Description: Indira Adhikari has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Banepa-7

Building Typology: RCC

Description: This house has received all three tranches of housing reconstruction grant after submitting the structural analysis report.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Banepa-6

Building Typology: RCC

Description: Sarita Sapkota has received third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Banepa-6

Building Typology: RCC

Description: Purushottam Sapkota has received the third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha
