

District Report

Nuwakot

4 – 17 January 2019

Summary of events during this period					
Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Attend the planning meeting to celebrated Earthquake Safety Day in Nuwakot. Uddab Bahadur Thapa DAO has chaired the meeting different government and Non-government representatives were presented in the meeting.	9 January , 2019			dc.nuwakot@hrrpnepal.org	
Field visit and ward level meeting in Likhu-1, Khanigau	9 January , 2019	4	2	dc.nuwakot@hrrpnepal.org	See Detail in field visit Section
Field visit and ward level meeting in Likhu-3, Suryamati	10 January , 2019	5	0	dc.nuwakot@hrrpnepal.org	See Detail in field visit Section
Participate in construction Starting Ceremony: 18 relocated hh from Kispang RM has started their building in Bidur-9, Japhati. Oxfam is supported for the construction and Sahayata Samajik Sanstha has implementing the construction. Santaman Tamang Chair of DCC, Nuwakot and Sanju Pandit Mayor of Bidur Municipality has jointly started the construction project.	10 January , 2019			dc.nuwakot@hrrpnepal.org	Photos
Participate in 21 st Earthquake Safety Day in 16 January. Rally has organized from Dhunge to Battar. Redcross, Oxfam, NSET and other organization have participated from NGO side and different GOs and Nepal army, APF has participated in Rally.	16 January			dc.nuwakot@hrrpnepal.org	Report
Communicating and working with POS for 5W and training database update				im.nuwakot@hrrpnepal.org	

Summary of events during this period

Uploaded training database on EHRP PMIS system				im.nuwakot@hrrpnepal.org	
--	--	--	--	--	--

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Level Coordination Meeting		HRRP Nuwakot	dc.nuwakot@hrrpnepal.org /im.nuwakot@hrrpnepal.org


Tranche Status

Rural /Municipality	Belkotgadhi NP	Bidur NP	Dupcheshwor RM	Kakani RM	Kispang RM	Likhu RM	Meghang RM	Panchkanya RM	Shivapuri RM	Suryagdhi RM	Tadi RM	Tarkeshwaor Rm
Total HHs Surveyed	9409	11203	5448	6157	1816	4003	4052	3692	5616	4197	4231	3760
Total HHs Eligible	11036	12667	5873	6916	2369	5107	4500	4226	6513	5019	4604	4353
Total HHs Enrolled	11278	12544	5911	6918	2375	5164	4471	4178	6604	5186	4646	4156
First Tranche	9651	11316	5486	6159	4164	4060	4023	3843	5707	4364	4413	3772
Second Tranche	8560	10329	5206	5397	3900	3652	3844	3622	4988	4008	4136	3531
Third Tranche	300	4250	3069	2733	2362	1987	2847	1930	2725	1754	2249	2359
Total HH Constructed												
Grievance Registered	2271	1693	425	1389	809	1329	511	910	995	923	701	672
Grievance Addressed	1627	1464	425	759	553	1104	448	534	897	822	373	593
RF HH Eligible	256	236	35	160	25	154	141	88	63	16	23	247
RF HH Enrolled		18	1	44		9		18	1	44		9
RF 1 st Tranche		18	1	44		9		18	1	44		9


as of 1st Dec 2018.

Source : GMALI Nuwakot

Graph of Tranche Status:

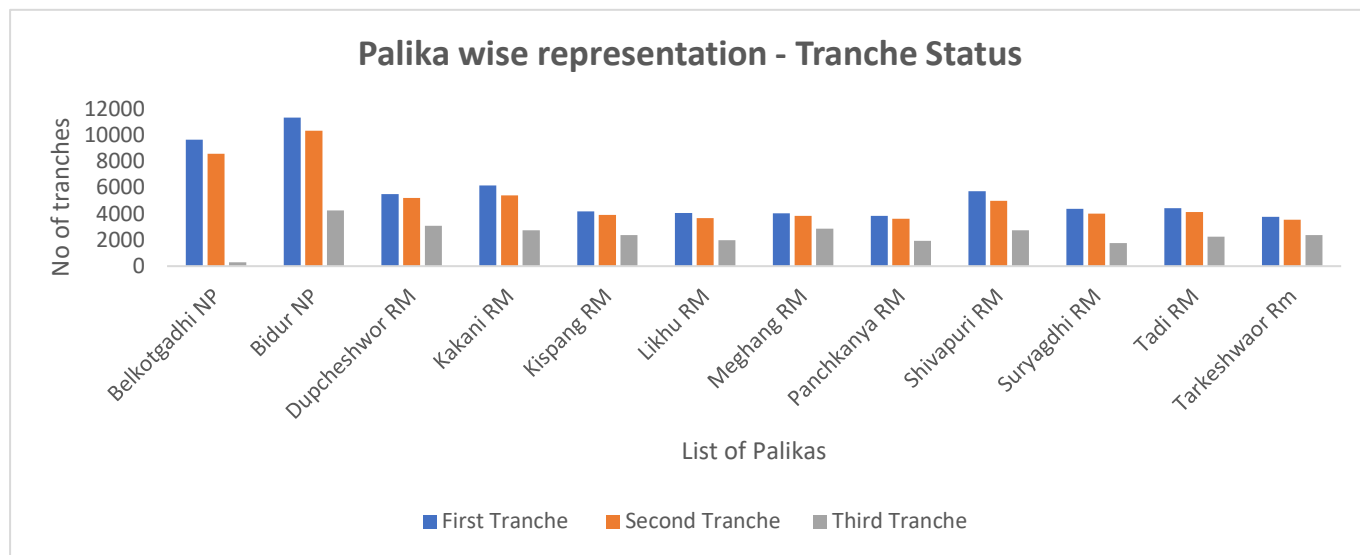

Graph for Grievance Status:

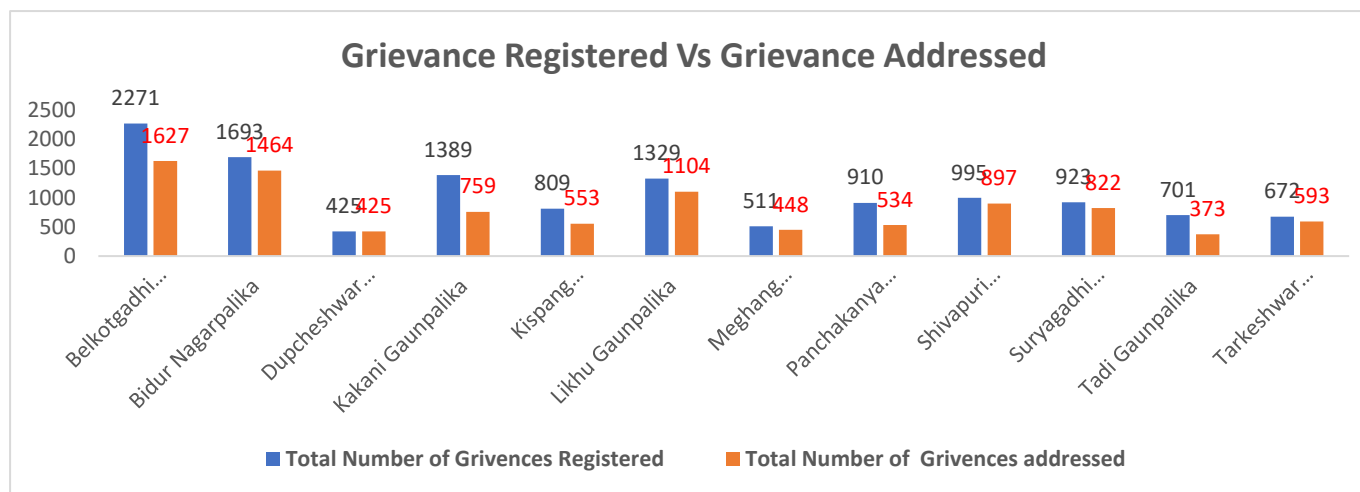

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Visit 1			
Date	Location	Participants from HRRP and stakeholders	
9 Jan, 2019	Likhu-1, Khanigaun	• Badri Pyakurel, DC HRRP • Pravuram Pokharel, DLPIU M&E Expert	
Objective(s)	• Objective 1: Joint Monitoring to assist on technical problem identification and Solution • Objective 2: To know the reconstruction trend and highlighting the issues related to grant • Objective 3: To understand the field challenges and best practice		
Summary	Likhu Gaupalika Ward on 1, is some parts of Khanigau. Kanigau VDC has divided into two wards of Likhu 1 and 2. Likhu 1 has former 1,2,3,4 and 8 wards of khanigau VDCs. It has 575 beneficiaries and 91 has settled from grievances in 1 st lot. There are not so many issue on reconstruction though some noncompliance issues are found in road level settlement. Most of the hilly settlement has used mud mortar construction. Some of them have used brick and cement in hilly area as well. As per the saying from ward chair during the ward level meeting they have controlled the one room construction in place of noncompliance issue. The team found that one room construction has controlled to the local levels. This would be the positive learning to other places as well.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Transportation of reconstruction Materials	promote to use locally available materials	POs, Ward offices	Regular
Quality of reconstruction materials	Quality assurance to local supplier	DCC, Rural Municipality	Regular
Social Issues			
Technical Issues on retrofitting, Vulnerable groups support			
Photos			
			
House Owner: Govinda Dhungana, 2 nd tranche received before one year. Owner claimed that his costruction has halted due to the lack of water, this seems not believable. We can see many such construction in rural level.		Meeting with Narahari Pandey , Ward Chair of Likhu-1, Khanigau. We found that he is supportive to reconstruction engineers and issues as well.	

Visit 2:		
Date	Location	Participants from HRRP and stakeholders
10 Jan, 2019	Likhu-3, suryamati	• Badri Pyakurel, DC HRRP • Pravuram Pokharel, DLPIU M&E Expert • Bola Prasad Sedhai, Ward Chair.
Objective(s)	• Objective 1: Joint Monitoring to assist on technical problem identification and Solution • Objective 2: To know the reconstruction trend and highlighting the issues related to grant • Objective 3: To understand the field challenges and best practice	
Summary	Likhu-3, is made from former Suryamati VDC. Most of its parts are not facilitate from transportation facility. As per saying of DLPIU Engineers, it is hard to travel to most of the places. We faced such travelling problem in different places as comparative to other wards of the palika. The Wards has 1131 beneficiaries. 800 was from the first survey and others are added from different grievances addresses. As per the ward record 12 among 44 beneficiaries from retrofit came to change in full beneficiaries. These files are forwarded to GMALI to change the beneficiaries' status. We found that one roomed construction has no barrier so majority of the construction are one roomed.	
		
Field visit team in Likhu RM ward no 3, Suryamati. Ward chair Bhola Raj Sedhai, Ward members, DLPIU Engineers, HRRP DC and Beneficiaries.		
Field visit team in Likhu RM ward no 3, Suryamati. Ward chair Bhola Raj Sedhai, Ward members, DLPIU Engineers, HRRP DC and Beneficiaries.		People are constructing house in isolated place but not staying there. We can see most of the case to receive government tranche.
		
		

Many rural construction has attracted to Brick Mortar Cement (BMC). People has belief that local construction materials are weaker than BMC.

DCC Chair Santa Man Tamang and Bidur mayor Sanju Pandit have started construction. 18 beneficiaries from kispang-1, Bhalche has relocated to Bidur-9, Japhati. Oxfam has supported them for the construction.

Housing Typology Report



House Owner: Kul Prasad Lamichhane
This House is constructed before the Earthquake. AS per the technical point of view the house is not safe due to lack of bands and other MRT. People are staying here.

Photo: Badri Pyakurel




House Owner: Namaraj Pandey
Location: Likhu-1, Dhikure
Tranche Status: 2nd tranche received (Non Compliance, File sent to DSE)
Typology: BMC

Photo: Badri Pyakurel



House Owner: Hit Bahadur Basnet
Location: Likhu-1, Khanigaun
Tranche Status: Third tranche received
Typology: Brick Mortar Cement (BMC)

Photo: Badri Pyakurel

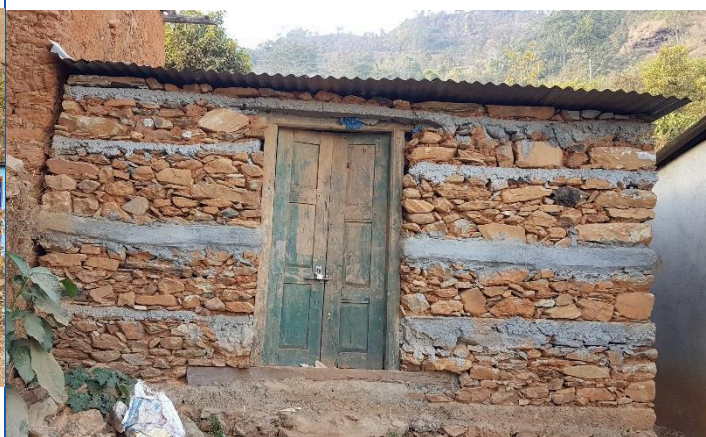

House Owner: Durga Bahadur Bogati
Location: Likhu-1, Khanigaun
Tranche Status: third tranche received
Typology: Stone Mud Mortar (SMM)

Photo: Badri Pyakurel



House Owner: Padam Kumari Kuwar (Ultra Poor)
Location: Likhu-1, Khanigaun
Tranche Status: Inspected for 2nd tranche
Typology: Stone Mud Mortar (SMM)

Photo: Badri Pyakurel



House Owner: Ishwar Kuwar
Location: Likhu-1, Khanigaun
Tranche Status: Received 3rd tranche
Typology: Brick Mortar Cement (BMC) (Left)

(People have not demolished the old house which may vulnerable for next disaster)

Photo: Badri Pyakurel



House Owner: Thakur Prasad Neupane
Location: Likhu-3, Suryamati
Tranche Status: Inspected for 3rd tranche (Fail from DSE)
Typology: Brick Mortar Cement (BMC)

Photo: Badri Pyakurel



House Owner: Kul Bahadur Rai
Location: Likhu-3, Suryamati
Tranche Status: 3rd Tranche Received
Typology: Brick Mortar Cement (BMC)

Photo: Badri Pyakurel

Challenges and Way Forward

Challenge

Lack of technical assistance in the hard to reach field area. NRA engineers are not in regular monitoring to the house. When they visited for the inspection, they only commented for non-compliance.

Delayed and partial addressing of grievance. Real victim from the earthquake has not addressed as beneficiaries. They have applied for grievance many times but not addressed.

Way Forward

MOUD-DLPIU should monitor the engineer and instruction for regular visit.

NRAs should address as soon as possible by the help of local elected persons, Like ward chair and other members.

Challenges and Way Forward

When will retrofit start? People don't have trained manpower for the retrofit, they are waiting the response from NRA side.

Training and other technical issue with proper communication to the common people should be done before monsoon starts.
