

Monthly District Report

Makwanpur, Chitwan, Nawalpur, Parasi

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	District Facilitation and Coordination Meeting	15 th May 2019	DCC Hall, Makwanpur, Hetauda Sub-Metropolitan	Kausal Bist Sachin Malego	Weblink Meeting Minutes
	Technical Coordination Meeting in Palika level and Joint Field Monitoring Visit;	20 th May 2019	Kailash Rural municipality	Kausal Bist Sachin Malego	Field Report and Photo available below
	Technical Coordination Meeting in Ward level and Joint Field Monitoring Visit;	21 th May 2019	Thaha Municipality-07	Kausal Bist Sachin Malego	Meeting Minute Thaha Municipality-07 click here...
	Technical Interaction with local government, and beneficiaries; Carried out Joint Field Monitoring Visit;	22 th May 2019	Makwanpurgadhi-08	Kausal Bist Sachin Malego	Field Report and Photo available below
	Technical Interaction with local government, and beneficiaries; Carried out Joint Field Monitoring Visit;	23 th May 2019	Hetauda Sub-Metropolitan	Kausal Bist Sachin Malego	Field Report and Photo available below
	Meeting Event Details uploaded to Google Calendar and website	17 th May 2019		Kausal Bist Sachin Malego	
	Skype Orientation provided to DCT's on website upload and Google Calendar update	20 th May 2019		Kausal Bist Sachin Malego	
	5W data segregation according to PO's completed	21 st May 2019		Kausal Bist Sachin Malego	
	Listed names of POs whose data needed to be verified	29 th May 2019		Kausal Bist Sachin Malego	
	Support to GMAI Chief of Makwanpur regarding preparation of POs activity list and details.	29 th May 2019		Kausal Bist Sachin Malego	Support Files
	Update Palika Profile data of Makwanpur	7 th June 2019		Kausal Bist Sachin Malego	Palika Profile Data
Chitwan	Coordination for district facilitation and Coordination Meeting	12 th May, 2019			Currently it is not required for district;
	Coordination for district facilitation and Coordination Meeting in Nawalparsi	13 th May, 2019			Regularly happening at the end of month but in this month it has not done.

Summary of events during this period

Nawalpur	Update Palika Profile data of Nawalpur	12 th June 2019		Kausal Bist Sachin Malego	Palika Profile Data
Parasi	Update Palika Profile data of Nawalpur	12 th June 2019		Kausal Bist Sachin Malego	Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation and Coordination Meeting	Tentative 19 th June, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLI/HRRP	makwanpur@hrrpnepal.org
Technical Coordination Meeting in Ward level and Joint Field Monitoring Visit Participants: M&E Specialist, DSE, HRRP team, Ward representatives, local technicians and Beneficiaries.	25 th to 27 th June, 2019; Hetauda Sub M. and Makwanpur Gadhi Rural Municipality	Joint Monitoring Team	makwanpur@hrrpnepal.org
Technical Coordination Meeting in Palika level and Joint Field Monitoring Visit	2 nd to 3 rd July, 2019; Kalika Municipality and IchhaKamana Rural Municipality	Joint Monitoring Team	chitwan@hrrpnepal.org
Technical Coordination Meeting in Palika level and Joint Field Monitoring Visit	4 th to 4 th July, 2019; Nawalparasi	Joint Monitoring Team	nawalparasi@hrrpnepal.org
District Facilitation and Coordination Meeting	Tentative not fixed yet; Naawalparasi	DCC/GMaLI/HRRP	nawalparasi@hrrpnepal.org

News & Updates

Retrofitting issues which become a vital problem in the district of Makwanpur but now UNOPS/Build Change started the retrofitting demonstration/model houses in different palikas of district and also we have encourage to beneficiaries for retrofitting; for this purpose, we have conducted orientation program and decision made at Thaha Municipality-07 previous Agra VDC.


[Meeting Minute Thaha Municipality-07 click here....](#)

Tranche Status (Makwanpur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2226	2226	1510	945	2176	1137	1125	0
Bakaiya Gaunpalika	8593	4017	2643	2599	1787	864	1960	691	565	0
Bhimphedi Gaunpalika	5236	2698	2213	2195	1821	1605	932	591	578	0
Hetauda Upamahanagarpalika	32696	6363	5302	4684	2722	2260	2024	1055	1055	0
Indrasarowar Gaunpalika	3726	2923	2562	2548	1930	1243	254	174	161	0
Kailash Gaunpalika	4737	2613	2112	1483	1177	886	731	324	320	0
Makawanpurgadhi Gaunpalika	5516	2216	1788	1763	1263	963	1437	746	746	0
Manahari Gaunpalika	8841	2337	1274	1274	1021	870	1487	622	622	0
Raksirang Gaunpalika	5091	1711	1547	1547	1415	1043	576	431	431	0
Thaha Nagarpalika	10519	6919	6072	5319	4044	2743	1369	655	651	0

Graph of Tranche Status:

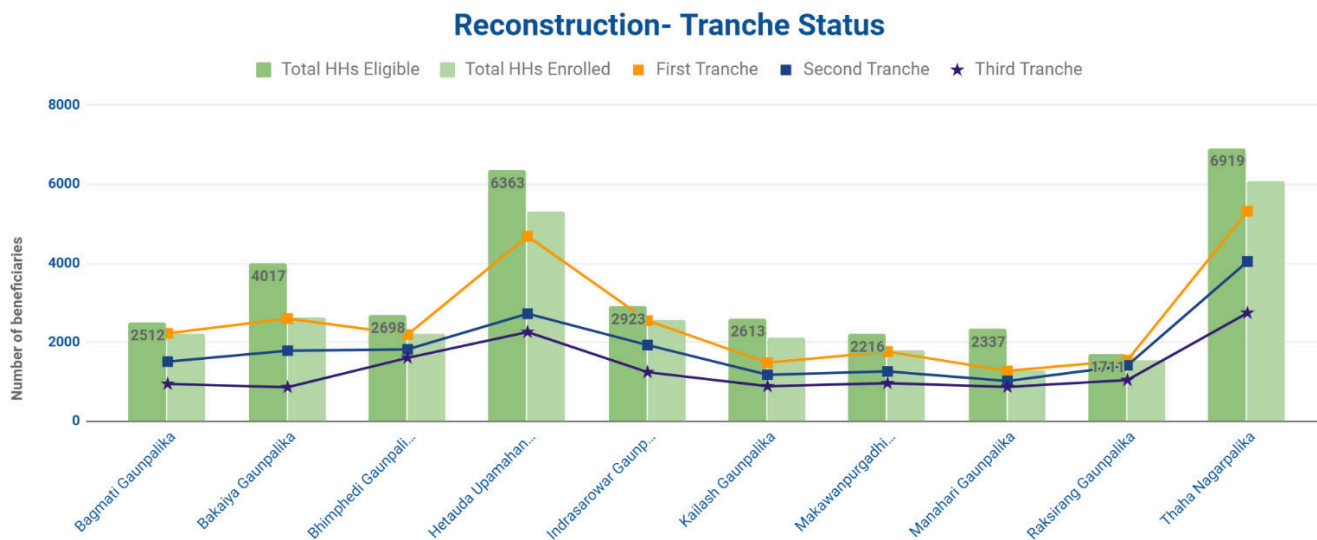

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

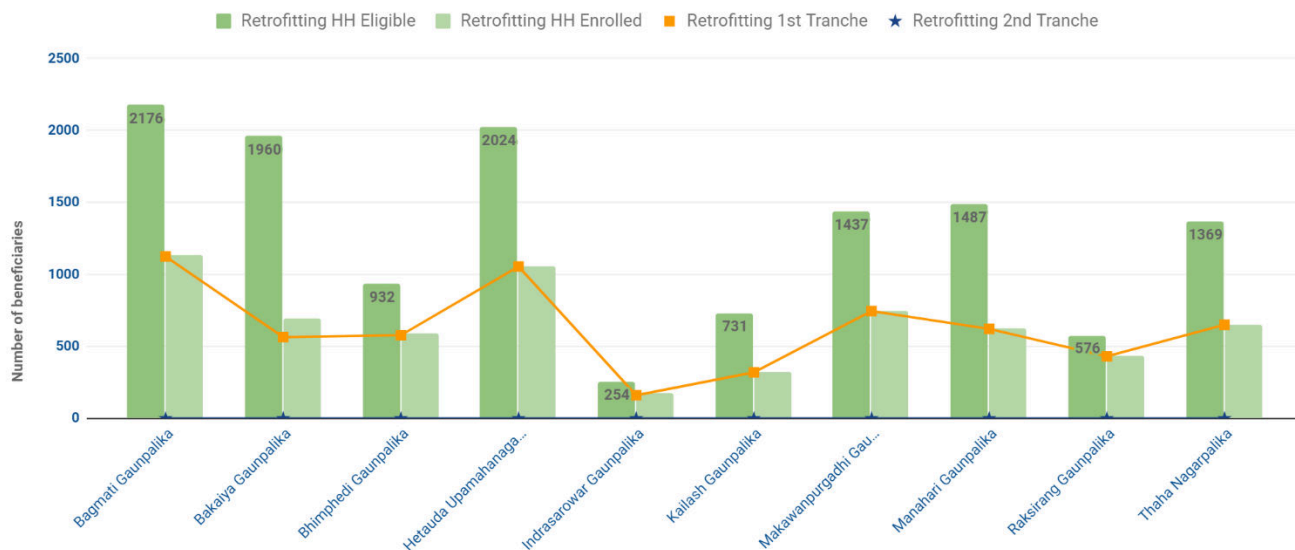


Tranche Status (Chitwan)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarpalika	2087	710	655	655	156	61	38	9	9	0
Ichchhyakamana Gaunpalika	3571	2353	2043	2043	1724	815	248	196	196	0
Kalika Nagarpalika	2565	916	611	611	341	97	42	27	27	0
Khairahani Nagarpalika	1566	559	523	523	237	178	4	4	4	0
Madi Nagarpalika	123	23	23	23	19	15	15	13	13	0
Rapti Nagarpalika	3594	2043	1266	1266	676	278	71	18	18	0
Ratnanagar Nagarpalika	1763	731	650	650	396	334	175	164	164	0


Graph of Tranche Status:

Reconstruction- Tranche Status

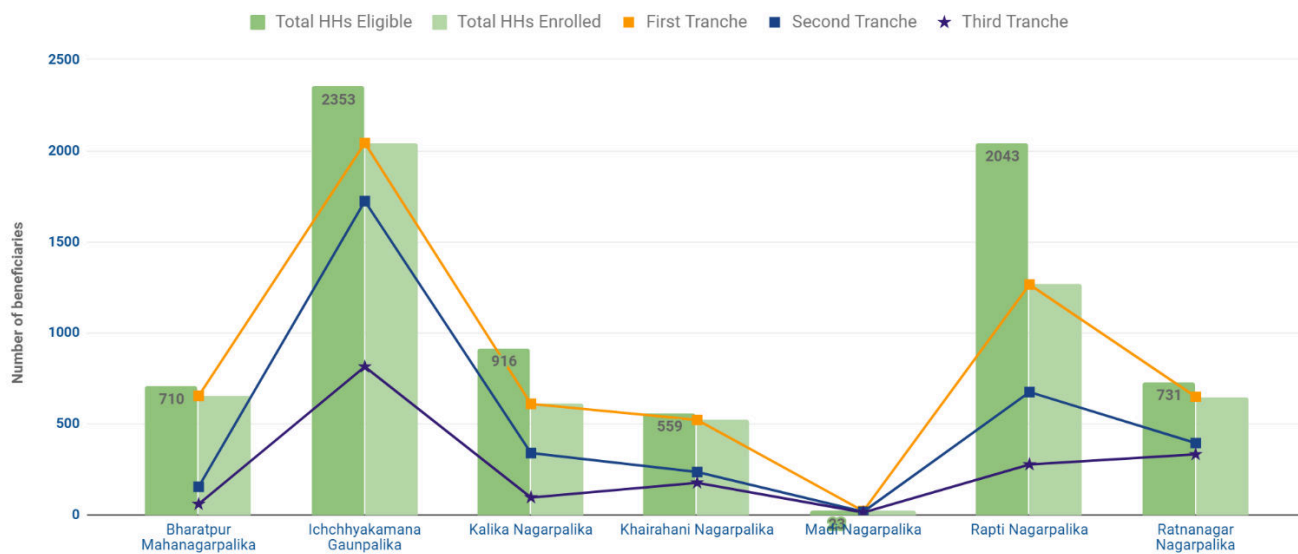

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

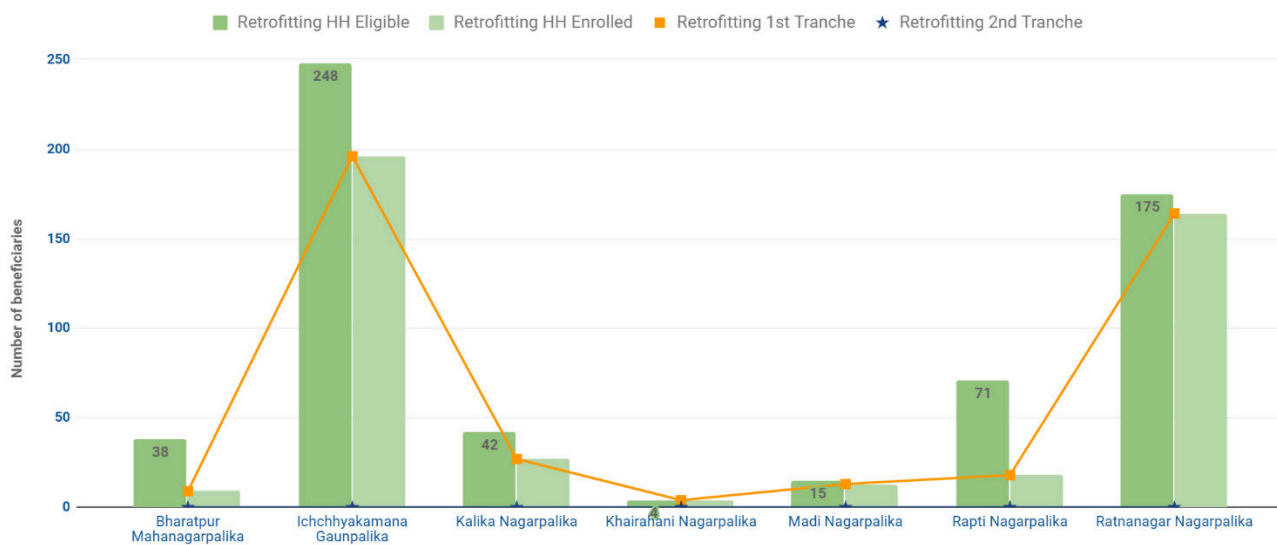


Tranche Status (Nawalparasi)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	3	2	0			
Binayee Tribeni Gaunpalika	70	66	65	65	58	50	2			
Bulingtar Gaunpalika	280	260	260	260	233	182	5			
Bungdikali Gaunpalika	133	72	72	72	67	59	1			
Devchuli Nagarpalika	177	177	177	177	171	116	1			
Gaidakot Nagarpalika	103	49	49	49	41	31	0			
Hupsekot Gaunpalika	155	139	139	139	127	92	2			
Kawasoti Nagarpalika	4	4	4	4	3	2	0			
Madhyabindu Nagarpalika	41	85	85	85	76	56	3			
Palhi Nandan Gaunpalika	1	4	4	4	3	3	0			
Pratappur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	3	3	0	0	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	1	1	0			


Graph of Tranche Status:

Reconstruction- Tranche Status

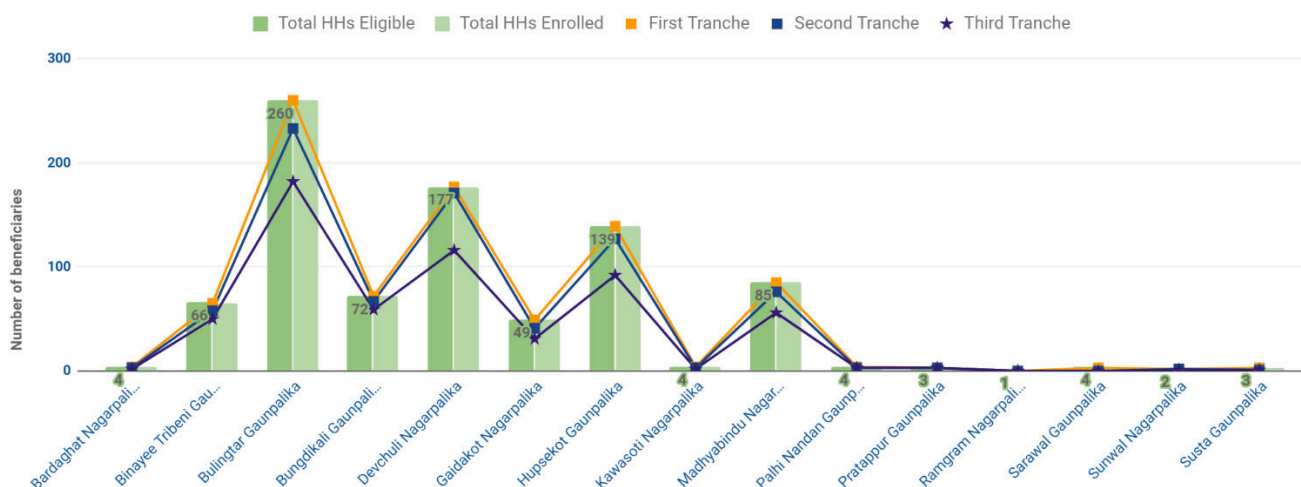

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

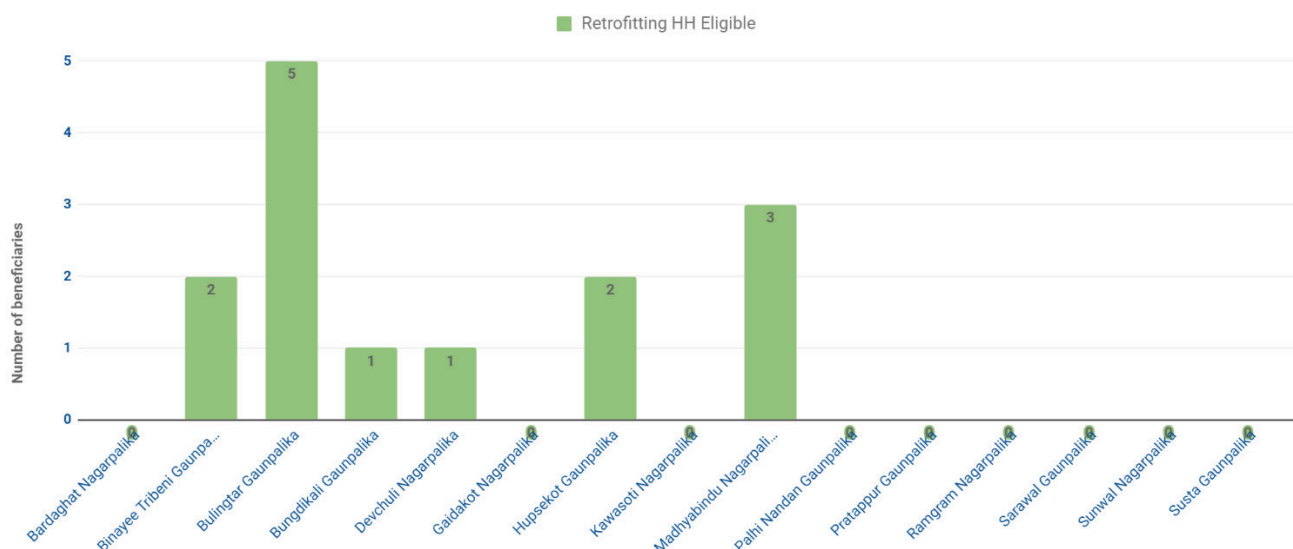

Field Visit Reports (Makwanpur)

Visit 1

Date	Location	Participants
20 th May, 2019	Kailash Rural Municipality, Makwanpur	M&E CLPIU specialist, District Support Engineer, HRRP, Local Government, Ward Technicians and Beneficiaries.
Objective(s)	- To organize technical coordination meeting in palika level and also interaction with technical persons, beneficiaries etc. - To carryout field visit and collect to housing typology in KOBO application, find out the major issues and solve the problems.	

Why was the visit carried out in this location?

- To know the status of reconstruction as well as CS entry, final inspection done or not and status of certificate distribution.
- To know the status of resurvey and re-verification & how is it conducting in wards.
- Promote to start up retrofitting houses.
- Solve the technical problems and suggest feedback for noncompliance issues and recommendation for measures and also collected if any major issues.

Summary

Field Visit:

Joint Monitoring team organized the technical coordination meeting in the palika office with present of local government, ward technicians and some beneficiaries. We found out, the reconstruction progress is rapidly increased but in similar way, we could not found out that, there is not starting of retrofitting. It is a vital problem in the district. And we have tried to start the retrofitting in their respective areas but they do not have convince in economically, available materials, manpower etc. In the wards there is little submitting the grievance. Still engineer is continuing working in this task. No any major issues in these wards of palika. Around 15nos. of noncompliance issues have already solved.

The latest reconstruction data as given below in tabular form;

1st tranche received HHs	Verified for 2nd tranche HHs	Received 2nd HHs	Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
2097	1835	1800	1478	1456	1375	

Challenges / Issues Identified	Solutions Provided	Responsible	Timeframe
CS entry, final inspection and distribution completion certificate with proper recorded.	- Now, for incentive; the weightage of CS entry is more so it should be complete to all inspections form with in Ashad Masant. - After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.	For CS entry; ward technicians Plan for completion certificate distribution; Local government and ward technicians and joint monitoring team.	Ashad Masant, Bhadra Msant and regular
Retrofitting Methodology and its implementation	Now UNOPS/Build Change is constructing demonstration at every palikas of Makwanpur district with involving of ward technicians so that we start a retrofitting with different option methodology of retrofitting.	For retrofitting ward technicians, joint monitoring team for coordination local government and beneficiaries.	Regular

Photos



Figure 1: Technical coordination meeting has been organized in Kailash Rural Municipality. There were around 15nos. of participants in the meeting.



Figure 2: Kailash Rural Municipality-03, Makwanpur; house owner Khel Bdr Praja; there are almost houses constructed with local materials such as stone, mud and wood. House owner received all tranches of government reconstruction grant. Almost houses completed with compliance in ward no 03, also in overall wards of Kailash Rural Municipality. It is good message to us. But we could not start the retrofitting. Hope it will be ahead.

Visit 2:

Date	Location	Participants
21th May, 2019	Thaha Municipality-07, Previous Agra VDC.	M&E CLPIU specialist, District Support Engineer, HRRP, Local Government, Ward Technicians, Build Change Representative and Beneficiaries.

Objective(s)	- To organize technical coordination meeting in palika level and also interaction with technical persons, beneficiaries etc. - To carryout field visit and collect to housing typology in KOBO application, find out the major issues and solve the problems.					
Why was the visit carried out in this location?						
To organize retrofitting orientation program in ward no 07, Thaha Municipality; organize technical coordination meeting in ward level and there are around 85% reconstruction completed but the final inspection and CS entry status have not satisfy. It is going slowly but in last time it is rapidly increasing for due to incentive weightage.						
Summary						
We had planned for retrofitting orientation program when we decision made, last month meeting of Thaha Municipality. But we did not see much more retrofitting beneficiaries in the event venue. It means there is no any interest for retrofitting or we don't have convinced them. For model house, around 2nos. of house completed of retrofitting in ward no 05, by UNOPS/BUILD CHANGE and we are continuing in this task. We have organized technical coordination meeting and orient some beneficiaries for retrofitting and finally they have agreed for this; we decision made in the meeting. For sample at least two house starts for sample in ward no 07.						
The latest reconstruction data as given below in tabular form;						
.						
1st tranche received HHs	Verified for 2nd tranche HHs	Received 2nd HHs	Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
6030	5090	4675	3598	3288	3176	
<i>We have organized technical coordination meeting in Thaha Municipality-07, previous Agra VDC; meeting minute has attached via link click here....</i>						
Challenges / Issues Identified	Solutions Provided		Responsible	Timeframe		
CS entry, final inspection and distribution completion certificate with proper recorded.	- Now, for incentive; the weightage of CS entry is more so it should be complete to all inspections form with in Ashad Masant. - After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.		For CS entry; ward technicians Plan for completion certificate distribution; Local government and ward technicians and joint monitoring team.	Ashad Masant, Bhadra Msant and regular		
Retrofitting Methodology and its implementation.	We decision made in the meeting. For sample at least two house starts for sample in ward no 07.		For retrofitting ward technicians, joint monitoring team for coordination local government and beneficiaries.	Regular		
Photos						



Figure 1: Technical coordination meeting has been organized in ward level at Thaha Municipality- 07, Previous Agra VDC. During meeting also we have conducted individual orientation program in small group but actually it is not effective but we will continue in this mission.



Figure 2: In Tistung and Agra VDCs currently Thaha Municipality-07 and 08; there have been around 588 houses constructed with local materials used and it credit goes to mainly Tear Fund/ RADO Nepal and supportive for local government. This house is one of the sample, all seismic reinforcement elements provided, wood band used and mainly concerned with space, demand fulfilled for beneficiaries because it constructed with one +attic.

Visit 3:

Date	Location	Participants
22 th May, 2019	Makwanpur Gadhi-08, Previous Budhichar VDC	M&E CLPIU specialist, District Support Engineer, HRRP, Local Government, Ward Technicians and Beneficiaries.
Objective(s)	- To organize technical interaction with local government, ward technicians and beneficiaries in ward. - To carryout field visit and collect to housing typology in KOBO application, find out the major issues and solve the problems.	

Why was the visit carried out in this location?

Solve the technical problems and suggest feedback for noncompliance issues and recommendation for measures and also collected if any major issues.

Summary

Field Visit:

Makwanpurgadhi Rural Municipality-08, we have organized interaction program with beneficiaries, ward technicians with involvement of ward president, secretary etc. with including some agendas such as; current reconstruction status, other problems and issues. Smoothly running of housing reconstruction as part of third tranche and final inspection but as per compare to total beneficiaries, it is not sufficient. We strongly put the agenda; when do we finish the reconstruction of housing? But this questions answer is unknown in grass root level. President, ward no 8 say, "we are planning to filtration the fake beneficiaries and reported to in the district. Many more HHs received first tranche but they have not started their house. It is next one issue in the field.

The progress of housing reconstruction is as follows with tabular forms;

1st tranche received HHs	Verified for 2nd tranche HHs	Received 2nd HHs	Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
1774	1455	1314	1029	960	950	

Challenges / Issues Identified	Solutions Provided		Responsible	Timeframe
Filtration the actual earthquake victim beneficiaries/filtration, receives the first tranche but construction not started yet except Vulnerable HHs.	Formally notified the first tranche received but construction not started yet beneficiaries give certain time line for construction start. If they have not started the construction except vulnerable HHs request to cancel their PA signed to NRA for with coordination of district agencies.		Local government, Ward technicians	Regular
Final inspection and CS entry	- Now, for incentive; the weightage of CS entry is more so it should be complete to all inspections form with in Ashad Masant. - After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.			

Photos



Figure 1: Interaction program conducted during field visit at Budhichaur VDC; currently Makwanpur gadhi Rural Municipality-08.



Figure 2: Makwanpur Gadhi Rural Municipality-08, Previous Budhichau VDC, almost houses are constructed except retrofitting. Also in this area, almost houses constructed only one story and two rooms but it would meet the seismic resistant. We have carried out interaction program in the ward office with agendas of latest reconstruction status, Resurvey and reverification status and final inspection and CS entry.

Visit 4		
Date	Location	Participants
23th May,2019	Hetauda Sub – Metropolitan-14	M&E CLPIU specialist, District Support Engineer, HRRP, Local Government, Ward Technicians and Beneficiaries.
Objective(s)	- To organize technical interaction with local government, ward technicians and beneficiaries in ward. - To carryout field visit and collect to the housing typology in Kobo application, find out the major issues and solve the problems.	

Why was the visit carried out in this location?

- To know the present status of reconstruction; status of resurvey and re-verification; Present scenarios of final inspection and CS entry.
- To promote complete certificate distribution certificate and digitized all documents;
- To carry out field monitoring visit; collecting the housing typology, interaction with beneficiaries;

Summary

In urban areas of Makwanpur district the construction rate is slow rather than others and currently Smoothly running of housing reconstruction. As part of final inspection and CS entry there is slow; now decided by NRA for incentive weightage of CS entry is high so it will increase. Past 1year big issues in block made houses, Land less issues but those issues have already solved by central level and bye DSE, joint monitoring team.

The progress of housing reconstruction is as follows with tabular forms;

1st tranche received HHs	Verified for 2nd tranche HHs	Received HHs	2nd Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
4678	2814	2675	2442	2185	2120	

Challenges / Issues Identified	Solutions Provided	Responsible	Timeframe
Intentionally they have not started the reconstruction and waiting for his/her favor of time as well many beneficiaries have already houses.	• Strongly we advised to the local government, filtration those types of beneficiaries and report to NRA throw GMAI for cancellation of their PA agreement.	Local Government, Ward technicians	regular
Final inspection and CS entry	• Now, for incentive; the weightage of CS entry is more so it should be complete to all inspections form with in Ashad Masant. • After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.	Local Government, Ward technicians	Ashad Masant and Bhadra Masant

Photos



Figure 1: Hetauda SM-14, RCC construction; now reconstruction is rapidly increasing at the urban areas. It is good message for us. House owner received second tranche and verified for third tranche by ward technicians.



Figure 2: House owner Ram Bdr Titung; he received all tranches of government reconstruction grant. Two room, one storey with attic and block material used, past 1years we faced block issues but last orientation of block material, Manual of block and with close supported of DSEs. Now almost houses of block would be constructed with compliance and they have received all tranches with no any issues.

Housing Typology Report



Figure 1: House owner; Ram Bdr Gole, the location of house is Hetauda-12, Load bearing brick and cement mortar, two rooms with one storey, flexible roof. he received all tranches of government reconstruction grant. Total construction cost is around 8lakh.



Figure 2: House owner; Akal Tiung, location is Hetauda SM-14, Load bearing brick and cement mortar masonry, he received all tranches of government reconstruction grant. Provided all seismic reinforcement elements such as horizontal members and vertical reinforcement, flexible roof. The total construction cost was around 22lakh.



Figure 3: House owner Akhal Ghlan, Thaha Municipality-07, two rooms with one storey an attic and flexible roof. This house construction with funded and technical supported by TEAR fund/ RADO Nepal. All materials were used local materials and it was a really appreciation work for reconstruction.



Figure 4: House owner; Buddi Maya yonjan, Makwanpurgadhi Rural Municipality-08, load bearing stone in mud mortar and two rooms, one storey with attic and flexible roof. The total construction was around 8lakh. House owner received all tranches of government reconstruction grant.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
In case of second tranche, we received the tranche on the time around 20days from the inspection checklist fill up but now why do delay in third tranche received?	Makwanpur Gadhi-08 Beneficiary	We have been continuing for this work to deliver the tranche distribution on time for starting and last 1.5year we are continuing deliver from the district within around 20 days from the receive date of inspection form from the technicians/ward office. Also it was a gap between form fill up VS send date of file. Last one month with absent of district chief we could not do it due to signature problem so now, it is going too smoothly.

Challenges and Way Forward

Challenge	Way Forward
Retrofitting and its implementation	- Now, UNOPS/Build Change is constructing demonstration at every palikas of Makwanpur district with involving of ward technicians. But they have only one method of retrofitting such as strong back but it is not sufficient for filed. So it is necessary to technician's linkage with retrofitting manual for easy access of different method of retrofitting. Here is one method is common; splint and bandage so that also it gives the option to beneficiaries. May be beneficiaries have motivate fast and they have quick access of materials. - Refer retrofitting manual for load bearing and RCC frame structure. Necessity to organize an awareness program at different palikas of district. We have organized awareness program in Thaha Municipality with convince the beneficiaries but they don't believe on financial cost, material and methodology and also skilled manpower, we have not any skilled manpower in field. We have decision made for sample two house will have retrofitting.
Final inspection, CS entry and complete certificate distribution	- Now the progress of CS entry is very high due to NRA announces for incentive and it is weightage is 30% so we complete the CS entry and final inspection. Final inspection is more important because of in field level beneficiaries modify their house in some places so it should be finalize who have full the all requirements and eligible for final inspection. - Also coordinate in completion certificate distribution. We have done formally program in Kogate VDC hope, we will coordination to organize same program in other places.

Challenges and Way Forward

Challenge	Way Forward
Filtration of fake beneficiaries	Last district facilitation and coordination meeting have decision made on fake beneficiaries. Who receive the first tranche but not started the house expect vulnerable HHs, who received second tranche but not started above DPC level, who have an already houses in those cases GMaLI have done interaction meeting in the palikas hope it will be positive result.
