


## FACTS AND FIGURES

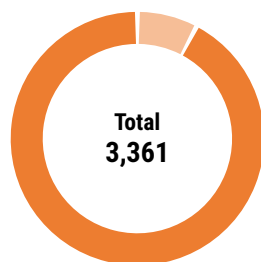

Damage Status - Private Structures

Damage Grade (1-2)  
**260**

Damage Grade (3-5)  
**3,101**

## MAJOR HOUSING TYPOLOGIES

| Typology                     | Municipal | District |
|------------------------------|-----------|----------|
| Stone and Mud Mortar Masonry | 97.83%    | 39.28%   |
| Adobe Structures             | 1.07%     | 34.86%   |
| Dry Stone Masonry            | 0.48%     | 0.31%    |
| Timber Frame Structure       | 0.33%     | 0.12%    |
| Others                       | 0.30%     | 25.44%   |

CBS damage assessment survey, 2015

## HOUSING RECONSTRUCTION & RETROFIT UPDATES

### Reconstruction Status

|                                    |       |
|------------------------------------|-------|
| Total Eligible HHs                 | 3,370 |
| PA Agreement                       | 3,099 |
| I <sup>st</sup> Tranche received   | 3,089 |
| II <sup>nd</sup> Tranche received  | 2,530 |
| III <sup>rd</sup> Tranche received | 1,854 |

### Houses

Under Construction: -

Completed: -

### Retrofitting Status

|                                   |     |
|-----------------------------------|-----|
| Total Eligible HHs                | 252 |
| PA Agreement                      | 110 |
| I <sup>st</sup> Tranche received  | 107 |
| II <sup>nd</sup> Tranche received | 252 |

### Grievances

Registered: 883

Addressed: 713

### Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-16 00:00:00

## P0 Presence

Active: CECI (Agriculture), CECI (DRM), CECI (Livelihood), CECI (Governance)

Phased Out: CDO-N (Health), CECI (Agriculture), CECI (DRM), CECI (Livelihood), FCA (Education), GON (Shelter), LWF (Shelter), NYF (Education), OXFAM-GB (Shelter)

## OTHER SECTORS



### Schools

Damaged: 66  
Under Construction: 48  
Construction Completed: 48



### Health Posts

Damaged: -  
Under Construction: -  
Construction Completed: -

## STATUS OF CONSTRUCTION MATERIALS

| Materials    | Unit           | Req. Quantity* | Ava. | Cost (NRs.)** |
|--------------|----------------|----------------|------|---------------|
| Stone        | m <sup>3</sup> | 48,987         | -    | -             |
| Aggregate    | m <sup>3</sup> | 51,777         | -    | -             |
| Sand         | m <sup>3</sup> | 5,243          | -    | -             |
| Timber       | cu. ft.        | 6,098          | -    | -             |
| Cement (PPC) | Sack           | -              | -    | -             |
| Cement (OPC) | Sack           | 170,214        | -    | -             |
| Rebars       | kgs.           | 527,263        | -    | -             |
| Tin          | bundle         | 6,952          | -    | -             |
| Bricks       | pcs.           | 204,186        | -    | -             |

### Types of Workers

1. Skilled mason
2. Labourer

### Avg. daily wage (NRs.)

-/-  
-/-

## KEY CONTACTS

### Municipal Office

Bir Bahadur Lopchan  
Mayor  
9841335585

### Municipal Office

Milan Sharma  
Focal Person  
9851255900

### Municipal Office

Ranjana Ghimire  
Deputy Mayor  
9862258749

### GMaLI/NRA

Bir Bahadur Rawal  
NRA Chief-District  
9851201088

### Municipal Office

Yubaraj Acharya  
Administration Officer  
9852040721

### DLPIU-Building

Chandra Kaji Gurung  
DUDBC.DLPIU Chief  
9841576783

## HHs WITH LAND ISSUES

No Reported Land Issues

## STATUS OF TECHNICAL STAFF

| Staff               | Available Nos.            | Additional Req. Nos.        |
|---------------------|---------------------------|-----------------------------|
| Engineers           | 6                         | -                           |
| Sub-Engineers       | 9                         | -                           |
| Asst. Sub-Engineers | 6                         | 1                           |
| Masons              | - (7 days)<br>7 (50 days) | - (7 days)<br>135 (50 days) |

Source: Municipal survey

## MASON TRAINING

Trainings (# out of total required)


7 days Training



351

Reached

50 days Vocational Training




123

Remaining

Source: HRRP Analysis

## TA ACTIVITIES MAP

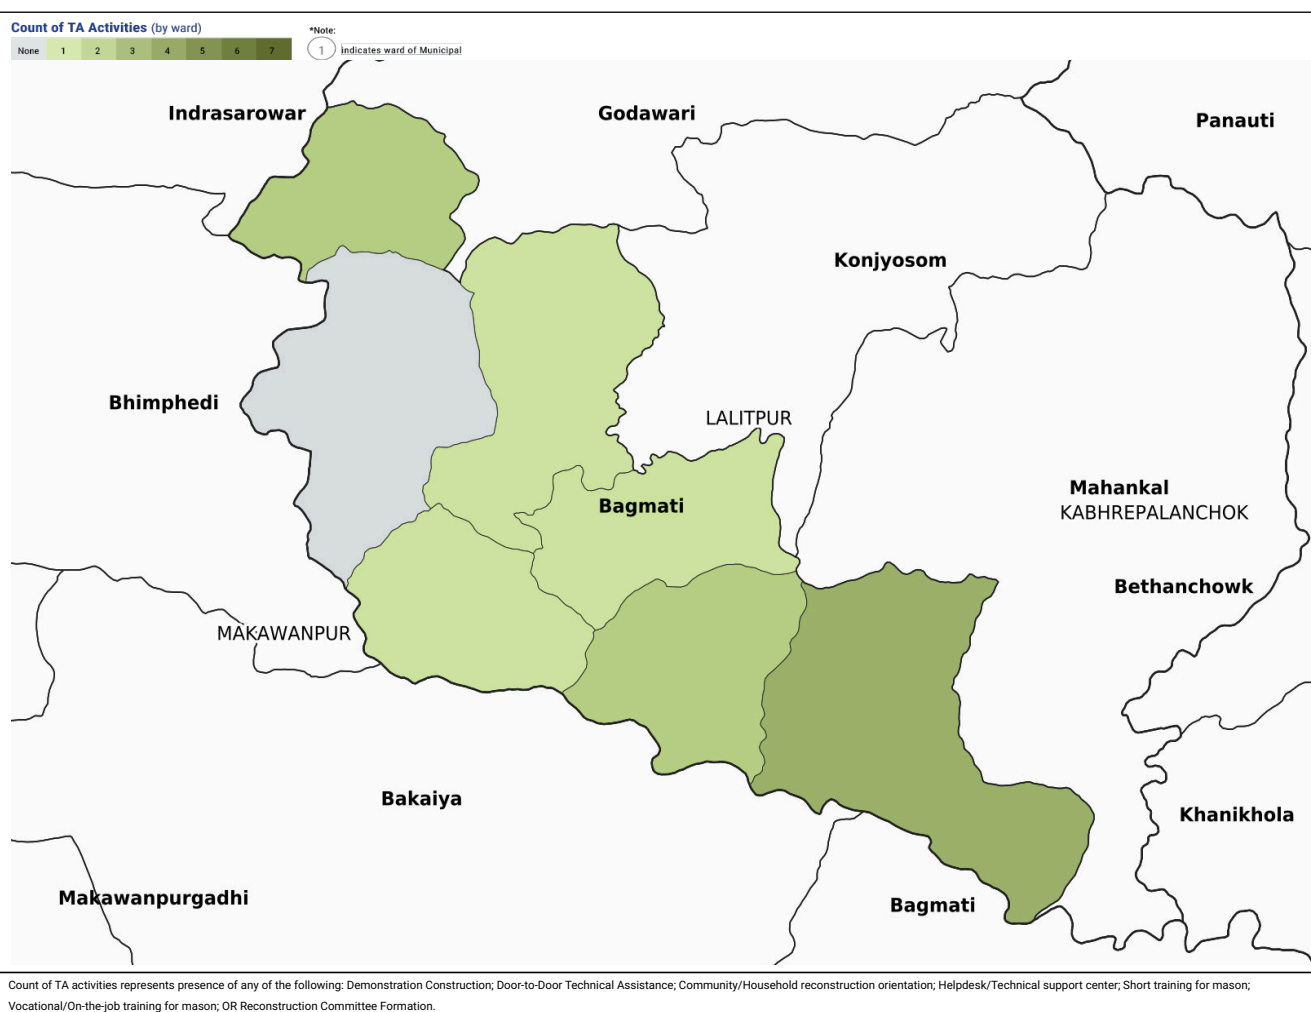

## FAQs

**Q: What documents are required for enrolment in the GoN housing reconstruction programme?**

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

**Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?**

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

**For further information** 1. Ambika Amatya (District Coordinator) 9841356409 2. (District Technical Officer) 9861796464 3. Sachin Malego (District Information Management Officer) 9849166793
