


FACTS AND FIGURES

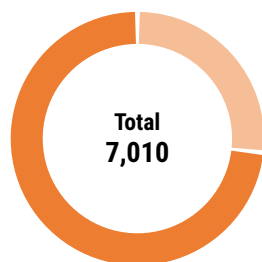

Damage Grade (1-2)
1,877

Damage Grade (3-5)
5,133

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	80.87%	85.43%
Reinforced Cement Concrete (RCC) Frame	7.86%	3.25%
Brick and Cement Mortar Masonry	6.46%	3.73%
Timber Frame Structure	3.42%	0.64%
Others	1.39%	6.94%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	5,538
PA Agreement	4,650
I st Tranche received	4,650
II nd Tranche received	3,894
III rd Tranche received	3,087

Houses

Under Construction: - Completed: 2,880

Retrofitting Status

Total Eligible HHs	618
PA Agreement	618
I st Tranche received	618
II nd Tranche received	618

Grievances

Registered: 1,690
Addressed: 599

Non-compliances

Registered: 22
Addressed: 20

Data Updated on: 2019-05-28 00:00:00

P0 Presence

Active: NSET (Shelter)

Phased Out: AATWIN (Social Protection), ADRA (Shelter), CY (Education), DCA (DRM), DCA (Livelihood), DCA (Health), DCA (Shelter), DCA (Hygiene), GON - DUDBC (Shelter), GON-PAF (Shelter), MCC (Agriculture), MCC (Health), OXFAM-GB (Shelter), UMN (Education), UMN (Shelter), UMN (Hygiene)

OTHER SECTORS



Schools

Damaged: 105
Under Construction: 64
Construction Completed: 64



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	97,205	Y	1,200
Aggregate	m ³	82,048	Y	1,500
Sand	m ³	10,212	Y	2,100
Timber	cu. ft.	11,173	Y	706,300
Cement (PPC)	Sack	-	-	715
Cement (OPC)	Sack	273,110	-	795
Rebars	kgs.	1,078,112	Y	80
Tin	bundle	11,125	Y	-
Bricks	pcs.	2,006,947	Y	13

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,000 /-
700 /-

KEY CONTACTS

Municipal Office

Pitta Bahadur Dallakoti
Mayor
9851229220

Municipal Office

Manoj Adhikari
Focal Person
9849201835

Municipal Office

Devi Prasad Silwal
Deputy Mayor
9810254793

GMaLI/NRA

Jaya Ram Shrestha
NRA Chief-District
9841265576

Municipal Office

Harsha Bahadur Thapa
Administration Officer
9851242149

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
9855046584

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	10	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

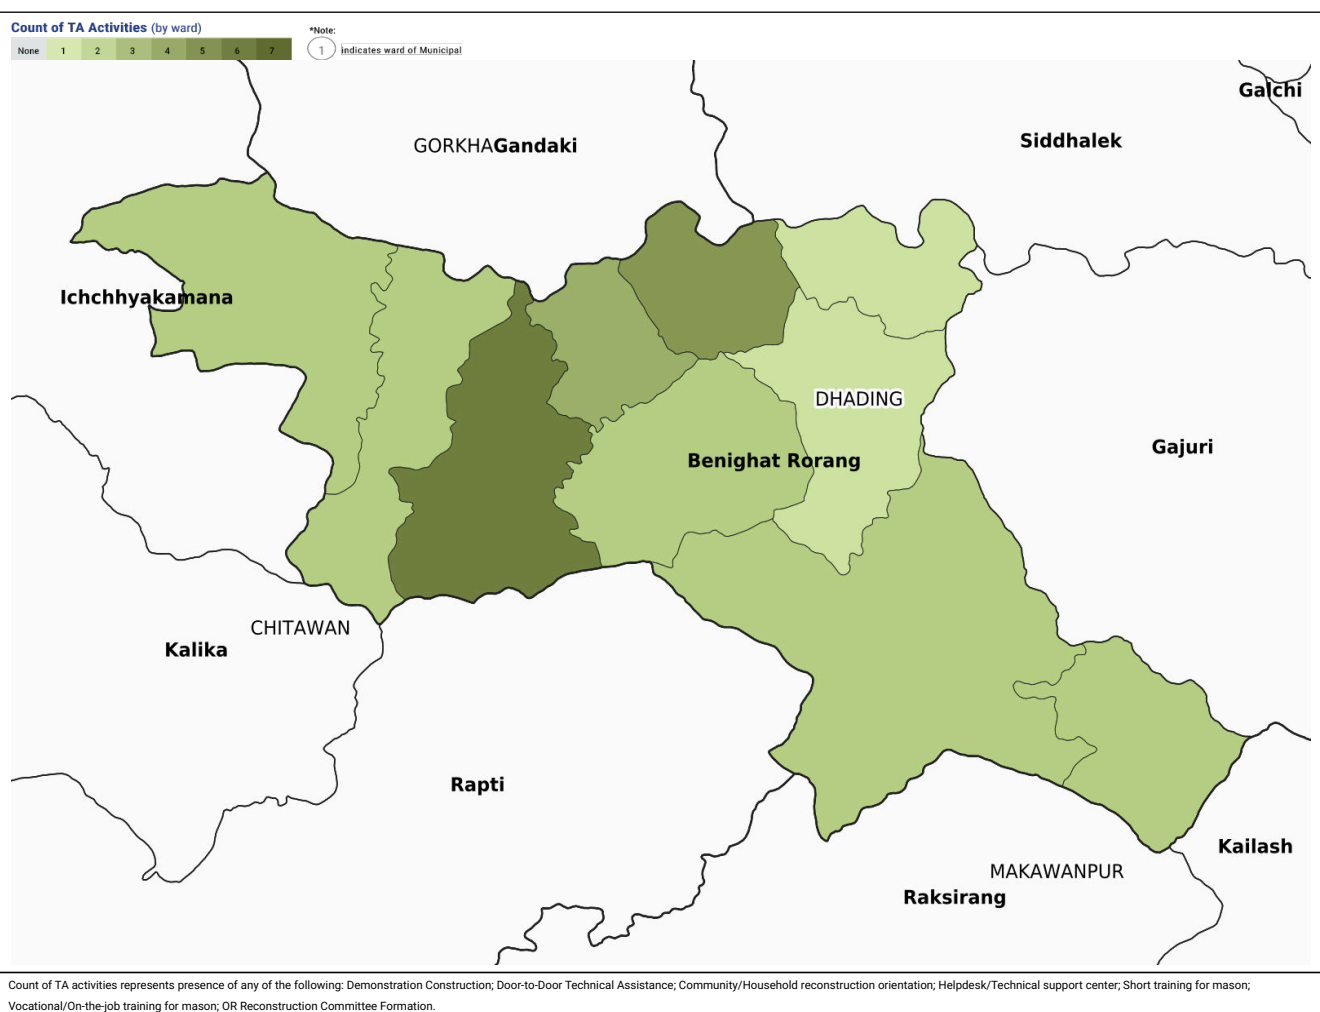

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Chandra Gurung (District Coordinator) 9841478742	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
