

District Report

Kavrepalanchok

15 February – 14 March 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint Monitoring Field Visit to Dhulikhel Gaupalika	14-15 Feb 2019	2	1	reshma@hrrpnepal.org	Field Visit Section below
Field Visit to Mangaltar, Roshi Gaupalika to monitor non-compliance issues	1 March 2019	2	1	reshma@hrrpnepal.org	Field Visit Section below
Training Database Update	25 Feb 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
5W Update	25 Feb 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Data Collection and Updating Palika Profiles in Municipal websites	16 Feb-14 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Housing Typology Update	7 Mar 2019	-	-	reshma@hrrpnepal.org	GD
Action Plan Update Follow-ups (Gulmi, Argakhachi)	1-14 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	NA
District Material Rate Update	8-11 Mar 2019	-	-	reshma@hrrpnepal.org	Mail
Transportation Cost Update	8 Mar 2019	-	-	reshma@hrrpnepal.org	Mail
GMALI/HRRP Coordination Meeting	12 Mar 2019	10	1	reshma@hrrpnepal.org	Draft Minutes
DPAC Meeting, HfH/ASF	12 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	NA
Tranche Return Update	14 Mar 2019	-	-	im.kavrepalanchok@hrrpnepal.org	NA
Support to GMALI on grievance handling	15 Feb-14 Mar 2019	-	-	reshma@hrrpnepal.org	NA

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Orientation on Hollow Concrete Block Manual	24-25 March 2019, Dhulikhel	HRRP	reshma@hrrpnepal.org
Joint Monitoring Field Visit to Temal Gaupalika	26-29 March 2019, 8:00 AM- 5:00 PM, Temal GP	HRRP	reshma@hrrpnepal.org
Joint Monitoring Field Visit to MandanDeupur Nagarpalika	3-4 April 2019, 8:00 AM- 5:00 PM, Temal GP	HRRP	reshma@hrrpnepal.org
Palika Level Coordination Meeting, Banepa Nagarpalika	9 April 2019, 11:00 AM, Banepa NP	Municipality/HRRP	reshma@hrrpnepal.org

Tranche Status


Municipality	Banepa	Bethanchok	Bhumlu	ChauriDeurali	Dhulikhel	KhaniKhola	Mahabharat	MandanDeupur	NamoBuddha	Panchkhal	Panauti	Roshi	Temal
Total HHs Surveyed	-	-	-	-	-	-	-	-	-	-	-	-	-
Total HHs Eligible	7070	4377	6206	6412	5995	2846	2951	9221	7637	9948	9188	6374	4848
Total HHs Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
1 st Tranche	6369	3767	5827	5543	5221	2736	2874	8497	6317	8965	8106	5479	4174
2 nd Tranche	3003	2703	4826	3848	2680	2220	2374	6630	3190	6066	4327	3977	2979
3 rd Tranche	2248	1580	3689	1964	1725	781	1431	4432	1905	3749	3107	2169	1765
Total HH Constructed	-	-	-	-	-	-	-	-	-	-	-	-	-
Grievance Registered	2226	1202	1038	1578	2151	683	1075	2300	2814	3041	2874	2257	2101
Grievance Addressed	2031	1202	971	1517	1919	681	1055	1762	2296	2932	2851	2203	2069
RF HH Eligible	-	-	-	-	-	-	-	-	-	-	-	-	-
RF HH Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
RF 1 st Tranche	76	73	14	43	39	43	143	25	20	108	123	129	103
RF 2 nd Tranche	1	0	1	0	0	0	0	0	0	14	0	0	1
Non-Compliance Registered	-	-	-	-	-	-	-	-	-	-	-	-	-
Non-Compliance Addressed	-	-	-	-	-	-	-	-	-	-	-	-	-

Tranche Status

Reconstruction Tranche Status (14 March 2019)

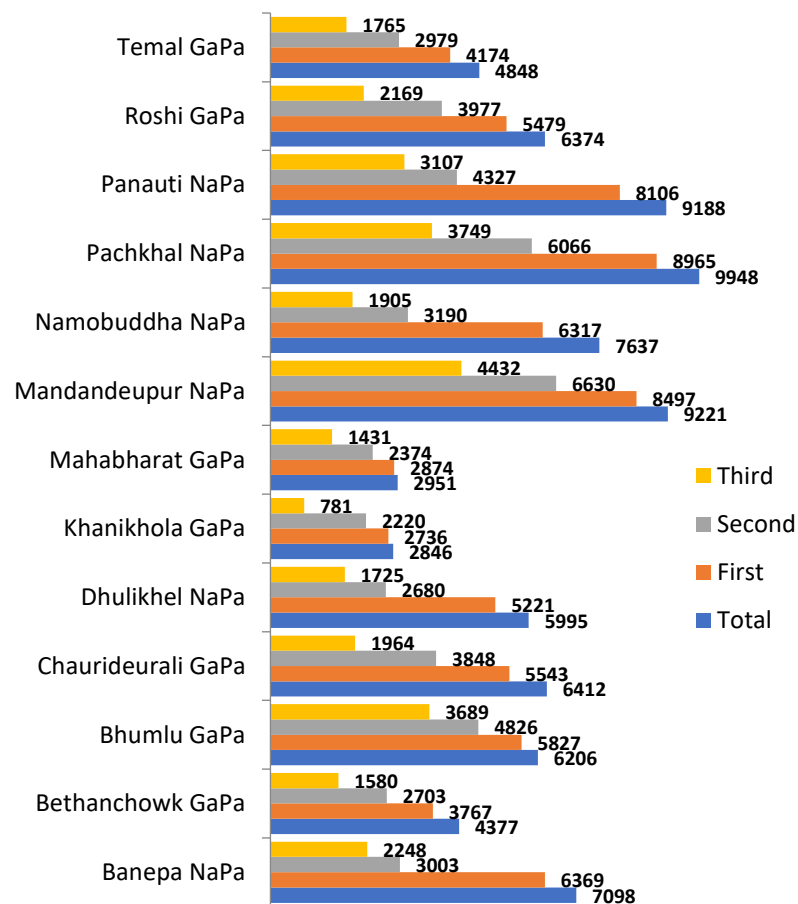

Grievance Addressal Status (14 March 2019)

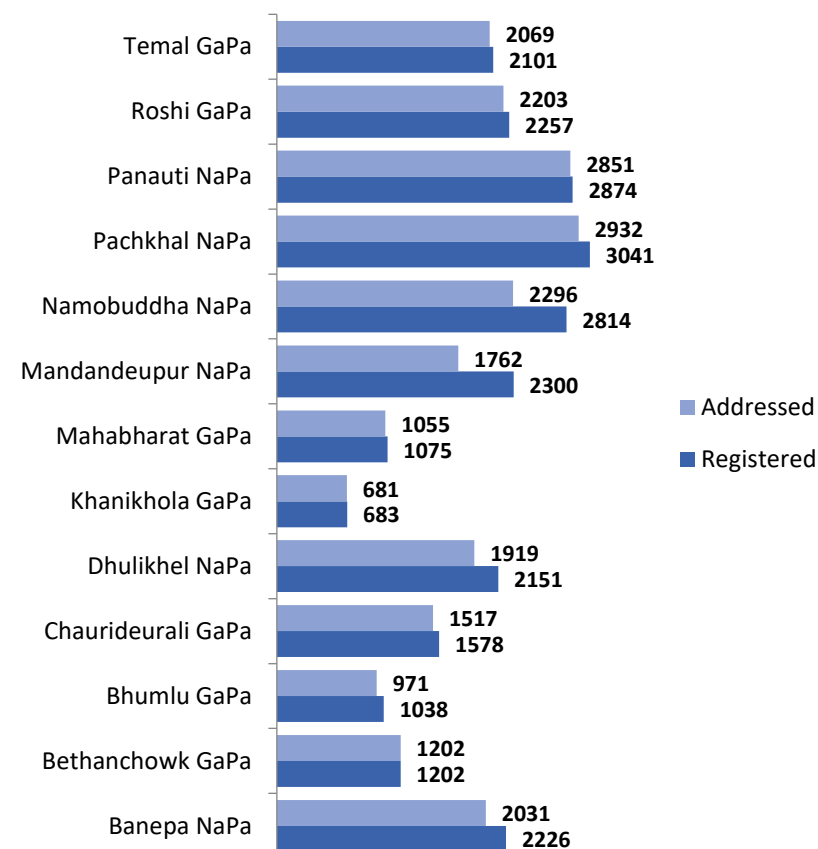

Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
14-15 Feb 2019	Dhulikhel 1,2,3,6,7,8	- Ishor Neupane, HRRP - Roshan Kesari, M&E DLPIU - Resham Lamsal, Engineer/DLPIU - Ratna Prasad Pokhrel, Sub Engineer/DLPIU
Objective(s)	- Meeting at ward level. - Monitoring of technical team. - Update on reconstruction status of each wards. - Monitor main non-compliance issues.	
Summary	During the field visit, Ward no 1, 2, 3, 6, 7 and 8 were visited where most of the reconstructed houses were RCC structures and BMC. During this visit, ward level meetings were conducted in Ward 1 and 8. The common points discussed in the meeting were: - Need of supports for grievance handling. - Delay in tranche release and files missing at DLPIUs. - Non-compliance cases; most of them constructed immediately after earthquake and difficulty in encouraging the beneficiaries to carry on the correction measures as suggested by DSE. - Need to support the vulnerable beneficiaries. - Reconstruction rate is comparatively slow in all over the municipality as most of the beneficiaries are not interested to reconstruct houses. - Inside the city area (ward 6 and 7) most of beneficiaries are not starting reconstruction due to the issues raised on removing the damaged houses.	

Photos



Milan Tamang is a low income beneficiary of Dhulikhel-2. So Hope Foundation has technically supported to reconstruct rice bag house. The house has been inspected for second tranche.
Photograph By: Ishor Neupane



Resident of Dhulikhel-1, Gyan Bahadur Tamang reconstructed RCC house and has received third tranche.
Photograph By: Ishor Neupane

Field Visit Report

Visit 2

Date	Location	Participants from HRRP and stakeholders
1 March 2019	Mangaltar, Roshi Gaupalika	- DSE - Reshma Shrestha, HRRP Kavre

Objective(s)	Monitor and collect details on the non-compliance issues of the ward
--------------	--

Summary	Mangaltar has the highest number of non-compliances in the district. There are a total of 40 non-compliances of RCC, SMM, BMC and Hollow Concrete Blocks. As per the ward chief, the major reason of non-compliances is the gap in technical assistance from technical persons. The Stone in Mud constructions are two storied and have larger percentage of openings than the standards. BMCs are constructed in 9" masonry with two storey, RCCs have insufficient steel rods whereas HCB houses too are two storied. During the visit, the details of each house visited were noted with the corrections to be specified after the detail analysis.
---------	---

Photos



Dhan Kumar Lama of Mangaltar, Roshi-9 constructed his house using hollow concrete blocks along with three other neighbors in same design. He has received second tranche but his house was classified as non-compliant for the third tranche.

Photograph By: Reshma Shrestha



Lal Bahadur Lama of Mangaltar, Roshi-9 constructed his house similar to his pre earthquake house with no technical guidance. He has received second tranche but his house is non-compliant for the third tranche.

Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Roshi-9

Building Typology: Stone in Mud

Description: Dirgha Bahadur Lama has received second tranche of housing reconstruction grant and he needs to correct his house to receive the third tranche.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Roshi-9

Building Typology: Stone in Mud

Description: Sarki Maya Tamang constructed two storied stone in mud house with larger openings similar to her pre earthquake house. So, her house was classified non-compliant for third tranche.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Roshi-9

Building Typology: Brick in Cement

Description: Laxmi Tamangni has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Roshi-9

Building Typology: RCC

Description: This house has received second tranche of housing reconstruction grant and also been inspected for the third.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Roshi-9

Building Typology: Stone in Mud

Description: Saneel Lama has received third tranche of housing reconstruction grant for his two storied SMM house.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Roshi-9

Building Typology: Brick in Cement

Description: Budhi Maya Lama has received third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha

Case Story

Non-compliant HCB houses at Mangaltar, Roshi-9

Dhan Kumar Lama, Mlangi Lama, Utar Kumar Lama and Krishna Gopal Lama opted to use Hollow Concrete Blocks for reconstructing their houses due to the ease in construction using hollow blocks. They were not aware of the standards for HCB constructions used HCBs similar to brick use. All four of them constructed together in similar plans. Though they have received second tranche, all were classified non-compliant for the third tranche.

Standard sized blocks have been used to construct two storied two room (12'X12' each) structure. 2" dia circular poles have been used at the corners and also to support the overhangs whereas 2" rectangular poles have been used for the floors. The foundation of the poles has been laid to a depth of 5' and all bands too have been laid as per the standards.



Left to Right: HCB houses of Dhan Kumar Lama, Mlangi Lama, Utar Kumar Lama and Krishna Gopal Lama



Interior of the HCB houses
