

Japan International Cooperation Agency (JICA)




TRANSITIONAL PROJECT IMPLEMENTATION SUPPORT
FOR
EMERGENCY RECONSTRUCTION PROJECTS
IN NEPAL

Public Awareness Campaign and Housing Reconstruction Survey

JICA Technical Assistance Team

January 2017

● JICA Target 38 VDC/Municipality

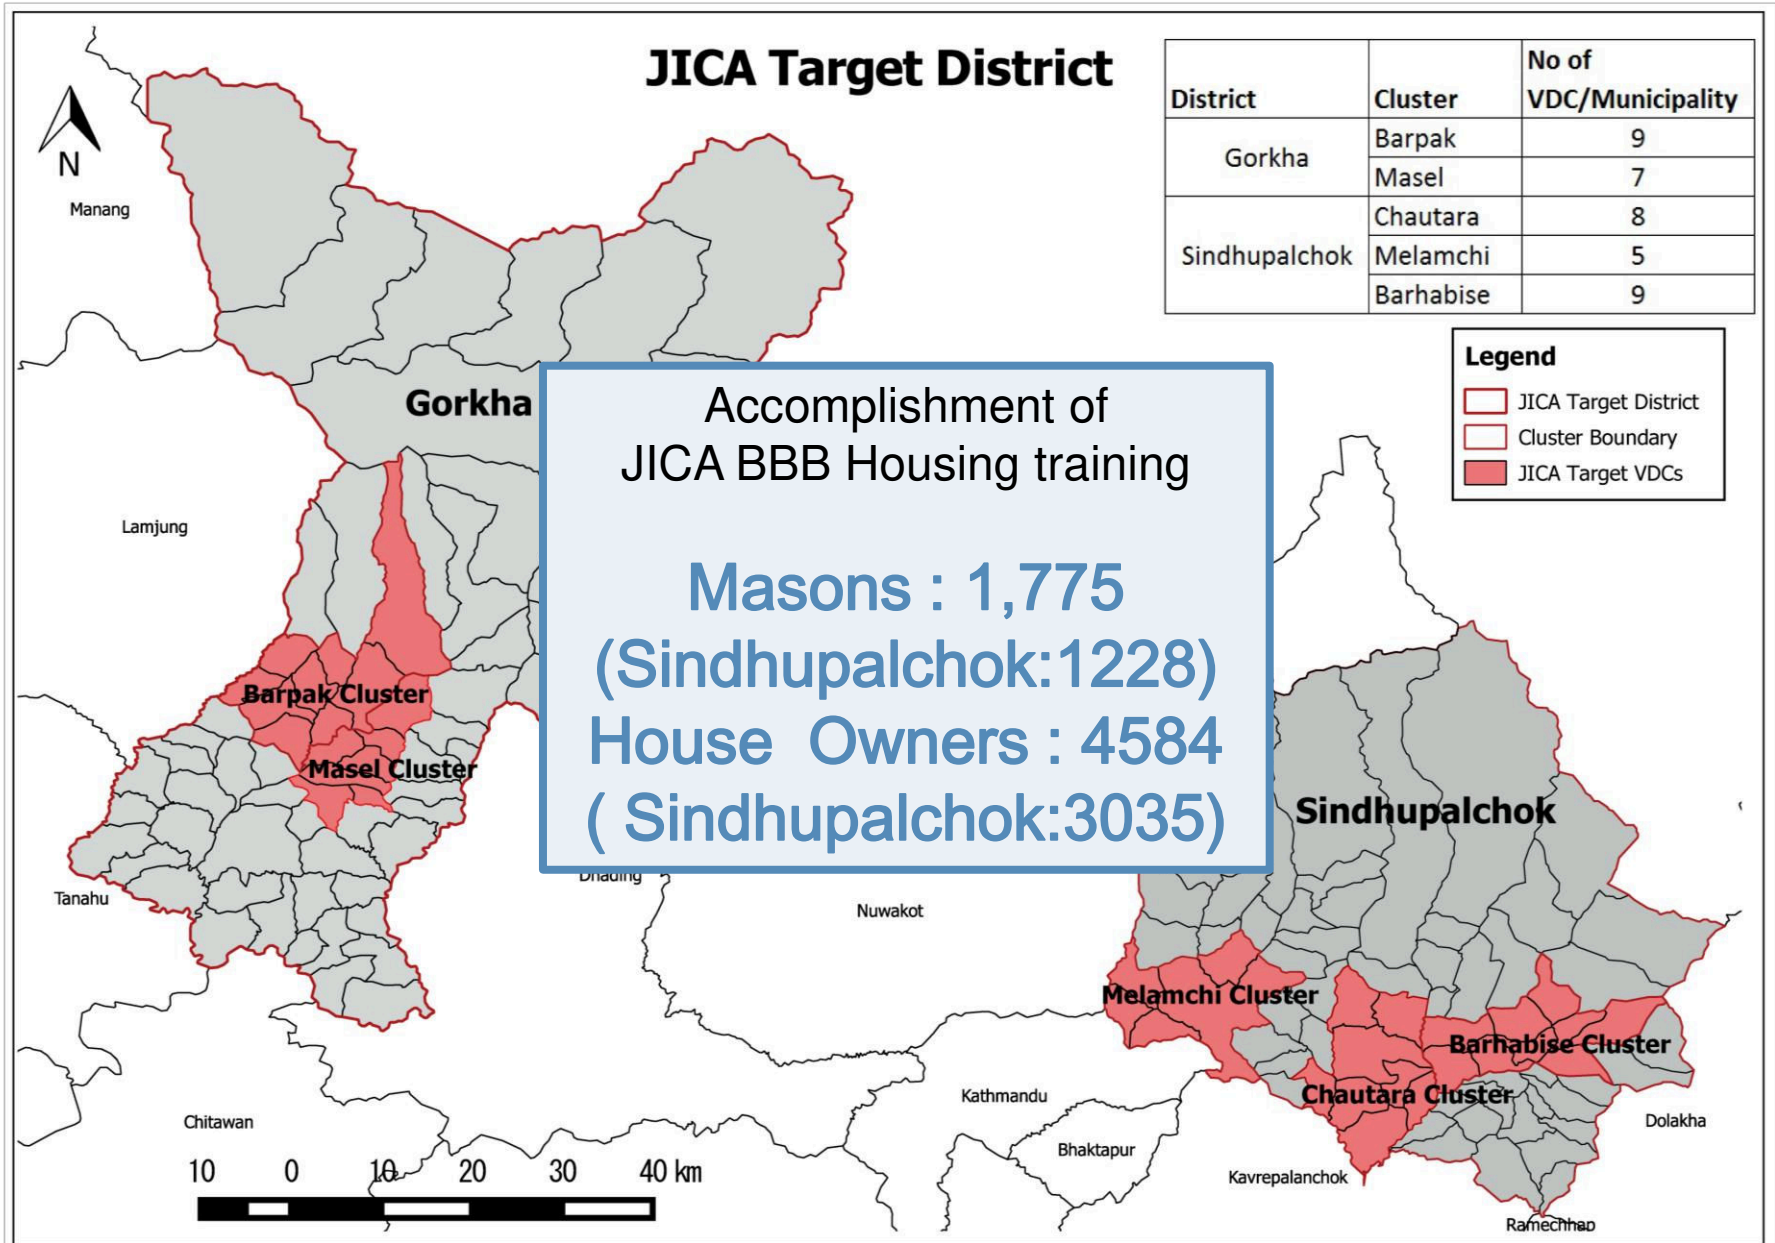

Monitoring & technical assistance Activities



नेपाल सरकार

राष्ट्रिय पुनर्निर्माण प्राधिकरण

(विकास सहायता समन्वय तथा बजेट व्यवस्थापन शाखा)



सिंहदरवार, काठमाडौं

फोन: ४२१११०३, ४२११०७१

मिति:- २०७३/०७/०२

प.सं.: PPMDCCD/2073/074

च.नं.: २९२

श्री सहरी विकास मन्त्रालय,
केन्द्रीय आयोजना कार्यान्वयन इकाई,
बबरमहल, काठमाडौं ।

विषय: समन्वय गरि दिनुहुन ।

Japan International Cooperation Agency (JICA) को Ref. No. JICA (NP) 10-18004 मिति October 18, 2016 गतेको पत्र मार्फत अनुरोध भई आए बमोजिम उक्त निकाय र नेपाल सरकारबीच मिति 9 July 2015 मा सम्झौता भएको Emergency Housing Reconstruction Project (EHRP) संचालनको लागि गोरखा र सिन्धुपाल्चोकमा तह्राबाट खटिएका प्राविधिक जनशक्तिलाई JICA बाट संचालन गरिने Public Awareness Campaign and Housing Reconstruction Survey कार्यक्रममा सरिक भई सहयोग तथा समन्वय गर्न निर्देशन दिनुहुन आदेशानुसार अनुरोध छ ।

(सूर्य प्रकाश बिष्ट)
शाखा अधिकृत



नेपाल सरकार

सङ्घीय मामिला तथा स्थानीय विकास मन्त्रालय

केन्द्रीय आयोजना कार्यान्वयन इकाई

भूकम्पीय आवास पुनर्निर्माण आयोजना

चाकुपट/UN/Pran, ललितपुर

UN प्राक
मल्लपुर, कैलाल
२०७३

प.सं.: २०७३/०७४

च.नं.: १६०

मिति: २०७३/०७/०३

विषय: समन्वय गरि दिनुहुन ।

श्री भूकम्पीय आवास पुनर्निर्माण आयोजना
जिल्ला आयोजना कार्यान्वयन इकाई
गोरखा र सिन्धुपाल्चोक

राष्ट्रिय पुनर्निर्माण प्राधिकरणको च.नं. २९३, मिति २०७३/०७/०२ को पत्रानुसार Japan International Co-operation Agency (JICA) र नेपाल सरकार बीच मिति 9 July, 2015 मा सम्झौता भएको Emergency Housing Reconstruction Project (EHRP) सञ्चालनका लागि त्यस जिल्लामा JICA बाट संचालन गरिने Public Awareness Campaign and Housing Reconstruction Survey कार्यक्रममा सरिक भई सहयोग तथा समन्वय गरि दिनुहुनु आदेशानुसार अनुरोध छ ।

देव नारायण प्रसाद यादव
इञ्जिनियर

● Monitoring & technical assistance Activities

Public Awareness Campaign



1 ward one gathering
Orientation on MR
Orientation on Inspection Guidelines
Orientation on CBRC
Discussion on issues
Interview with WCF representatives



+

Survey



Survey of hhs
Interview of house owner
Interview of masons
Technical Assistance



● Public Awareness Campaign and Survey

Mobile team
(1 **engineer** + 1 **social mobilizer**)

×
12 teams

Total number of interview with WCF

Sindhupalchowk:204

Gorkha:144

Total Number of Campaigns

Sindhupalchok:279 number

Gorkha:144 number

Total number of buildings

surveyed:2126

780 hhs were in planning stage



1346 hhs (Under construction/Completed)



Monitoring & technical assistance Activities

House Survey			
SN	: 6	Ward No.	: 2
House Owner	: Nachar Man Tamang	PA Number	: 23-67-2-0-112
Coordinate	27°51'8.362"N		85°30'20814"E
Mason	:NA		
HO knows MR	:No	Mason knows MR	: <u>NA</u>
Structure	: SMM	Cost	: 300,000
Ward No.	: Area (30m ²) Length (10m) Breadth (3m) Storey (2) Rooms (2) Attic(yes)		
Start Date	: 1-Jan-17	Completion Date	: 1-Feb-17
Progress	:Completed	Compliant	:No
Findings			
• No bands are used. • Two storey house with heavy gable wall			
Photo			
			
Overall 1		Overall 2	
			
No Bands		Heavy material in gable	

● Compliant and Non-compliant Houses in field



● Compliant and Non-compliant Houses in field



● Compliant and Non-compliant Houses in field



● Compliant and Non-compliant Houses in field



● Compliant and Non-compliant Houses in field



● Ratio of Houses Compliant with MR


VDC	Surveyed Houses			
	Total	House Owner knows MR	Mason knows MR	Compliant with MR
Overall	1346 (100%)	640 (47.5%)	894 (66.4%)	247 (18.4%)
Constructed by Masons trained by TPIS-ERP	358 (100%)	194 (54.2%)	330 (92.2%)	89 (24.9%)

More than 92.2% of Mason knows MR **but just 24.9% is compliant (Overall 18.4%)**

How to increase the number of Compliant houses??

● Ratio of Houses Compliant with MR

MR Compliant Ratio

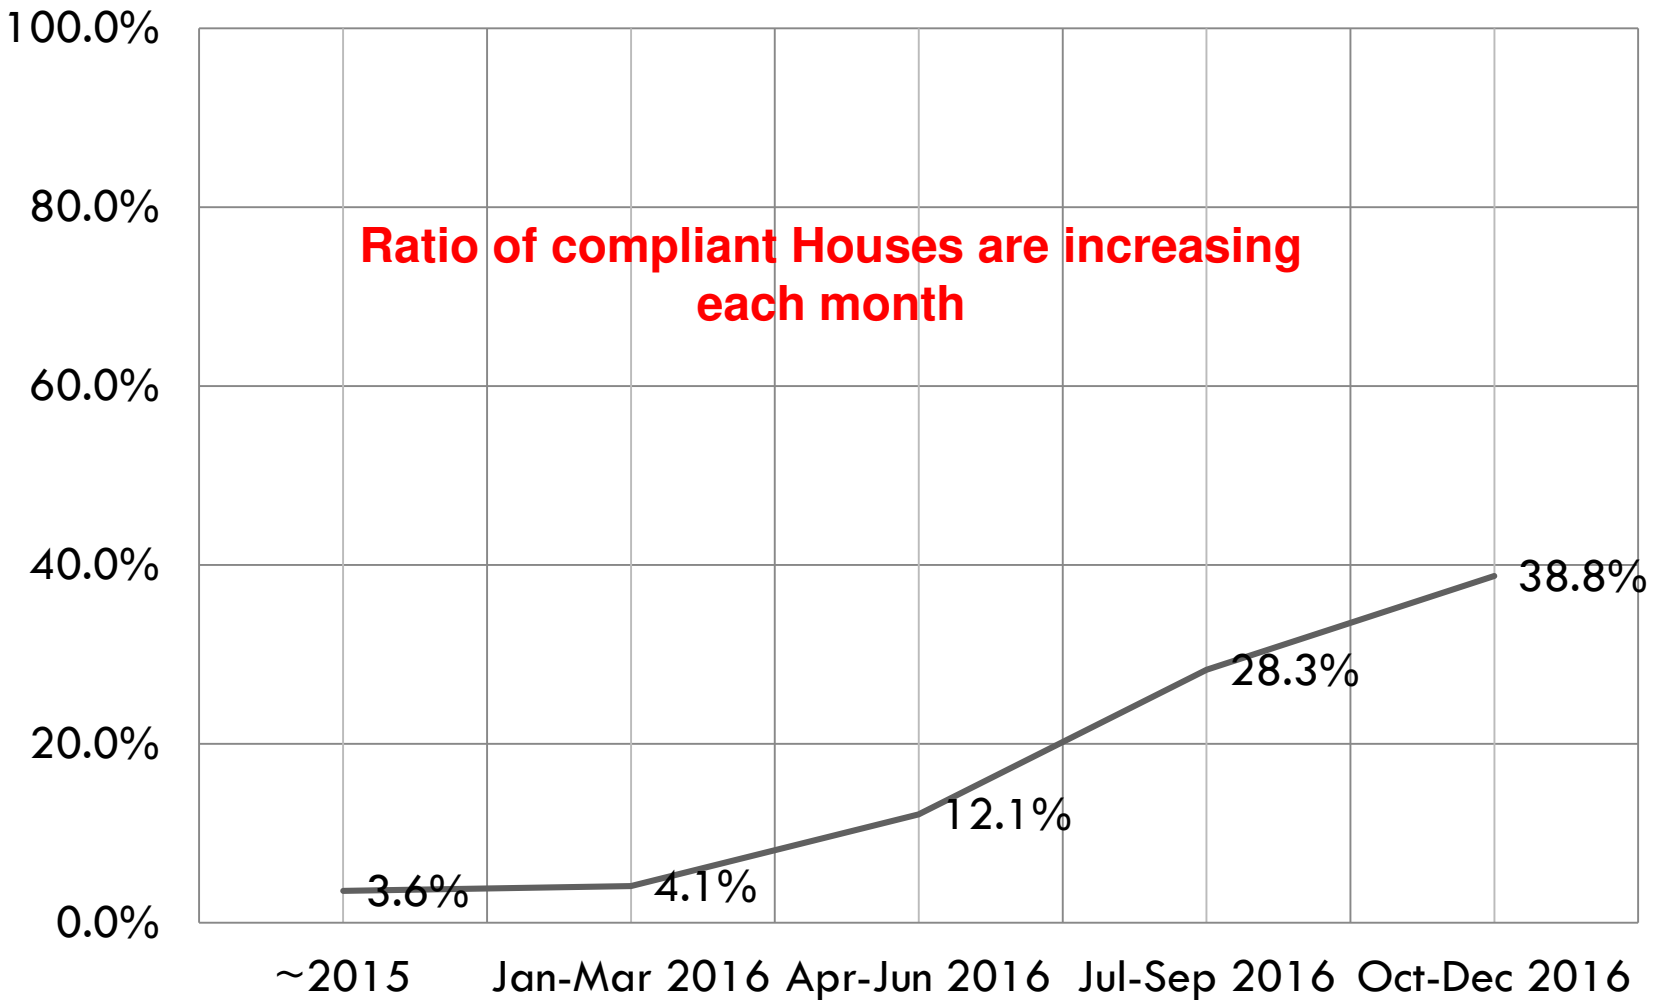


● Ratio of Houses Compliant with MR

VDC	Overall		~Plinth Band		~Roof Band			Completed	
	Total	Compliant with MR	Total	Compliant with MR	Total	Compliant with MR		Total	Compliant with MR
Total	1346	247 (18.4%)	242	114 (47.1%)	283	78 (27.6%)		821	55 (6.7%)

Till Plinth Band, compliant Houses are 47.1%
But when they complete the construction, it became just 6.7%

**How to keep 47.1% of compliant ratio
till Completion of the work?**

● Findings

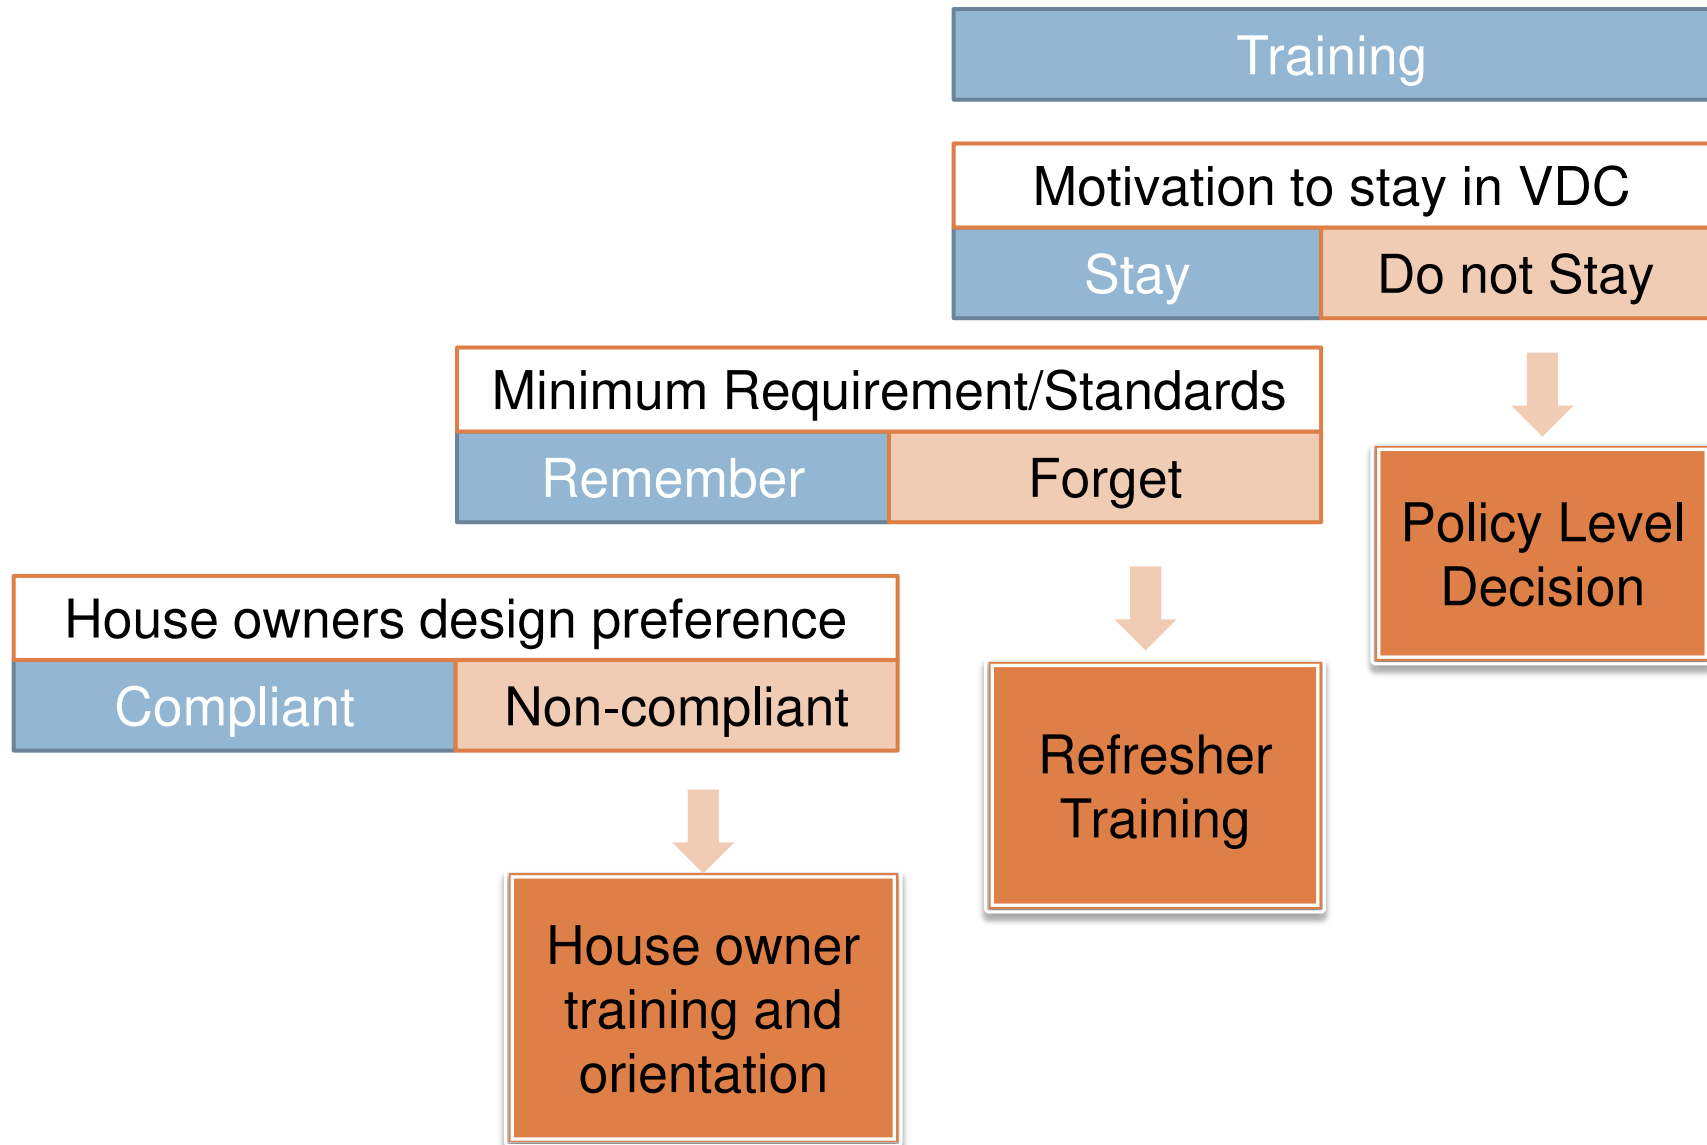

● Refresher Training Schedule

Time		Day 1
9:00	9:15	Registration
9:15	10:00	Course objective/overview, introduction and Pre test
10:00	10:30	Tea Break
10:30	12:00	Minimum Requirement (With Small Scale Demo Model)
12:00	12:45	Lunch Break
12:45	13:30	Non Complaint issues (Photos)
13:30	14:15	Discussion on technical issues
14:15	14:30	Tea Break
14:30	15:15	Training Video with key Information
15:15	16:00	Role of mason and Inspection Guideline
16:00	17:00	Post test, evaluation of the training and Closing



Session 1.2 Minimum Requirements (With Small Scale Demo Model

1



Vertical Member



Vertical Wooden post (75
mmx100 mm)

Wooden post 50 mm x38
mm @500 mm cc

Horizontal member, 2x 75
mm x 38 mm



23



● Refresher Training




JICA BBB Housing Training

Session: 1.3


Compliant and Non Compliant Houses




Correction Manual




1 Clean the surface and drill holes.

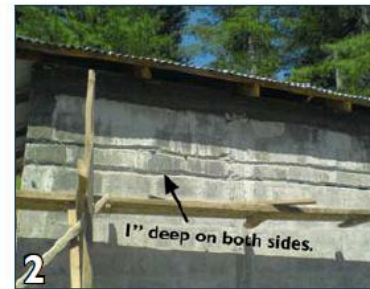

2 Make grooves on both faces to place reinforcement.

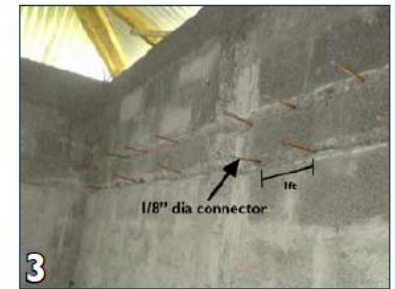

3 Insert connectors at every 1 ft.

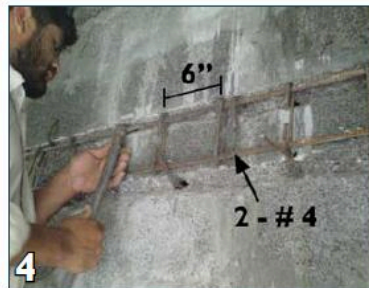

4 Place reinforcement at both faces and fix them firmly with 1/8" dia connectors.



5 Place shuttering and pour concrete.



6 Cure concrete for at least 10 days.

ORIENTAL CONSULTANTS CO., LTD.
Global Consulting H.Q.
