


FACTS AND FIGURES

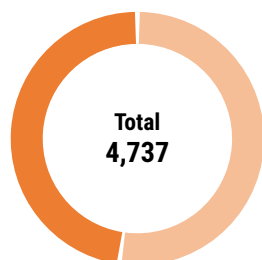

Damage Grade (1-2)
2,478

Damage Grade (3-5)
2,259

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	84.36%	44.19%
Timber Frame Structure	12.70%	16.91%
Adobe Structures	1.04%	2.85%
Stone and Cement Mortar Masonry	0.78%	1.32%
Others	1.12%	34.72%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	2,609	
PA Agreement	2,083	526
I st Tranche received	2,083	526
II nd Tranche received	1,516	1,093
III rd Tranche received	1,536	1,073

Houses

Under Construction: 1,573

Completed: 1,100

Retrofitting Status

Total Eligible HHs	666	
PA Agreement	244	422
I st Tranche received	239	427
II nd Tranche received		666

Grievances

Registered: 1,557

Addressed: 1,557

Non-compliances

Registered: 90

Addressed: 85

Data Updated on: 2019-04-22 00:00:00

P0 Presence

Active: PIN (Shelter)

Phased Out: AATWIN (Social Protection), BC (Shelter), EBMF (Education), FCA (Education), HELVETAS (Shelter), NRCS (Agriculture), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), PLAN (GESI), PLAN (Social Protection), SDA (Education)

OTHER SECTORS



Schools

Damaged: 45
Under Construction: 23
Construction Completed: 23



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	17,013	-	-
Aggregate	m ³	17,600	-	-
Sand	m ³	1,818	-	-
Timber	cu. ft.	2,103	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	58,297	-	-
Rebars	kgs.	184,202	-	-
Tin	bundle	2,383	-	-
Bricks	pcs.	157,980	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

KEY CONTACTS

Municipal Office

Tanka Moktan
Chairman
9855068590

Municipal Office

Sub er Narendra dutta bhatta
Focal Person
9848784643

Municipal Office

Sukmaya Thing
Deputy Chairman
9845503704

GMaLI/NRA

Som Raj Timilsena
NRA Chief-District
9855030632

Municipal Office

Tanka Bahadur Negi
Chief Administration Officer
9855088266

DLPIU-Building

Sudip Acharya
DUDBC.DLPIU Chief
9851153206

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING

Trainings (# out of total required)

7 days Training




50 days Vocational Training



Source: HRRP Analysis

TA ACTIVITIES MAP

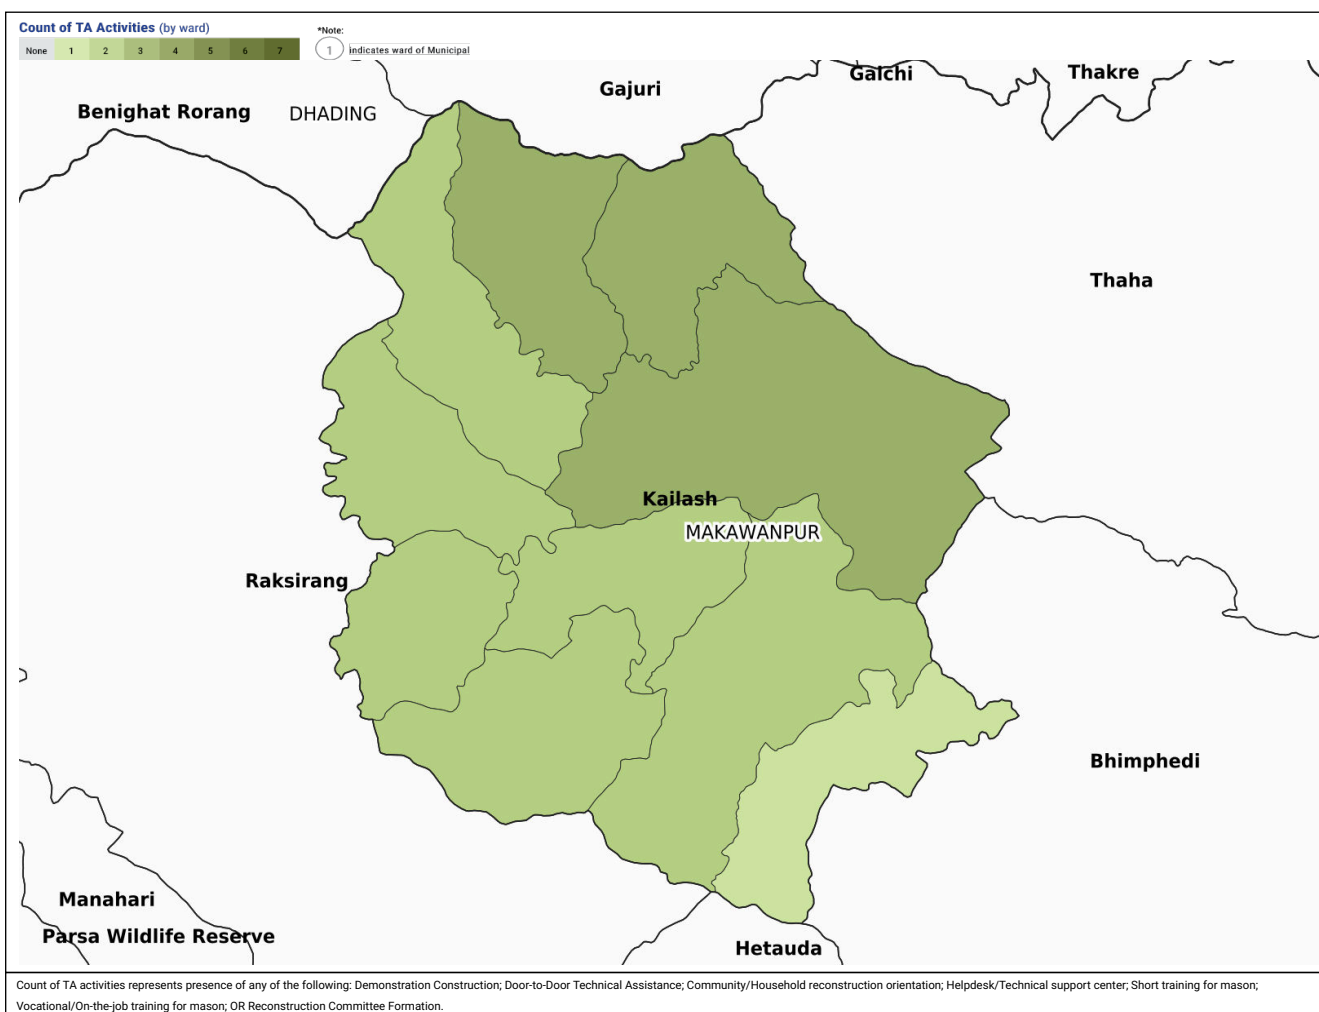

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. (District Coordinator) 2. Kausal Bist (District Technical Officer) 3. Sachin Malego (District Information Management Officer)
9849787273 984166793
