


### FACTS AND FIGURES

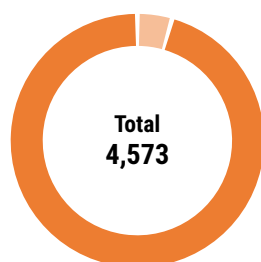

Damage Status - Private Structures

### MAJOR HOUSING TYPOLOGIES

| Typology                               | Municipal | District |
|----------------------------------------|-----------|----------|
| Stone and Mud Mortar Masonry           | 98.42%    | 89.07%   |
| Reinforced Cement Concrete (RCC) Frame | 0.57%     | 3.05%    |
| Brick and Cement Mortar Masonry        | 0.33%     | 2.11%    |
| Adobe Structures                       | 0.33%     | 4.25%    |
| Others                                 | 0.36%     | 1.52%    |

CBS damage assessment survey, 2015

### HOUSING RECONSTRUCTION & RETROFIT UPDATES

#### Reconstruction Status

|                                    |       |
|------------------------------------|-------|
| Total Eligible HHs                 | 4,459 |
| PA Agreement                       | 4,336 |
| I <sup>st</sup> Tranche received   | 4,336 |
| II <sup>nd</sup> Tranche received  | 4,013 |
| III <sup>rd</sup> Tranche received | 3,351 |

#### Houses

Under Construction: - Completed: 3,023

#### Retrofitting Status

|                                   |     |
|-----------------------------------|-----|
| Total Eligible HHs                | 254 |
| PA Agreement                      | 3   |
| I <sup>st</sup> Tranche received  | 3   |
| II <sup>nd</sup> Tranche received | -   |

#### Grievances

Registered: 672  
Addressed: 593

#### Non-compliances

Registered: -  
Addressed: -

Data Updated on: 2019-06-24 00:00:00

### P0 Presence

Active: No POs Reported

**Phased Out:** ACF (Shelter), GIZ (Health), NRCS (Health), OXFAM-GB (Agriculture), OXFAM-GB (Livelihood), OXFAM-GB (Shelter), OXFAM-GB (Hygiene), PA (Shelter), RoomTR (Education), SCI (DRM), SCI (Education), SCI (Livelihood), SCI (Shelter), SCI (Social Protection), SCI (Hygiene)

### OTHER SECTORS



#### Schools

Damaged: 42  
Under Construction: 13  
Construction Completed: 13



#### Health Posts

Damaged: -  
Under Construction: -  
Construction Completed: -

### STATUS OF CONSTRUCTION MATERIALS

| Materials    | Unit           | Req. Quantity* | Ava. | Cost (NRs.)** |
|--------------|----------------|----------------|------|---------------|
| Stone        | m <sup>3</sup> | 76,162         | Y    | 6,000         |
| Aggregate    | m <sup>3</sup> | 79,252         | N    | 12,000        |
| Sand         | m <sup>3</sup> | 8,142          | N    | 9,000         |
| Timber       | cu. ft.        | 9,433          | Y    | 3,500         |
| Cement (PPC) | Sack           | -              | Y    | 900           |
| Cement (OPC) | Sack           | 262,074        | Y    | 1,000         |
| Rebars       | kgs.           | 823,462        | Y    | 98            |
| Tin          | bundle         | 10,710         | -    | -             |
| Bricks       | pcs.           | 618,317        | Y    | 16            |

#### Types of Workers

1. Skilled mason
2. Labourer

#### Avg. daily wage (NRs.)

1,200 /-  
1,000 /-

### KEY CONTACTS

#### Municipal Office

Ramesh Wosthi  
Mayor  
9841291082

#### Municipal Office

Dipak Kumar Yadav  
Focal Person  
9844458865

#### Municipal Office

Taradevi Rimal  
Deputy Mayor  
9841548330

#### GMAI/NRA

Sambhu Kumar Shah  
NRA Chief-District  
9847068897

#### Municipal Office

Ashok Prasad Dahal  
Administration Officer  
9851246206

#### DLPIU-Building

Koshnath Adhikari  
DUDBC.DLPIU Chief  
98550465884

## HHs WITH LAND ISSUES

3

250

Landless

Guthi land

## STATUS OF TECHNICAL STAFF


| Staff               | Available Nos.            | Additional Req. Nos.      |
|---------------------|---------------------------|---------------------------|
| Engineers           | -                         | -                         |
| Sub-Engineers       | -                         | -                         |
| Asst. Sub-Engineers | -                         | -                         |
| Masons              | - (7 days)<br>- (50 days) | - (7 days)<br>- (50 days) |

Source: Municipal survey

## MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

## TA ACTIVITIES MAP

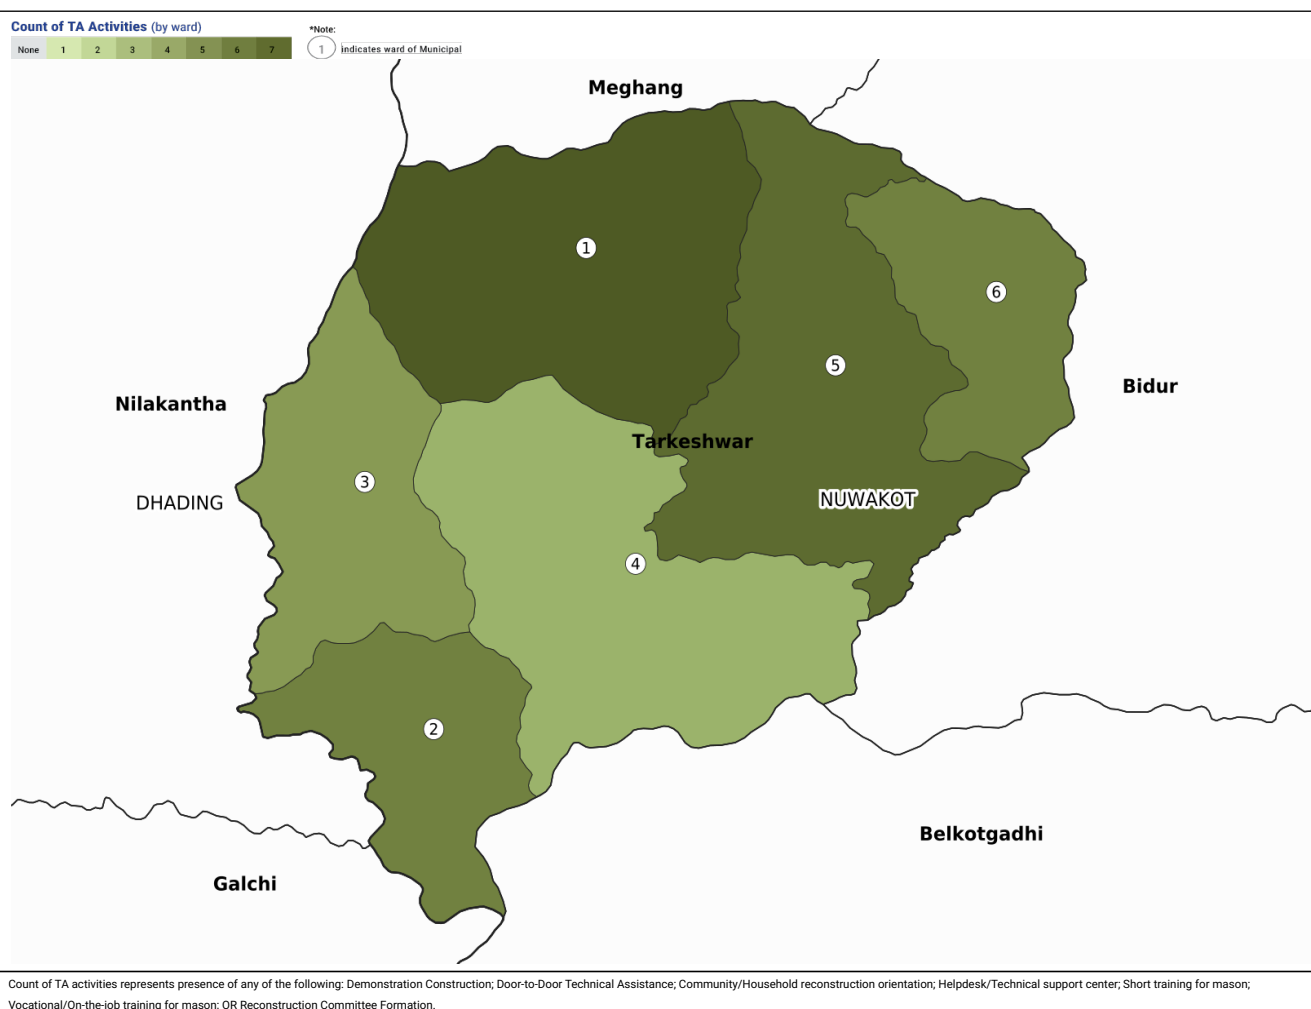

## FAQs

**Q: What documents are required for enrolment in the GoN housing reconstruction programme?**

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

**Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?**

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

**For further information** 1. Badri Pyakurel (District Coordinator) 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer)  
9851154201 9842062006
