

District Report

Ramechhap

6 - 19 July 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
HRRP Ramechhap team with the CLPIU M&E Consultant, DLPIU Engineer conducted field monitoring visit successfully to Liknu Tamakhosi Rural municipality at Dhobi Bazar starting from 4 th July to 6 th July 2018.	4/07/2018	4	0	Mr. Prakash Bishwakarma	Report
Joint field visit to Gothgaun of Ramechhap Municipality as successfully completed on 5 th of July 2018. A total of 4 people were take participant in the joint monitoring visit from HRRP, CLPIU M&E Consultant and DLPIU Engineer. The objective of the field visit was to interaction with the beneficiaries in regards to discussion on noncompliance house.	5/07/2018	4	0	Prakash Bishwakarma	
Coordination activity was conducted in Ramechhap district with an objective to make good relation and coordination among partner organization and government office. - Participant in the orientation and program planning workshop organized by Red cross Ramechhap. The objective of the workshop was to have interaction between partner organization working in the district. Red cross is going to implemented project to support vulnerable beneficiaries in the district which as approved by NRA. - A short coordination meeting was organized with the chief of MOUD-DUDBC Prachit Kadariya on 11th July 2018. The objective of the meeting was to provide the information and update of Partner organization and discussion about HRRP upcoming district activity. - Coordination meeting with Gmali Chief regarding new government organization restricting and discussion about HRRP upcoming events.	10/07/2018				
	11/07/2018				
	18/07/2018				

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Coordination meeting	24 July 2018, DTO, office, Manthali	HRRP	Prakash Bishwakarma
Orientation on 4W to 5W	26 July 2018, GS Hotel, Manthali	HRRP	Prakash Bishwakarma

News & Updates

Reconstruction status of Ramechhap upto Ashar 32. Source: Gmali, Ramechhap

CONSTRUCTION STATUS

- अनुदान सम्झौता सम्पन्न लाभग्राहीसंख्या
- दोश्रोकिस्ता भुक्तानीका लागि प्रमाणिकरण गरिएको लाभग्राहीसंख्या
- तेस्रो किस्ता भुक्तानीका लागि प्रमाणिकरण गरिएको लाभग्राहीसंख्या

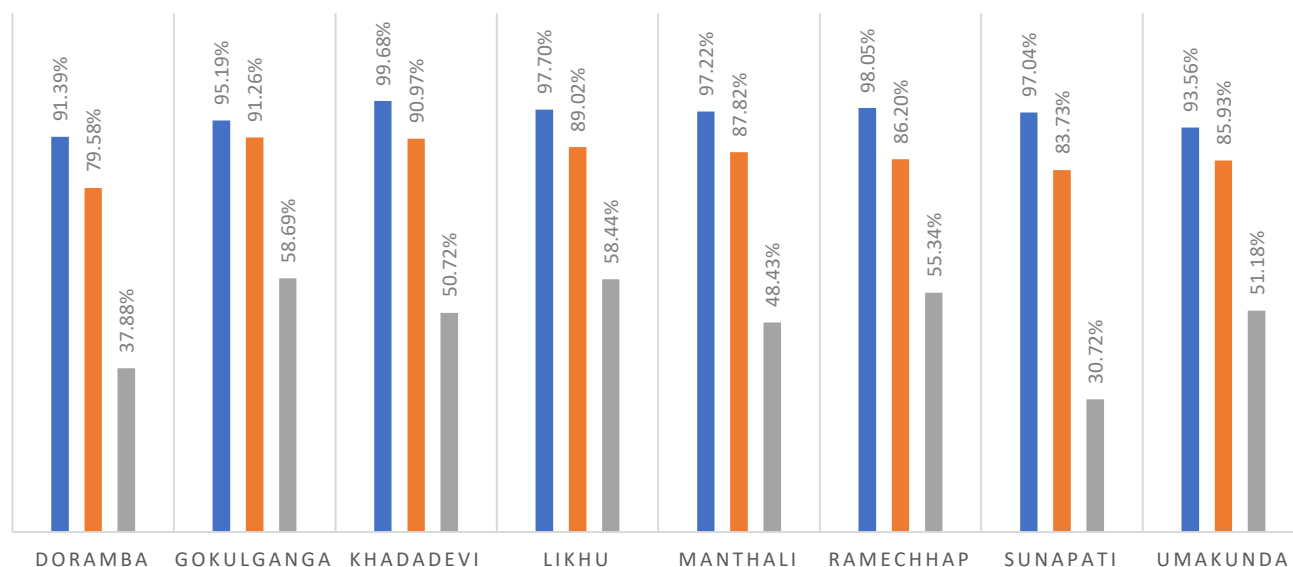

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
4 th July 2018	Likhu Tamakhosi Rural Municipality (Dhobi)	Prakash Bishwakarma (HRRP), Tulasi Ram Lamichhane (HRRP) Keshab Pandey (DSE), Deepak Thagunna (DLPIU Engineer), Janak Raj Joshi (M&E Consultant)
Objective(s)	To observe the reconstruction status of the beneficiaries	

	• To provide inputs to the beneficiaries in regards of housing reconstruction and for grant receive process • Interaction with the local representatives and beneficiaries to find the challenges and issues in the reconstruction.
Summary	Ramechhap, one of the districts of province number 3 is one of the 14 most earthquake affected districts. It comprises of 6 Rural Municipalities and 2 Municipalities. Among 6 Rural municipalities Likhu Tamakhusi is one of the rural municipality of Ramechhap district. It is about 35 km far away from the District headquarter, Manthali to the east. Dhobi is one of the village market located in the Likhu Tamakhosi Rural Municipality. The area was severely damaged during the Gorkha Earthquake 2015. Dhobi/Bijulikot is one of fast growing market in Ramechhap district after Manthali. The most of the damage houses were of traditional type design mostly of stone in mud mortar. A total of 1296 were beneficiaries in Dhobi/Bijulikot. In Dhobi/Bijulikot almost all beneficiaries who have signed PA agreement have started the reconstruction. The house under construction are mostly of stone in mud and cement mortar as stone locally available. But the availability of other construction materials such as bricks, cement and iron is difficult due to high cost of transportation. One Engineer (Narendra Basyal) and an Assistant Engineer have been deployed in the area by DLPIU-Ramechhap. With the effort from the technical person of DLPIU the work and reconstruction rate of the area is very good. The government staffs have been conducting community orientation and door to door technical assistant on regular basis. The continuous effort from them and community people enthusiasm has resulted as a good work and reconstruction rate is found satisfactory. In this regards on 20th June 2018 a joint monitoring visit was successfully completed with an objective to interaction with the beneficiaries and discussion about the challenges and issues regarding reconstruction. A total of 4 persons were participants in the monitoring program from DLPIU and HRRP. <u>Some highlights of the visits:</u> A total of 8 houses around Dhobi bazar in reconstruction phase were observed by the monitoring team. Reconstruction process has been boosted after the extension of government deadline for the tranche to end of the Ashard 2075. Some of the observed houses have completed the construction while DPC works of some houses were on going during the visit. Engineer and sub Engineer have been deployed in the area by DLPIU-Ramechhap, with the effort from the technical person, the reconstruction rate of the area is being improved. The government technical staffs have been conducting community orientation and door to door technical assistant on regular basis. The reconstruction in the area is fully supported by the local representative and community. During the visit short meeting was organized in Rural Municipality office with presence of executive officer, monitoring team and DLPIU engineer. ▪ The Rural Municipality and ward office has been supporting technical staffs in disseminating the information on the safer reconstruction and government grant procedure as well as guideline. ▪ DLPIU engineer shared the issues of changing the name of beneficiaries through it is difficult to receive government grant. ▪ During the meeting with Gaun palika Executive officer said that Right of road joining two district has been set 11 meters which has hindered the house lying with in the area for approval. ▪ Some of the noncompliance house were inception during the visit and interaction with the beneficiaries to incorporate the correction manual. ▪ Beneficiaries have positive attitude towards the government support and have been following the government guideline during the reconstruction.

	The construction rate as found very satisfactory. The support of government technical personnel was helpful and the presence and working modality of NGO/INGOs in the area was also constructive.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Name of the beneficiaries was found double in the reconstruction record. Due to the double name it is difficult to receive government tranche.	DLPIU Engineer and M&E should support to make correction of beneficiaries' name and make easy way to received government tranche.	DLPIU Engineer	AS soon as possible.
Right of road joining two districts has been set 11 meters which has hindered lying with in the area for approval.	Rural municipality should make policy.	Rural municipality	As soon as possible.
Photos			
			
Participant in Gaun palika level meeting at likhu Tamakhosi.		M&E consultant, DLPIU DSE and NRA engineer having discussion regarding reconstruction at Likhu tamakhosi rural municipality, Ramechhap.	
			
HRRP Technical Coordinator interaction with the house owner regarding the reconstruction at Dhobi Ramechhap. The house has been constructed using stone in mud mortar and file has been forwarded for the 2 nd tranche.		The house constructed in Likhu Tamakhosi rural municipality Ramechhap. The house has been constructed using brick in cement mortar and RCC Bands have been provided and file has been forwarded for the 3 rd government tranche.	

Visit 2			
Date	Location	Participants from HRRP and stakeholders	
5 th July 2018	Ramechhap-1, Gothgaun	Prakash Bishwakarma(HRRP), Tulasi Ram Lamichhane (HRRP), Janak Raj Joshi (M&E Consultant) and Anil Mahat (DLPIU Engineer)	
Objective(s)	- To observe the reconstruction status of the beneficiaries - To provide inputs to the beneficiaries in regards of housing reconstruction and for grant receive process - Interaction with the local representatives and beneficiaries to find the challenges and issues in the reconstruction.		
Summary	A Joint monitoring visit along with CLPIU M&E consultant, DLPIU Engineer and HRRP Ramechhap team successfully completed on 5th July 2018. A total of 4 person and ward Engineer and assistant engineer jointly observation the houses of Goatgaun of Ramechhap Municipality ward no-1. A total of 10-12 houses were observation and inspection in Goatgaun Ramchhap -1 by monitoring team. Most of the houses were constructed using stone in mud mortar and RCC Bands have been provided. The gable wall was being constructed using heavy materials without gable band. After the consultation and inspection of the NRA Engineer, the heavy gable wall has been removed and will be replaced by light structures. After the correction NRA engineer have forwarded the document for next government trance. The government technical staffs have been conducting community orientation and door to door technical assistant on regular basis. The reconstruction in the area is fully supported by the local representative and community. Through the motivation and consultation from NRA engineer beneficiaries were motivated to make correction in their houses according to the guideline from the technical person. Some of the Highlights of the Gothgaun visit: - A total of 12 noncompliance houses were inspection and interaction with the beneficiaries to make correction for the government grant. - The ward office has been supporting technical staffs in disseminating the information on the safer reconstruction and government grant procedure as well as guideline. - Beneficiaries have positive attitude towards the government support and have been following the government guideline during the reconstruction According to the NRA engineer a total beneficiaries is 630 amongst them 611 have received 2nd trance and 200 beneficiaries have received 3rd tranche and remaining are forwarded to NRA for necessary action.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
10-12 houses are in non-compliances	NRA engineer should interaction with beneficiaries and motivated them to make correction.	NRA Engineer and beneficiaries	As soon as possible.

Photos



Monitoring team interaction with the community people and beneficiaries regarding the reconstruction at Ramechhap-1, Goatgaun.



The house of Ros Bahadur Nepali constructed in Gothgaun, Ramechhap-1. The house has been constructed using stone in mud mortar and RCC Bands have been provided. The gable wall has been constructed using heavy materials without gable band. The house owner has received second tranche of reconstruction grant



Interaction with the beneficiaries at Gothgaun, Ramechhap-1. After the consultation of the NRA Engineer, the heavy gable wall has been removed and has been replaced by light structures. The house of Kalu Sarki constructed in Gothgaun, Ramechhap-1. The house has been constructed using stone in mud mortar and RCC Bands have been provided. The house owner has received second tranche of reconstruction grant and has been forwarded for the third tranche.



The house has been constructed using stone in mud mortar and RC banda have been provided. The gable wall has been constructed using heavy materials without gable band. The house owner has received second tranche of reconstruction grant.

Housing Typology Report



The house of Bel Kumar Basnet being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. RC bands have been provided to the house. The house has been constructed up to sill level. The house owner has received second tranche of reconstruction grant. The house has been constructed under TA of KFS Nepal



The house of Bharat Kumar Karki being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. Timber bands have been provided to the house. The house owner has received third tranche of reconstruction grant. Bracing has been provided in truss. The house has been constructed under TA of KFS Nepal



The house of Bikram Bhujel being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. RC bands have been provided to the house. The house has been constructed up to intermediate band level. Double framed windows and doors have been used. The house owner has received second tranche of reconstruction grant. The house has been constructed under TA of KFS Nepal.



The house of Bel Kumar Basnet being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. RC bands have been provided to the house. The house has been constructed up to lintel level. The house owner has received second tranche of reconstruction grant. The house has been constructed under TA of KFS Nepal. Chandra Bahadur Tamang



The house of Chaturman Darji being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. RC bands have been provided to the house. The house has been constructed up to intermediate band level. Double framed windows and doors have been used. The house owner has received second tranche of reconstruction grant. The house has been constructed under TA of KFS Nepal.



The house of Dhal Bahadur Magranti being constructed in Saipu, Likhu Tamakoshi RM-2. The house has been constructed by using stone with mud mortar. RC bands have been provided to the house. The house has been constructed up to intermediate band level. Double framed windows and doors have been used. The house owner has received second tranche of reconstruction grant. The house has been constructed under TA of KFS Nepal.
