


FACTS AND FIGURES

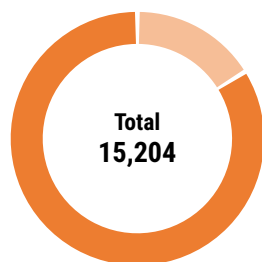

Total
15,204

Damage Grade (1-2)
2,455

Damage Grade (3-5)
12,749

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	65.62%	89.07%
Adobe Structures	14.64%	4.25%
Reinforced Cement Concrete (RCC) Frame	11.47%	3.05%
Brick and Cement Mortar Masonry	5.01%	2.11%
Others	3.26%	1.52%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	12,693
PA Agreement	11,929
I st Tranche received	11,929
II nd Tranche received	11,113
III rd Tranche received	7,926

Houses

Under Construction: - Completed: 7,544

Retrofitting Status

Total Eligible HHs	240
PA Agreement	90
I st Tranche received	90
II nd Tranche received	240

Grievances

Registered: 1,693
Addressed: 1,464

Non-compliances

Registered: -
Addressed: -

Data Updated on: 2019-06-24 00:00:00

P0 Presence

Active: BC (Shelter), NSET (Shelter)

Phased Out: ACF (Shelter), BO (Education), GIZ (Health), GON-PAF (Shelter), HFH (DRM), HFH (Livelihood), HFH (Shelter), HFN (Shelter), ICIMOD (Renewable Energy), ICIMOD (Livelihood), ICIMOD (Shelter), ICIMOD (Social Protection), ICIMOD (Hygiene), MI (Shelter), MIDSON (Health), NF (Education), NRCS (Health), NSET (Shelter), OXFAM-GB (Agriculture), OXFAM-GB (Livelihood), OXFAM-GB (Shelter), PA (Shelter), Paribartan-N (Education), RDB (Education), RoomTR (Education), RoundTN (Education), SCI (Education), SCI (Shelter), WFP (Education), WR (Shelter), WVIN (Hygiene)

OTHER SECTORS



Schools

Damaged: 89
Under Construction: 48
Construction Completed: 48



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	242,747	Y	6,000
Aggregate	m ³	253,082	Y	7,000
Sand	m ³	25,954	Y	5,000
Timber	cu. ft.	30,078	Y	4,500
Cement (PPC)	Sack	-	Y	850
Cement (OPC)	Sack	835,260	Y	950
Rebars	kgs.	2,621,748	Y	94
Tin	bundle	34,127	Y	-
Bricks	pcs.	1,695,063	Y	12

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

900 /-
600 /-

KEY CONTACTS

Municipal Office

Sanju Pandit
Mayor
9851049721

Municipal Office

Uttam Shah
Focal Person
9841645323

Municipal Office

Gita Kumari Dahal
Deputy Mayor
9841087449

GMAI/NRA

Sambhu Kumar Shah
NRA Chief-District
9847068897

Municipal Office

Sudev Kumar Pokhrel
Administration Officer
9851250111

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
98550465884

HHs WITH LAND ISSUES

89

Landless

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

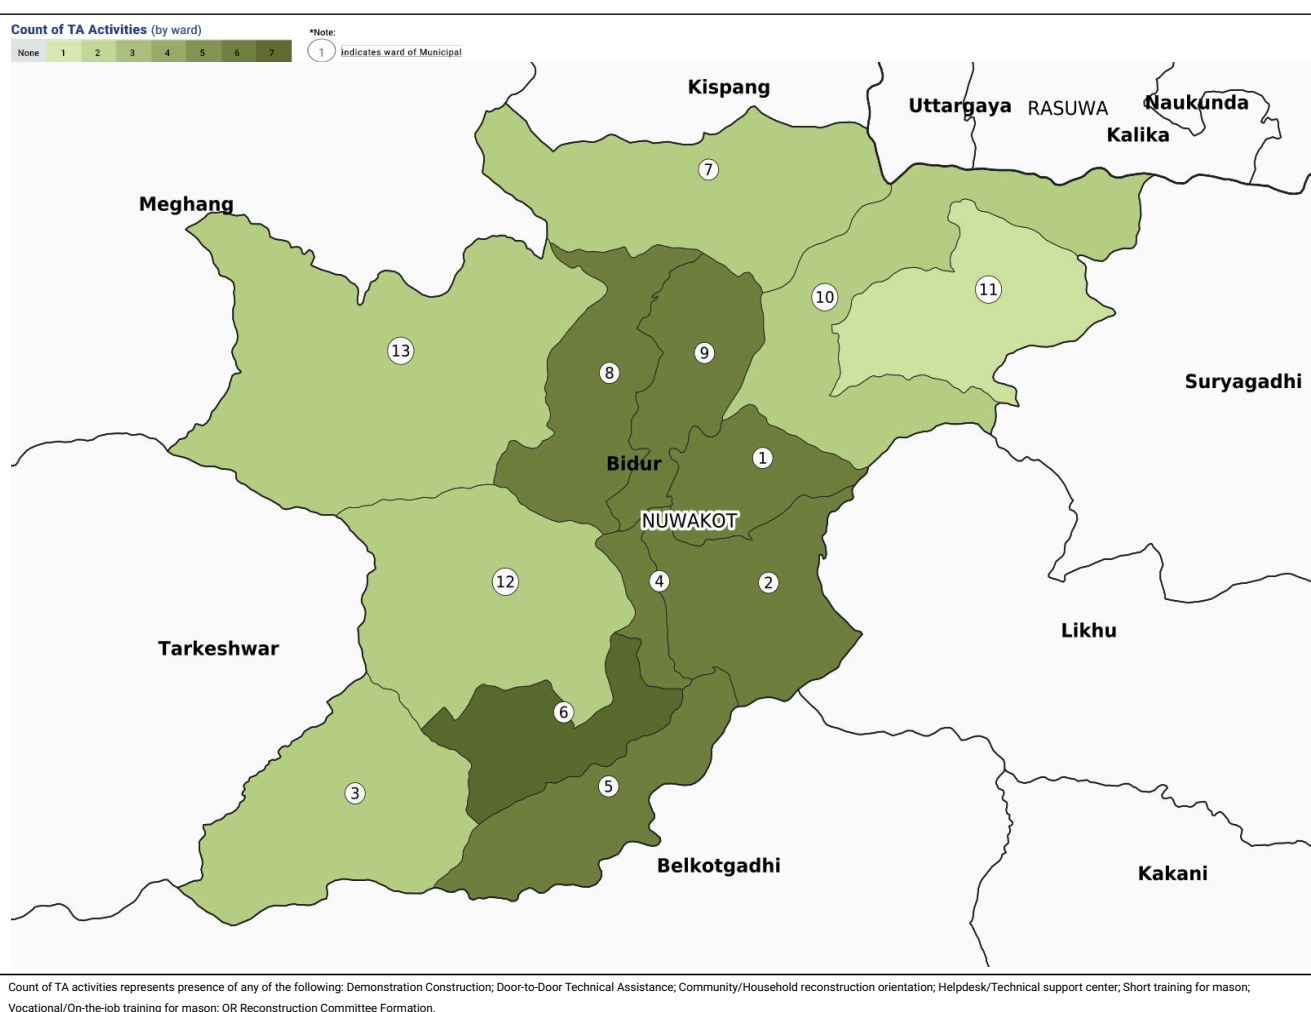

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Badri Pyakurel (District Coordinator) 9851154201 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer) 9842062006
