


HRRP BULLETIN

6 August 2018



Buddha Lal Sunar's shelter in ward no. 8, Dakshinkali Municipality, Kathmandu; the kitchen (L), inside the shelter (centre), and the toilet (R). Buddha lives in the shelter with his three children and his wife. Their shelter is around the average size of 20.5m² and is built on land that they own where their house used to be. They are eligible to receive the GoN housing reconstruction grant, and have already received the first tranche of 50,000 NPRs, but they have yet to start rebuilding their home as they are still saving to cover the cost of reconstructing and they have not had access to any technical assistance. (From [HRRP Temporary Shelter Research Report](#))

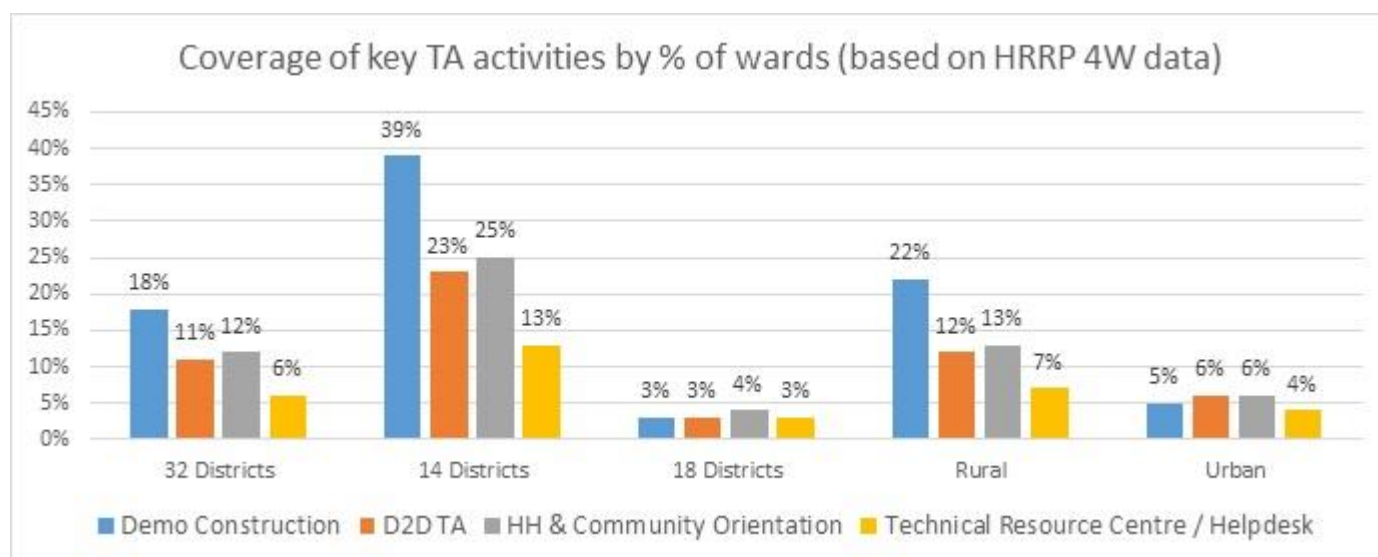

HRRP 4W Data on coverage of key technical assistance activities clearly illustrates major issues with coverage. Overall coverage is low, but for the 18 moderately affected districts and for urban areas, coverage is well below that of the 14 most affected districts and rural areas. HRRP estimates that 75 million USD is required for socio-technical assistance to cover gaps and support households to completion of earthquake resilient houses across all 32 earthquake affected districts. Whilst this is an enormous investment it represents just 7% of the amount of money yet to be disbursed through the GoN's housing reconstruction grant.

Highlights


- HRRP advocates for the tranche disbursement deadlines to be extended for at least the next two building seasons in rural areas, and the next four in urban areas, to allow a realistic period for households to complete their reconstruction.
- [NRA Newsletter, July 2018](#)
- Initial findings from **NRA, Building DLPIU technical staff survey** (survey form in [English](#) and [Nepali](#))
- Update from Hollow Concrete Block Technical Working Group on field visit to Kaski
- [HRRP Temporary Shelter Research Report](#)
- [HRRP Input for World Bank Stakeholder Consultations as part of EHRP Mid-Term Review Process](#)
- [Presentations from 6 August Urban Technical Session](#)
- **Third tranche inspection:** issues with standards related to solar panels and toilets
- Update from **CBDRM Platform Partner's Consultative Meeting**, 6 August
- **Transition from HRRP 4W to NRA 5W:** POs are requested to submit activity updates at district level by the 23rd of each month, using the data collection template which can be downloaded [here](#). First round of IM products based on NRA 5W data will be available from next week.
- During HRRP municipal level coordination meeting in **Barhabise Municipality, Sindhupalchok**, on 27 July participants shared that the NRA's tranche disbursement deadline is leading to households living in high risk areas to reconstruct in these risky areas to meet the deadline and not miss out on the GoN housing reconstruction grant.
- [Revised HRRP FAQs](#), please send questions for inclusion or suggestions for improvements to Anu Prasai Lama, nco1@hrrpnepal.org
- [Global Shelter Cluster Strategy, 2018-2022](#)

UPDATES & REQUESTS

National

NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 1 August:

	8 July	23 July	1 August
Total No. Eligible HHs	807,486	807,486	807,486
HHs Enrolled	721,281	722,087	722,101
HHs Received 1st Tranche	712,943	713,999	714,174
HHs Applied for 2nd Tranche	475,619	490,167	502,742
HHs Received 2nd Tranche	441,307	465,903	468,516
HHs Applied for 3rd Tranche	243,440	261,924	271,895
HHs Received 3rd Tranche	195,657	225,830	226,791

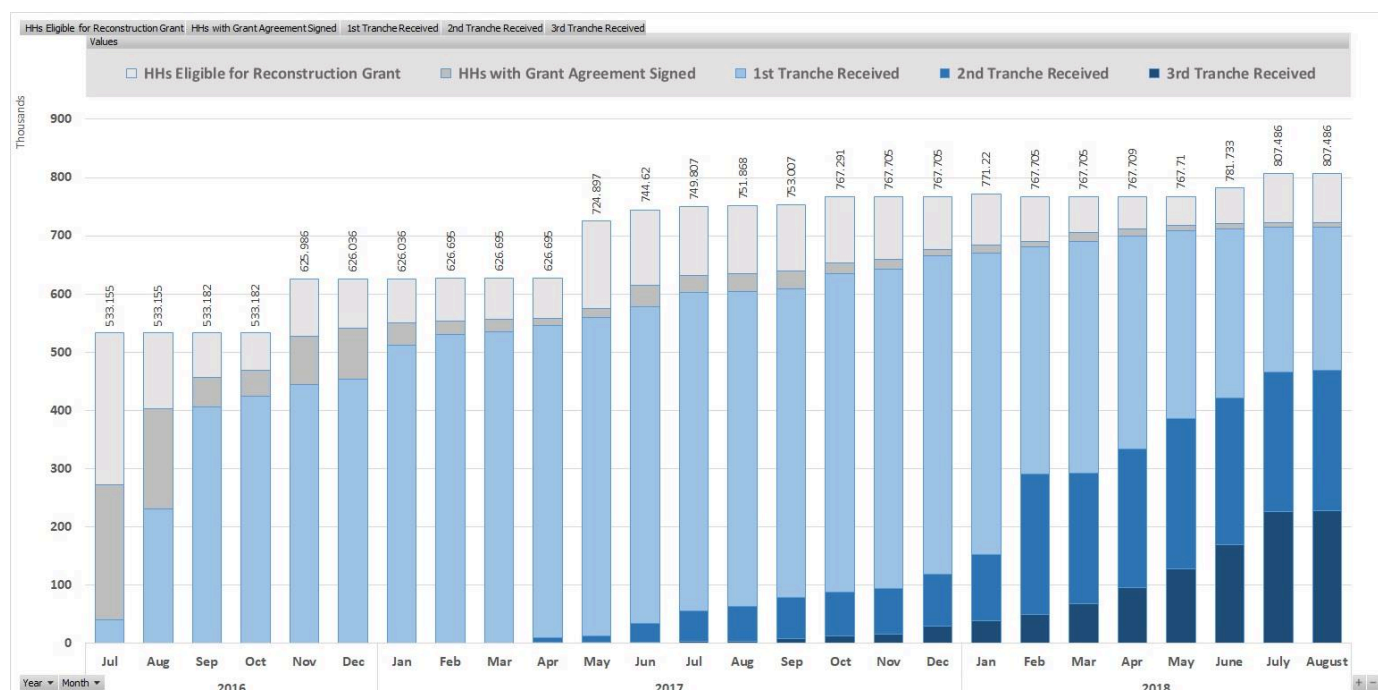

Housing reconstruction progress based on MoFALD CLPIU enrolment data from July 2016 to 1 August 2018.

NRA, Building DLPIU Technical Staff Survey: this survey was launched in July with the objective of understanding how technical staff in the NRA, Building DLPIUs access information, how they share information with households, and to gather more information on their experience of reconstruction. The survey also provides space for the respondents to share what support they feel they need in the role. The survey form is available in [English](#) and [Nepali](#). A total of 489 responses have been received, with a minimum of 25 respondents from each of the 14 most affected districts as well as responses from Gulmi, Tanahun, Lamjung, Myagdi, Baglung, Bhojpur, Khotang, Arghakhanchi, and Nawalpur in the 18 moderately affected districts. 64% of respondents are engineers, 21% sub-engineers, and 15% assistant sub-engineers. 1% of respondents were recruited in 2015, 41% in 2016, 34% in 2017, and 24% in 2018. 51% of respondents had not received any training before being deployed and 24% have not received training after deployment. Walking is the primary mode of transport for 84% of respondents. Other modes of transport include local bus (24%), using their motorbike (28%), and using a motorbike provided by work (12%). Respondents reported visiting an average of 34 households per month.

Hollow Concrete Block Technical Working Group Update, Kaski Field Visit: members of the HCB TWG from HRRP conducted a field visit in Kaski from 30 July to 3 August. They were accompanied on the field visit by the District Support Engineer, NRA, Building DLPIU engineers, Rupa Annapurna Rural Municipality Mayor, and the Ward Secretary. The purpose of the visit was to meet with HCB producers, masons that are constructing with HCBs, and households that have chosen to reconstruct their house with HCBs to collect further information to support preparation of a HCB manual for producers and construction workers, as well as information material for households. During the visit they observed the configuration of HCB houses, the construction process, and how earthquake resistant elements are being incorporated. If you have any questions or would like to be part of the HCB TWG, please contact Kuber Bogati, HRRP National Technical Coordination Officer, techofficer1.national@hrrpnepal.org.



Rupa Rural Municipality, Kaski: a house constructed using HCBs with an attempt at confined masonry. The household has yet to receive for the second tranche of the GoN housing reconstruction grant.



Rupa Rural Municipality, Kaski: load bearing building using HCB, four rooms with passage, RCC columns were constructed at junction of wall with 4 no., 12mm diameter bars in each column. The household has yet to receive for the second tranche of the GoN housing reconstruction grant.


CBDRM Platform Partner's Consultative Meeting, 6 August: the meeting was organised by MoFAGA with coordination and operational support from the IFRC. Participants included MoHA, Kathmandu Metropolitan City, and more than 30 POs including, WFP, IRC, Save The Children, Practical Action, Australian Aid, NSET, UNICEF, Tearfund, DCA World Vision, and VSO. It was agreed during the meeting that all POs should develop projects focused on capacity development of local bodies and that DRM project mapping will be introduced. POs are requested to provide all project information to MoFAGA before approval and implementation. It was also agreed that a CBDRM platform focal person will be selected from each participating agency as well as all three tiers of GoN to ensure effective communication. MoFAGA committed to strengthen inter-ministerial coordination mechanisms. It was also agreed that the MoFAGA website will be updated within 15 days with details of POs working in DRR. MoFAGA are working to develop a uniform training package on DRR for local authorities. A roster of trainers, from POs, with different expertise in capacity development will be developed and endorsed by MoFAGA.

Second Tranche Disbursement Deadline, 16 July: it has been almost one year since the NRA first announced the tranche disbursement deadlines ([see HRRP Bulletin from 24 July 2017](#)) and there has been mounting evidence that the deadline is causing trauma and stress for people trying to manage their housing reconstruction. The deadlines are part of the reason for the [large-scale borrowing at high interest rates that look set to cause a potential debt crisis](#). They are also the reason for people building small houses just to collect the grant. These houses do not meet people's living requirements and cannot represent a successful housing reconstruction. It is very positive that the numbers of households progressing with their construction is consistently increasing, but as of 1 August there are 580,695 households that need support to get to completion. This is not possible within the current deadlines. Experience from other post-disaster reconstruction efforts shows that approximately 5 years is required at least, and urban requires more time. **HRRP advocates for the deadlines to be extended for at least the next two building seasons in rural areas, and the next four in urban areas, to allow a realistic period for households to complete their reconstruction.**

Transition from HRRP 4W to NRA 5W: the HRRP 4W has been phased out from July 2018 to streamline data collection fully to the NRA 5W. HRRP is supporting data collection from POs for the 5W using a revised template for data collection which can be downloaded [here](#). The 5W will be collected by HRRP district teams to make 5W reporting timely. To support with the process, POs are requested to submit activity updates by the 23rd of each month. Please contact your relevant [HRRP District Coordination Team](#) or Uttam Paudel, im.manager@hrrpnepal.org, if you have any questions or need support. The first round of data collection is now complete – many thanks to all the POs that have submitted their data. IM products are currently being prepared based on this data and will be shared next week.

Monsoon Impact: heavy rainfall since the beginning of July has caused loss of life and damage to property and infrastructure in many areas of Nepal. The infographic below from the UN RCO, provides a summary of the situation as of [28 July](#).

NEPAL: Monsoon Weekly Update (as of 28 July 2018)

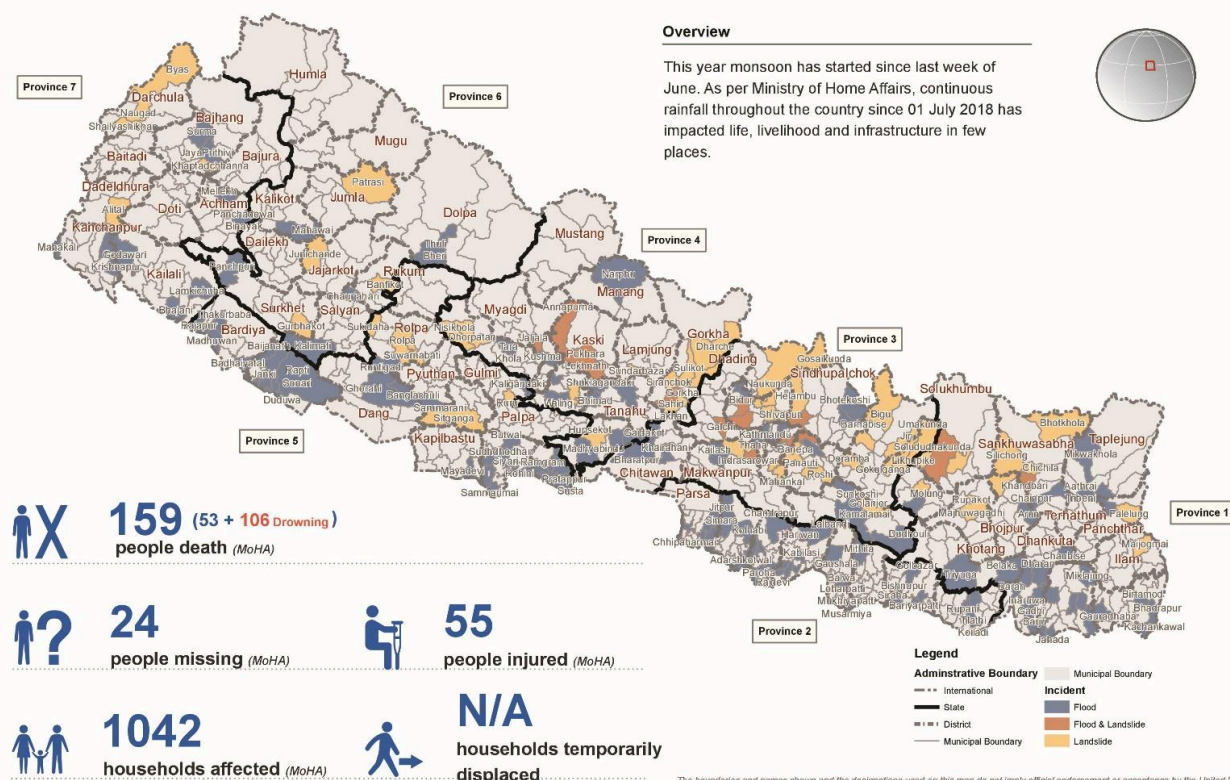

Districts & Municipalities

Third tranche inspection, issues with standards related to solar panels and toilets: as per the inspection guidelines, 25,000 NPRs of the third tranche of the GoN housing reconstruction grant is tied to construction / repair of the household toilet (mandatory) and installation of solar panels (not mandatory). NRA, Building DLPIU technical staff in each of the 14 most affected districts are including toilets in the third tranche inspection. However, there is no standard process or technical requirements in place so the approach adopted depends on the district. For example, in Gorkha if there is no toilet the engineer will not conduct an inspection, even if the house is complete, and it is mandatory to have water seal pan and soak pit. In Sindhuli, it is not mandatory to have completed the toilet to be approved for the third tranche, it is just necessary that it is under construction. In Kavre, as there are no specific criteria for inspection of toilets the engineers simply check if there is a toilet present or not and pre-earthquake toilets that are still in place are accepted without specific requirements for repair / improvement. There have been some cases where engineers approved a house for third tranche but the municipality blocked it as a toilet had not been constructed. In Bhaktapur, the engineers observe the suitability of toilet according to the housing typology and provide advice on corrections / improvements that are needed.

'Parks, not parking lots: Exemplary community effort to restore open space gives hope for a greener Kathmandu', Nepali Times, 20 July: positive story of urban regeneration focused on the community redevelopment of Nandi Keshwor Garden from a smelly rubbish dump five years ago to a community garden that provides open space in emergencies (including the 2015 earthquake).



Left: Nandi Keshwor Garden before community redevelopment. Right: Nandi Keshwor Garden after redevelopment.

Practical Action Learning Workshop, Strengthening the Supply Chain of Construction Materials in Earthquake Affected Districts, Makwanpur, 19 July: the event brought together local authorities from Lamjung and Makwanpur to discuss and share learnings from the UKaid funded project, Strengthening the Supply Chain, as well as to share plans for support to 500 of the most vulnerable families through UKaid funding for 'Leave No One Behind' initiatives. The 'Strengthening the Supply Chain' project has already established 64 CSEB (Concrete Stabilized Earth Bricks) enterprises, 44 stone cutting enterprise, and 12 timber treatment facilities as part of its objective to supply quality construction materials. In addition, the project has established 41 resource centers and depots in the two pilot districts of Rasuwa and Nuwakot and three scale-up districts of Dhading, Sindhupalchowk and Gorkha. Through the "Demand Aggregation" initiative, the project has been able to provide construction materials at a cheaper rate to more than 8,500 households.

HRRP District and Municipal Coordination Meetings, 23 July – 6 August: during this period district coordination meetings took place in Ramechhap (24 July), Nuwakot (25 July), and Dolakha (26 July). Municipal level meetings took place in Sunkoshi Rural Municipality, Sindhupalchok (26 July), and Barhabise Municipality, Sindhupalchok (27 July). Some of the highlights from these meetings include:

- In **Ramechhap**, it was highlighted that Sunapati and Doramba Rural Municipalities are quite behind in reconstruction compared to other Rural Municipalities. Difficulty in transportation of construction materials due to bad road condition, unavailability of man power for long time and local mason and beneficiaries engaged in agricultural works have slowed down the reconstruction during monsoon. Regarding the non-compliance cases in the district, beneficiaries have started getting Government tranche after the issues have been addressed by the District Support Engineer.
- In **Nuwakot**, GMAI Chief requested coordination between POs and concerned Government stakeholders such that any issues would be solved together and on time. He further requested that POs update their project status on time and stay in close coordination with GMAI and HRRP. Regarding relocation, 191 out of 377 beneficiaries have been relocated and received land certificate. There are other places at high risk of collapsing due to landslide. Some places like Mulbari in Shivapuri Rural Municipality are also at risk to landslide but there are beneficiaries who have already built houses and taken Government grant which has created difficulty in relocation.
- In **Dolakha**, GMAI Chief requested POs to support the verification of vulnerable household list in the district and to update name lists of beneficiaries and reconstruction status of the wards of Gaunpalikas and Municipalities of Dolakha which was not updated till date (ward chairs know the numbers of beneficiaries, but they don't know/record of the beneficiary name lists and don't know how many houses reconstructed). The GMAI Chief also wished speedy recovery for the recently wounded focal person/engineer of GMAI Dolakha Mr. Narayan Prasad Siwakoti.
- In **Sunkoshi Rural Municipality**, there are still people waiting for the resurvey since they have been missed by the resurvey team. This has also caused difficulty for the elected representatives to face households as some genuine earthquake affected HHs have not been included in the grievance list. On contrary, there are HHs listed in non-eligible list even without the resurvey. Concerns were raised regarding delays in

reconstruction due to transfer of technical persons. Ward representatives proposed that they be consulted and taken approval from them before the technical persons are transferred to minimise the gap in reconstruction. Some ward chiefs want to use different colors of CGI sheets to make the village beautiful visually. Some ward chiefs have also refrained from signing the files unless CGI sheets are installed. Many households have already taken loans from banks at higher interest rate for the reconstruction. They would want to convert their loans to the provision of concessional loans, but this has not happened yet.

- In **Barhabise Municipality**, discussions were: Grievance Management Committees have been formed in different wards to address grievances at the local level but not many households are aware of this. Many Rural/Municipalities representatives have been receiving complaints regarding grievances since the resurvey team were not able to reach all the wards and the resurvey was conducted without consultation with the elected representatives so many earthquakes affected HHs have been missed. There are several landless people who are waiting for the decision of NRA on how to move ahead. Identification of landless has also been difficult due to the lack of identification. In case of the settlements at high risk areas in Jure, no action has been taken yet to relocate them elsewhere while the Ward Chairpersons are also unaware of the procedure of addressing the issues. The NRA deadline has reported to have negative impact on the households living in high risk areas with increasing construction in these risky areas to meet the deadline and not to miss the tranche.

[HRRP District Coordination Team Dolakha, Weekly District Report, 20 July – 2 August 2018](#)



Ward No. 4, Bhimeshor Municipality, Dolakha: under construction house up to DPC level. The home owner is waiting for the construction material from the local crusher for the construction of superstructure. The owner has received the first tranche of the GoN housing reconstruction grant and has been approved for the second tranche.

HRRP District Coordination Team Gorkha, Weekly District Report, 20 July – 2 August 2018



Ward No. 6, Dharche Rural Municipality, Gorkha: a single storey, stone masonry house with RCC band. The owner has received all three tranches of the GoN housing reconstruction grant.

HRRP District Coordination Team Kathmandu, Weekly District Report, 20 July – 2 August 2018



Ward No.6, Changunarayan Municipality, Bhaktapur: a single storey, load bearing structure made up of ACC light weight blocks and CGI roof with steel post used as vertical reinforcement. The owner has received the second tranche of the GoN housing reconstruction grant. The owner has submitted all the documents including the test reports of the blocks and applied for third tranche.

HRRP District Coordination Team Kavre, Weekly District Report, 20 July – 2 August 2018



Ward No.1, Panauti Municipality, Kavre: a two-room, stone and mud mortar masonry house with RCC bands and flexible roof. The owner has received the second tranche of the GoN housing reconstruction grant and has been approved for the third tranche.

HRRP District Coordination Team Makwanpur, Weekly District Report, 20 July – 2 August 2018



Ward No. 12, Hetauda Municipality, Makwanpur: a single storey, two-roomed, brick in cement mortar, attic and flexible roof. The owner has received all three tranches of Government housing reconstruction grant.

HRRP District Coordination Team Nuwakot, Weekly District Report, 20 July – 2 August 2018



Ward No. 3, Tadi Rural Municipality, Nuwakot: brick and cement mortar masonry houses. 73 vulnerable households of Urleni (Tadi-1) are relocated to Kharanitar (Tadi-3). Till date, twenty-four houses have been constructed and 46 more will be constructed after the rainy season. These houses are built with support from OXFAM.

Requests for Partner Support

Call for Presentations for next '20x20 Partner Sharing Session', 17 August: many thanks to the partners that presented at the first of these sessions on 14 June. Partners interested to present are requested to write to Ruplal Aidi, HRRP National Coordination Officer, nco2@hrrpnepal.org, to indicate their interest to present and what the proposed topic of the presentation is. N.B. this session will use the 'Pecha Kucha', 20 X 20 style of presentation. Each presentation will have 20 slides with 20 seconds allowed per slide, totaling 6 minutes and 40 seconds. The presentation is automated and therefore no additional time is possible.

DOCUMENTS & PRODUCTS

Government of Nepal

[NRA Newsletter, July 2018](#)

HRRP

[HRRP Input for World Bank Stakeholder Consultations as part of EHRP Mid-Term Review Process:](#) many thanks to all the partners that participated in the session on 19 July to review and prepare the key points. Any feedback or suggestions for improvement to this document can still be shared with Siobhan Kennedy, HRRP Recovery Advisor, siobhan@hrrpnepal.org.

Temporary Shelter Research Report: HRRP launched this research to document the status of temporary shelters across the 14 districts most affected by the earthquakes, to explore the reconstruction issues and challenges that affect families that are in temporary shelter, and to assess needs in terms of further temporary shelter support. During the research data was collected from a total of 441 respondents. Based on the research findings, the following recommendations have been developed:

- Socio-technical assistance needs to be accessible to those that have not started construction, and include information on topics particular to that situation such as budgeting, material quality and purchasing, hiring of labour, designing the house, etc.
- HRRP advocates for the GoN deadlines for disbursement of the housing reconstruction grant tranches, to be extended for at least the next two building seasons to allow a realistic period for households to complete their reconstruction.
- Roll out information and support for maintenance and improvement of shelters. This could include information on rainwater harvesting and drainage that is equally applicable and important for construction of houses.

Urban Housing Reconstruction: urban housing reconstruction is a complex process, and will require more time than rural housing reconstruction. HRRP is working to document the status of urban housing reconstruction and to facilitate reconstruction actors to collectively develop a way forward to scale up the urban housing reconstruction.

- [Presentations from 6 August technical session:](#) presentations are from M&E CLPIU Building, NSET, Lalitpur Metropolitan City, and Lumanti. Partners interested to present at subsequent sessions may contact Bhubaneswori Parajuli, HRRP National Technical Coordinator, techcord.national@hrrpnepal.org.
- [Map of Urban Wards in Earthquake Affected Districts:](#) these wards have been identified through consultations with municipal and district officials, NRA, Building DLPIU technical staff, and HRRP District Coordination Teams. 589 wards were identified as urban across the 32 districts and these are spread across 10 Rural Municipalities, 79 Urban Municipalities, 1 Sub-Metropolitan City, and 4 Metropolitan Cities.
- [Updated HRRP Tool to prioritize additional support for Vulnerable HH:](#) the tool now includes a column for rural / urban so that the analysis can be done on the basis of rural or urban wards.

Revised HRRP FAQs: we are pleased to share an updated version of the HRRP FAQs. The '[FAQs](#)' section of the HRRP website is being updated to reflect the revisions and we expect this to be completed by the middle of this week. Please send questions for inclusion or suggestions for improvements to Anu Prasai Lama, nco1@hrrpnepal.org.

[18 Districts, Updated Overview of Reconstruction Status in Moderately Affected Districts](#)

Housing Reconstruction Progress Maps: based on MoUD CLPIU inspection data as of 22 July.

[Partnership Agreement between HHs and GoN](#)
[Construction Started](#)
[1st tranche received](#)
[Compliance rate 2nd tranche](#)
[Compliance rate 3rd tranche](#)
[Construction Completed](#)

Partners

Global Shelter Cluster Strategy, 2018-2022: the strategy has been developed with the aim of supporting shelter gaps identified in the evaluation of the [2013-17 GSC strategy](#) and talks to the need for greater integrated response in collaboration with other sectors. If you have any questions regarding the strategy, please contact Pablo Medina Deputy Global Shelter Cluster Coordinator, IFRC, pablo.medina@ifrc.org, and Miguel Urquia, Deputy Global Shelter Cluster Coordinator (Geneva), UNHCR, urquia@unhcr.org.

Baliyo Ghar TV, Episodes 114 and 115: last week's episode covered the story of Lambari, a Dalit village in Lamidada of Kalinchowk Rural Municipality and Nepali Gaun, a Dalit village in Laduk of Bigu Rural Municipality. Villagers shared their experience of reconstruction and discussed the impact of technical assistance. The episode also include an interview with Mr. Nishan Budhathoki, Ward Chief, Ward No. 3, Kalinchowk RM and Mr. Boktam Tamang, Ward Chief, Ward No. 4, Bigu RM on the reconstruction status. This week's episode is focused on reconstruction policies and guidelines, looking at how the policies and guidelines eased the reconstruction process, how they have been implemented so far, and discussing the role of NSET in developing different guidelines and policies.



बलियो घर
BALIYO GHAR

नेपालको पुनर्निर्माण:
नीति, कार्यविधिको निर्माण तथा कार्यान्वयन भाग - ११५

साथै
एनसेटको भूमिका

Sunday 7:00 PM, Monday 02:30 AM
& 01:30 PM

Wednesday 8:00 AM, 2:00 PM
& Thursday 04:30 AM

Saturday 8:30 AM
Sunday 04:30 AM & 03:00 PM

Supported By: USAID

Presented By: NSET

Media Partner:

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)
