


FACTS AND FIGURES

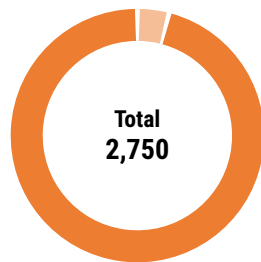

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Dry Stone Masonry	57.95%	4.17%
Stone and Mud Mortar Masonry	39.54%	82.76%
Timber Frame Structure	1.20%	0.88%
Stone and Cement Mortar Masonry	0.69%	1.27%
Others	0.63%	10.93%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	2,275
PA Agreement	1,941
I st Tranche received	1,941
II nd Tranche received	1,586
III rd Tranche received	1,403

Houses

Under Construction: 183 Completed: 1,403

Retrofitting Status

Total Eligible HHs	49
PA Agreement	0
I st Tranche received	7
II nd Tranche received	0

Grievances

Registered: 279
Addressed: 54

Non-compliances

Registered: 10
Addressed: 10

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: CRS (Agriculture), CRS (Livelihood), CRS (Shelter), OXFAM-GB (Shelter), SP (Shelter), SP-N (Education), SP-N (Shelter), SP-N (Hygiene), Tsum (Education), WFP (Livelihood)

OTHER SECTORS



Schools

Damaged: 19
Under Construction: 18
Construction Completed: 18



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	17,453	-	-
Aggregate	m ³	18,163	-	-
Sand	m ³	1,866	-	-
Timber	cu. ft.	2,160	-	-
Cement (PPC)	Sack	-	Y	900
Cement (OPC)	Sack	59,769	Y	900
Rebars	kgs.	188,308	-	-
Tin	bundle	2,441	-	-
Bricks	pcs.	96,746	N	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

2,500 /-
1,200 /-

KEY CONTACTS

Municipal Office

Dhan Bahadur Gurung
Chairman
9851015492

Municipal Office

Ajeet Tiwari
Focal Person
9849032790

Municipal Office

Kumari Gurung
Deputy Chairman
9756004044

GMAI/NRA

Ram Sharan Acharya
NRA Chief-District
9856042637

Municipal Office

Pradip Giri
Chief Administration Officer
9841502456

DLPIU-Building

Sunita Shrestha
DUDBC.DLPIU Chief
9841632087

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	3	0
Sub-Engineers	1	3
Asst. Sub-Engineers	3	2
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

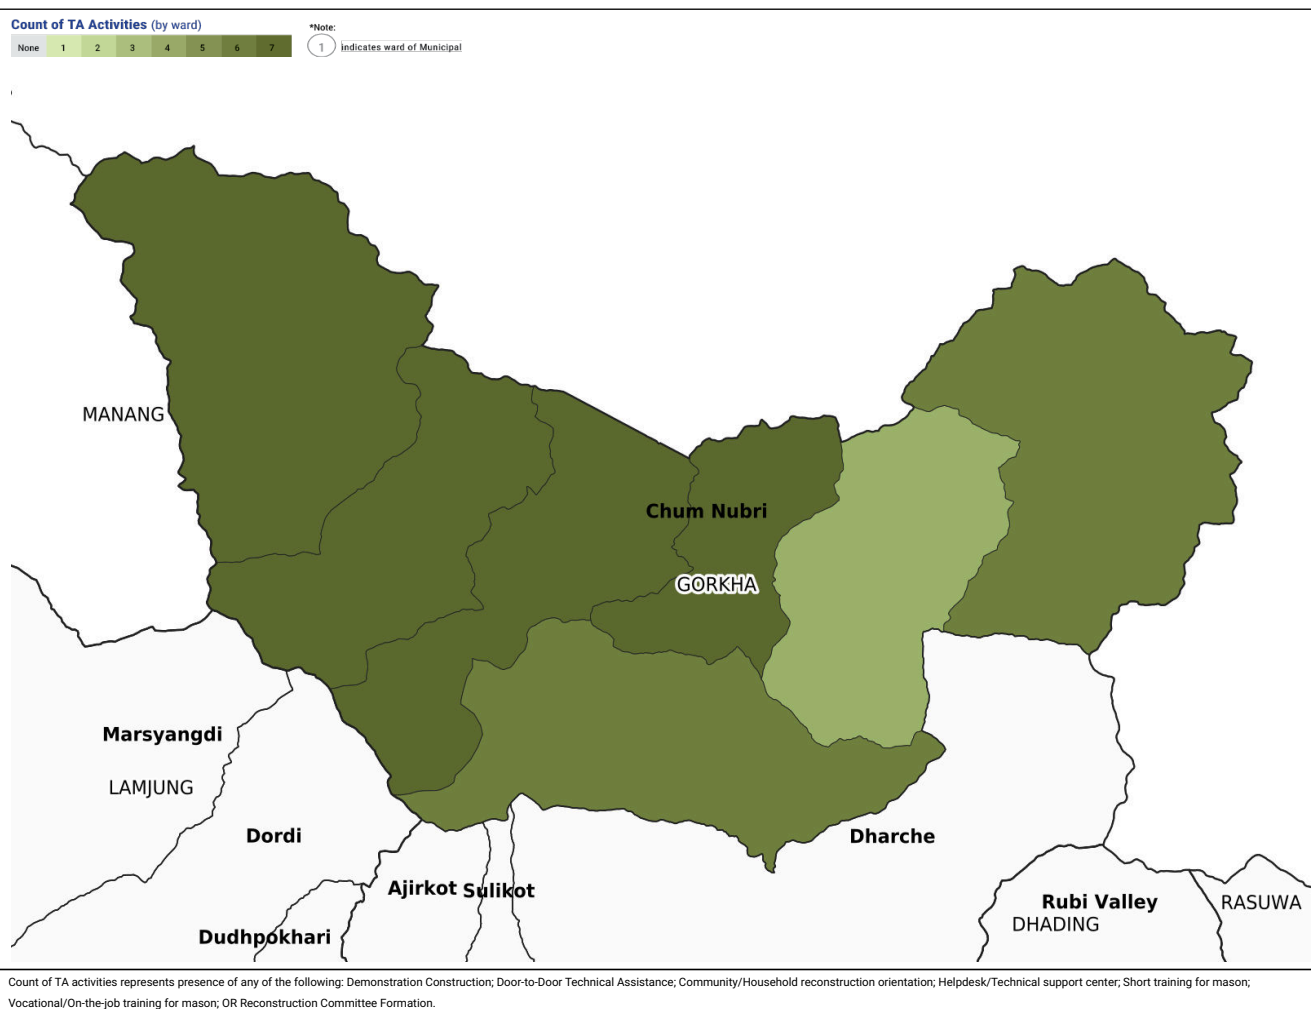

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Chandra Gurung (District Coordinator) 9841478742 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer) 9842062006
