

District Report

Makwanpur

21 Dec 2018 – 3 Jan 2019

Summary of events during this period

Name of activity/event	Event date	Participant Summary		Contact Person	Reference Document
		M	F		
<u>NRA Orientation and Review Workshop on Private Shelters Reconstruction</u> Participants: - Hon'ble members of provincial and federal parliaments representing from Makwanpur. - High level officials from NRA and CLPIUs - Chairs/Mayors, CA Officers and Focal Engineers of local bodies - Chief and Staffs of DLPIU-GMaLI - HRRP-DMT Coordinator and District Team Venue/Location: Hotel Samana, Hetauda, Makwanpur Outcomes: - In-depth interaction on key issues and concerns of private shelter reconstruction done. - Agreement between NRA and Local Bodies on handover of private shelter reconstruction done.	21 st to 22 nd December, 2018			teammakwanpur@hrrpnepal.org	
<u>Ward/Palika Level Meeting:</u> Location: Bagmati Rural Municipality-06 Fapaarbari. Participants: M&E Specialist, CLPIU-Building, DSEs, Ward Chair and Ward Secretary, HRRP DCT and local engineers Agenda: - Reconstruction progress review - Final inspection of shelters, CS Entry and Completion Certification - Retrofitting issues - Non-compliance issues Decisions: ☞ Overall progress in reconstruction of the ward is around 70 to 80 per cent but retrofitting could not be started yet. ☞ The meeting concluded to accomplish final inspection of houses and immediately complete CS Entry. For those whose CS entry has completed would be further processed and coordinated for certification from relevant authority. ☞ Retrofitting inspection forms (Annex 17.1 and Annex 17.2) have just been made	26 th Dec, 2018 12:30AM onwards	10	0	techcord.makwanpur@hrrpnepal.org	Meeting Minute available on: https://drive.google.com/drive/u/0/folders/0B1qABhotx8FSZnhWMmFMRGhmbTA

Summary of events during this period

available at district, hence, we have just reached to initiate the process of retrofitting. ☞ Total of 80 Nos. of non-compliance files were submitted to DSE and 73 out of them have been analyzed and forwarded for tranche release and remaining 7 are under correction process.					
<u>Interaction with Media/Journalists:</u> Venue: Hotel Oshin, Hetauda Participants: ☞ Journalists and Media Houses ☞ DLPIU-GMaLI Chief and staffs ☞ DLPIU-Building Staffs ☞ HRRP District Team Agenda: ☞ Sharing of latest reconstruction status ☞ Dissemination of reconstruction updates ☞ AoB. Decisions: ☞ DLPIU-GMaLI and DLPIU-Building shared latest updates, issues and challenges of overall reconstruction of the district. ☞ Concerns and issues raised by the participant journalists were properly addressed. ☞ Participants/journalists agreed to conduct discussions among all journalists and media to develop a better procedure for the dissemination of reconstruction related news, updates and issues.	2 nd Jan, 2019 8:30AM onwards	35	2	im.makwanpur@hrrpnepal.org	Event Report under preparation
<u>Brief Meeting with Chief of DCC and GMaLI:</u> Venue: Chamber of Chief of DCC Participants: Chiefs of DCC, DLPIU-GMaLI & DC of HRRP Agenda: ☞ District Coordination Meeting ☞ AoB. Decisions: ☞ Agreed to call District Coordination Meeting (DRFC Meeting) on 10 th Jan, 2019.	3 rd Jan, 2019 3:30PM	3	0	dc.makwanpur@hrrpnepal.org	


Upcoming Events and Meetings

Name of Event/Activity	Date, Time and Location	Organizer	Contact Person
NRA Orientation/Review Workshop	Chitwan and Nawalparasi	NRA	dc.makwanpur@hrrpnepal.org
Palika/Ward Meeting & Joint Monitoring Visit	10 th Jan, 2019 Manahari RM	DLPIUs and HRRP	techcord.makwanpur@hrrpnepal.org
District Coordination Meeting	10 th Jan, 2019	GMaLI and HRRP	dc.makwanpur@hrrpnepal.org


Tranche Status

Municipality	Bagmati	Bakia	Bhimfedi	Hetauda	Indrasarowar	Kailash	M'Gadhi	Manahari	Raksirang	Thaha	Total
Total HHs Surveyed	3454	2384	1056	1636	599	1095	2029	2322	968	1596	17139
Total HHs Eligible	2467	3990	2696	6324	2921	2609	2209	2321	1710	6727	33974
Total HHs Enrolled	1742	2308	2104	5274	2458	1997	1640	1222	1516	5960	26221
First Tranche	1877	2310	2099	4641	2428	2005	1667	1246	1517	6007	25797
Second Tranche	1350	1583	2016	2561	1754	1439	1289	1019	1401	4724	19136
Third Tranche	805	622	1613	2458	1093	1193	848	809	932	2933	13306
Total HH Constructed	610	405	1410	2010	950	1010	655	625	750	2650	11075
Grievance Registered	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
Grievance Addressed	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
RF HH Eligible	1941	1616	929	1881	245	606	1372	1330	537	1178	11635
RF HH Enrolled	532	404	397	1012	167	185	277	494	358	612	4438
RF 1 st Tranche	511	254	383	1012	152	277	177	489	358	612	4225
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	79	316	189	656	49	90	292	489	54	267	2481
Non-Compliance Addressed	71	311	185	631	49	85	282	463	54	238	2369

TRANCHE UPDATES

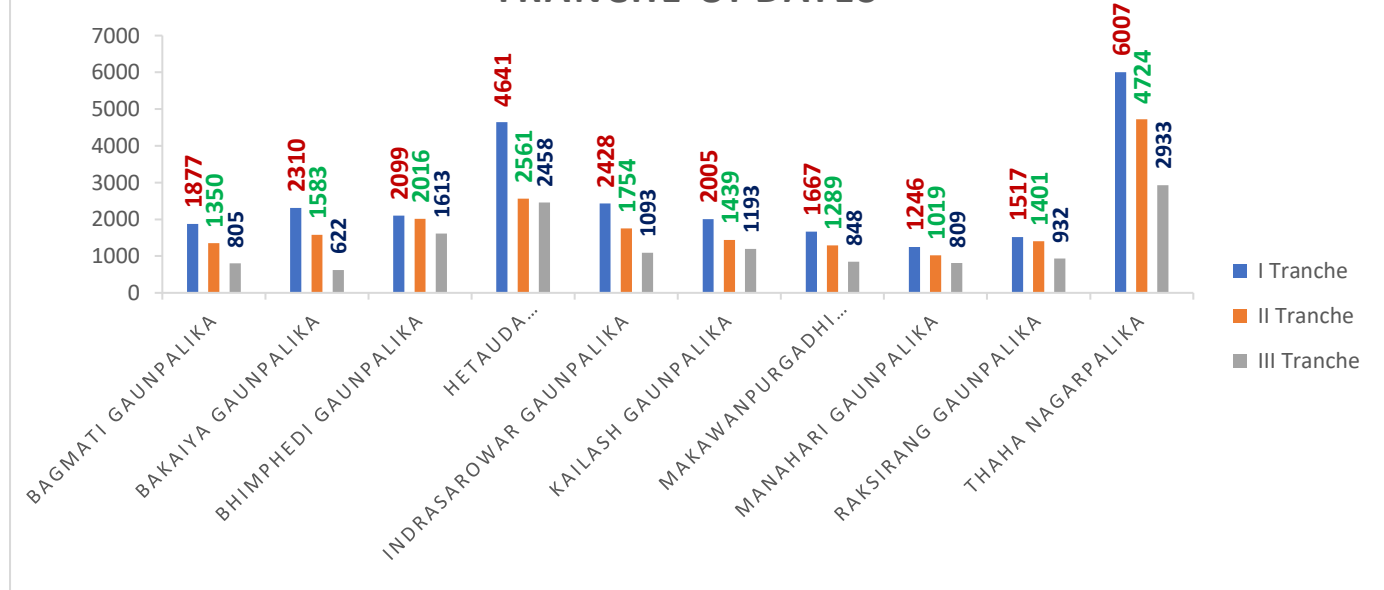

RETROFITTING UPDATE

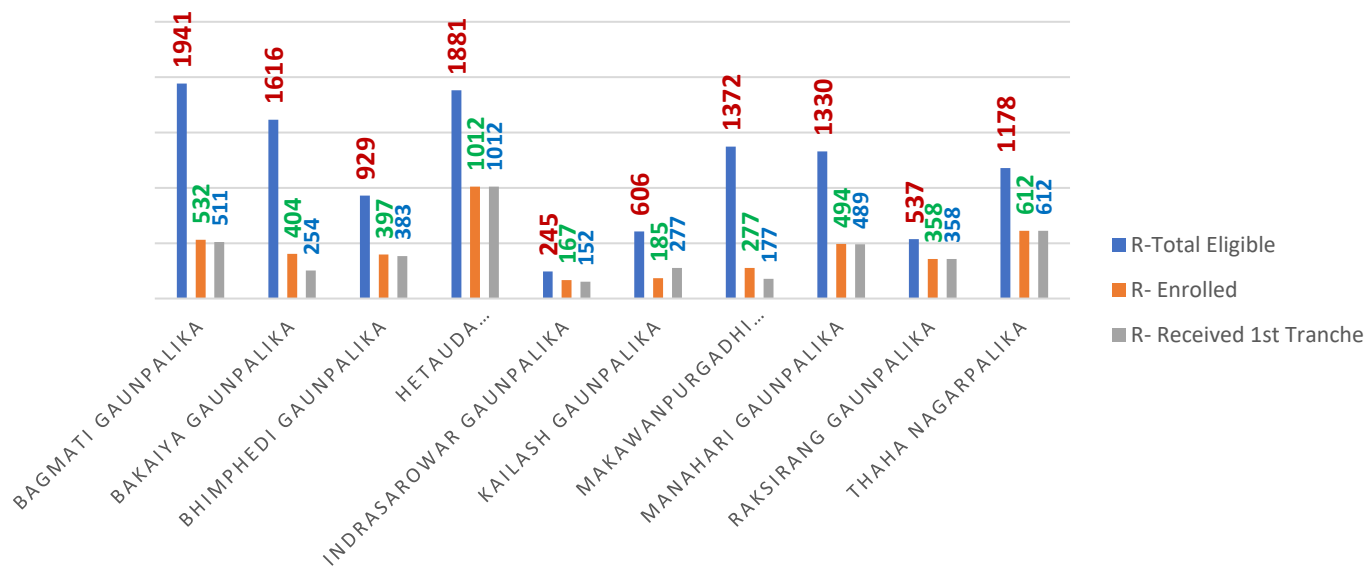

GRIVANCE STATUS



Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders												
26 th December, 2018	Bagmati Rural Municipality-06 (Fafarbari VDC)	Joint Monitoring Visit; M&E CLPIU Specialist, DSEs, local government, ward engineers, beneficiaries and HRRP district technical coordinator.												
Objective(s)	- To organize technical coordination meeting in ward level and separate interaction with ward technicians and beneficiaries. Know the present scenarios of reconstruction in those areas as well as collection of housing typology. - Promote to early final inspection for completed HHs and CS entry. - Monitoring to noncompliance issues and recommended for correction.													
Summary	We are continuing to organize the technical coordination meeting in ward level during field visit time. In case of Bagmati Rural Municipality-06, almost same problem including other areas of Makwanpur district. Focal engineer presented the data of present housing reconstruction. Data visualized with satisfactory. Also we separate interaction with beneficiaries as well. The agendas of meeting were; - Current status of housing reconstruction, retrofitting issues. - Final inspection of completed houses, CS entry and planning for distribution certificate for completed houses. - Completion time frame, who has received first tranche and PA signed except retrofitting beneficiaries. - Noncompliance issues and applied for correction, if any. <table><tr><th>PA Signed</th><th>First tranche received HHs</th><th>Second tranche received HHs</th><th>Third tranche received HHs</th><th>Completed HHs</th><th>Remarks</th></tr><tr><td>780</td><td>765</td><td>652</td><td>450</td><td>480</td><td>Previous Fafarbari VDC</td></tr></table> We briefly discussed in agendas of current status of reconstruction, the following data has been found; Almost areas of Makwanpur district's R/Municipality, the completed housing reconstruction rate is in around 70-90% except retrofitting issues. In every field visit, we faced retrofitting issues; we could not organize any awareness program about lack of information between retrofitting and repairs. Our technicians don't apply his training skills. They had received 4days training of retrofitting for mud mortar houses before 4month ago but till to the date, we could not see any retrofitting done houses. So, it is vital and serious problem in field. Early it should be solve in field level. We don't have skilled manpower in field for retrofitting. So, quickly organize the OJT type training with including some technicians. For sample, each rural municipality, it should be happen. From another way, we are far slow in final inspection and CS entry and we couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, in every visit, we delivered the message to technicians done for final inspection, CS entry and distribute the certificate but it couldn't happen rapidly. Decision Made of the meeting - The meeting concluded that final inspection and CS entry done and makes to plan to distribute completion certificate for completed houses and would be further processed coordinate with district authorized agencies. - Now available retrofitting forms annex 17.1 and 17.2 in district and early starting the retrofitting for moderately damage houses. - As almost houses have been completed, the meeting decided to follow up with remaining HHs for completion of remaining shelters within Chaitra, 2075. Monitoring on non-compliance issues and collected housing typology; Around 80nos. of noncompliance files were submitted for analysis in district among them 71nos. of files recommended for tranches and some files are return back to field for correction. During visit also we have		PA Signed	First tranche received HHs	Second tranche received HHs	Third tranche received HHs	Completed HHs	Remarks	780	765	652	450	480	Previous Fafarbari VDC
	PA Signed	First tranche received HHs	Second tranche received HHs	Third tranche received HHs	Completed HHs	Remarks								
	780	765	652	450	480	Previous Fafarbari VDC								

collected the different types of construction housing typology. There were almost brick in cement mortar, RCC frame structure, hybrid structure and block houses.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
- Retrofitting issues for moderate damages houses (Retrofitting Beneficiaries) - Final Inspection and CS entry.	- To organize awareness program about lack of information between retrofitting and repairs. Our technicians don't apply his training skills. They had received 4days training of retrofitting for mud mortar houses before 4month ago but till to the date, we could not see any retrofitting done houses. So, it is vital and serious problem in field. Early it should be solve in field level. - We don't have skilled manpower in field for retrofitting. So, quickly organize the OJT type training with including some technicians. For sample, each rural municipality, it should be happen. - From another way, we are far slow in final inspection and CS entry and we couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, should do inspection, CS entry and distribute the completion certificate.	NRA DLPIU, Building, For OJT training NRA CLPIU, Building, Joint Monitoring visit, local government, ward technicians	Regular

Photos



Figure 1: Technical coordination meeting has been organized in Bagmati Rural Municipality-06, (Fafrbari VDC); the agendas were; Current status of housing reconstruction, retrofitting issues; final inspection of completed houses, CS entry and planning for distribution certificate for completed houses; completion time frame, who has received first tranche and PA signed except retrofitting beneficiaries and noncompliance issues and applied for correction, if any.



Figure 2: Bagmati Rural Municipality-06, around 25-30nos. of houses built with our cultural beauty before 30-40 years old. No, we are in reconstruction of housing and others infrastructures but we couldn't see these types of architectural. These houses built with two storey an attic, provided band in some places. Now we can see in some houses only normally crack.in this community, only 5nos. of houses moderate damages and 2nos. of houses heavy damage.

Housing Typology Report



Figure 3: House owner; Shambhu Rai, Bagmati Rural Municipality-6, he is a reconstruction beneficiary, completed his house and received second tranche and verified for third tranche after structural analysis.



Figure 4: House owner; Indra Rai, Bagmati Rural Municipality-06, block masonry structure with all seismic reinforcement elements. Two room with light CGI sheet. He has received all tranches of government grant. Total construction cost is around 4lakh.



Figure 5: House owner; Karn Bahadur Gole, Bagmati Rural Municipality-04, brick in cement mortar with two rooms, flexible roof. Provided all vertical and horizontal bands. But he does not provide gable band for heavy material used. He received all tranches but for completion certificate, this house not eligible for certificate.



Figure 6: House owner; Bhim Bahadur Lama, Bagmati Rural Municipality-08, brick in cement mortar, two rooms with light CGI sheet and gable wall. He has received all tranches of government grant. Total construction cost is around 7lakh.

Challenges and Way Forward

Challenge	Way Forward
- Retrofitting issues for moderate damages houses (Retrofitting Beneficiaries) - Final Inspection, CS entry and distribute completion certificate.	- To organize awareness program about lack of information between retrofitting and repairs. - Quickly organize the OJT type training with including some technicians in field level. For sample, each rural municipality, it should be happen. - Actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, should do inspection, CS entry and distribute the completion certificate.
