


FACTS AND FIGURES

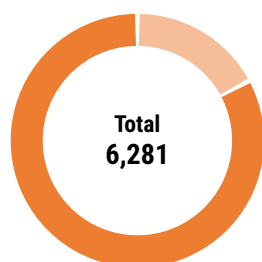

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	94.70%	82.76%
Brick and Cement Mortar Masonry	3.17%	2.57%
Timber Frame Structure	0.61%	0.88%
Adobe Structures	0.46%	1.79%
Others	1.06%	12.01%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	5,619
PA Agreement	4,841
I st Tranche received	4,841
II nd Tranche received	4,236
III rd Tranche received	3,003

Houses

Under Construction: 1,233

Completed: 3,003

Retrofitting Status

Total Eligible HHs	441
PA Agreement	29
I st Tranche received	30
II nd Tranche received	0

Grievances

Registered: 1,390

Addressed: 142

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: UNDP (Shelter)

Phased Out: ACN (Shelter), DCA (Agriculture), DCA (DRM), DCA (Education), DCA (Livelihood), DCA (Health), DCA (Shelter), DCA (Hygiene), GON-PAF (Shelter), HELVETAS (Shelter), IOM (Shelter), NRA (Shelter), Sailung (Education), UNDP (Shelter), UNWOMEN (Shelter)

OTHER SECTORS



Schools

Damaged: 70
Under Construction: 44
Construction Completed: 44



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	79,409	-	-
Aggregate	m ³	81,037	-	-
Sand	m ³	8,476	-	-
Timber	cu. ft.	9,769	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	269,081	-	-
Rebars	kgs.	862,113	-	-
Tin	bundle	10,999	-	-
Bricks	pcs.	892,200	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

KEY CONTACTS

Municipal Office

Hom Bahadur Rana Magar
Chairman
9856040100

Municipal Office

Manisha Gurung
Focal Person
9813212372

Municipal Office

Lalita Adhikari
Deputy Chairman
9846070449

GMA/IRA

Ram Sharan Acharya
NRA Chief-District
9856042637

Municipal Office

Rakesh Gurung
Chief Administration Officer
9856040976

DLPIU-Building

Sunita Shrestha
DUDBC.DLPIU Chief
9841632087

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

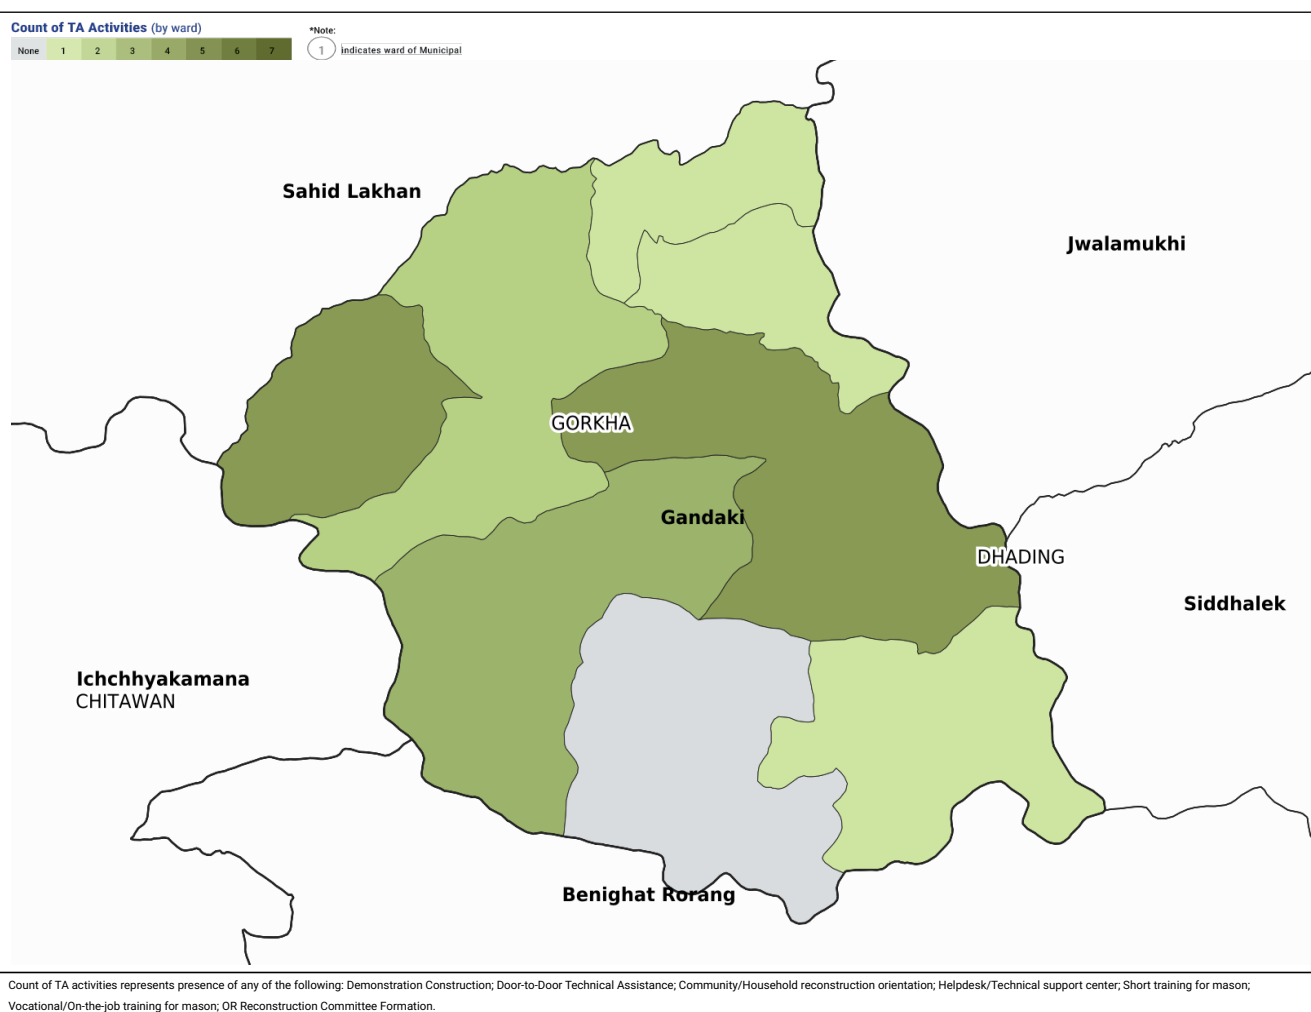

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Chandra Gurung (District Coordinator) 2. (District Technical Officer) 3. Manisha Rai (District Information Management Officer)
9841478742 9842062006
