


FACTS AND FIGURES

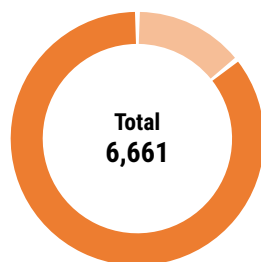

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	82.89%	85.43%
Adobe Structures	8.43%	3.32%
Brick and Cement Mortar Masonry	6.82%	3.73%
Stone and Cement Mortar Masonry	0.72%	1.10%
Others	1.13%	6.41%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	6,746
PA Agreement	6,041
I st Tranche received	6,041
II nd Tranche received	5,330
III rd Tranche received	3,674

Houses

Under Construction: - Completed: 3,200

Retrofitting Status

Total Eligible HHs	314
PA Agreement	314
I st Tranche received	36
II nd Tranche received	314

Grievances

Registered: 1,273
Addressed: 728

Non-compliances

Registered: 130
Addressed: 91

Data Updated on: 2019-05-28 00:00:00

P0 Presence

Active: NSET (Shelter)

Phased Out: ADRA (Shelter), DCA (DRM), DCA (Hygiene), GON (Shelter), GON - DUDBC (Shelter), GON-PAF (Shelter), HELVETAS (Shelter), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), Nyayik (Agriculture), Nyayik (Education), Nyayik (GESI), RainbowCN (Health), SCI (DRM), SCI (Education), SCI (Shelter), SCI (Social Protection), SCI (Hygiene)

OTHER SECTORS



Schools

Damaged: 59
Under Construction: 29
Construction Completed: 29



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	156,389	Y	1,200
Aggregate	m ³	139,324	Y	1,500
Sand	m ³	16,507	Y	2,100
Timber	cu. ft.	18,343	Y	706,300
Cement (PPC)	Sack	-	-	715
Cement (OPC)	Sack	468,549	-	795
Rebars	kgs.	1,731,683	Y	80
Tin	bundle	19,138	Y	-
Bricks	pcs.	3,624,441	Y	13

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,000 /-
700 /-

KEY CONTACTS

Municipal Office

Krishnahari Shrestha
Mayor
9851087251

Municipal Office

Om Narayan Yadav
Focal Person
9807352305

Municipal Office

Radha Timsina
Deputy Mayor
9841686488

GMaLI/NRA

Jaya Ram Shrestha
NRA Chief-District
9841265576

Municipal Office

Dan Bahadur Aidi
Administration Officer
9851105982

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
9855046584

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	9	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

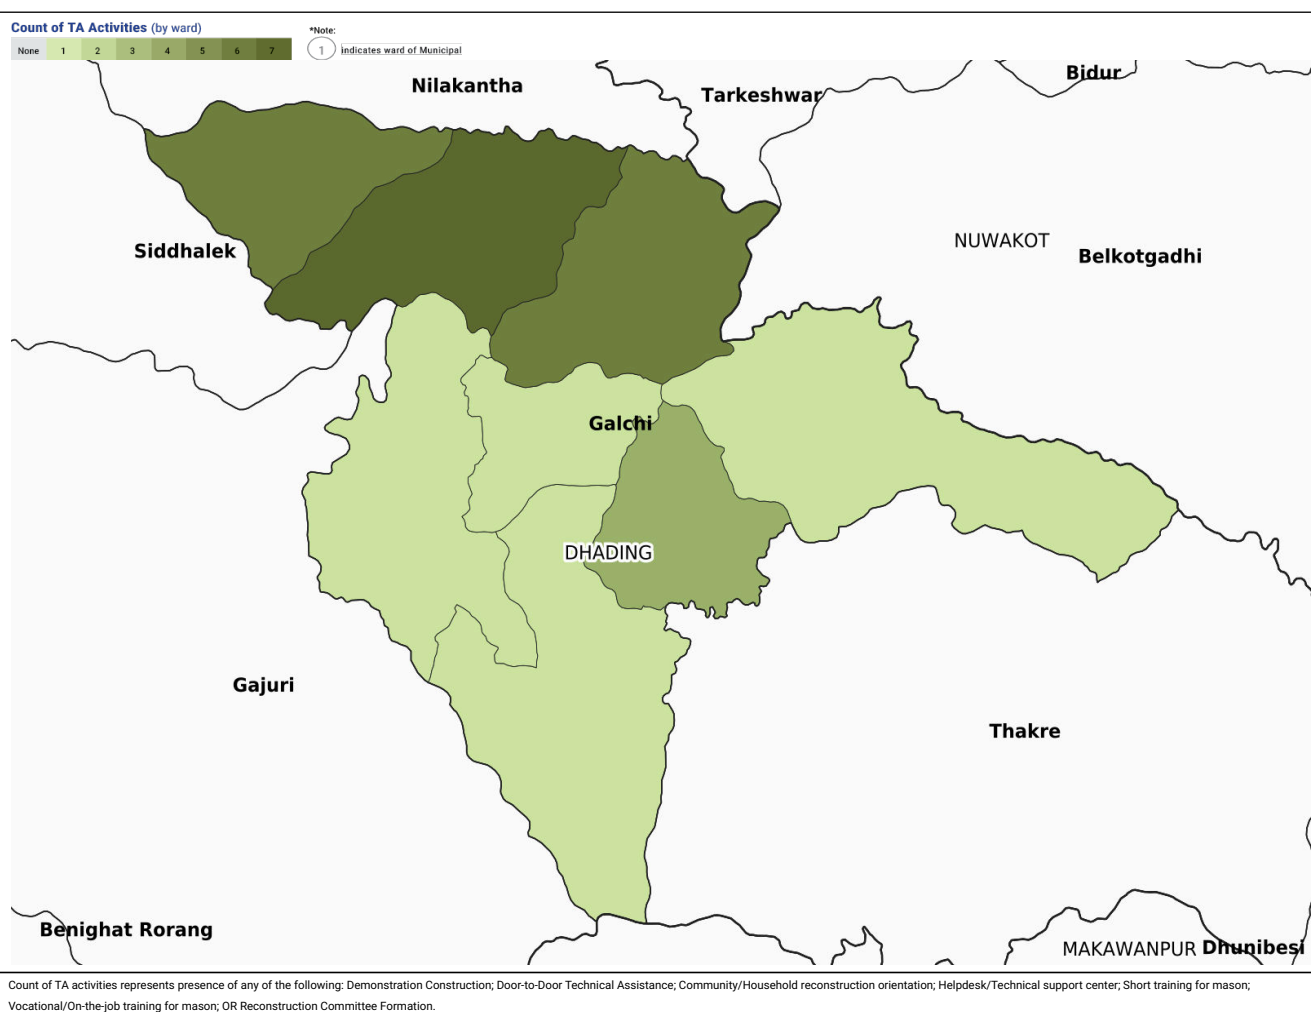

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Chandra Gurung (District Coordinator) 9841478742	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
