

District Report

Sindhupalchok

15 February - 14 March 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Coordination meeting, Tripurasundari RM-6	18/02/2019	6	1	Pradip Sharma, Pranjal Bhandari	GD link to the meeting minutes
Coordination Meeting, Tripurasundari RM-5	19/02/2019	4	3	Pradip Sharma, Pranjal Bhandari	GD link to the meeting minutes
Coordination Meeting, Tripurasundari RM-1	20/02/2019	11	0	Pradip Sharma, Pranjal Bhandari	GD link to the meeting minutes
Coordination Meeting, Tripurasundari RM-3	21/02/2019	8	1	Pradip Sharma, Pranjal Bhandari	GD link to the meeting minutes

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Hollow Concrete Block Manual Orientation	18 th and 19 th March, 2019	HRRP	Pradip Sharma, Pranjal Bhandari

Tranche Status


Rural /Municipality	Balefi RM	Barhabise Mun	Bhotekoshi RM	Chautara sangachok gadhi Mun	Helambu RM	Indrawati RM	Jugal RM	Lisankhu Pakhar RM	Melamchi NP	Panch pokhari Thangpal RM	Sunkoshi RM	Tripura Sundari RM
Total HHs Surveyed												
Total HHs Eligible	6043	7903	4225	13989	5421	8323	5665	5374	13374	7181	5739	4591
Total HHs Enrolled	5964	7727	4128	13718	5163	8049	5523	4926	13055	6784	5563	4461
First Tranche	5964	7727	4128	13718	5163	8049	5523	4926	13055	6784	5563	4461
Second Tranche	5770	7284	3346	13214	4676	7624	5315	4138	11957	5676	5200	4251
Third Tranche	5064	5590	1650	11729	3636	5801	4167	2793	8244	3291	4215	3407
Total HH Constructed												
Grievance Registered	1240	2490	1150	3513	1333	2421	1260	2269	2557	2937	1127	930
Grievance Addressed	464	775	450	1540	379	660	365	1134	810	1424	805	485
RF HH Eligible	24	74	69	96	52	38	17	39	113	16	33	19
RF HH Enrolled	8	19	11	39	12	11	8	8	25	3	11	5
RF 1 st Tranche	8	18	10	37	6	7	6	8	5	3	10	5

RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0	0
Non- Compliance Registered												
Non- Compliance Addressed												


Graph of Tranche Status:

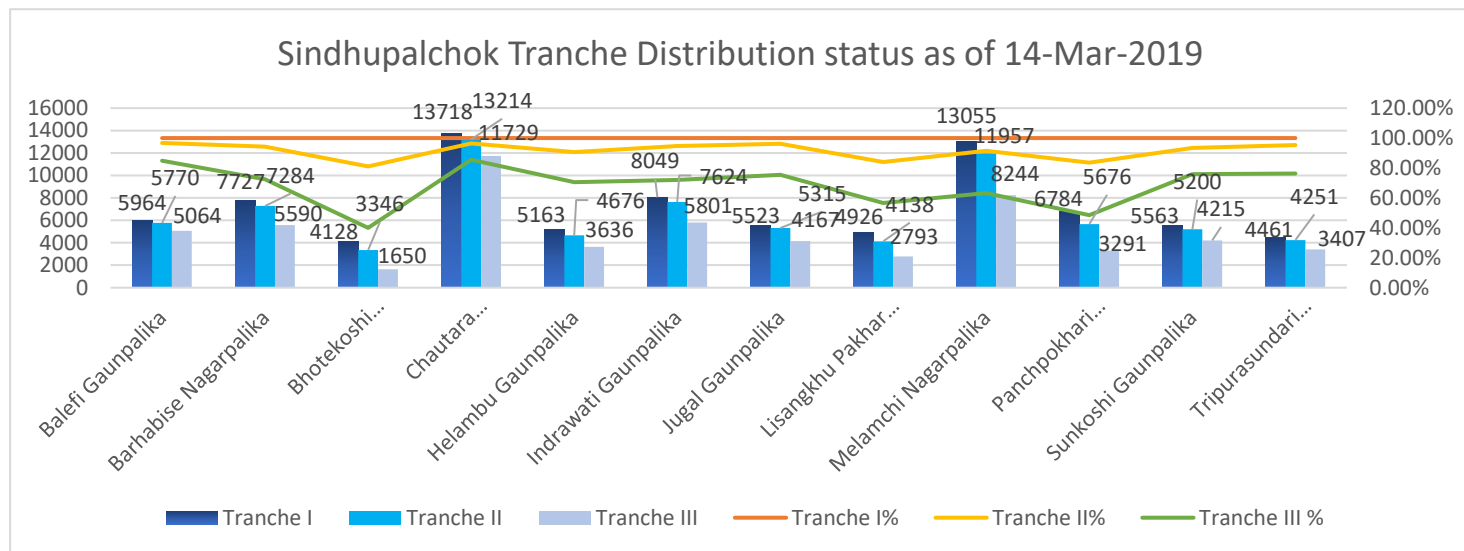

Graph for Retrofitting Status:

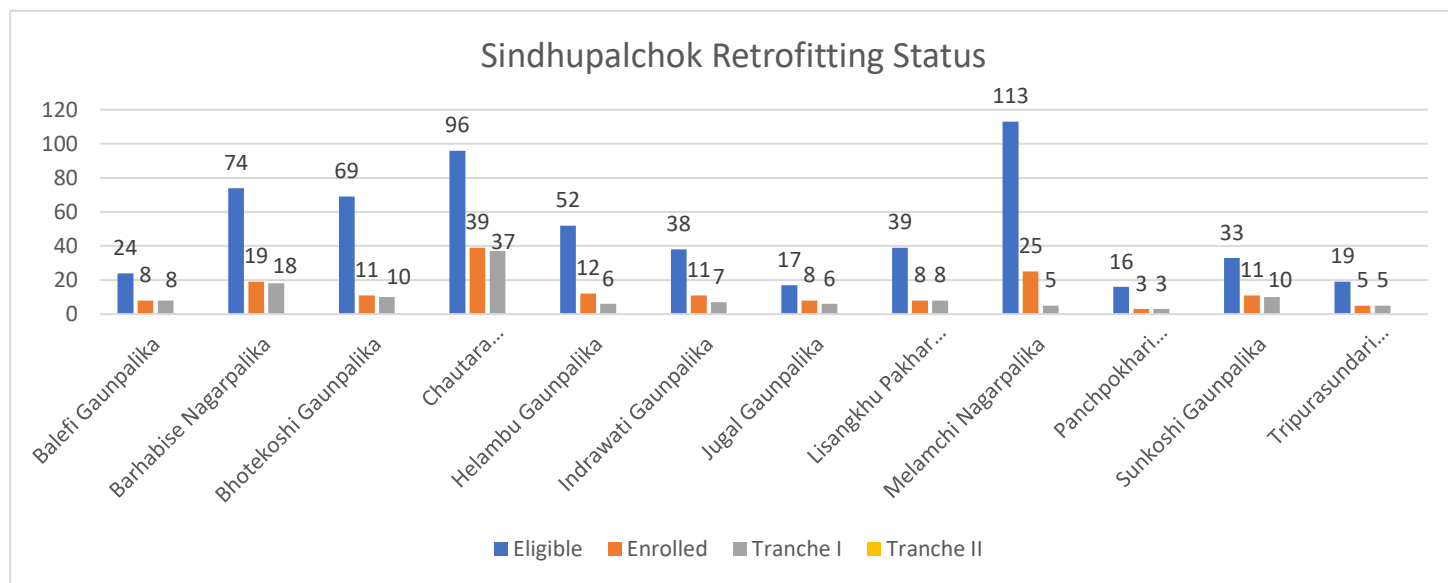

Graph for Grievance Status:

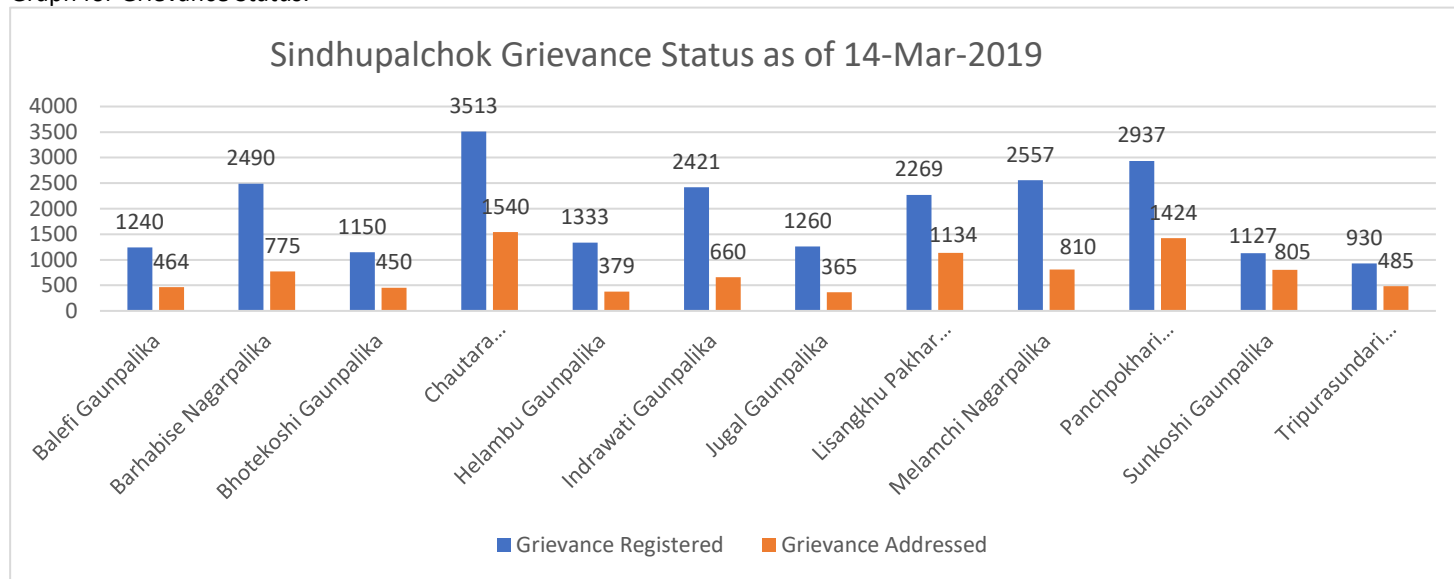

Field Visit /Joint Field Monitoring Visit Event

Visit 1

Date	Location	Participants from HRRP and stakeholders
18 th Feb, 2019	Tripurasundari RM-6, Tekanpur	Pradip Sharma, Binod Sah and Roshan Kesari
19 th Feb, 2019	Tripurasundari RM-5, Tauthali	Pradip Sharma, Binod Sah and Roshan Kesari
20 th Feb, 2019	Tripurasundari RM-1, Ghorthali	Pradip Sharma, Binod Sah and Roshan Kesari
21 st Feb, 2019	Tripurasundari RM-3, Dhuskun	Pradip Sharma, Binod Sah and Roshan Kesari
22 nd Feb, 2019	Tripurasundari RM-2, Dhuskun	Pradip Sharma, Binod Sah and Roshan Kesari

Objective(s)

- To know the updates of reconstruction by visiting the private houses.
- Identify the issues and challenges facing at the field level, identify and help correct prevalent non-complaint issues.
- To Collect Housing typologies.
- To conduct Ward and Palika level coordination meeting.

Summary

Day 1: Visited Tripurasundari RM Ward No. 6 (Tekanpur) and conducted Ward Level Coordination Meeting:

- The presence of field engineer is very poor. According to the ward chief, the engineer comes to the field only once in a month only for attendance approval. The presence of Sub-engineers and Assistant Sub Engineers too is poor but satisfactory as compared to that of the engineers. The Ward Chief informed that he would initiate the process with DLPIU-Building, Chautara to change the field technicians.
- Due to the negligence from the field technicians coupled with the delay in tranche distribution from the district, the beneficiaries have not been able to receive tranche since the last two months.

Day 2: Visited Tripurasundari RM ward No.5 (Tauthali) and conducted Ward Level Coordination Meeting:

- According to the field engineer, there are many non-compliant houses in the ward in which there is difficulty in applying correction and impossible to retrofit.
- The presence of engineers in the ward is very good. The ward chief provided the letter of appreciation for their satisfactory work to the CLPIU M&E specialist.

Day 3: Visited Tripurasundari RM Ward No. 1 (Ghorthali) and conducted Ward Level Coordination Meeting:

- During the field visit in October 2018, we had raised an issue that there were some households who have received tranches without even beginning construction. We had alarmed the DLPIU offices in Chautara too, but the beneficiaries have not yet started construction.
- The presence of the Field engineers is very poor. Months have passed by since the engineers were present in the ward. The ward chairman was visibly irate with the field engineers that he drafted a letter to the DLPIU-Building demanding he don't need them.

Day 4: Visited Tripurasundari RM Ward No 3 (Dhuskun) and conducted Ward Level Coordination Meeting:

- The ward chairman lamented the lack of presence of the field engineers in the ward. According to him, the engineer comes to the office only at the end of the month and does his work in haste. The ward chief has not approved his attendance since last month demanding his presence throughout the month.
- Strangely, the ward chief has received pressure from the beneficiaries to approve the attendance of the field engineers blaming the disapproval for the delay in tranche.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
The presence of the field engineers is very poor in the Palika.	Urgent need to take actions by the concerned authorities	DLPIU Building, M&E consultant, ward	ASAP
The CS entry of the Palika is Poor	Need to install reliable ISP at the ward offices and the engineers need to be provided with orientation on	DLPIU Building, CLPIU MIS Consultant	ASAP

Photos



Picture of the Ward Level coordination meeting at Tripurasundari RM 3, Dhuskun



Ward Level Coordination Meeting at Tripurasundari RM 1, Ghorthali



The House is located at Tripura Sundari Rural Municipality ward no.6, the house belongs to Mr. Bhim Dhoj Bohora. He has not received any tranches yet. The house is Reinforced Cement Concrete Framed Building (RCC) 9"x9" column 4 number of rebar 16mm and 2 numbers of rebar 12mm, infill wall Brick Masonry with Cement Mortar the house is 4 room and One storey.

Photo



The house is located at Tripura Sundari Rural Municipality ward no.-06, Sindhupalchok. the house owners name is Mr. Tek Bahadur. He has received Second tranche and third tranche is Processing. The house is a Load Bearing Brick and Cement Mortar Masonry and One story without attic and Two rooms, Rigid Roof.



The house is located at Tripura Sundari Rural Municipality ward no.-05, Sindhupalchok. The house owner's name Mrs. Nara Maya Shrestha. The house owner has received all three tranches. The house belongs to Load Bearing Brick and Cement Mortar Masonry and One story without attic and Two rooms, CGI Roofing.



The House is located at Tripura Sundari Rural Municipality ward no.5, the house owner's name is Mr. Bhakta Bahadur Shrestha. The owner has received all three tranches. The house is a Reinforced Cement Concrete Framed Building (RCC) with 12"x12" column with 4 number of rebar 16mm and 4 numbers of rebar 12mm. The infill wall is Brick Masonry with Cement Mortar. The house is 4 room and Two storey.

Case Study: Mr. Narayan Thami, Tripura Sundari RM, Ward No. 2, Chokati

Mr. Narayan Thami hails from Sindhupalchowk Tripura Sundari Rural Municipality ward No. 2, Chokati. He lived in a joint family of six members: a daughter, a son, his wife and his parents. In search of a secured future he had chosen to pursue foreign employment, but all his dreams shattered when Nepal was hit by the disastrous earthquake on 12 April 2015. In the earthquake, His house was completely collapsed, and both his son and daughter were covered in the rubble. The villagers were able to save his son but by the time they pulled out his daughter, she had already taken her last breath.

The company in which he was working did not provide him a leave to perform last rites of his daughter. So, if he were to come to Nepal, he had to leave the job. He was in great dilemma as the income from the company was the only thing he has been able to support his family with and he was knee deep in debt for this job and he had only just started. So, he somehow managed to console himself and stay put in the job hoping the time would heal everything. However, his grief was compounded when his wife ran away with someone else months after losing his daughter. Now there were just four members in his family: a son who was a minor and his elderly parents. His elderly father would always be in mental tension due to the state of his family and in the carelessness arising from the tension, he lost the earthquake relief card or red card. Due to this, he was unable to receive first tranche.



Pic: the plinth level that Narayan Thami has been able to complete since his return.

His father was unaware of what to do and whom to contact. He completely ignored the reconstruction of the house and stayed idle hoping that his son would return and begin the process while the rest of the villagers were reconstructing and receiving second and third tranches.

Three long years passed this way after which Narayan was granted leave to visit his home in March 2018 by his employer and as soon as he returned, he began reconstructing his house. By this time, the National Reconstruction Authority (NRA) had announced the first deadline for the disbursement of the first tranche for 13 April 2018.

He started to build four roomed, two story Reinforced Cement Concrete (RCC) house. He has been able to complete up to plinth level in the same location where his original house was destroyed by the earthquake, but he still wasn't aware how he would receive the tranches provided by the government. He wanted to receive the tranches, but he was unaware of the standards and the limited presence of the engineers did not help the matter either. Due to this lack of awareness, he put 9"x12" columns which had led to his house being non-compliant for two story.

During our visit, we informed him of the process he needs to follow. He was suggested to contact the DLPIU GMALI office and we provided the details of the contact person in order to receive a copy of PA book in order to receive the tranches and informed him that with the 9"x12" column that he installed in his house, he would only be able to build a single story house in order to make the house compliant. He agreed and thanked us for the instructions and told us he would promptly contact the district GMALI office and let us know if any issue arose.
