

District Report

Kathmandu Valley

21 Dec 2018– 3 Jan 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
A joint monitoring visit of DLPIU building Kathmandu and HRRP Kathmandu valley team to Ward no 3, 8 and 9 of Gokarneshwor Municipality, Kathmandu district.	2 Jan. 2019	2	3	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org Contact: 9861796464	
The general ward level coordination meeting was conducted at Ward no. 3, Baluwa, Gokarneshwor Municipality, Kathmandu.	2 Jan. 2019	3	3	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org Contact: 9861796464	
A joint monitoring visit of DLPIU building Kathmandu and HRRP Kathmandu valley team to Ward no 1 and 8 of Suryabinayak Municipality, Bhaktapur district.	3 Jan. 2019	3	5	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org Contact: 9861796464	
HRRP Kathmandu valley team collected case study of one beneficiary who have returned 1 st tranche. The case history and studies were collected from Ward no. 6, Pharping, Dakshinkali Municipality, Kathmandu	3 Jan. 2019	2	2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
The general ward level coordination meeting was conducted at Ward no. 6, Kochi Tole, Pharping, Dakshinkali Municipality, Kathmandu. Key highlights of ward-level coordination meeting is- Reconstruction has boosted in areas of Ward no. 6 due to new deadlines of NRA. ➤ Key reconstruction issues of Ward no. 6 is related with small parcel land, unregistered land, households struggling with eccentric footing and issues of multiple beneficiaries. ➤ Handful of beneficiaries have reconstructed houses already but without building permit. Their building permit has been in pending stage. They havenot accessed 2 nd tranche yet.	3 Jan. 2019	8	9	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	

Summary of events during this period

Upload of training database and relevant other information has been updated in 5W.	21 Dec. 2018 – 3 Jan. 2019			Ms. Manisha Rai IM Officer HRRP Kathmandu Valley im.ktm@hrrpnepal.org Contact: 9842062006	
--	----------------------------	--	--	---	--

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in districts of Kathmandu Valley	Date- 1 st week -3 rd week of January 2019	HRRP Kathmandu valley team	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org
Municipality level and Ward level Coordination meeting to be conducted by HRRP Kathmandu Valley team in coordination with concerned Municipalities of Kathmandu valley	Date: 1 st week -3 rd week of January 2019	HRRP Kathmandu valley team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409
General Coordination Meeting of DLPIU NRA GMaLI Lalitpur	Date: 17 January 2019	DLPIU NRA GMaLI Lalitpur	Mr. Yamnath Giri M & E Specialist EHRP/ DLPIU NRA GMaLI Lalitpur district Contact: 9851239785 yamnathgiri2014@gmail.com
General Coordination Meeting of DLPIU NRA GMaLI Kathmandu	Date: 3 rd week of January 2019	DLPIU NRA GMaLI Kathmandu	Mr. Achyut Shrestha Section officer DLPIU NRA GMaLI Kathmandu Contact: 9860784954 achyutshrestha121@gmail.com

News & Updates



Beneficiaries from Kathmandu valley who un intends to rebuild shelters have returned 1st tranche *(based on data taken from respective DLPIU NRA GMAI offices of Kathmandu, Lalitpur and Bhaktapur)*

District	Municipality	Name of Beneficiary	PA Number	Reasons for returning 1 st tranche
Bhaktapur	Bhaktapur, Ward no 4	Mr. Kedar Krishna Joshi	26-3-12-1-079	Received from another Ward
	Changunarayan, Ward no. 9	Mr. Bhakku Shah	26-1-11-1-201	NA
	Bhaktapur, Ward no 7	Mr. Sitaram Tuitui	26-3-7-1-003	Received from another PA
	Bhaktapur, Ward no	Mr. Dash Faiju	26-3-1-1-270	Received from another PA
	Bhaktapur, Ward no 7	Mr. Shree Bhakta Kisi	26-3-7-2-040	Received from another PA
Kathmandu	Tarkeshwor, Ward no 10	Mr. Kiran Khadka	27-18-20-0-038	Beneficiary returned the whole tranche amount after he got back his another house that was on lease for 10 years
	Dakshinkali, Ward no 6	Mr. Mahendra Raj Rajopadhyaya	27-48-10-0-010	Beneficiary cited the lack of well-trained mason, lack of water and lack of proper amount of money to rebuild the house
	Kathmandu Metro City, Ward no.11	Mr. Rajan Kumar Shrestha	27-31-11-0-050	Beneficiary has another house
	Kirtipur, Ward no 6	Mr. Bharat Thapa	27-33-15-1-042	Beneficiary has no intentions to rebuild house/owns another house
	Gokarneshwor, Ward no. 8	Mr Prabir Kumar Thapa	27-44-11-0-111	Owens houses in other areas
	Lalitpur Metro City, Ward no. 11	Mr. Nem Bahadur Amatya	25-27-22-0-062	Owens houses in other areas/due to uninterest shown by another beneficiary, damaged house couldnot be demolished and transportation cost is high to remove rubbles.


Tranche Status

Kathmandu

Municipality	Budhanilkant ha	Chandragiri	Dakshinkali	Gokarneshwor	Kageshwori-Manahara	Kathmandu MC	Kritipur	Nagarjun	Shankharapur	Tarakeshwor	Tokha
Total HHS Surveyed	2693	5785	4091	2977	3667	7514	2941	4362	6064	6193	1752
Total HHS Eligible	2693	5785	4091	2977	3667	7514	2941	4362	6064	6193	1752
Total HHS Enrolled	2054	4707	3760	2491	3239	5953	2475	4103	5509	5124	1549
First Tranche	2054	4661	3731	2484	3228	5928	2459	4099	5470	5093	1530
Second Tranche	906	1055	1178	1202	1573	1308	860	1254	2024	1596	595
Third Tranche	623	911	669	922	779	995	684	971	1248	1289	403
RF HH Enrolled	0	46	29	7	4	25	16	4	39	31	19
RF 1 st Tranche	0	46	29	7	4	25	16	4	39	31	19
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0

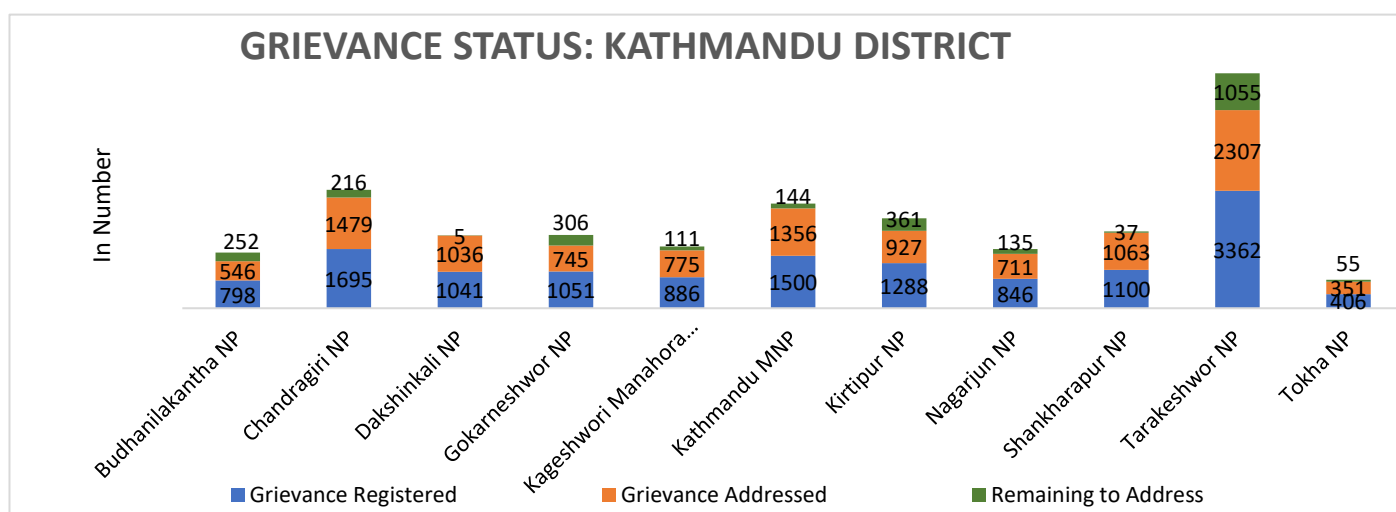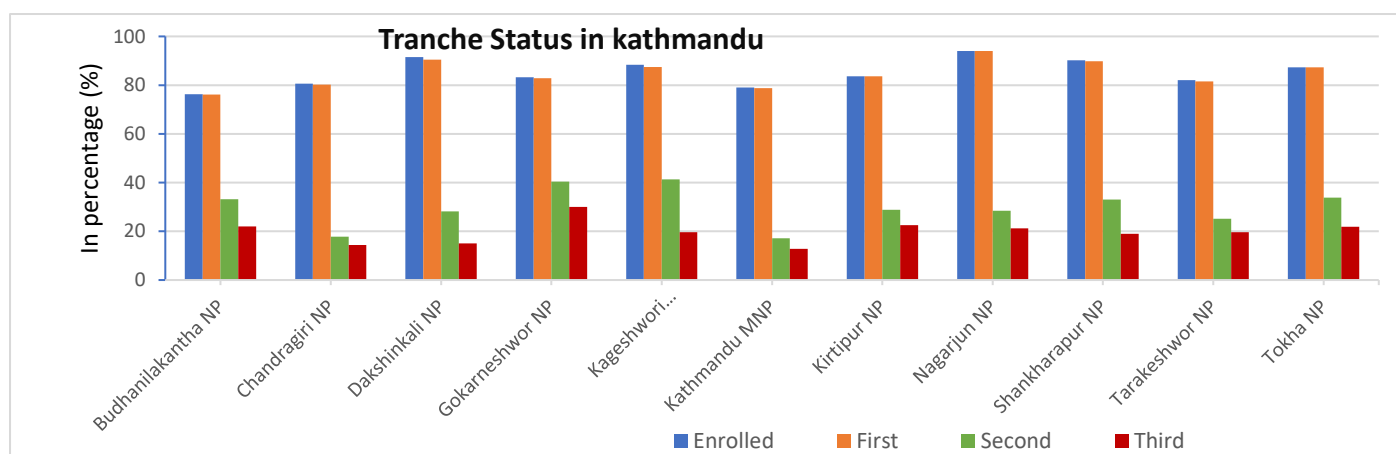


RETROFITTING STATUS: KATHMANDU DISTRICT

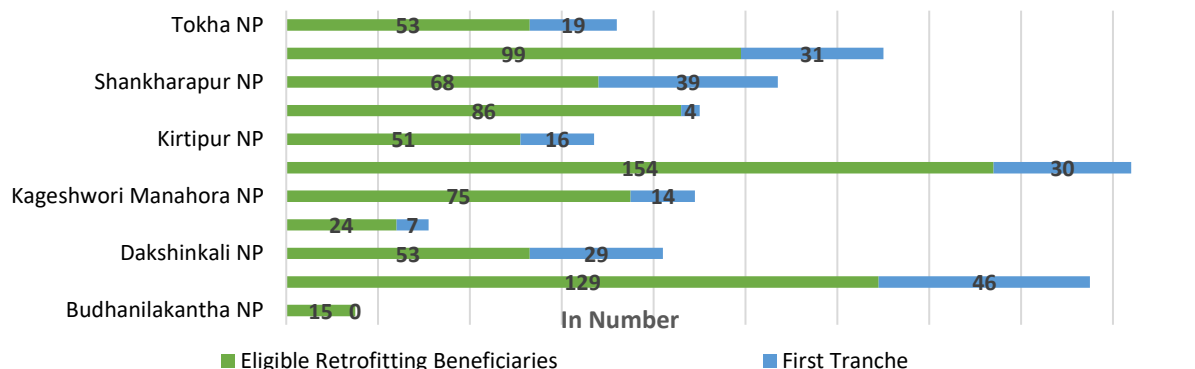


Lalitpur

Rural /Municipality	Mahankal RM	Konjyosom RM	Bagmati RM	Godawari UM	Mahalaxmi UM	Lalitpur MC
Total HHs Surveyed	2267	2154	3370	9588	3657	7346
Total HHs Eligible	2267	2154	3370	9588	3657	7346
Total HHs Enrolled	98.32%	96.32%	92.27%	82.00%	83.89%	85.59%
First Tranche	98.27%	96.1%	91.74%	81.31%	82.13%	85.27%
Second Tranche	70.18%	76.48%	68.21%	22.70%	19.68%	15.03%
Third Tranche	35.49%	51%	43.96%	16.65%	15.24%	8.75%
Grievance Registered	549	919	882		863	
Grievance Addressed	294	484	658		795	
RF HH Eligible	61	372	252	325	90	281
RF HH Enrolled	42	231	8	60	2	119
RF 1 st Tranche	42	231	8	60	2	119


Tranche Status in Lalitpur District

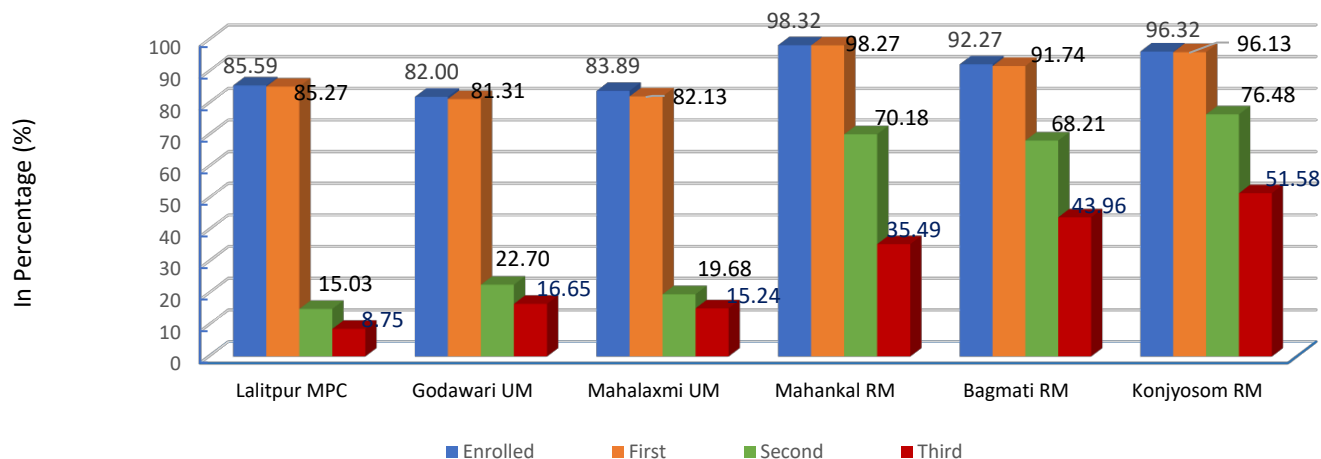

GRIEVANCE STATUS: LALITPUR DISTRICT

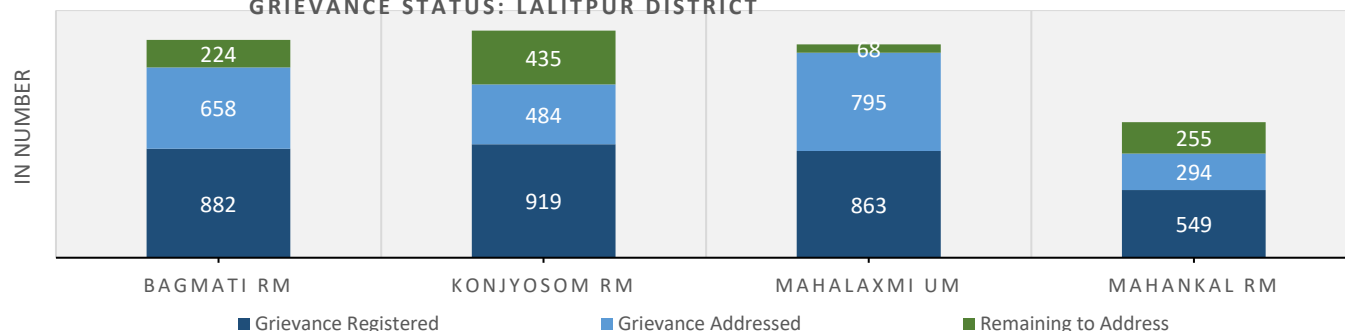


RETROFITTING STATUS: LALITPUR DISTRICT

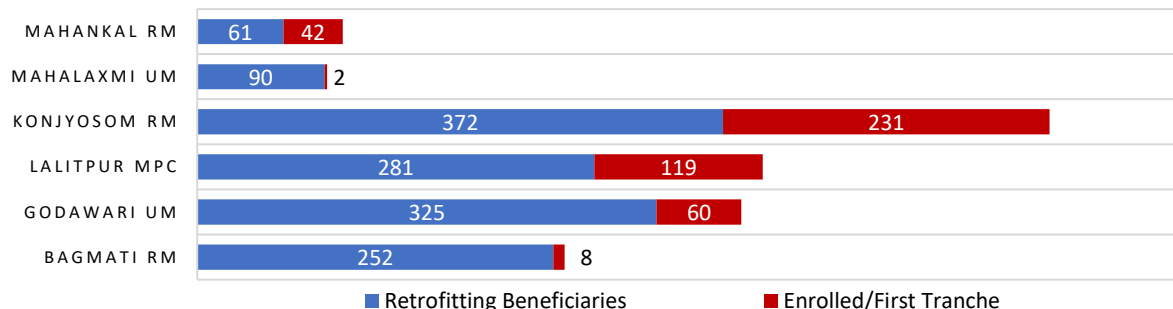


Bhaktapur


Municipality	Bhaktapur	Changunarayan	Madhyapur Thimi	Suryabinayak
Total HHs Surveyed	7622	10937	2333	7416
Total HHs Eligible	7622	10937	2333	7416
Total HHs Enrolled	5583	9651	2050	6941
First Tranche	5583	9651	2050	6940
Second Tranche	1493	2672	589	2161
Third Tranche	1285	2536	548	2027
Grievance Registered	1592	2096	2407	1926
Grievance Addressed	1542	1696	1431	1661
RF HH Eligible	148	212	101	233
RF HH Enrolled	148	212	101	233
RF 1 st Tranche	39	84	56	88

Tranche Status: Bhaktapur District

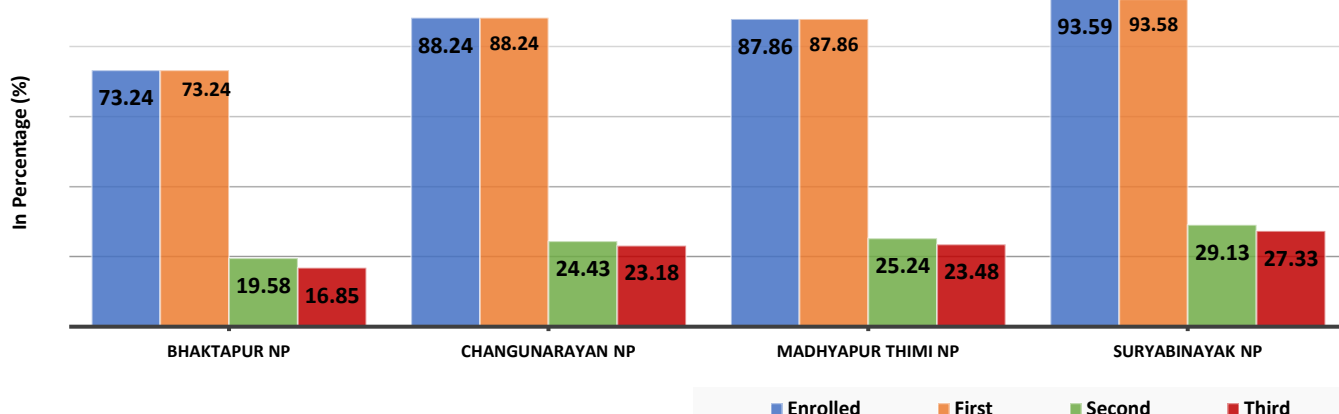

GRIEVANCE STATUS- BHAKTAPUR DISTRICT

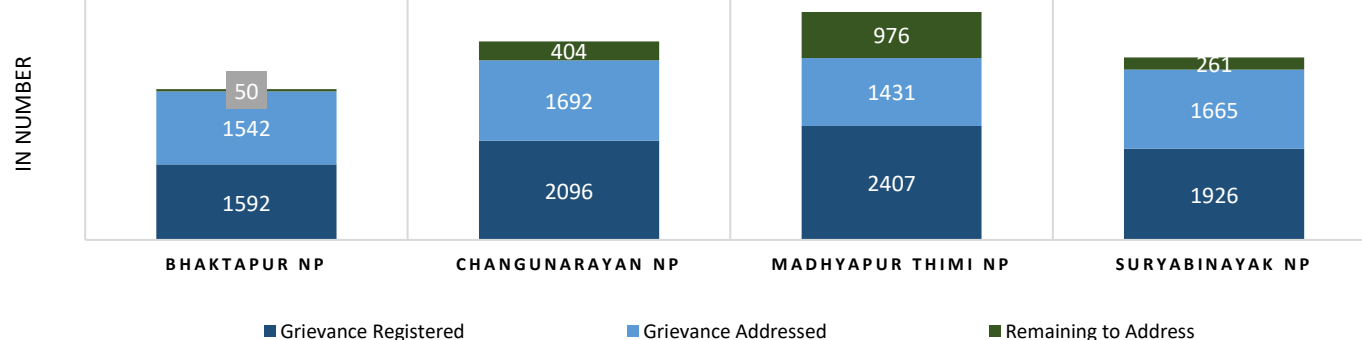

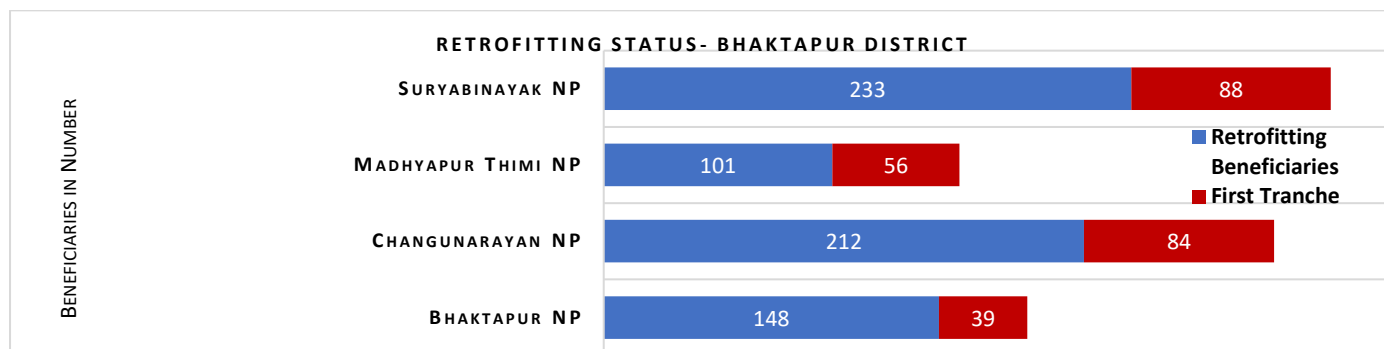

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
2 January 2018	Ward no 3, 8 and 9, Gokarneshwor Municipality	- Narakanta Sapkota, M & E Consultant/ DLPIU NRA-Building - Sweata Sijapati, District Technical Coordinator, HRRP Kathmandu Valley Team - Prajwal Karki, DSE, Kathmandu - Kusum Deo, Engineers, DLPIU Building, Gokarneshwor Municipality - Sudha Shrestha, Engineers, DLPIU Building, Gokarneshwor Municipality
Objective(s)	- To interact with local representatives along with engineers of municipality regarding the reconstruction issues and ways forward. - To observe the reconstruction status of the beneficiaries. - To provide inputs to the beneficiaries in regarding the technical assistance.	
Summary	HRRP Kathmandu valley team along M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 3, 8 and 9 of Gokarneshwor Municipality, Kathmandu district. The field visit was mainly focused on the observation of the Non-compliance cases and beneficiaries claiming for the 2nd tranche under retrofitting in the ward. The visit was accompanied by the DSE who gave suggestion to the beneficiaries for being eligible for the tranche. Most of the houses claiming to have done retrofitting was found to be technically non-compliance and couldn't be recommended for the tranche. In total 15 houses were visited among which 4 houses had requested to change from full damage to retrofitting. During the visit small community orientation was conducted in Tarebhir, Baluwa ward no 3. Due to the issues of Ghuthi land and low economic status the reconstruction was delayed. The beneficiaries were told about the government deadlines and the type design published by NRA/MOUD. Interaction with Ward Chief- Ward 03, Baluwa, Gokarneshwor Municipality: Before the visit to Tarebhir area, a brief meeting at ward office was conducted to discuss on the reconstruction status. As notified by the Mr. Rajendra Kumar Bhandari, Ward Chief, Ward no. 3, the cases of Baluwa is very complicated with issues of multiple beneficiary and duplication in the PA number. In Nagarkoti Basti of the same ward, beneficiaries have small land parcel which has delayed the reconstruction. Most of the land in the area have Tenant Farmers/ Land owner	

	(Mohi/Talsing) issues. The reconstruction in such land has been made flexible through the decision from board meeting of Gokarneshwor Municipality. The board decisions includes applying public inquiry deed for houses to be reconstructed on same land of landowners where house was damaged by earthquake. Public inquiry deed provides approval for building permit. However, if beneficiary wants to rebuild house in other place other than in property of landowners then, written consent need to be provided by landowners to beneficiaries. But beneficiaries (tenant farmers) have not been able to get in contact with the Talsing (land owners) due to reasons such as- land property were found to be neglected by landowners' family, death of main landowner etc. Ward office has coordinated with the municipality in being flexible through public inquiry deed, applying municipal bylaws but have not been successful. Mr. Bhandari, Ward Chief ensured that the municipality will support the technical staffs to coordinate with the ward staffs as well as beneficiaries to increase the reconstruction rate and solve the issues which has been delaying the progress.
--	---

Challenges / Issues Identified	Action Required	Responsible	Timeframe
The beneficiaries claiming for the retrofitting have conducted repair/ restoration and are not technically complaint.	The misunderstanding between repair and retrofitting must be cleared. Also, the guideline and procedure for the retrofitting is required to solve the such cases.	NRA, CLPIU (Building), DLPIU (Building), Technical staffs	As soon as possible
The issues of Mohi/Talsing in the ward no 3 has affected the reconstruction though NRA has provided guidelines to solve such issues.	Ward and Municipality must work on this issue and help people under common agreement to proceed with the reconstruction.	Ward office, Municipality, GMaLI, NRA	Before Poush 2075 deadline

Photos



Beneficiary Name: Ananda Prasad Sharma Bhandari, ward no 3, Gokarneshwor Municipality. The beneficiary has requested to change from full damage to retrofitting name list. The beneficiary has claimed to have retrofitting two storey BMM structure. Steel post of been used to form a frame structure in the second storey of the house. The beneficiary was suggested to reconstruct another house as the structure is not considered to be retrofitted.



Beneficiary Name: Subash Tamang, ward no 3, Tarebhir, Gokarneshwor Municipality. One storey 3 room SMC structure with flexible roof. The beneficiary has construed the house as per the design catalogue SMM 1.1 modified to SMC. During the inspection process the structure was found to be compliant and the inspection of 2nd, 3rd and completion was conducted at once.

Visit 2			
Date	Location	Participants from HRRP and stakeholders	
3 January 2019	Ward no. 6, Tipi Tole, Pharping, Dakshinkali Municipality	- Monika Shrestha Bajimaya, District IM Coordinator, HRRP - Ambika Amatya, District Coordinator, HRRP Kathmandu Valley Team - Prithvi Man Shrestha, Sub Engineer, Dakshinkali Municipality - Mahendra Raj Rajopadhyaya, beneficiary of Ward no. 6, Tipi Tole, Dakshinkali Municipality	
Objective(s)		- To collect case study of beneficiary who have returned 1st tranche in face of unintending to rebuild the earthquake damaged house. - To conduct Ward- level coordination meeting and discuss on reconstruction related issues and challenges in the ward.	
Summary		HRRP Kathmandu valley team visited Ward no. 6, Kochi Tole, Pharping area, Dakshinkali Municipality in order to collect case study of one beneficiary who returned 1st tranche as he was uninteresting to rebuild his house. Further, the team also conducted Ward level coordination meeting at Ward no. 6, Pharping. The meeting was facilitated by Prithvi man Shrestha, Sub Engineer, Dakshinkali Municipality. Key reconstruction issues of Ward no. 6 is related with small parcel land, unregistered land, households struggling with eccentric footing and issues of multiple beneficiaries. <u>Beneficiary who uninterests to rebuild the house</u> Mr. Mahendra Raj Rajopadhyaya cited the reason of lack of well trained mason, time consuming in search of personnel to sketch building drawing and lack of water in his area. Also, the beneficiary did not want to face hurdles of fine payment and blacklist.	
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Awareness on low cost design typology along with enough technical assistance is lacking in core urban wards.	Ward office along with municipality should conduct awareness programs or arrange help desk on technical assistance with a purpose to instill knowledge about low cost design typology among beneficiaries who cannot afford much to rebuild house with RCC typology	Municipality, Ward office, concerned POs	By Baishak 2076

Photos



Photo: Front view of Mr. Mahendra Raj Rajopadhaya's earthquake damaged house. Mr. Rajopadhaya has recently returned 1st tranche as he unintended to rebuild his house.



Photo: Temporary shelter owned by Mr. Mahendra Raj Rajopadhaya. This T-shelter is still in use by Mr. Rajopadhaya's family.



Photo: General Ward-level coordination meeting is in progress at Ward no. 6, Kochi Tole, Pharping, Dakshinkali Municipality




Photo: Attendance of participants involved in Ward level meeting conducted at Ward no. 6, Pharping, Dakshinkali NP

Housing Typology Report



Beneficiary name: Ms. Putali Tamang, Ward no. 6, Bakhri Gaun, Nagarkot, Changunarayan Municipality, is single storey and made from interlocking bricks with flexible roof. DPC works has been properly done. The owner has approved building drawing and applied for 2nd and 3rd together.



Beneficiary name: Mr. Niran Nepali, Ward no. 6, Pipalbot, Nagarkot, Changunarayan Municipality, reconstructed his house with hollow concrete blocks, single storey and wall system with flexible roof. The beneficiary revealed that tie beam and bands has been properly kept. The owner has approved building drawing and applied for 2nd and 3rd together.

Visit 3

Date	Location	Participants from HRRP and stakeholders
3 Jan, 2019	Ward no. 1, Sirutar/ Biruwa, wWrd no. 7, Gundu and Ward no. 8, Ganesthan, Suryabinayak Municipality, Bhaktapur district	- Narakanta Sapkota, M & E Consultant/ DLPIU NRA-Building - Manisha Rai, District Information Management Officer, HRRP Kathmandu Valley - Prabesh Adhikari, DSE, Bhaktapur - Manju Khadka, Engineer, DLPIU Building, Bhaktapur - Suraj Shrestha, Engineer, DLPIU Building, Bhaktapur - Jeena Suwal, Engineer, Suryabinayak Municipality - Rajani Shrestha, Sub-engineer, Suryabinayak Municipality - Dhan Kumari Tamang, Engineer, Suryabinayak Municipality
Objective(s)	- To observe and assess the non-compliance structures - To provide inputs to the beneficiaries in regarding the technical assistance.	
Summary	HRRP Kathmandu valley team along with M & E Consultant and Technical team from DLPIU NRA Building conducted joint field monitoring in ward no. 1, 7 and 8 Sirutar/Biruwa, Gundu and Ganeshsthan areas respectively of Suryabinayak Municipality, Bhaktapur district. Most of those houses were reconstructed immediately after the earthquake before the publication of the NRA guideline. So,	

field engineers could not forward them for 2nd and 3rd tranche. After assessing those structures in during the field visit, M&E consultant and DSE recommended to forward some houses for the remaining tranches. Similarly, some beneficiaries were suggested to adapt the correction measures.

Details of some houses-

- The 2 storey house of Sulochana Karki, Ward no. 8, is BMC load bearing with flexible roof. It house constructed immediately after earthquake was registered as non-compliance as it had 9" wall, missing lintel beam, no vertical reinforcement and incomplete sill bands. The monitoring team suggested beneficiary to wait until the decision from NRA to address such cases comes out.
- Govinda Hari Chalise, a beneficiary located in ward no. 8, reconstructed 2 storey hybrid structure, BMC in ground floor and prefab for the 2nd storey with flexible roof. The M&E and DSE recommended to forward the house for 2nd and 3rd tranche after the structural analysis.
- Rajaram Basnet located in ward no. 7, Gundu had applied for 2nd and 3rd tranche along with structure analysis report of 2 storey hybrid structure with rolling shutters. It is recommended as compliance after analyzing the used steel post, proper connection of the post and the rolling shutters and other materials.
- The one storey masonry structure of Pampha Karki in ward no. 1, Sirutar, has 2 rooms with flexible roof. The case was not recommended for 2nd and 3rd tranches as it was found to be non-compliance. The structure was found to have larger opening sections than recommended by the MRT, missing vertical bars and less wall thickness.
- Nakul Prasad Ghimire of ward no. 1, Biruwa had applied for the last 2 GoN grant installment of the 4 roomed one storey BMC structure with flexible roof. The rooms had partition of plywood. Though he has used enough steel bar as vertical reinforcement the proper connection of walls were missing.
- Bhagwan Pandey, a retrofitting beneficiary from Sirutar ward no.1 requested to observe his repaired house and expected for the last installment. A RCC structure with 9"X9" column was damaged and was listed it for retrofitting and had received 1st tranche, although, he just repaired the damaged portion of wall and the landing beam but have not done the retrofitting of the column as per manual. However, monitoring team suggested him to wait until the new guideline to address such issues who repaired only damaged wall or portion.
- Sita K.C., ward no.1, Sirutar had applied for 2nd and 3rd tranches of her reconstructed of one roomed one storey RCC structure with 9" wall. The structure was found to be compliant during initial inspection. But the beneficiary has added another storey and is connected to her son's house. The case is on hold and will be discussed further at DLPIU.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
The houses constructed immediately after the	Ward office, Municipality should find the number of such houses	Technical Staffs, DLPIU Building, NRA	As soon as possible

earthquake are mostly non-compliance and beneficiary are not willing to apply the correction measures. Some houses cannot be addressed by the correction/exception manual published by the NRA.	and coordinate with DLPIU Building and NRA to find a way forward to address such cases. Technical staffs must explain the needs and importance of such correction measures where applicable.		
---	--	--	--

Photos



Beneficiary name: Sulochana Karki, Ward no. 8, BMC load bearing with flexible roof. The house is constructed immediately after earthquake, was registered as non-compliance as it has 9" wall, missed lintel beam, no vertical reinforcement and incomplete sill bands. The monitoring team suggested beneficiary to wait until the decision from NRA to address such cases comes out.



Beneficiary name: Govinda Hari Chalise, a beneficiary located in ward no. 8, reconstructed 2 storey hybrid structure, BMC in ground floor and prefab for the 2nd storey with flexible roof. The M&E and DSE recommended to forward the house for 2nd and 3rd tranche after the structural analysis.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Due to weak financial condition, I am not being able to reconstruct the house. Is there any way I can get soft loans as announced by the government?	Beneficiary	NRA and the Bank association have come to an agreement to provide soft loan of NRP 300,000 with 5% interest for the beneficiaries who have not requested for the 2 nd tranche. More information on this loan can be provided by the banks. (M&E consultant, Kathmandu)
Still there are some earthquake affected people whose grievances have not been heard. In light of tight deadlines of NRA, can those people be listed as beneficiaries?	Ward member	NRA Central and CLPIU GMaLI will cross check all the unsolved grievances and new grievances too, which will soon be compiled to address for final time to put an end to grievances in order to meet the deadlines of shelter reconstruction of NRA by 2 years. Those people who wants to conduct resurvey of their house, they should as early as possible submit application in concerned Ward office for filing grievances. (HRRP team member)

Challenges and Way Forward

Challenge	Way Forward
With no signs of reconstruction of houses in core urban wards, chances are high that those beneficiaries will miss deadlines and are propelled to return 1 st tranche.	Municipality should push Ward office to conduct door to door visit to track reasons of delays in shelter reconstruction. Concerned elected members should accelerate to address core issues that has hindered reconstruction. Municipality should take proactive paths to solve local shelter reconstruction issues.
The land cases related with tenants and land owners (Mohi/Talsing) will perpetuate to delay the process of taking building permit approval. Overall delays affects the deadlines.	Concerned ward office should intervene with beneficiaries and coordinate with land owners to address this case or beneficiaries should be consulted enough to expediate steps to negotiate the case with land owners.
