


FACTS AND FIGURES

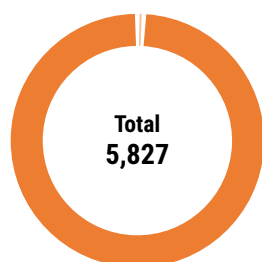

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	98.92%	89.07%
Adobe Structures	0.50%	4.25%
Stone and Cement Mortar Masonry	0.17%	0.64%
Brick and Cement Mortar Masonry	0.12%	2.11%
Others	0.29%	3.93%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	5,884
PA Agreement	5,691
I st Tranche received	5,691
II nd Tranche received	5,356
III rd Tranche received	4,416

Houses

Under Construction: -

Completed: 4,138

Retrofitting Status

Total Eligible HHs	35
PA Agreement	1
I st Tranche received	1
II nd Tranche received	35

Grievances

Registered: 425

Addressed: 425

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: ACF (Health), BO (Education), GIZ (Agriculture), GIZ (Education), GIZ (Health), GIZ (Shelter), GIZ (Hygiene), GON-PAF (Shelter), IMC (Health), NRCS (Health), OXFAM-GB (Shelter), PA (Shelter), SP-N (Education), SP-N (Hygiene), WR (Livelihood)

OTHER SECTORS



Schools

Damaged: 61
Under Construction: 23
Construction Completed: 23



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	158,047	Y	6,000
Aggregate	m ³	135,969	Y	6,000
Sand	m ³	16,638	Y	7,000
Timber	cu. ft.	18,326	Y	3,200
Cement (PPC)	Sack	-	Y	950
Cement (OPC)	Sack	459,180	Y	1,050
Rebars	kgs.	1,758,504	N	98
Tin	bundle	18,753	-	-
Bricks	pcs.	4,153,403	Y	14

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,200 /-
1,000 /-

KEY CONTACTS

Municipal Office

Yogindra Sing Tamang
Mayor
9851071953

Municipal Office

Anju Acharya
Focal Person
9849457675

Municipal Office

Anju Acharya
Deputy Mayor
9849457675

GMaLI/NRA

Bickey Lakha
NRA Chief-District
9849179333

Municipal Office

Ram Hari Gajurel
Administration Officer
9851126899

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
98550465884

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

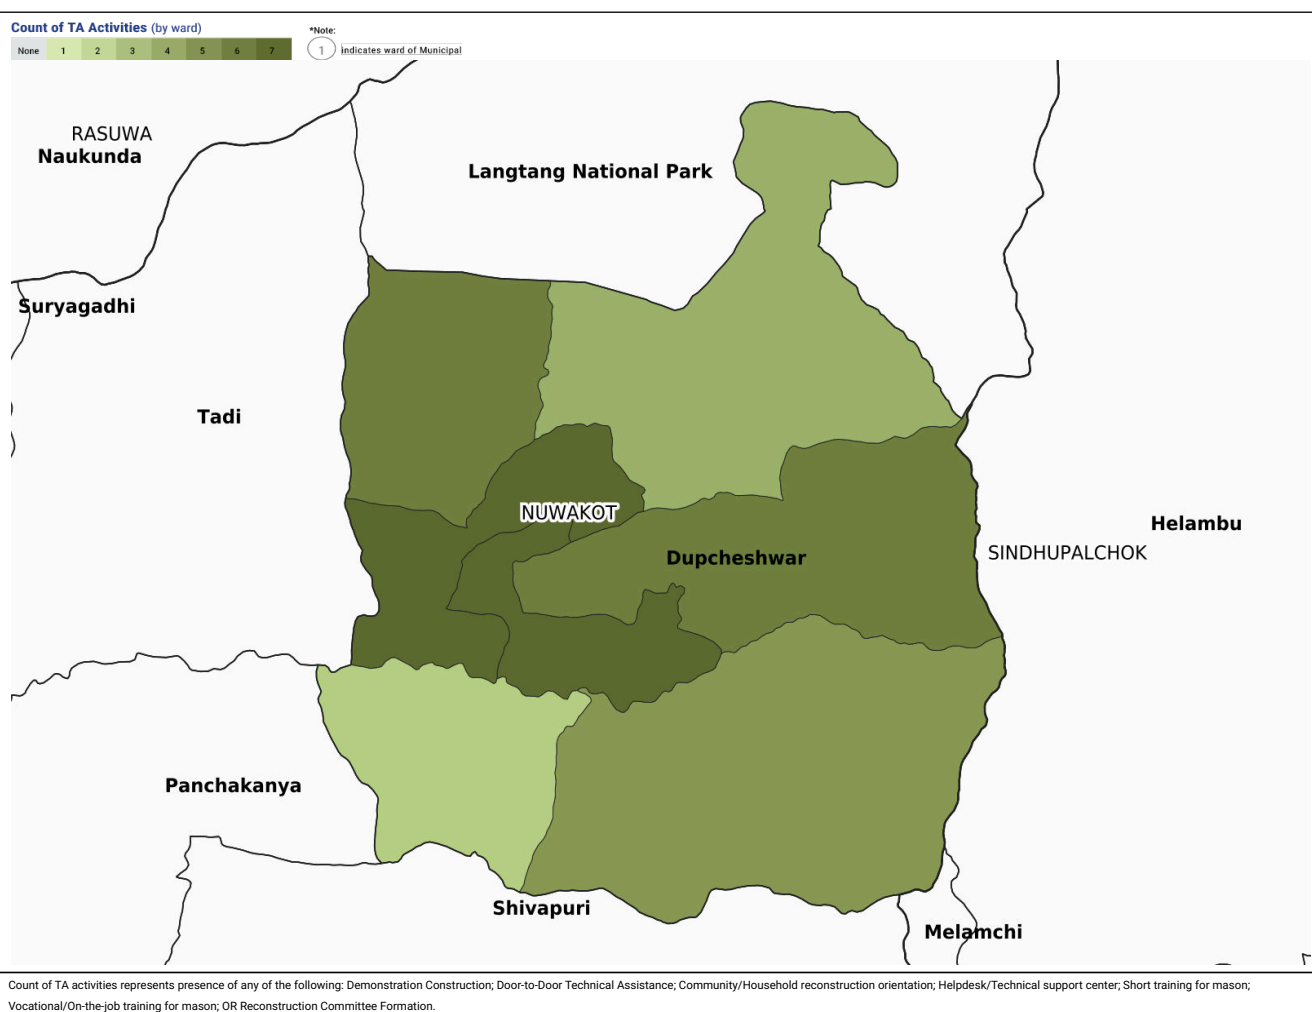

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Badri Pyakurel (District Coordinator) 9851154201	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
