


FACTS AND FIGURES



Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	97.23%	89.07%
Adobe Structures	1.03%	4.25%
Reinforced Cement Concrete (RCC) Frame	0.94%	3.05%
Brick and Cement Mortar Masonry	0.34%	2.11%
Others	0.48%	1.52%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	4,592
PA Agreement	4,472
I st Tranche received	4,472
II nd Tranche received	4,156
III rd Tranche received	3,344

Houses

Under Construction: - Completed: 3,151

Retrofitting Status

Total Eligible HHs	23
PA Agreement	3
I st Tranche received	3
II nd Tranche received	23

Grievances

Registered: 701
Addressed: 373

Non-compliances

Registered: -
Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: GIZ (Health), IMC (Health), MIDSON (Health), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), OXFAM-GB (Agriculture), OXFAM-GB (DRM), OXFAM-GB (Livelihood), OXFAM-GB (GESI), OXFAM-GB (Shelter), OXFAM-GB (Hygiene), PA (Shelter), RoomTR (Education), SP-N (Education), SP-N (Hygiene), WR (Livelihood), WVIN (Hygiene)

OTHER SECTORS



Schools

Damaged: 49
Under Construction: 38
Construction Completed: 38



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	97,852	Y	7,000
Aggregate	m ³	99,454	Y	7,000
Sand	m ³	10,441	Y	8,000
Timber	cu. ft.	12,021	Y	4,000
Cement (PPC)	Sack	-	Y	900
Cement (OPC)	Sack	330,492	Y	1,000
Rebars	kgs.	1,063,195	Y	98
Tin	bundle	13,510	-	-
Bricks	pcs.	1,158,128	Y	14

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,300 /-
1,000 /-

KEY CONTACTS

Municipal Office
Narayan Prasad Pandey
Mayor
9841459652

Municipal Office
Ashok Bista
Focal Person
9841284598

Municipal Office
Ishwori Upreti
Deputy Mayor
9841167206

GMaLI/NRA
Bickey Lakha
NRA Chief-District
9849179333

Municipal Office
Ashok Bista
Administration Officer
9841284598

DLPIU-Building
Koshnath Adhikari
DUDBC.DLPIU Chief
98550465884

HHs WITH LAND ISSUES



STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)

7 days Training




50 days Vocational Training



Source: HRRP Analysis

TA ACTIVITIES MAP

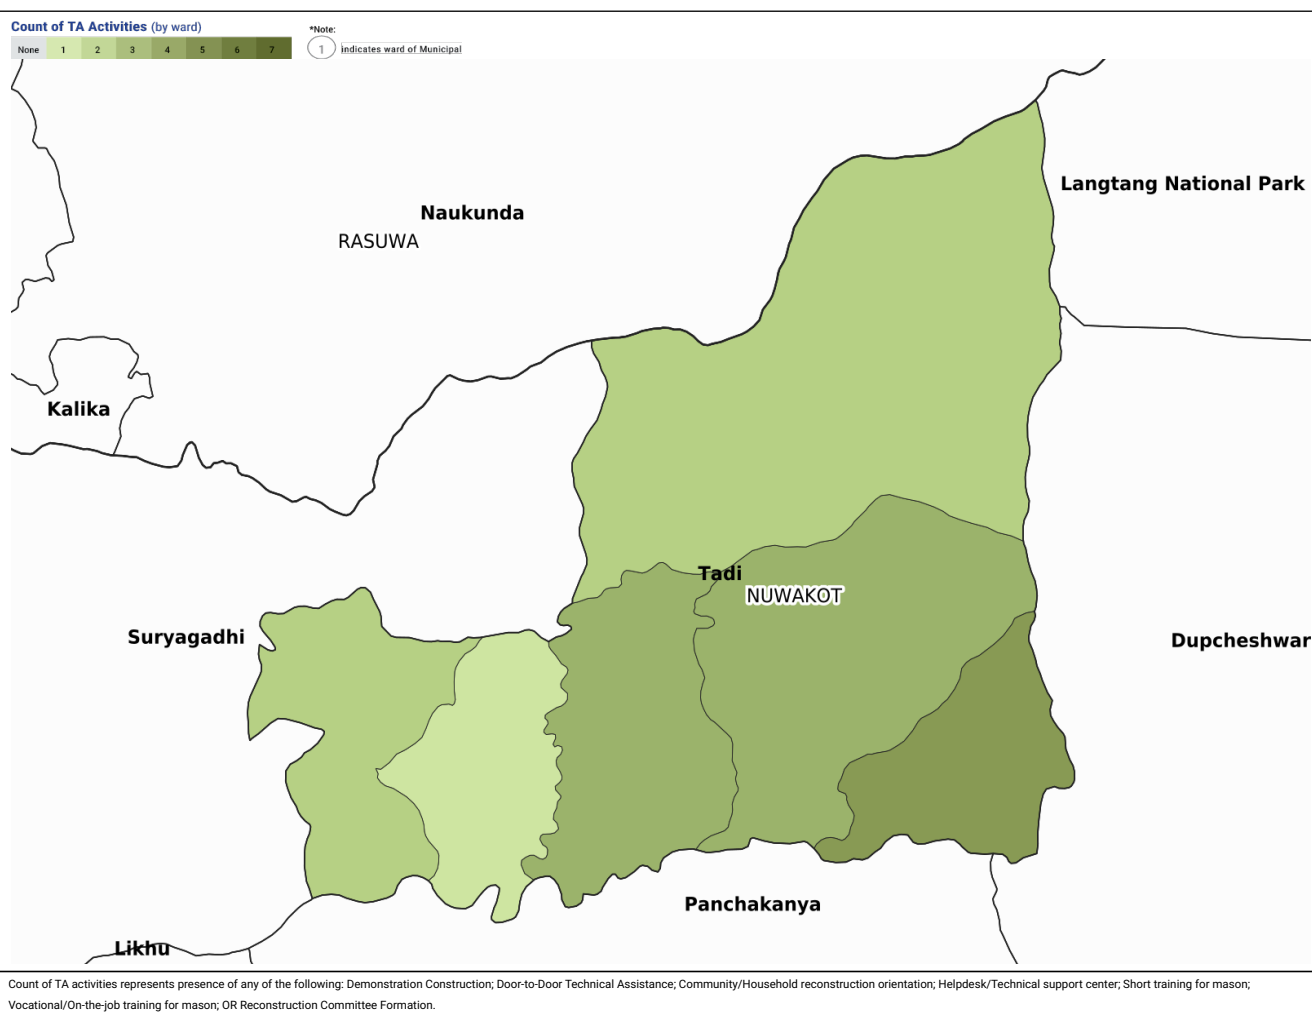

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Badri Pyakurel (District Coordinator) 9851154201	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
