

District Report

Dolakha

21 Dec 2018 – 3 Jan 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
DGCM concluded: District General Coordination Meeting (DGCM) concluded in district. In the meeting, Coordination Meeting. The key decisions taken in the meeting were development partners should coordinate with local levels(Ward/Palika) while working in their working areas. Some grievances heard from ward secretary in Bigu Gaunpalika during HRRP coordinated recent visits which raised by DLPIU(Building) focal person.	26 th Dec 2018	13	1	Rita Lamsal, Information Officer, GMaLI Dolakha Cell: 9846075504 Email: ritalamsal@gmail.com	
Orientation and review concluded: CLPIU(Building) organized orientation and review meeting on private housing construction in district. Local bodies, reconstruction stakeholders like GMaLI, DLPIU(Building/Education), District Treasury Comptroller Office, CDO, DCC, Banks, journalist, POs participated. Subsequently, local bodies and GMaLI signed on the handover documents where lots of authorities have been transferred to local bodies. 9 Palikas have signed in the document. Mr. Hareram Parajuli, Executive Member of NRA sort out lots of issues in the programme. HRRP especially facilitated for Palika profile and action plan of local level.	21-22 Dec 2018	81	27	Bhogendra Sah, Focal Person, DLPIU(Building), Dolakha, Cell: 9844432509 Email: mouddlpiu.dolkha@gmail.com	
Refresher Training for DLPIU Engineers, SEs and ASEs concluded: DLPIU(Building) conducted Refresher training to DLPIU(Building) Engineers, Sub-Engineers and Assistant Sub-engineers from Dolakha. DLPIU(Building), GMaLI, HRRP facilitated the training.	28 th Dec 2018	21	5	Bhogendra Sah, Focal Person, DLPIU(Building), Dolakha, Cell: 9844432509 Email: mouddlpiu.dolkha@gmail.com	

News & Updates

ढेक्कापड्डामा हेडमास्टर

रवीन्द्र गौतम | चरीकोट

हेडमास्टर नै ठेकेदार भएर विद्यालय भवन पुनर्निर्माणमा लागेपछि दोलखाका अधिकांश विद्यालयको पढाइ प्रभावित भएको छ। तीन वर्षदेखि शिक्षण सिकाइ उपलब्धि घट्दो क्रममा रहेको स्रोत शिक्षकको भनाइ छ।

भूकम्पपछि जिल्ला आयोजना कार्यान्वयन इकाइ (शिक्षा) दोलखाले विद्यालय व्यवस्थापन समितिमार्फत पुनर्निर्माण गराएको छ। पुनर्निर्माणमा हेडमास्टर खर्चिदा निर्यात पढाइमा समस्या परेको गुनासो स्थानीय तहबाट आएको दोलखा इकाइ प्रमुख देवकुमार बरालको भनाइ छ। जिल्लाका १ सय ९२ विद्यालयमध्ये अधिकांशमा हेडमास्टरले नै

दोलखाका अधिकांश विद्यालयमा हेडमास्टरले नै पुनर्निर्माणको काम गरिरहेको अभिभावकको गुनासो।

पुनर्निर्माणको काम गरिरहेको अभिभावकको गुनासो छ।

‘हेडमास्टरचाहिँ कमिसन खान टिपर चढेर निर्माण सामग्री खोज्दै हिँड्ने, अरू शिक्षकले के पढाउँछे?’ अभिभावक रामबहादुर थामीले भने, ‘अनि, कसले पढाउने? छोराछोरी त २ बजे नै घर आइपुग्छन्।’

उनका अनुसार ७२ विद्यालय पुनर्निर्माण भइसकेका छन्। ७२ वटा निर्माणाधीन छन्। निर्माणाधीनमध्ये

पनि ९० प्रतिशत भवन हेडमास्टरले नै निर्माण गरिरहेका छन्।

पुनर्निर्माण प्राधिकरणका प्रमुख कार्यकारी सुशील ज्ञवाली सिंगटी पुगेका बेला विगु गाउँपालिका उपाध्यक्ष सञ्जीव ओलीले अनुगमन गर्न आग्रह गरेका थिए। विद्यालय भवन पुनर्निर्माणमा ठेकेदारजसरी हेडमास्टर लागेपछि पढाइ प्रभावित हुने गरेको सेलुङ गाउँपालिकाका अध्यक्ष भरत दुलालले बताए। मेलुङमा पनि यही अवस्था रहेको गाउँपालिकाका प्रवक्ता हीरा थोकरको भनाइ छ। ‘स्कुलमा हेडमास्टर भेटिँदैनन्’, उनले भने, ‘फोन गर्दा आफू कहिलेसिमेन्ट, कहिले ईट्टालिन गएको भन्छन्।’

शिक्षक महासंघ दोलखाका अध्यक्ष पदम जिरालका सबै हेडसर यस्तो

नभए पनि कतिपयले व्यवस्थापन समितिलाई गुमराहमा राखेर ठेकेदारजस्तो बनेका छन्। सरकारले खरिद ऐन मिचेर करोडौंका निर्माण कार्य व्यवस्थापन समितिलाई सुमिँदा समस्या भएको जिल्ला निर्माण व्यवसायी संघका अध्यक्ष शमशेर घिसिङको भनाइ छ।


जिरी नगरपालिका मालीस्थित हलेश्वर आधारभूत विद्यालयका हेडमास्टर भक्त केसीले यो रहर नभई बाध्यता भएको बताए। व्यवस्थापन समितिले चासो नदेखाएका कारण ढुंगा, गिट्टीदेखि बालुवा, सिमेन्टसम्म आफैँ बोक्नुपरेको उनको दुखेसो छ। ‘नयाँ भवन आएको छ, आवश्यकता पनि छ’, उनले भने, ‘व्यवस्थापन समिति चासो दिँदैन, अनि हामीले नबनाए कसले बनाउँछ?’

Headteacher in contract of schools, Rabindra Gautam, Charikot, Annapurna Post daily, December 28, 2018


Tranche Status

Rural /Municipality	Baiteshwor	Bhimeshwor	Bigu	Gaurishankar	Jiri	Kalinchowk	Melung	Sailung	Tamakoshi
Total HHs Surveyed	8550	13693	6799	6656	5991	9062	8067	8524	7537
Total HHs Eligible	8308	12394	6699	6762	5805	8866	7474	8110	7428
Total HHs Enrolled	7563	11810	6186	5576	4948	8060	6337	6762	6245
First Tranche	7649	10285	5879	5587	4754	8184	6325	6437	6429
Second Tranche	6435	7411	5007	5028	3447	7088	5349	5034	5671
Third Tranche	5742	5305	4355	4733	2618	6549	4313	3714	4879
Total HH Constructed	5763	5329	4384	4751	2632	6572	4327	3727	4891
Grievance Registered	248	546	132	123	222	378	1191	226	84
Grievance Addressed	1795	2235	719	760	961	1238	1100	1257	828
RF HH Eligible	339	348	34	74	153	32	402	746	110
RF HH Enrolled		50	2						
RF 1 st Tranche		50	2						
RF 2 nd Tranche		0	0						
Non-Compliance Registered	1827 (9 Palikas in total)								
Non-Compliance Addressed	1491 (9 Palikas in total)								

Tranche Update

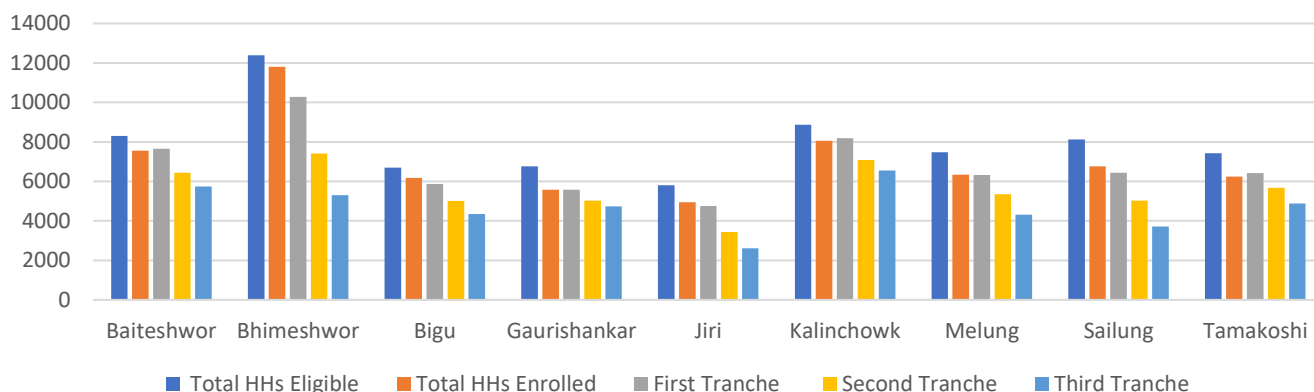

Retrofit Update

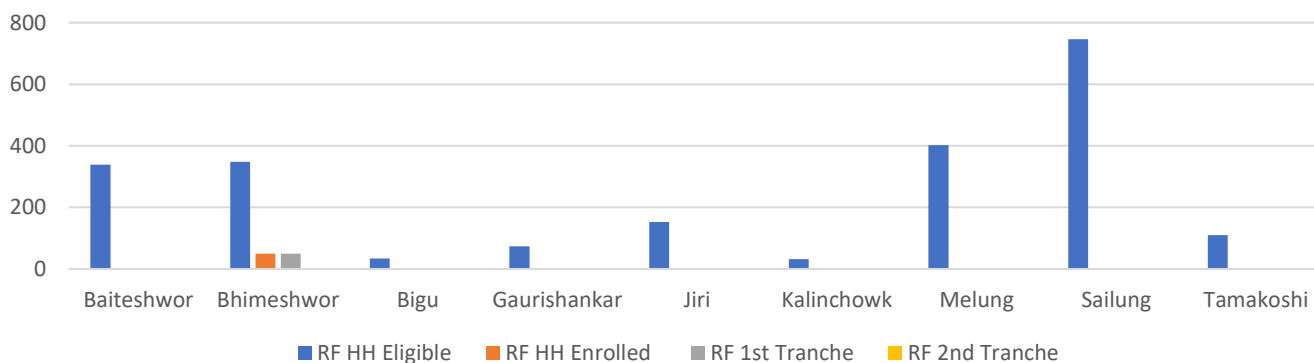

Grievance Update



Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
23 rd Dec 2018	Sundrawati, 09-ward of Kalinchowk RM	- Binod Kumar Kalauni - Kamal B Mahat - Janak Raj Joshi (M&E) - Bhogendra Kr Sah (DLPIU/Focal Person) - Mohan Pokhrel, DSE - Bhimshen Maskey (Account Officer/DLPIU) - Devi Prasad Chaulagai (Computer Operator) - Rajiv Thakur (Sub-Engineer/DLPIU)


Objective(s)

- To conduct Palika Level Meeting
- To Collect Housing Typologies
- To Talk about completion certificate and correction needed

Summary

Palika level meeting was conducted at Sundrawati, 09-ward of Kalinchowk RM. The meeting was chaired by ward president Mr. Ram Prasad Mainali. During the meeting mainly, the problem related to the reconstruction was discussed. In the meeting non-compliance cases which were initially forwarded to DLPIU were not forwarded with correction measures regarding this ward chairperson requested for fast decision on such files. In this DLPIU representative answered that such cases will be forwarded as soon as possible. We came to know that technical staff are not regularly present at ward. This was serious issue on which DLPIU representative suggested ward chairperson to provide a register for the attendance of every day of technical staff. This will be helpful in verifying their attendance at the end of the month also useful to track their presence at field. Additionally, DLPIU representative requested ward president to carry forward the final inspection of those houses who have received third tranche and completed their roof level. In this ward office/ward representative act as lead since it is the main government body at ward level and technical staffs have to do final inspection. Furthermore, we (joint monitoring team) suggested ward president and engineer to conduct the corrections prescribed by the world bank after the survey of sample houses by the third-party monitoring agent in which we told that if there will be any technical problem in implementing the correction then orientation or directed implementation in the presence of the DSE can be done. Different typologies were collected during the field visit. Though this was not scheduled but while traveling to the field we met with the ward chairperson and he requested to have tea talk this created the environment of meeting with minute.

Photos

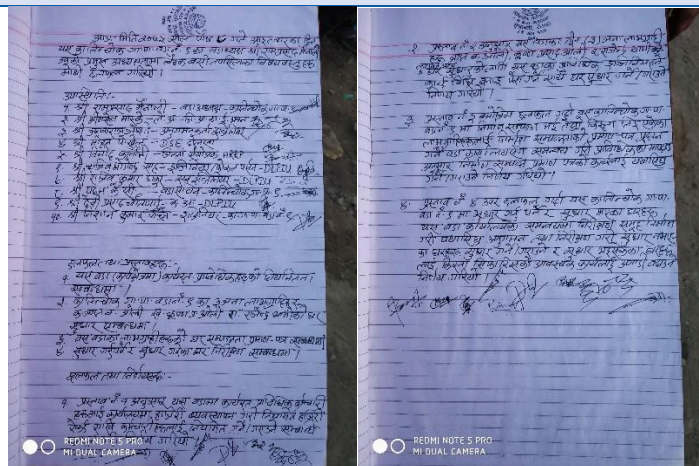

Ward Level Meeting Minute of Sundrawati, 09-ward of Kalinchowk RM. Pc = Binod Kalauni




Ward Level Meeting Minute of Sundrawati, 09-ward of Kalinchowk RM. Pc = Binod Kalauni

Field Visit /Joint Field Monitoring Visit Reports

Visit 2

Date	Location	Participants from HRRP and stakeholders
23 rd Dec 2018	Khopachangu, 08-ward of Bigu RM	- Binod Kumar Kalauni - Kamal B Mahat - Janak Raj Joshi (M&E) - Bhogendra Kr Sah (DLPIU/Focal Person)


		- Mohan Pokhrel, DSE - Bhimshen Maskey (Account Officer/DLPIU) - Devi Prasad Chaulagai (Computer Operator) - Rajiv Thakur (Sub-Engineer/DLPIU)
Objective(s)		- To conduct Palika Level Meeting - To Collect Housing Typologies - To Talk about completion certificate and correction needed
Summary		Palika level meeting was conducted at Khopachangu, 08-ward of Bigu RM. The meeting was chaired by ward chairperson Mr. Khem Bahadur Khadka. During the meeting mainly, the problem related to the reconstruction was discussed. In which we found that some houses have been constructed without keeping DPC, vertical member and band at required locations. Additionally, lintel/roof band is discontinuous in many houses which has been noticed and reported to DLPIU from third party monitoring team of world bank. We also found that due to the infrequent presence of technical staff at field has created problem in forwarding files for the tranches and implementation of correction after prescription from DSE. In this DLPIU representative requested ward president to carry forward the final inspection through ward for the distribution of the construction completion certificate. In this regards ward president was very positive to conduct final inspection. Additionally, we suggested ward president and engineer to conduct the corrections prescribed by the DSE in which we told that if there will be any technical problem in implementing the correction then orientation or directed implementation in the presence of the DSE can be done. According to the data from third party monitoring maximum number of non-compliance were seen in Khopachangu among other wards of Bigu RM. Further the different typologies were collected during the field visit.
Photos		
		
Ward Level Meeting Minute of Khopachangu, 08-ward of Bigu RM. Pc = Binod Kalauni		Ward Level Meeting Minute of Khopachangu, 08-ward of Bigu RM. Pc = Binod Kalauni

Field Visit /Joint Field Monitoring Visit Reports

Visit 3

Date	Location	Participants from HRRP and stakeholders
24 th Dec 2018	Bigu, 07-ward of Bigu RM	• Binod Kumar Kalauni • Kamal B Mahat • Janak Raj Joshi (M&E) • Bhogendra Kr Sah (DLPIU/Focal Person) • Mohan Pokhrel, DSE • Bhimshen Maskey (Account Officer/DLPIU) • Devi Prasad Chaulagai (Computer Operator) • Rajiv Thakur (Sub-Engineer/DLPIU)
Objective(s)		
• To conduct Palika Level Meeting • To Collect Housing Typologies • To discuss about completion certificate and correction needed		
Summary		
Palika level meeting was conducted at Bigu, 07-ward of Bigu RM. Ward chairperson was not present because he was in Kahmandu for medical treatment therefore ward member, acting ward chairwomen Mrs. Indira Basnet chaired the meeting. During the meeting mainly, the problem related to the reconstruction was discussed. During the meeting ward secretary told that almost 80% houses have been constructed till date and only 20% houses are remaining to complete. Further he raised the issue of delay in forwarding the tranche from respective authorities of reconstruction. He questioned who is responsible for the follow up since many beneficiaries they came to the ward office after forwarding the file for the tranche, but they don't have any information regarding the tranche. He requested for the sharing of information to the ward office after the tranche deposited in the individual account number that will be helpful for the beneficiaries to know status of tranche otherwise everyone has to go Charikot for the information which is tedious and expensive. Additionally, we got to know that major non-compliance is in SMM which includes addition of attic, additional story are the major issues. Another topic was about the presence of the technical staff of DLPIU/Building in which ward secretary told that till now they have done satisfactory performance so no grievance regarding presence of technical staff. Further DLPIU focal person suggested to keep attendance of technical staff which will be helpful for verifying their monthly attendance and their presence at ward level. Additionally, DLPIU representative requested ward secretary to carry forward the final inspection of those houses who have received third tranche and completed their roof level. In this ward office/ward representative act as lead since it is the main government body at ward level and technical staffs have to do final inspection. In this we found ward very positive to conduct final inspection. Additionally, we suggested ward chairperson and engineer to conduct the corrections prescribed by the DSE in which we told that if there will be any technical problem in implementing the correction then orientation or directed implementation in the presence of the DSE can be done. Further, different typologies were collected during the field visit.		

Photos



Ward Level Meeting Minute of Sundrawati, 07-ward of Kalinchowk RM. Pc= Binod Kalauni



Ward Level Meeting Minute of Sundrawati, 09-ward of Kalinchowk RM. Pc= Binod Kalauni

Field Visit /Joint Field Monitoring Visit Reports

Visit 4

Date	Location	Participants from HRRP and stakeholders
24 th Dec 2018	Aalampu, 06-ward of Bigu RM	- Binod Kumar Kalauni - Kamal B Mahat - Janak Raj Joshi (M&E) - Bhogendra Kr Sah (DLPIU/Focal Person) - Mohan Pokhrel, DSE - Bhimshen Maskey (Account Officer/DLPIU) - Devi Prasad Chaulagai (Computer Operator) - Rajiv Thakur (Sub-Engineer/DLPIU)

Objective(s)

- To conduct Palika Level Meeting
- To Collect Housing Typologies
- To discuss about completion certificate and correction needed

Summary

Palika level meeting was conducted at Aalampu, 06-ward of Bigu RM. Ward chairperson was not present because he was in Charikot for meeting therefore we did informal tea talk with ward secretary. During the talk mainly, the problem related to the reconstruction was discussed. During the meeting ward secretary told that almost 80% houses have completed their construction and only 20% houses are remaining to complete. Main issue of the ward was 65 people are identified who are genuine earthquake victims but not included in the list of the beneficiaries. Therefore, he requested visiting team what can be done for such people. Answering to that question DLPIU/Building focal person and M&E jointly suggested to keep record of such genuine people who has not been listed yet as earthquake victim list because NRA is going to conduct resurvey and verification at that time such cases will be surveyed and addressed. Additionally, we got to know that major non-compliance is in SMM which includes addition of attic, additional story are the major issues. Another topic was about the presence of the technical staff of DLPIU/Building in which ward secretary told that they frequently absent at ward. Additionally, he told that technical staff they just come for one week in a month and does inspection of houses after that they absent for whole month and came again at the time of attendance verification and signature for the salary claim. Further DLPIU focal person suggested to keep attendance of technical staff which will be helpful for verifying their monthly attendance and their presence at ward level. Additionally, DLPIU representative requested ward secretary to carry forward the final inspection of those houses who have received third tranche and completed their roof level. In this ward office/ward representative act as lead since it is the main government body at ward level and technical staffs have to do final inspection. In this we found ward very positive to conduct final inspection. Additionally, we suggested ward chairperson to conduct the corrections prescribed by the DSE in which we told that if there will be any technical problem in implementing the correction then orientation or directed implementation in the presence of the DSE can be done. Further, different typologies were collected during the field visit. Minuting was not possible as the ward office was closed.

Photos



Ward Level Meeting at Aalampu, 06-ward of Bigu RM. Pc = Mohan Pokharel, DSE/DLPIU/Building



Ward Level Meeting at Aalampu, 06-ward of Bigu RM. Pc = Mohan Pokharel, DSE/DLPIU/Building

Housing Typology Report



Hybrid structure with dry stone masonry in ground floor and Light timber frame structure in First floor has been constructed in Bigu, 7-ward of Bigu RM. Sanche Maya Tamang is the house owner and she has received third tranche. After receiving third tranche to meet living requirement house owner has added light structure above ground floor.

Pic: Binod Kalauni



Hybrid structure with dry stone masonry in ground floor and Light timber frame structure in First floor has been constructed in Aalampu, 6-ward of Bigu RM. Dhan Kr. Thami is the house owner and he has received third tranche. After receiving third tranche to meet living requirement house owner has added light structure above ground floor.

Pic: Binod Kalauni



Load bearing stone and cement mortar masonry building has been constructed in Hundling, 05-ward of Bigu RM. Hom Bahadur Khadka is the house owner and he has received third tranche.

Pic: Binod Kumar Kalauni



Load bearing stone and cement mortar masonry building has been constructed in Hundling, 05-ward of Bigu RM. Bhimsen Nepali is the house owner and he has received third tranche.

Pic: Binod Kumar Kalauni



Hybrid Structure in which SMM in ground floor and Light timber frame structure in first floor has been constructed in Chilankha, 05-ward of Bigu RM. Bir Bahadur Nepali is the house owner and he has received third tranche of housing grant. Bracing in the first floor has not been provided because the owner doesn't know about its importance. Pic: Binod Kumar Kalauni



Hybrid Structure in which SMM in ground floor and Light timber frame structure in first floor has been constructed in Chilankha, 05-ward of Bigu RM. Subash Nepali is the house owner and he has received third tranche of housing grant. Pic: Binod Kumar Kalauni

Case Study



Figure1: Interaction with house owner of hybrid building(without bracing) at Chilankha, 05-ward of Bigu RM Pc = Binod Kalauni

Figure2: Hybrid structure building (without bracing) at Chilankha, 05-ward of Bigu RM, Pc= Binod Kalauni

Field visit to Bigu RM was quite surprising at the end of the day when we were traveling back to the duty station. We visited few houses in Chilankha, 05-ward of Bigu RM where we came to know that people are unknown about the cross bracings which is the key element to resist earthquake force in hybrid structure (Masonry in ground floor and light timber frame in first floor). First photograph is clearly supporting the statement and people standing in front of the photograph are masons and house owner.

Mr. Double Bahadur Nepali is the house owner with him we asked about the bracing and its importance in light timber frame structure, but he was unable to answer even the masons working at site was also unable to answer it. We asked masons does they have taken trainings they replied that they had but about the bracing no one has taught them. This was seriously surprising and shocking for the visiting team. We explained the importance of bracing and suggested to keep bracings with details. We asked house owner does he has requested for the technical assistance from DLPIU technical team he replied that it is hard to get technical person at building site because presence of DLPIU engineer at site is quite low. He further told that his brother has also not provided bracings (building shown in second photograph). We also asked why he has added light frame structure he replied that ground floor is not only sufficient to meet living space requirement also the building is attached with road so ground floor can also be used as commercial purpose i.e. shop or tea hotel.

This type of space need fulfillment without proper technical advice creating major issue in the final inspection of the houses. Data shared by the third-party monitoring agent of World Bank has also showed that major non-compliances are tracked after receiving third tranche i.e. lintel/roof band. To sort out this presence of technical staff is not only enough parallelly an awareness is necessary among the beneficiaries that what element is important in which type of structure to resist the earthquake or seismic load otherwise the aim that NRA has set BBB (Build Back Better) would not be possible. Correction to such houses is also not easy without the support from local government because people are not willing to do corrections after receiving third tranche. People are not giving that much importance to completion certificates therefore it is challenging for the NRA how to add value to the completion certificate by seeking support from the local government will going to be even more challenging.
