

Fortnightly District Report

Makwanpur

18 – 31 January 2019

Summary of events during this period

Name of activity/event	Event date & Venue	Participant Summary		Contact Person	Reference Document
		M	F		
Interaction with Partner Organizations: As part of implantation of Decision No. 1 (c) of last meeting of District Reconstruction Facilitation Committee held on 10th January, 2019, DLPIU-GMaLI Makwanpur and HRRP Makwanpur, in collaboration with DRFC, have successfully organized "Interaction with Local Banks" on 21st January, 2019. Participants: ☞ Chief of DCC, Makwanpur ☞ Dignitaries from NRA/CLPIU ☞ DLPIU-GMaLI Chief and staffs ☞ DLPIU-Education and DLPIU-Building ☞ Representatives of 20 different banks ☞ HRRP District Team Objectives: ☞ To identify the key issues related to the transfer of tranches of housing grants and delivery of soft housing loan provisioned for earthquake affected beneficiaries. ☞ To seek possible way forward for the difficulties associated with the service delivery of the banks. Key Activities: ☞ Mr. Som Raj Timilsena, Chief of DLPIU-GMaLI, shared the reconstruction updates, key issues and challenges. The summary of presentation is annexed herewith. ☞ Mr. Kedar Man Joshi, Financial Management Specialist, NRA: Mr. Joshi made a presentation on details of financial management and mitigation of financial risks associated with the financial institutions being engaged in disbursement of post-earthquake housing grants. ☞ Plenary Discussion: After the presentation, participants, mainly the representatives of local banks and officials of DLPIUs participated in plenary discussion. Major concerns were concentrated on difficulties in release of tranches of housing grants due to lack of documents to be submitted by the respective beneficiaries. ☞ Adjourn: With votes of thanks and a brief opinion, Mr. Raghu Nath Khulal, finally adjourned the event.	21st Jan, 2019 2:00PM onwards DCC Meeting Hall, Hetauda, Makwanpur	50	13	dc.makwanpur@hrrpnepal.org	Event Report available at: https://drive.google.com/drive/u/0/folders/123NC30C558sDgfN-QJ5kxd9BkLoMT928

Summary of events during this period

Palika Level Technical Coordination Meeting at Raksirang - 6: Chaired by: Mr. Singh Lal Praja, Ward President, Raksirang R. M. Ward No. 6 Participants: Members of Tole Development Organizations, DSEs, DC, DTC and IMO of HRRP, Engineers, few beneficiaries and local school teachers. Minute Prepared by: Hari Thalang, District Coordinator, HRRP. Agenda: 1. Reconstruction updates review. 2. Final inspection, CS entry and distribution of completion certificates to the completed houses. 3. AoB. Decisions: - Based on the reconstruction updates shared by local engineer and ward chair, it has been concluded that progress in reconstruction in Raksirang – 6 is satisfactory; and, except new beneficiaries added from grievances, construction of houses of all beneficiaries will be completed within the current FY. The progress is as follows: - First Tranche released: 266 - Second Tranche released: 266 - Third Tranche released: 122 - Third Tranche approved: 8 - Non-compliance issues - no more serious non-compliance issues observed. - The meeting agreed to include Final Inspection and Completion Certificate Distribution in Agenda of next Monthly Ward Meeting, being held on 4th of Falgun, 2075. District team agreed to provide Final Inspection Forms to field technicians. It was also agreed to initiate CS entry of the completed houses. - The ward chairperson urged to overcome delay in release of tranches after submission of approved inspection forms. - It was agreed to mobilize local CBOs, namely– Tole Development Organizations formed in different toles of the ward.	23rd Jan, 2019 11:00AM onwards Rakshrang – 6, Silinge	10	3		Meeting Minute available at: https://drive.google.com/drive/u/0/folders/12Uf7vZvxGYgNSQ6-umEvLOCeVk5fX_EZ
Joint Field Monitoring Visit: Joint monitoring visit has been accomplished at Ward No. 6 of Raksirang Rural Municipality. Participants: - DSEs, - Local representatives, - HRRP DTC, - NRA technicians - Beneficiaries. Objectives: - To organize technical coordination meeting and carry out field visit; to collect measure issues, housing typology.	Date: 23rd and 24th Jan 2019 Time: 7:00AM onwards Location: Raksirang Rural Municipality-06,07(Kakda VDC)	10	6	techcord.makwanpur@hrrpnepal.org	Report & Photos

Summary of events during this period

- ☞ Plan to prepare distribute the completion certificate for completed houses and promote to early final inspection and CS entry.
- ☞ Monitoring to noncompliance issues and recommended for correction, if any.


Upcoming Events and Meetings

Name of Event/Activity	Date, Time and Location	Organizer	Contact Person
ToT on Construction of Earthquake Resisting Building	6 th – 12 th Feb, 2018 8:00AM DCC Hall, Hetauda	CLPIU-Building DLPIU-Building HRRP-Technical support	techcord.makwanpur@hrrpnepal.org
District General Coordination Meeting	7 th Feb, 2019 2:00PM onwards. DCC, Makwanpur	DLPIUs and HRRP	dc.makwanpur@hrrpnepal.org


Tranche Status

Municipality	Bagmati	Bakaiya	Bhimfedi	Hetauda	Indrasarowar	Kailash	M'Gadhi	Manahari	Raksirang	Thaha	Total
Total HHs Surveyed	3454	2384	1056	1636	599	1095	2029	2322	968	1596	17139
Total HHs Eligible	2467	3990	2696	6324	2921	2609	2209	2321	1710	6727	33974
Total HHs Enrolled	1880	2393	2114	5284	2485	2005	1677	1248	1528	6017	26631
First Tranche	1877	2310	2099	4641	2428	2005	1667	1246	1517	6007	25797
Second Tranche	1403	1648	2037	2586	1815	1458	1289	1024	1403	4829	19492
Third Tranche	859	693	1640	2518	1148	1226	862	814	940	3138	13838
Total HH Constructed	610	405	1410	2010	950	1010	655	625	750	2650	11075
Grievance Registered	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
Grievance Addressed	3756	3893	1378	3419	1104	1557	2153	2819	1224	2658	23961
RF HH Eligible	1941	1616	929	1881	245	606	1372	1330	537	1178	11635
RF HH Enrolled	532	404	397	1013	167	185	277	494	358	612	4439
RF 1 st Tranche	511	254	383	1013	152	177	277	489	359	612	4227
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	79	334	190	661	49	90	294	489	54	273	2513
Non-Compliance Addressed	71	328	187	635	49	85	286	464	54	248	2407


TRANCHE UPDATES

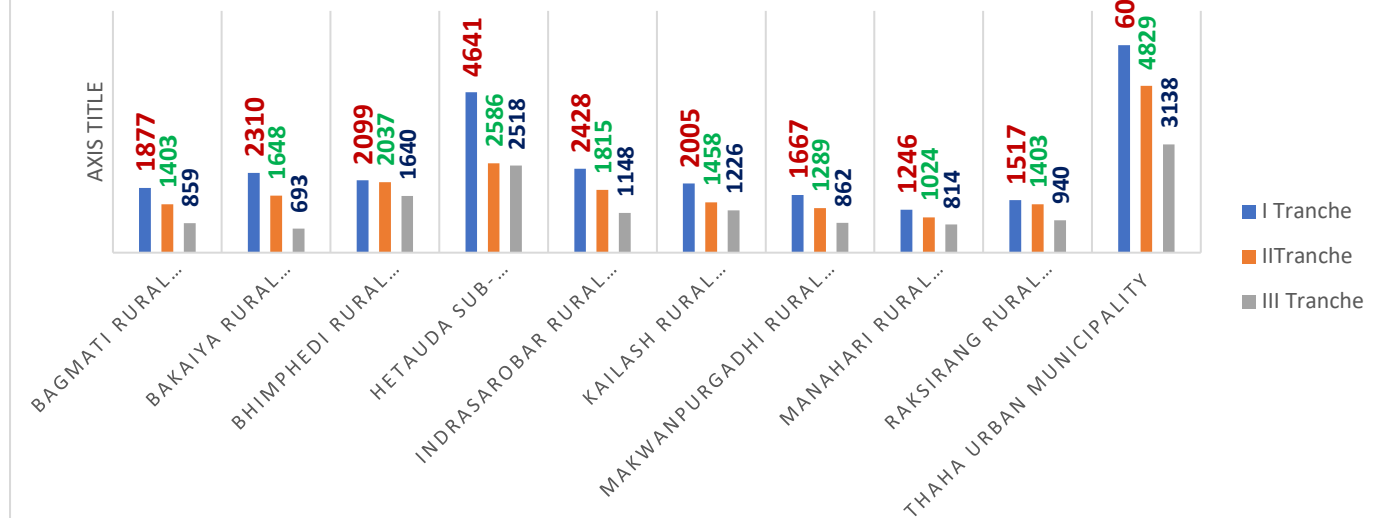

RETROFITTING UPDATES

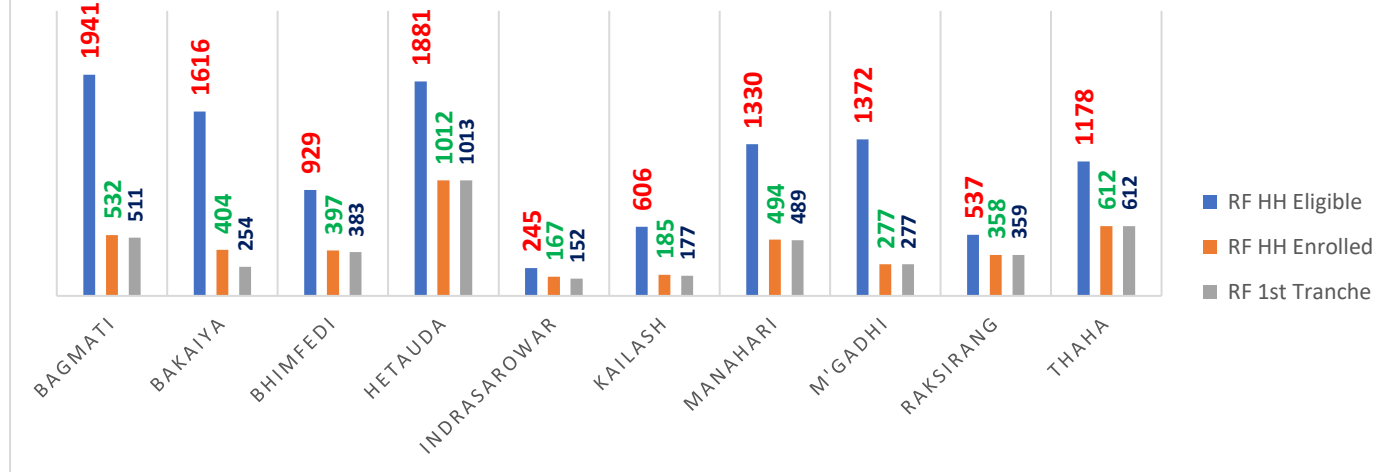

GRIVANCE STATUS

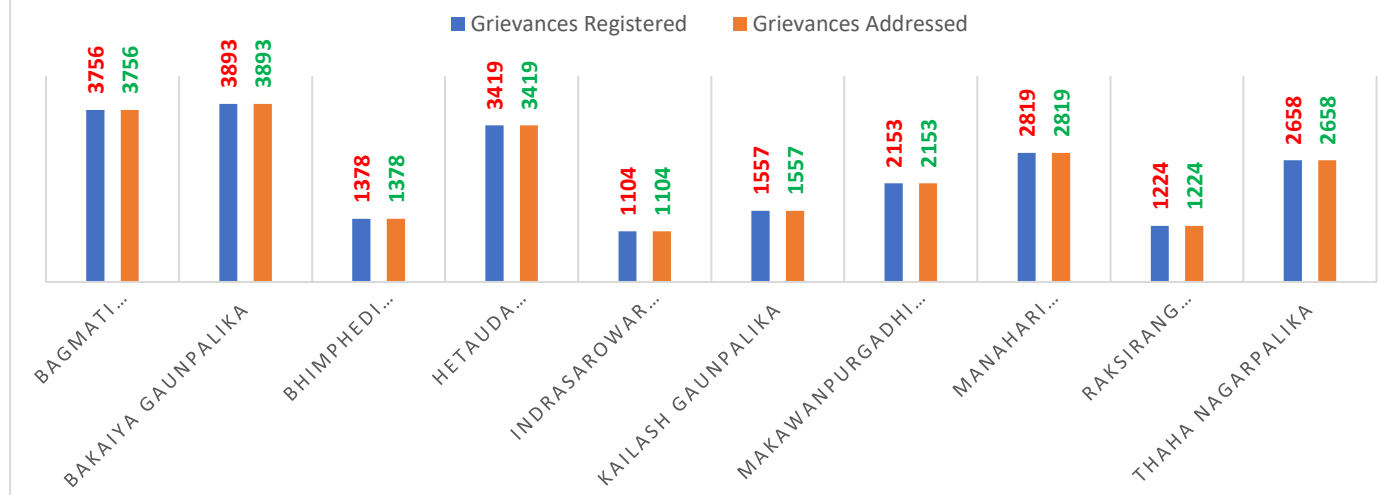

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
23 rd and 24 th Jan 2019	Raksirang Rural Municipality-06 & 07	Joint Monitoring Visit; DSE, local government, ward engineers, beneficiaries and HRRP team.

Objective(s)	- To organize technical coordination meeting and carry out field visit; to collect measure issues, housing typology. - Plan to prepare distribute the completion certificate for completed houses and promote to early final inspection and CS entry. - Monitoring to noncompliance issues and recommended for correction, if any.
---------------------	--

Raksirang is a one of the remote rural municipality of Makwanpur District. There are 4nos of previous VDCs lies on this rural municipality namely Raksirang, Kakda, Sarikhet and Khairang. We have organized technical coordination meeting and carried out field visits in ward no 6 and 7 of Raksirang rural municipality (Previous Kakda VDC). First of all, we have been conducted technical coordination meeting in ward no. 6. Also we had planned to visit in ward no. 07 but we faced obstacle like as earthen road blocked due to heavy rain and cancelled them.



Figure 1: During field visit, road blocked in way of ward nos. 6 and 7 of Raksirang Rural Municipality (Previous Kakda VDC) in date 2019-01-23.

The agendas of meeting in ward no 06 were as follows;

- Present scenarios of reconstruction, presented by ward engineer and ward president.
- Final inspection of completed houses, CS entry and plan to distribute the completion certificate.
- Non-compliance issues and retrofitting issues; if any in the ward.

We briefly discussed in agendas of current status of reconstruction, the following data has been found;

First tranche received HHs	Second tranche received HHs	Third tranche received HHs	Completed HHs	Remarks
715	713	467	650	Previous Kakda VDC

Decision Made of the meeting

- Almost houses have been completed but they don't receive the completion certificate and those houses necessary to final inspection and CS entry but it could not see during field visit. We strongly minute this agenda and decision made. For completed houses done final inspection, CS entry and distribution certificate for completed houses within the end of Chaitra, 2075.
- During visit, we recommended around 3 nos of houses for correction and it will eligible for third tranche. From meeting day, proper regular supervision of reconstruction for under construction houses and for correction.

Non-compliance issues and retrofitting issues

We faced retrofitting issues; it is vital and serious problem in field. Early it should be solve in field level. We don't have skilled manpower in field for retrofitting. So, quickly organize the OJT type training with including some technicians. For sample, in each rural municipality, it should be happen. From another way, we are far slow in final inspection and CS entry and we couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, in every visit, we delivered the message to technicians done for final inspection, CS entry and distribute the certificate but it couldn't happen rapidly.

During visit also we have collected the different types of construction housing typology. There were almost load bearing stone in mud mortar and in some places; near excess to road other types of materials used.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
- Retrofitting issues - CS entry and final inspection.	- Required OJT type of retrofitting training for masons with including some technicians in field level. For sample, in each rural municipality, it should be happen. - We couldn't distribute the completion certificate of completed houses; actually in field almost houses fulfilled by seismic requirements elements and met to compliance; also they have received all tranches of government grant. So finally, should do inspection, CS entry and distribute the completion certificate. - We strongly minute the agendas of CS entry, Final inspection and distribute the completion certificate for completed houses within Chaitra Masant.	NRA, Local government, Ward technicians	Regular

Photos



Figure 1: Technical coordination meeting has been organized in Raksirang Rural Municipality-06; the agendas were To organize technical coordination meeting and carry out field visit; to collect measure issues, housing typology. Plan to prepare distribute the completion certificate for completed houses and promote to early final inspection and CS entry. Monitoring to noncompliance issues and recommended for correction, if any and AoB.



Figure 2: Almost houses have been completed in Raksirang Rural Municipality -06 but they don't have received the completion certificate of completed houses. We still put this agenda in the ward meeting and made decision. Till the date; technicians don't start the final inspection and CS entry.

Housing Typology Report



Figure 3: Raksirang Rural Municipality-06, House owner; Sanch Lal Chepang. Load bearing stone in mud mortar with all seismic resistant components, two rooms and he plan to use light roof. He received second tranche and verified for third tranche.



Figure 4: House owner; Man Kumar Chepang, Raksirang Rural Municipality-06. Load bearing stone in mud mortar with RCC band. Provided all horizontal and vertical bands. He received all tranches of government grant. According to grant policy, if completed up to roof band level and make toilet, eligible for third tranche. He is planning to use heavy material in gable wall but it will become noncompliance. All most areas of rural municipality after received all tranches, house owner modified the structure themselves. It creates be problems for completion certificate distribution.



Figure 5: House owner; Dil Bahadur Chepang, Raksirang Rural Municipality-06. Stone in mud mortar with MRT and up ground floor he has used timber structure. In this house vertical reinforcement doesn't connect up to roof level. Also proper connection is not sufficient in truss (rafter, purlin). He used also heavy materials in roof with not proper connection with truss. He received all tranches of government grant.



Figure 6: House owner; Govind Praja, Raksirang Rural Municipality-06, load bearing stone in mud mortar with RCC band. It is a demonstration house during OJT type training of HELVATES Nepal. It had demonstration up to ground floor of roof band level and house owner has received all tranches of government reconstruction grant. But till now he has constructed up to first floor roof band. It is a non-compliant and it gives wrong message in the community. Our technicians faced problem in certificate distribution in some cases of this types of houses.



*Figure 7: House owner; Man Bahdur Thikng, Raksirang Rural Municipality-06. Load bearing hollow concrete block used, he provided all vertical and horizontal bands in necessary portions. Also he provided 12"*12" column size. He received second tranche and verified for third tranche.*



Figure 8: House owner; Kanxchi Maya Tamang, Raksirang Rural Municipality-06. Load bearing brick in cement mortar used. Two rooms with light CGI sheet. She received all tranches of government reconstruction grant.

Challenges and Way Forward

Challenge	Way Forward
- Retrofitting issues and noncompliance issues in self-constructed houses before deployed the technicians. - CS entry and final inspection.	- Required OJT type of retrofitting training for masons with including some technicians in field level. For sample, in each rural municipality, it should be happen. - Refer correction manual.
