


FACTS AND FIGURES

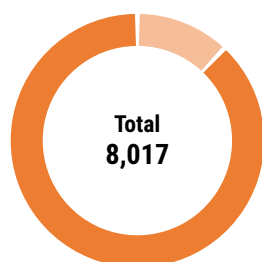

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	85.72%	85.43%
Brick and Cement Mortar Masonry	4.65%	3.73%
Adobe Structures	4.18%	3.32%
Reinforced Cement Concrete (RCC) Frame	2.75%	3.25%
Others	2.68%	4.26%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	6,780
PA Agreement	6,226
I st Tranche received	6,226
II nd Tranche received	5,325
III rd Tranche received	3,792

Houses

Under Construction: - Completed: 3,200

Retrofitting Status

Total Eligible HHs	255
PA Agreement	255
I st Tranche received	10
II nd Tranche received	245

Grievances

Registered: 1,310
Addressed: 341

Non-compliances

Registered: 275
Addressed: 160

Data Updated on: 2019-05-28 00:00:00

P0 Presence

Active: NSET (Shelter)

Phased Out: ADRA (Shelter), COSAN (Education), DCA (DRM), DCA (Hygiene), GON - DUDBC (Shelter), GON-PAF (Shelter), Nyayik (Agriculture), Nyayik (Education), Nyayik (GESI), RoomTR (Education), SCI (DRM), SCI (Education), SCI (Shelter), SCI (Social Protection), SCI (Hygiene)

OTHER SECTORS



Schools

Damaged: 63
Under Construction: 39
Construction Completed: 39



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	144,826	Y	1,200
Aggregate	m ³	134,554	Y	1,500
Sand	m ³	15,336	Y	2,100
Timber	cu. ft.	17,227	Y	706,300
Cement (PPC)	Sack	-	-	715
Cement (OPC)	Sack	449,943	-	795
Rebars	kgs.	1,593,460	Y	80
Tin	bundle	18,378	Y	-
Bricks	pcs.	2,738,207	Y	13

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,000 /-
700 /-

KEY CONTACTS

Municipal Office

Ram Kumar Acharya
Mayor
9851011682

Municipal Office

Radhakant Deo
Focal Person
9852821995

Municipal Office

Ambika Rupakheti
Deputy Mayor
9849567020

GMAI/NRA

Jaya Ram Shrestha
NRA Chief-District
9841265576

Municipal Office

Surya Prasad Upadhyaya
Administration Officer
9851204398

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
9855046584

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	8	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)

7 days Training




50 days Vocational Training



Source: HRRP Analysis

TA ACTIVITIES MAP

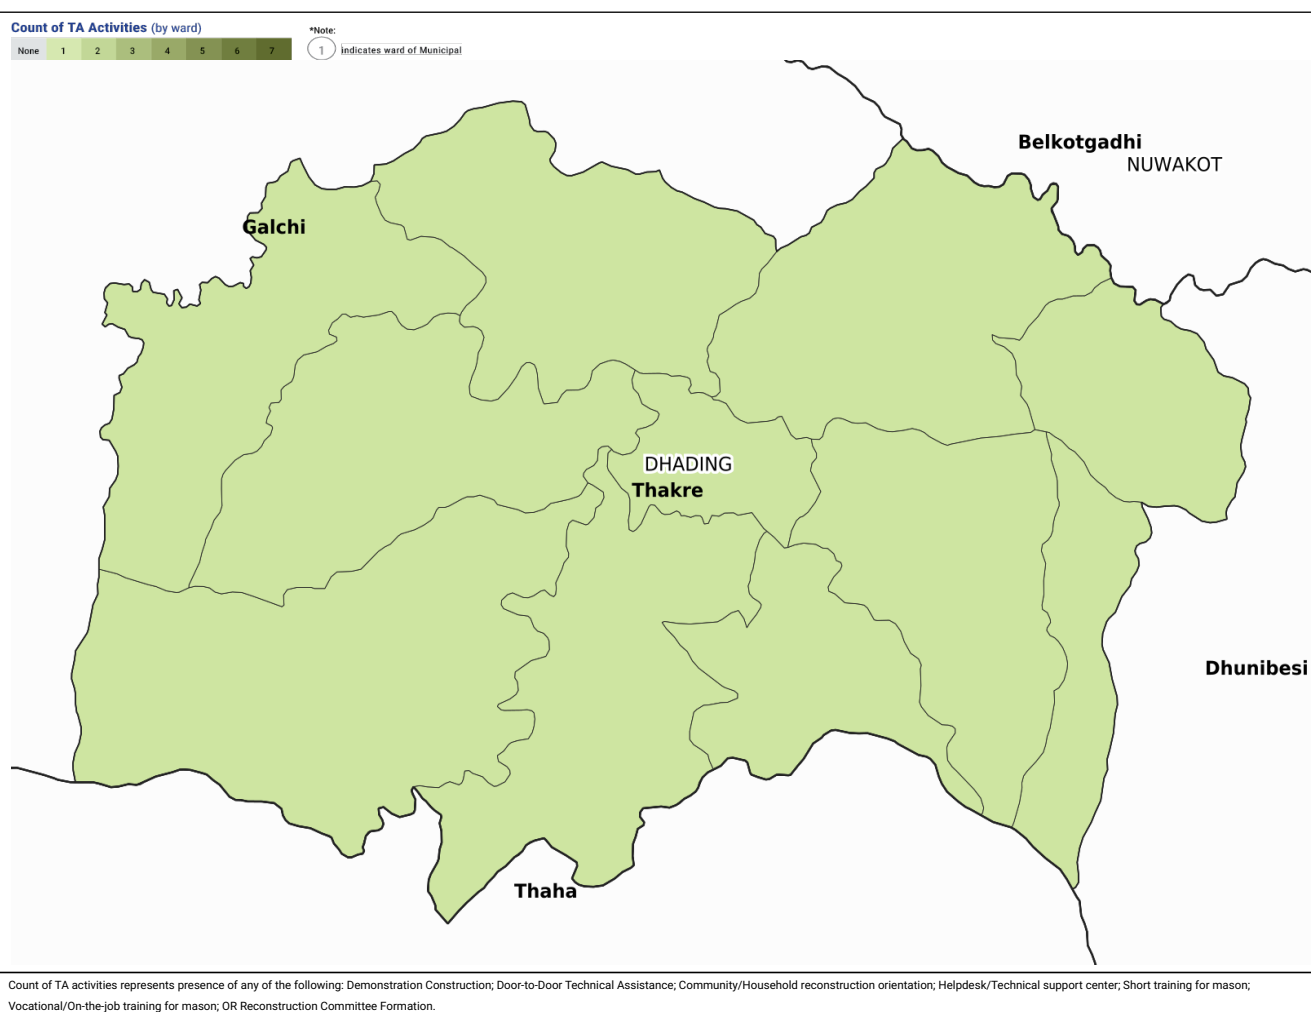

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Chandra Gurung (District Coordinator) 9841478742	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
