

District Report

Kavrepalanchok

4 – 17 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Field Visit to Boldefediche, Temal Gaupalika to assess the rock fall prone site	4 Jan 2019	4	1	reshma@hrrpnepal.org	Field Visit Section below
GMALI/HRRP Coordination Meeting	9 Jan 2019	2	2	reshma@hrrpnepal.org	Meeting Minutes
Palika Level Coordination Meeting, NamoBuddha Nagarpalika	9 Jan 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Field Visit to Devitar to research on reconstruction challenges	14 Jan 2019	-	-	reshma@hrrpnepal.org	Field Visit Section below
21 st Earthquake Safety Day Program	16 Jan 2019	-	-	reshma@hrrpnepal.org	News and Update section below
Data Collection and Updating Palika Profiles in Municipal websites	8-17 Jan 2019	-	-	im.kavrepalanchok@hrrpnepal.org	Municipal website (Dhulikhel, Namobuddha, Mahabharat)
Update on beneficiaries returning the first tranche	17 Jan 2019	-	-	im.kavrepalanchok@hrrpnepal.org	GD
Housing Typology Update	17 Jan 2019	-	-	reshma@hrrpnepal.org	GD
ToT to DUDBC/DLPIU engineer	7-13 Jan 2019	-	-	roshan_1369@yahoo.com	NA
Support to GMALI on grievance handling		-	-	reshma@hrrpnepal.org	NA

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Field Visit to Dhunkharka, Bethanchok GP to support the documentary preparation of Baliyo Ghar	21 Jan 2019, 8:00 AM-5:00 PM, Bethanchok GP	All Three Media House/Baliyo Ghar	reshma@hrrpnepal.org
Field Visit to Nagregagarche, Majhifeda and Sanowangthali to update on vulnerable settlement and monitor reconstruction activities	23-24 Jan 2019, 8:00 AM-5:00 PM, Chaurideurali GP	HRRP/GMALI	reshma@hrrpnepal.org
Field visit to Raviopi to research on reconstruction challenges in peri urban areas	29 Jan 2019, 8:00 AM- 4:00 PM, Dhulikhel NP	HRRP	reshma@hrrpnepal.org

News & Updates

The 21st Earthquake Safety Day was marked with a short rally and interaction program by District Administration Office at Dhulikhel, Kavrepalanchok on 16th January 2019. The program was attended by the representatives from DAO, DCC, DUDBC, GMALI, Nepal Police, Nepal Army, Nagarpalikas/Gaupalikas, Political parties, Press, Red Cross, FNCCI, DLSA and POs.

The rally started from Saraswati bazar at Dhulikhel with participants displaying placards on earthquake safety messages. The rally converted into a formal program at DCC Hall, chaired by the Chief District Officer Krishna Bahadur Raut. Short presentations from DUDBC and GMALI included brief introduction of earthquake history, national building code, preparedness drills and reconstruction progress. During the open floor discussion, participants raised the topics on: Norms of relief distribution, relief materials stockpiling, need of disaster awareness programs, involving youths and passa groups in disaster awareness, changing the focus from individual/specific hazard resilience to multi hazard resilience, moving beyond relief response to all phases of disaster management cycle, disaster acts and local structures, municipal disaster funds and implementation of NBC.

The CDO in his closing remarks expressed the positive hopes of improved disaster risk reduction in the district. He requested all the local structures who have the right to work under all four phases of disaster management cycle to plan and implement resilient programs along with implementation of national building codes in order to build a culture of safety whole across the district.



Participants at the rally




CDO, GMALI/DLPIU Chief and DUDBC Chief respectively addressing the formal program

Tranche Status


Municipality	Banepa	Bethanchok	Bhumlu	ChauriDeurali	Dhulikhel	KhaniKhola	Mahabharat	MandanDeupur	NamoBuddha	Panchkhal	Panauti	Roshi	Temal
Total HHs Surveyed	-	-	-	-	-	-	-	-	-	-	-	-	-
Total HHs Eligible	7070	4377	6203	6411	5968	2842	2950	9195	7593	9937	9178	6262	4847
Total HHs Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
1 st Tranche	6250	3724	5723	5176	4950	2726	2800	8407	6109	8766	7906	5425	4055
2 nd Tranche	2735	2526	4706	3677	2430	2128	2348	6370	2981	5743	4071	3695	2761
3 rd Tranche	2006	1262	3349	1523	1491	495	1188	3579	1520	3316	2573	1597	1493
Total HH Constructed	-	-	-	-	-	-	-	-	-	-	-	-	-
Grievance Registered	2226	1202	1038	1578	2151	683	1075	2300	2814	3041	2874	2257	2101
Grievance Addressed	2031	1202	971	1517	1919	681	1055	1762	2296	2932	2851	2203	2069
RF HH Eligible	-	-	-	-	-	-	-	-	-	-	-	-	-
RF HH Enrolled	-	-	-	-	-	-	-	-	-	-	-	-	-
RF 1 st Tranche	73	73	14	42	35	43	143	21	20	88	11	129	100
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	12	0	0	1
Non-Compliance Registered	-	-	-	-	-	-	-	-	-	-	-	-	-
Non-Compliance Addressed	-	-	-	-	-	-	-	-	-	-	-	-	-

Tranche Status

Reconstruction Tranche Status (17 Jan 2019)

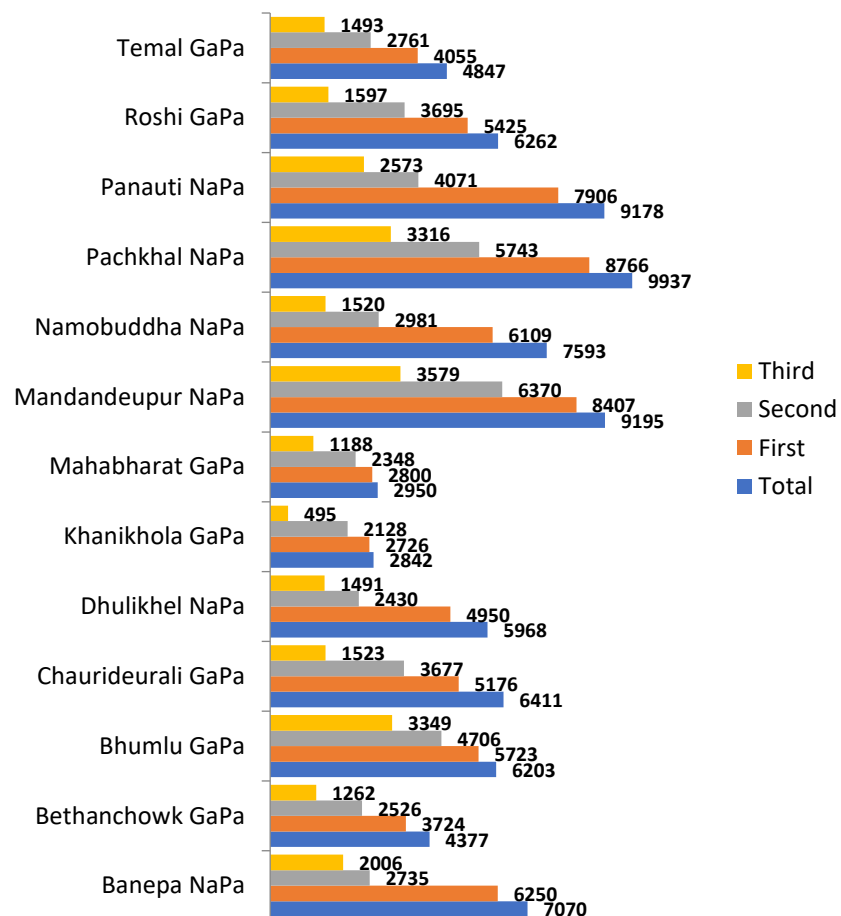

Grievance Addressal Status (17 Jan 2019)

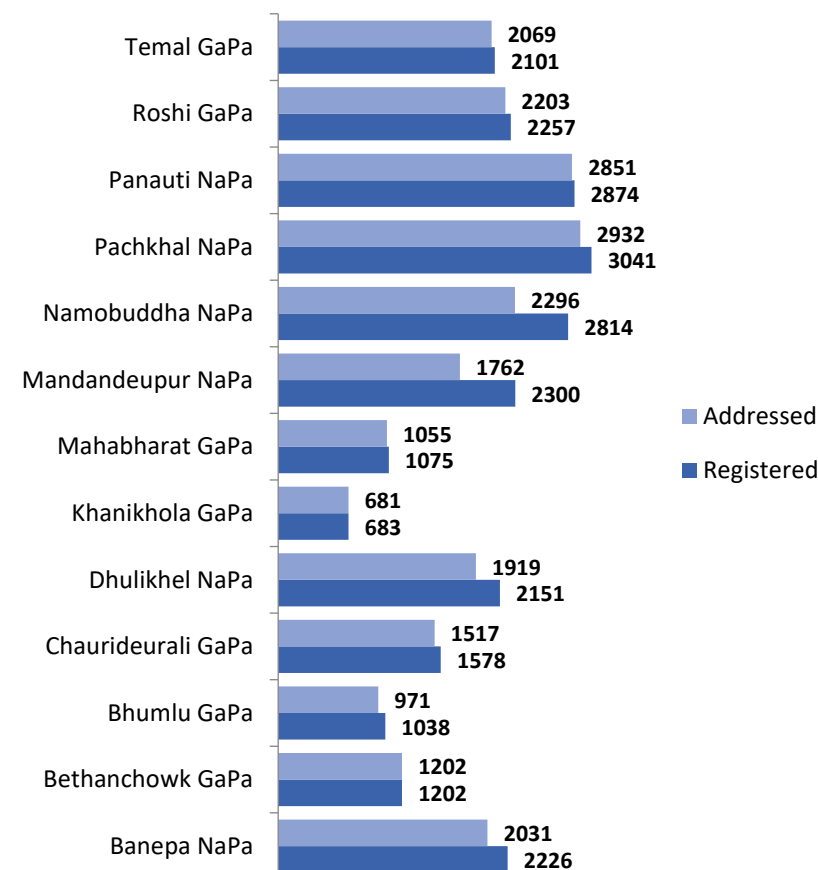

Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
4 Jan 2019	Temal Gaupalika	• Lok Nath Regmi, GMALI Kavre • Salam Singh, Temal Gaupalika Chief • Geologists from NRA • Reshma Shrestha, HRRP Kavre

Objective(s)	• Assess the vulnerability of rock-fall prone area and suggest appropriate mitigation measure.
--------------	--

Summary	Nangle Dhunga at BoldeFediche of Temal Gaupalika was listed vulnerable due to the 2015 earthquake and its aftershocks. The tremors resulted in disintegration of hard rock and large cracks to a depth of 1 meter. A team of monitoring geologists assessing the site declared the site not vulnerable but mitigation measures had to be adopted. As no mitigation measures were adopted, the residents downhill still feel the risk of probable rock-fall. The settlement sits 150 meters below the hill and 800 meters away from the toe of the hill. A total of 92 beneficiaries reside in the settlement. Though the earlier inspection results by the NRA team suggested constructions, the residents still were awaiting some mitigation measures to reduce the risks to move ahead with their reconstructions. As the deadlines for housing reconstruction tranche were nearing, about 80 people have constructed till the plinth level. They though have started construction have made multiple requests for final detailed assessment of the probable hazard. The monitoring team will prepare the detailed report. The preliminary investigation by the geologists suggested the settlement is not vulnerable from the probable rock fall. The rock as have the physical properties of disintegrating quickly will not pose high risk to the settlement but some mitigation measures around the rock site was suggested to reduce the risks to the people travelling nearby the hill.
----------------	---

Photos



The inspected hill posing the risk of rock fall.
Photograph By: Reshma Shrestha



The nearest settlement at the tsite oe of the risky hill. A total of 92 beneficiaries are settling in the area.
Photograph By: Reshma Shrestha

Field Visit Report

Visit 2

Date	Location	Participants from HRRP and stakeholders
14 Jan 2019	Devitar, Dhulikhel Nagarpalika	- Reshma Shrestha, HRRP Kavre - Ishor Neupane, HRRP Kavre
Objective(s)	Case research on reconstruction challenges of peri urban areas.	
Summary	Devitar, now Dhulikhel Municipality Ward 1, is one of the recent VDCs to be restructured into an urban municipality. There are a total of 712 beneficiaries in the ward. 682 have received first tranche, 271 have received second tranche and 144 have received third tranche of the housing reconstruction grant. Additional 22 files have been forwarded for second tranche and 34 for third tranche. The ward neighbored the oldest municipality of the district and hence has had influences of the urban construction market and technologies. Initially dominated by the stone in mud housing typology pre earthquake, the current reconstruction is dominated by Brick in Cement typology, a transition technology between the rural Stone in mud and the urban RCC. More than 60% of the new constructions are Brick in cement, 22 houses are RCC, 2 are Prefabs, 2 Interlocking blocks and the rest are Stone in mud. The shift to an urban municipality and easy access to urban markets has also shifted the mindset of people to desire and adopt urban materials for construction rather than reusing the pre dominant construction materials. This is one of the major reconstruction challenges in the ward. Beneficiaries have long paused their reconstruction to source finance for urban building materials and technology resulting in low reconstruction progress of the ward. Whilst access to urban materials is eased once finance is available, there still remains challenge in correct implementation of urban technology. A total of 20 RCC houses with 9 X 12 pillars constructed before the technical persons were mobilized were non-compliant. 18 of these houses recently received the third tranche after non-compliance addressal and signing the non-compliance consent form. The ward had the advantage of neighboring RaviOpi, the first VDC to be enrolled in the district. As soon as the enrolment process began, the immediate need was focused on mason training programs. Almost 60 masons have been trained through short and vocational trainings by SABAL and HELVETAS. The challenges that could have occurred due to incomplete knowledge of urban constructions were reduced by these mason trainings. The ward officials too reported that mason training is the most essential assistance to achieve compliance as the construction in the ward is majorly mason dependent. They also were strict in supervising the constructions through the NRA technical persons. Another advantage is the continuation of the staffs from VDC to new ward. The working process, data and records were easily transitioned to the new structure and the newly appointed Ward Chief had back support to proceed with the reconstruction process. Grievances are collectively taken at the ward level. Instead of referring individual cases to the district offices, the ward members themselves in turn visit the district offices fortnightly for grievance addressal. This transition also has its drawbacks. As a ward of an urban municipality, building permits were to be made mandatory. Despite the multiple requests from the municipality to strict on building permit system, the ward members in mutual consent have made the permits compulsory only for RCC structures. There is no record system for other construction typologies at current. The ward abided by this decision seeing the permit system as an added financial burden to the beneficiaries and not to discourage people for reconstruction. The mixed type of construction typologies in the peri urban areas creates complexities to reconstruction. Had it been rural area, the constructions would be the duplications of limited designs and had it been urban, the constructions would be RCC designed by the engineers. There are learnings from other municipalities like Panchkhal for the building permit system to provide some rights to ward level and there are also challenges associated with it. These are under consideration at the ward level.	

Photos



Purna Bahadur Lama of Devitar is reconstructing his RCC house to meet the Paush deadline. He just had his house inspected for the second tranche. About 20 houses in the ward are currently being constructed till the plinth level to meet the Paush deadline.

Photograph By: Reshma Shrestha



Indra Bahadur Tamang, a trained mason is reconstructing his house at Devitar. His house is the last one being constructed in his group of seven trained masons. All of them participated in the vocational training provided by SABAL. They took in turns to construct their own house within the group. He has applied for the inspection for the second tranche of housing reconstruction grant.

Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Temal-5

Building Typology: Stone in Mud

Description: Hari Man Tamang has received second tranche of housing reconstruction grant and his house has been inspected for the third tranche. Water was most difficult to avail for the construction which he bought at NPR 1.25 per liter from Bhakundebesi.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Temal-5

Building Typology: Stone in Mud

Description: Hem Bahadur Lama has received third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Temal-4

Building Typology: Stone in Mud

Description: Indra Lama has received third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Temal-4

Building Typology: Stone in Mud

Description: Kancha Lama has received second tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Dhulikhel-1

Building Typology: Stone in Mud

Description: Maili Tamang received the second tranche of housing reconstruction grant a year ago and is currently reconstructing her house. She demolished her pre earthquake house and is using the stones for her new house. She also produced raw bricks by herself which is being used for the inner walls as the stones from her demolished house were insufficient. She has estimated a total of NPR 7 lakhs including the finishing and furnishings.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Dhulikhel-1

Building Typology: RCC

Description: Lanam Dorje Lama received the third tranche of housing reconstruction grant in Asadh. The construction cost was NPR 17 lakhs.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Dhulikhel-1

Building Typology: Brick in Cement

Description: Karshang Lama has received the second tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha




Address: Kavrepalanchok, Dhulikhel-1

Building Typology: Brick in Cement

Description: Kanchi Maya Tamang has received the second tranche of housing reconstruction grant. She has plans to construct an attic with two way sloped roof.

Photographed By: Reshma Shrestha

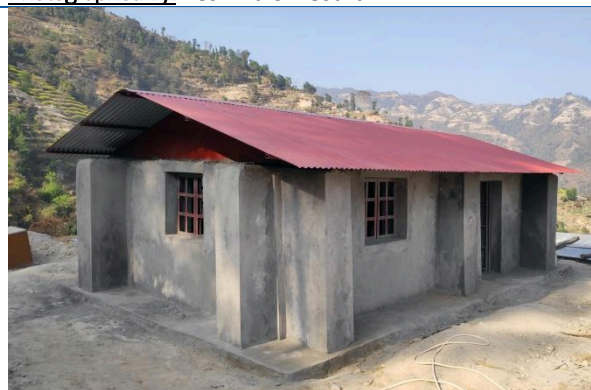


Address: Kavrepalanchok, Dhulikhel-1

Building Typology: Stone in Mud

Description: Ful Maya Tamang has received the third tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha




Address: Kavrepalanchok, Dhulikhel-2

Building Typology: Earth Bag

Description: Nabin Lama has received the first tranche of housing reconstruction grant. He has contracted his house for NPR 3 lakhs.

Photographed By: Reshma Shrestha



Case Study

Earth bag construction contractor in RaviOpi, Dhulikhel 2

Nabin Lama of RaviOpi, Dhulikhel 2 is constructing an Earth-bag house as per the design in Design Catalogue for alternative construction materials and technology. When an engineering firm, Kingdom Engineering Firm approached his ward office to gather interests in contracting for earth bag house, he immediately applied for the construction. A total of 90 pre-applications were received when the ward published the notice for earth-bag house construction.

The firm approached the ward to gather interest in earth bag constructions. The work modality was to construct the house in NPR 3 lakhs; the total sum of housing reconstruction grant and the beneficiaries need to pay the contractor/firm the sum as soon as they receive the tranche and this is the point where the ward has the major role. The ward needs to sign a guarantee that the beneficiaries pay the total NPR 3 lakhs to the firm in return of supporting the beneficiaries construct their houses as suggested by the ward.

When asked about the reason to come up with the plans to be a guarantor, the ward secretary replied that this was a much needed step, mostly to support the vulnerable beneficiaries. The deadlines are coming soon and there still are many beneficiaries yet to reconstruct, most of them needing support for labor and materials. As this technology used locally available material “Earth”, this could be easily promoted in the area. Whilst the contract is technically supervised by trained workmen from the firm, the construction too is time friendly; 12 days in average and the design is a complete copy of the approved DUDBC design so there are no risks of failing for the tranches if strict supervision from the ward too is done. The firm has contracted seven houses as on 14th Jan 2019 and this is the first one they are constructing. Approaching completion, this house as is the first one, will be completed in a total of NPRs 4 lakhs. The extra cost will be on the firm’s part and they are working on techniques to reduce the cost with no bargain on the quality side. They are yet to work on modalities where some of the materials are assisted by the home owner; some can use their pre available CGI sheets or doors/windows. The contract covers the cost of the whole foundation and superstructure construction with construction materials, white CGI roofing, doors/ windows, plastering, three coats of painting and labor cost. The extra cost of using colored CGI sheets instead of white sheets, false ceiling and extra finishing needs to be borne by the owner. The firm also essentially checks the date of PA Form prior contract to ensure the deadlines can be met and beneficiaries are eligible to apply for the tranches. Earth-bag houses though are their first attempt; they have earlier worked under same modality with interlocking blocks at Godamchaur, Lalitpur.



Back Isometric View



Interior View
