


FACTS AND FIGURES

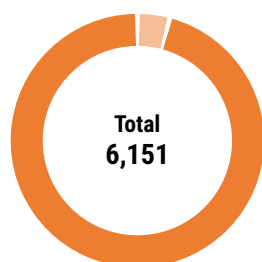

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	97.04%	69.19%
Brick and Cement Mortar Masonry	1.27%	5.98%
Reinforced Cement Concrete (RCC) Frame	1.01%	4.65%
Adobe Structures	0.42%	15.32%
Others	0.27%	4.86%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	6,208
PA Agreement	5,845
I st Tranche received	5,864
II nd Tranche received	5,038
III rd Tranche received	4,110

Houses

Under Construction: -

Completed: -

Retrofitting Status

Total Eligible HHs	89
PA Agreement	14
I st Tranche received	17
II nd Tranche received	1

Grievances

Registered: 1,038

Addressed: 971

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-15 00:00:00

P0 Presence

Active: EcoH-N (Health), EcoH-N (Social Protection)

Phased Out: AA (DRM), AA (Education), AA (Livelihood), AA (GESI), EcoH-N (Education), Garuda-N (Education), Garuda-N (Hygiene), HELVETAS (Shelter), HI (DRM), HI (Livelihood), HI (Nutrition), HI (Shelter), HI (Hygiene), LWF (Agriculture), LWF (Livelihood), LWF (Hygiene), NN (Shelter), NRCS (Agriculture), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), SABAL (Shelter), Tdh (Health)

OTHER SECTORS



Schools

Damaged: 44
Under Construction: 16
Construction Completed: 16



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	98,363	Y	3,000
Aggregate	m ³	97,349	N	5,000
Sand	m ³	10,473	N	5,000
Timber	cu. ft.	11,973	-	-
Cement (PPC)	Sack	-	N	1,000
Cement (OPC)	Sack	325,118	N	1,100
Rebars	kgs.	1,074,268	N	100
Tin	bundle	13,294	-	-
Bricks	pcs.	1,535,500	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,200 /-
1,000 /-

KEY CONTACTS

Municipal Office

Guman Dhoj Kunwar
Mayor
9851084808

Municipal Office

Amrita Khanal
Focal Person
9843574073

Municipal Office

Kalpana Shrestha
Deputy Mayor
9841648772

GMA/NI/NRA

Lok Nath Regmi
NRA Chief-District
9851146403

Municipal Office

Hari Ballav Ghimire
Administration Officer
9841831427

DLPIU-Building

Mahalaxmi Joshi
DUDBC.DLPIU Chief
9751090249

HHs WITH LAND ISSUES



STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)

7 days Training




50 days Vocational Training



Source: HRRP Analysis

TA ACTIVITIES MAP

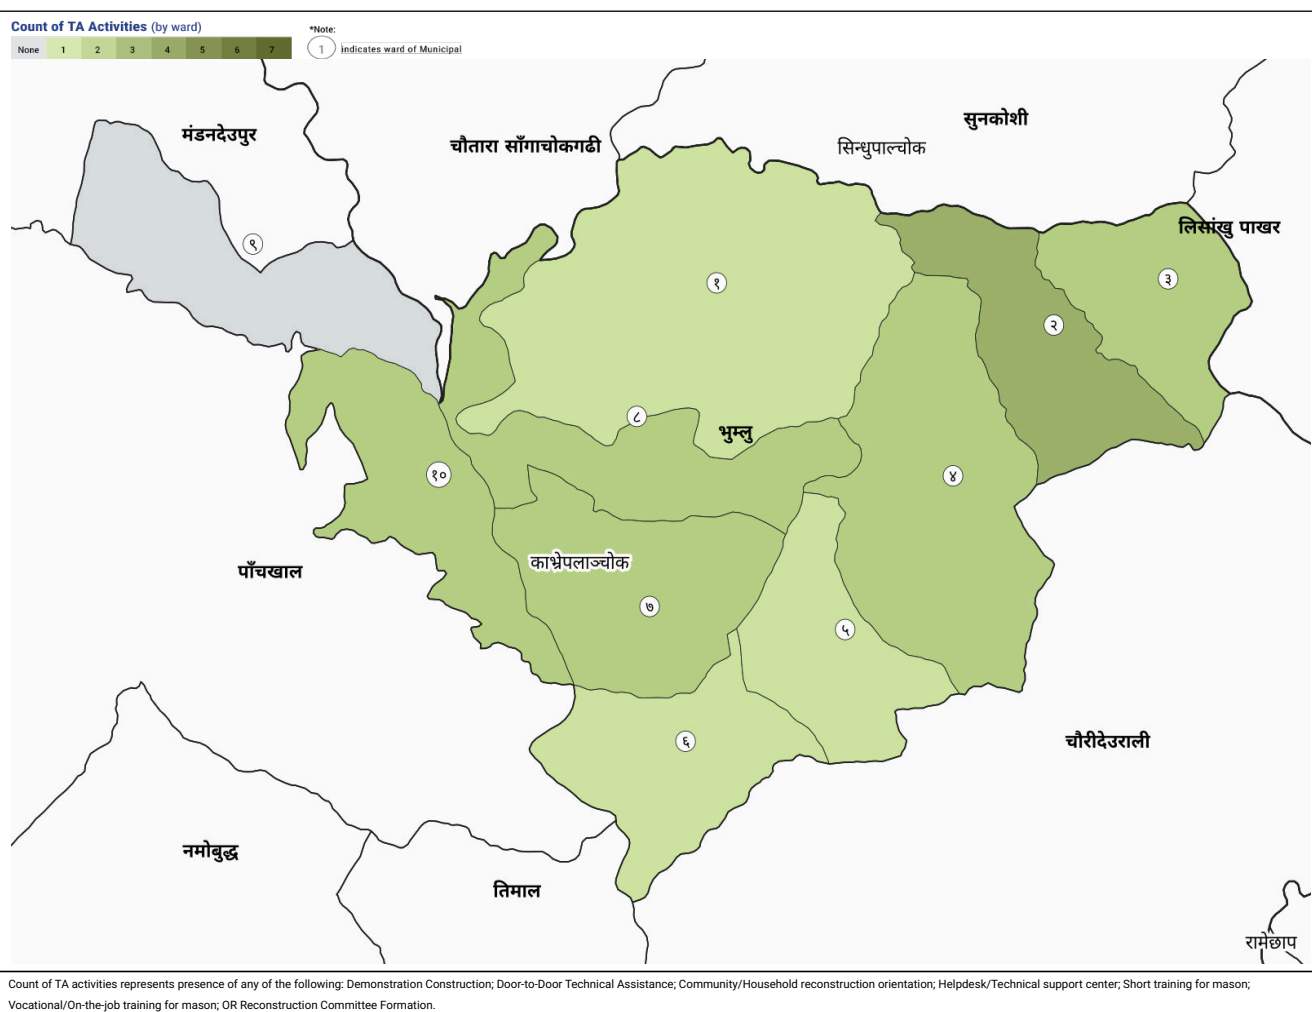

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Reshma Shrestha (District Coordinator) 2. (District Technical Officer) 3. Ishor Neupane (District Information Management Officer)
9841264190 9801317265
