

Monthly District Report

Lamjung, Tanahun, Kaski, Syangja

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lamjung	Joint monitoring field visit is conducted at Beshisahar NP ward number 6. HRRP together with district support engineer Mr.Umesh Dangol, GMaLI representative Mr. Binayak Dawadi, palika engineer Mr.Anoja Chilwal and Mr.Durga Lal Shrestha carried monitoring visit on this ward. Visit team conducted ward level meeting at ward office and also monitor few non-compliance and completed houses at field level.	12-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District Facilitation coordination committee meeting for the month of Kartike is completed. Meeting was chaired by district coordination committee chief Mr. Loke Raj Pandey and officers from different related government agency, focal engineers of all palika participated the meeting. District level reconstruction issues were presented by GMaLI chief and more importantly focal engineers raised burning reconstruction issues of their respective palka on that form. DFCC made few decision to addressing the issues of district.	8-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	HRRP team conducted ward level meeting at Beshisahar NP ward number 6. Meeting was chaired by ward president Mr. Bhoj Bahadur Rimal in the presences of palika level technical person, DSE, HRRP and other staffs of ward office. Ward level reconstruction issues were discuss during meeting also way forward and	12-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	solution was provided to technical staff. Reconstruction related info-pack, recent meeting decision of central NRA and district level DFCC meeting were handover and also brief to ward president.				
	Coordination meeting with DLPIUs GmaLI and Building is conducted at GMaLI office in presence of DSE and HRRP team. Meeting was mainly focused on the discussion of tranche related issues and to make tranche information uniform between two offices. Meeting gave responsibility to both DLPIU's computer operator to make this process more effective and made HRRP district coordinator Mr.Rijan Gajurel as a advisor of both operators.	3-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika level tranche information for this round is updated in palika profile template.	10-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District level contact list is updated for this round. Few contact details of government officers were added in this round.	15-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Tanahau	Palika level tranche information for this round is updated in palika profile template.	10-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District level contact list is updated for this round.	15-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Kaski	Joint monitoring field visit is conducted at Rupa kot rural municipality ward number 4 and 5. HRRP team together with district support engineer Mr. Ganesh Bahadur Thapa, palika level technical person Mr. Pukar Regmi, Subash Dawadi, Nand Laal Ray-Asst Sub Engineer-DLPIU Building .	14-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	Monitoring visit team conducted ward level meeting at ward number 4 and monitor few non-compliance and retrofitting listed beneficiary houses and provided proper suggestion and feedback to individual HHs.				
	Joint monitoring field visit is conducted at Anapurna rural municipality ward number 1. HRRP team together with district support engineer Mr. Ganesh Bahadur Thapa, palika level engineer Rajan Gautam, Kishor Yadav, Hemanta Pradhan conducted visit at ward level. Ward level coordination meeting at ward number 1 is carried out and field monitoring of few non-compliance and retrofit listed houses were done during this visit.	15-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika level tranche information for this round is updated in palika profile template.	10-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District level contact list is updated for this round.	15-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Ward level meeting is conducted at Rupakot rural municipality ward number 4. Current raising reconstruction issues were discuss during meeting, some good practices carried out in other places were also shared. HRRP team shared different information product and central and district level meeting decision with ward representative.	14-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Syangja	Joint monitoring field visit is conducted at Putalibazar Nagarpalika ward number 7. This visit is mainly focused to collect retrofitting beneficiary houses status information and to interact directly with individual households . Out of 44 retrofit enlisted HHs 30	19-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	were presented at interaction program organized at ward office. Also, ward level meeting is conducted in the chairmanship of ward chairperson-Biseshwor Prasad Regmi. The interaction program mainly focused on listing the technical feasibility, Housing typology, interest of house owner on retrofit (if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU-Technicals, DSE and HRRP Team.				
	Joint monitoring field visit is conducted at Putalibazar Nagarpalika ward number 13. This visit is mainly focused to collect retrofitting beneficiary houses status information and to interact directly with individual households. Also, ward level meeting is conducted in the chairmanship of ward chairperson-Biseshwor Prasad Regmi. The interaction program mainly focused on listing the technical feasibility, Housing typology, interest of house owner on retrofit (if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU-Technicals, DSE and HRRP Team.	20-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Joint monitoring field visit is conducted at Galyang Municipality ward number 13. This visit is mainly focused to collect retrofitting beneficiary houses status information and to interact directly with individual households. Also, ward level meeting is conducted in the chairmanship of ward chairperson-Natra Parsad Pandey. The interaction program mainly focused on listing the technical feasibility, Housing typology, interest of house owner on retrofit (if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU-Technicals, DSE and HRRP Team.	21-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika level tranche information for this round is updated in palika profile template.	10-Nov		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District level contact list is updated for this round.	15-Nov		Rijan.gajurel@hrrpnepal.org	

Summary of events during this period


				Biren.shah@hrrpnepal.org	
--	--	--	--	--	--

Tranche Status (Lamjung)


Tranche Status Table: 25-Nov ,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Besishahar Nagarpalika	2851	1308	1257	1259	1815	452	11	6	6	0
Dordi Gaunpalika	3375	2238	2206	2206	373	278	25	3	3	0
Dudhpokhari Gaunpalika	2667	2437	2361	2367	109	65	6	4	4	0
Kwholasothar Gaunpalika	740	314	271	272	869	300	72	0	0	0
MadhyaNepal Nagarpalika	2346	1505	1448	1449	671	466	54	0	0	0
Marsyangdi Gaunpalika	1936	911	877	880	1359	849	176	158	158	0
Rainas Nagarpalika	4362	2989	2947	2951	2079	825	105	99	99	0
Sundarbazar Nagarpalika	4084	2257	2157	2158	708	220	90	19	19	0

Graph of Tranche Status:

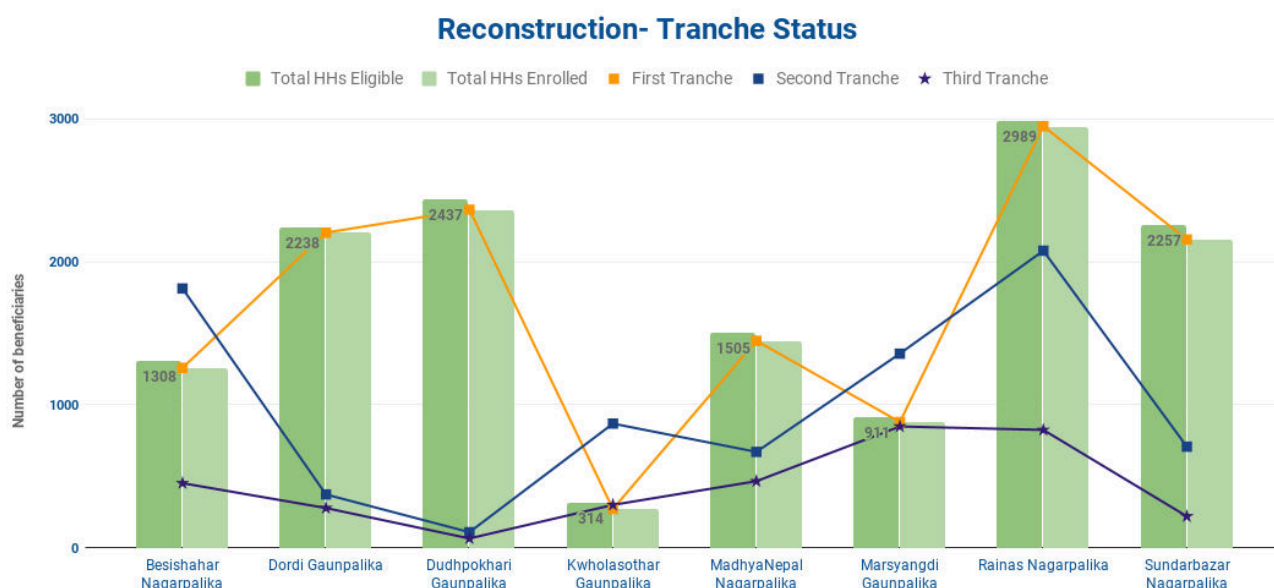

Graph for Retrofitting Status:

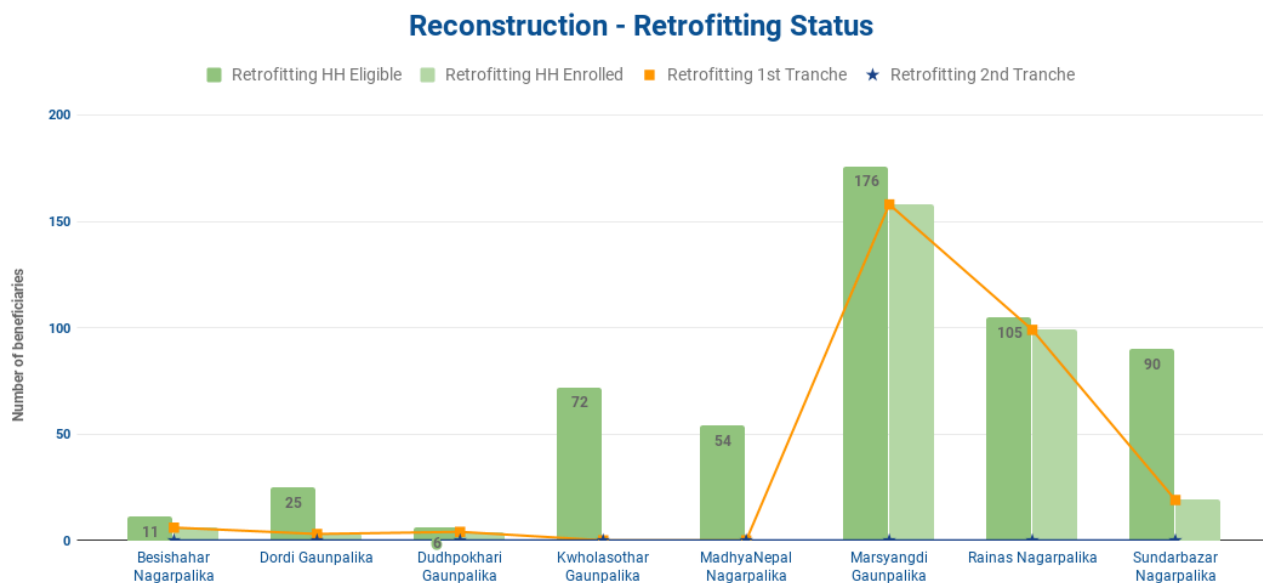


Tranche Status (Tanahau)


Tranche Status Table: November

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Anbukhaireni Gaunpalika	1050	710	705	705	477	400	21	5	5	0
Bandipur Gaunpalika	1226	609	1055	590	298	234	33	32	32	0
Bhanu Nagarpalika	7540	4219	4147	4198	2433	1579	75	12	12	0
Bhimad Nagarpalika	2680	987	974	975	512	190	46	0	0	0
Byas Nagarpalika	4626	2486	1981	2401	1439	988	163	180	180	0
Devghat Gaunpalika	960	725	499	499	328	127	32	8	8	0
Ghiring Gaunpalika	969	254	232	232	120	80	0	0	0	0
Myagde Gaunpalika	1877	1292	1065	1066	653	417	38	33	33	0
Rhishing Gaunpalika	1771	680	473	473	283	170	34	0	0	0
Shuklagandaki Nagarpalika	2837	1859	1740	1742	981	519	24	1	1	0

Graph of Tranche Status:

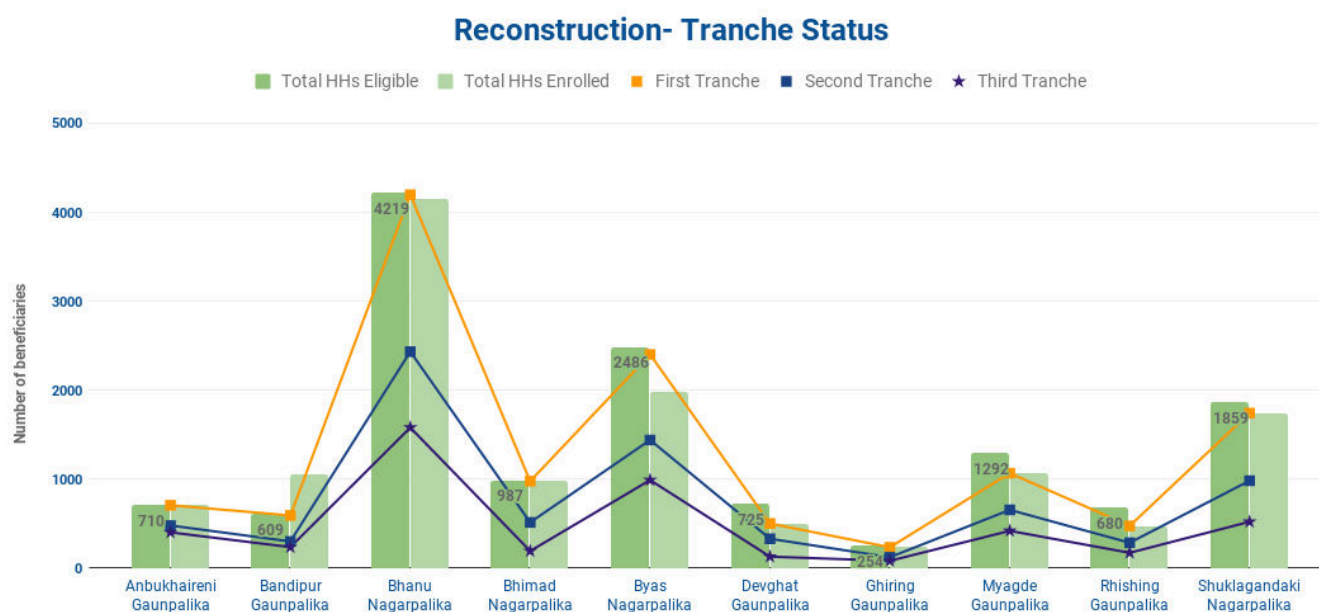

Graph for Retrofitting Status:

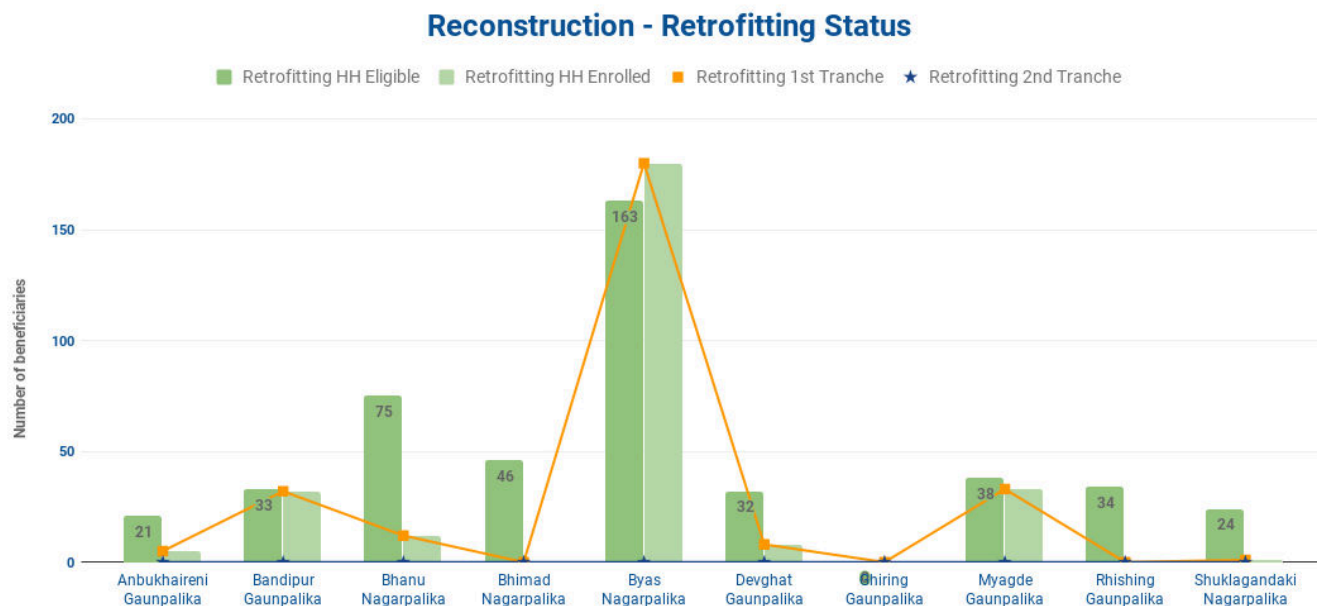


Tranche Status (Kaski)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Annapurna Gaunpalika	667	395	395	395	179	74	19	12	12	0
Machhapuchchhre Gaunpalika	781	427	427	427	265	34	30	5	5	0
Madi Gaunpalika	2296	1160	1160	1160	512	97	40	12	12	0
Pokhara Lekhnath Mahanagarpalika	5276	2774	2421	2421	1153	281	111	84	84	0
Rupa Gaunpalika	2054	1270	1222	1222	455	238	42	26	26	0


Graph of Tranche Status:

Reconstruction- Tranche Status

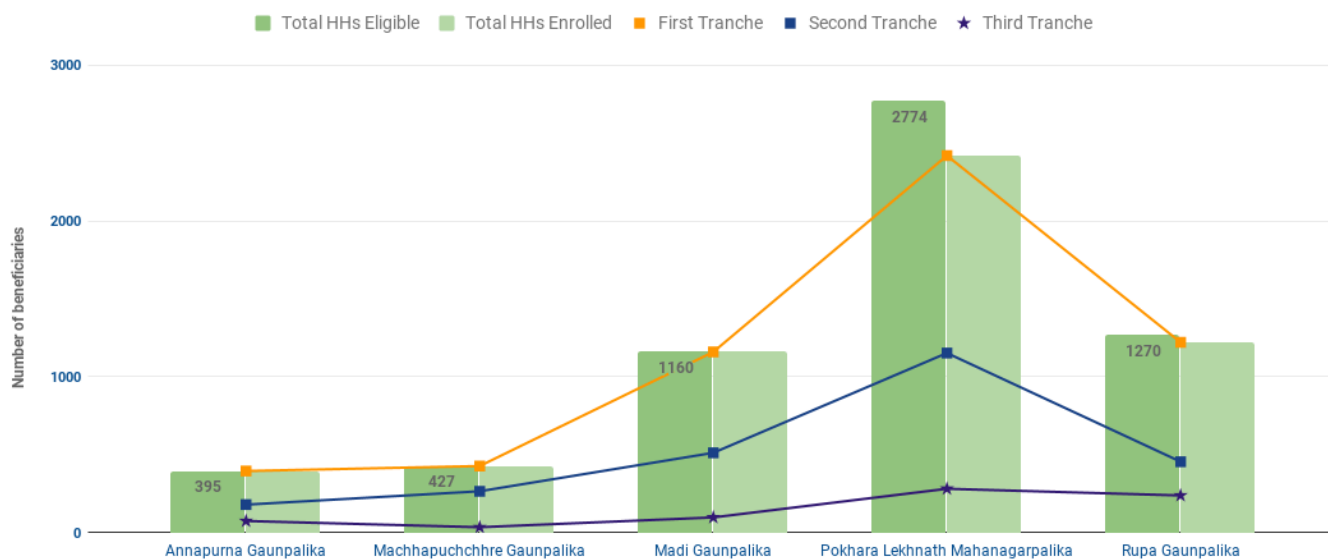

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

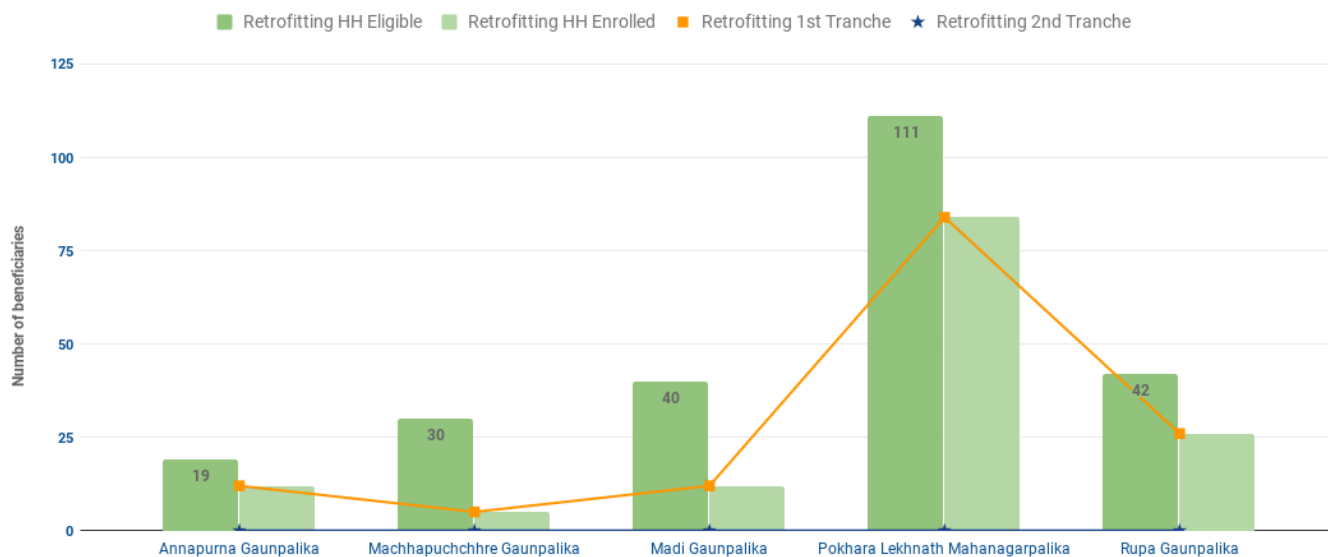


Tranche Status (Syangja)

Tranche Status Table: November


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Aandhikhola Gaunpalika	1515	843	825	825	391	194	72	57	57	0
Arjunchaupari Gaunpalika	803	509	476	476	257	208	64	50	50	0
Bhirkot Nagarpalika	2099	1042	1002	1002	324	159	26	21	21	0
Biruwa Gaunpalika	1024	638	621	621	212	145	40	22	22	0
Chapakot Nagarpalika	1815	804	798	798	435	281	12	4	4	0
Galyang Nagarpalika	1294	634	621	621	327	267	101	99	99	0
Harinas Gaunpalika	912	435	406	406	189	125	1	1	1	0
Kaligandagi Gaunpalika	752	493	415	415	161	126	2	2	2	0
Phedikhola Gaunpalika	403	278	265	265	125	103	10	9	9	0
Putalibazar Nagarpalika	2798	1471	1461	1461	768	578	325	310	310	5
Waling Nagarpalika	2696	1671	1621	1621	801	417	54	35	35	0

Graph of Tranche Status:

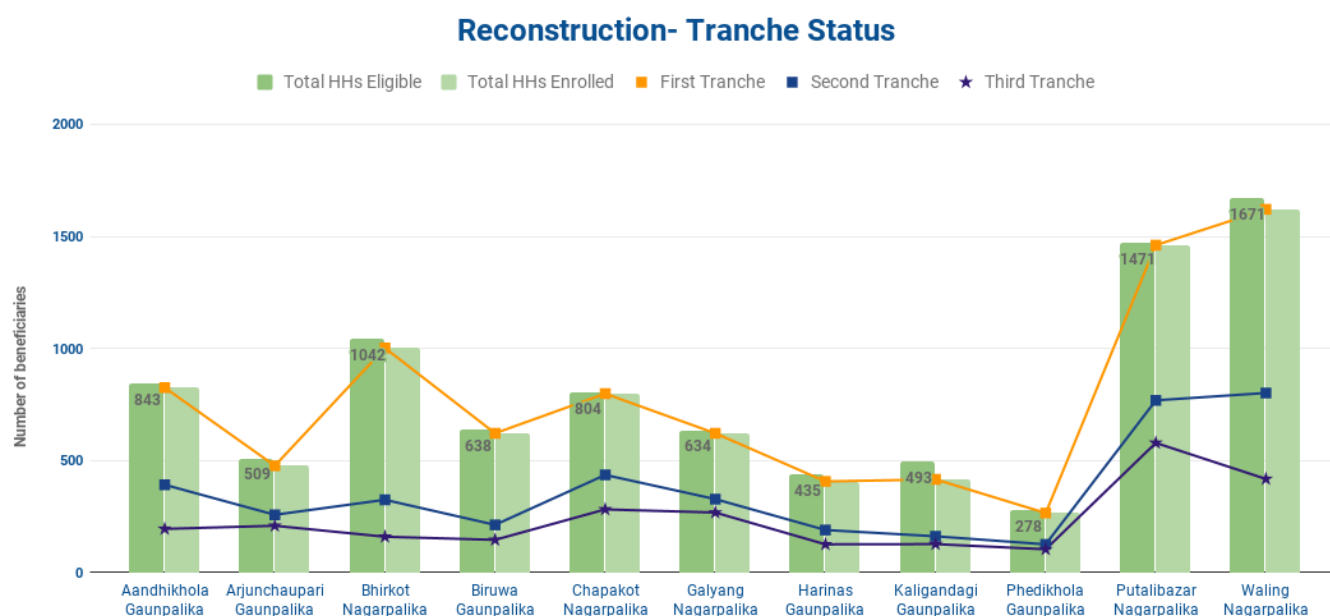

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

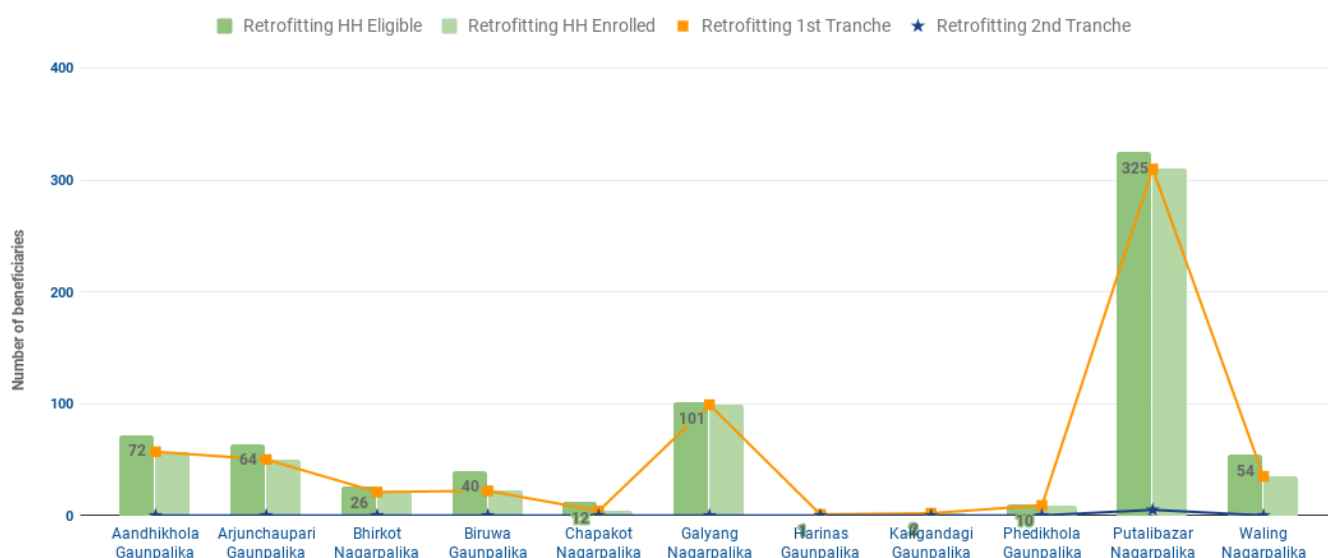

Field Visit Reports (Lamjung)

Visit 1

Date	Location	Participants
12-Nov,2019	Ward no-6, Besisahar Municipality, Lamjung	Biren Shah-HRRP Rijan Gajurel-HRRP Umesh Dangol-DSE, NRA Anoj Chiluwal-Engineer,DLPIU-Building Durga Lal Shrestha-Sub-Engineer-DLPIU Building
Objective(s)	• Ward level coordination meeting • To address the non-compliant issues of the ward • To collect Housing Typology • Interaction with retrofitting Beneficiaries	
Why was the visit carried out in this location? Priority wise, Write any other reason		
The progress of the retrofitting beneficiaries were stagnant due to the lack of knowledge and information regarding retrofit techniques , methods and cost.So, interaction with the beneficiaries who were enlisted in the list was conducted.Some of the non-compliant houses were not forwarded for the third tranche so inorder to address thoses cases , the field visit was carried out.		
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.		
Previous Issues		Current Issues

Summary				
Field Visit: The field visit was conducted jointly by DLPIU-Building, DLPIU-GMali and HRRP Team. During the field visit ward level meeting was conducted in the chairmanship of ward chairperson Mr. Bhojraj Regmi. Majorly Load Bearing Stone Masonary in Mud mortar houses were found in the ward. Major issues and challenges were discussed during the visit and the way forward was also discussed. Meeting with ward chief ward no-6, Besisahar Municipality, Lamjung The ward np-6 has 78 beneficiaries under reconstruction of which 78 has received the first tranche, 32 has received the second tranche and 24 has received the third tranche. Majority of the houses are load bearing stone masonry in mud mortar. Non-compliance cases like absence of gable band , 4" partition wall in masonry houses are seen. The non-compliance were majorly seen as the Nagarpalika has passed the 4" partition wall of masonry house in drawing but was not forwarded for the tranche from the DLPIU-Building. - No. of HHs visited:5 - No. of meetings/interaction with engineers:1 - No. of engineers interacted with:3 - No. of meetings/interaction with local officials:1 - No. of local officials interacted with: 1				
Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
4" partition wall in Masonary houses resulting in non-compliant housing	Replace the wall with 9" wall or provide buttress wall	The technical are requested to provide the technical assistance as for the given solutions.	DLPIU-Building	ASAP
Lack of gable band in the houses.	Addition of Gable band	The technical are requested to provide the technical assistance as for the given solutions.	DLPIU-Building	ASAP
Advantages of retrofitting processes have not been sufficiently reached to beneficiaries' level (ground level).	There is need of adequate orientation and information dissemination on retrofitting process among beneficiaries and in communities as a whole.	Retrofitting task force by DLPIU Building office have targeted orientation and site visits for disseminating key messages of retrofitting procedures.	DLPIU-Building	ASAP

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

Issues regarding Retrofit:

The beneficiaries have already received the first tranche and due to lack of information, technical assistance and vulnerability of the house, they have repaired their houses in their own way in the form of plaster, etc. The amount of first tranche has been spent in the repair and now after the dissemination of knowledge of retrofit they lack financial support as they must start the retrofit process on their own expense. Due to this reason the beneficiaries are repelling to retrofit their houses. Some of the beneficiaries under retrofit have demolished their houses completely and have reconstructed new house and want to get changed from RTR to RCB.



Caption: Retrofitting beneficiary who has already repaired his house after getting the first tranche and financially has no support to further retrofit

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

- Lack of awareness and knowledge in the vulnerable regarding tranche release process.
- Received the first tranche but haven't started the reconstruction.

Ward number-1 , Rainas Municipality, Lamjung

Rajbir Gurung – a differently able beneficiary who lost both of his hands and partially damaged eye. His house was damaged in the 2072 earthquake and had been living in that house even after earthquake as he was not able to reconstruct new house. Due to his poor economic condition, and his poor physical condition, he was not been able to demolish his damaged house and start reconstruction. Thereafter he had been enlisted in the vulnerable list supported with top-up of additional 50,000 Rs by COPADEX. Recently, 8/9 months ago he had signed the agreement and received the first tranche and now demolished the old earthquake affected house and is looking forward for the vulnerable top-up support to start the reconstruction process.



Photos



Field Visit Reports (Kaski)

Visit 1

Date		Location	Participants
14-November, 2019		Ward no-4 and ward no-5, Rupa kot Rural Municipality	• Biren Shah-HRRP • Rijan Gajurel-HRRP • Ganesh Thapa-DSE, NRA • Pukar Regmi-Engineer,DLPIU-Building • Subash Dawadi-Engineer-DLPIU Building • Nand Laal Ray-Asst Sub Engineer-DLPIU Building
Objective(s)	• To observe the status of house under retrofit. • To interact with beneficiaries to understand the reconstruction/retrofitting issues and status. • To address the non-compliant issues		
Why was the visit carried out in this location? Priority wise, Write any other reason			
The houses under retrofit have no progress and also due to the deadline of the second tranche within kartik month the beneficiaries are haphazardly constructing the house resulting in non-compliance. So to address these issues the field visit was carried out.			
If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.			
Previous Issues		Current Issues	
Summary			

Field Visit:

HRRP Kaski Team along the newly formed Retrofitting task force comprising of DSEs and Engineers (DLPIU Building) and technical staffs of Rupakot RM Kaski district. The field visit was mainly focused on the observation of the current status of the houses under retrofit and convincing the beneficiaries for retrofit. During the visit, it was found that the houses were repaired rather than retrofitted. In total 6 houses were visited of both retrofit and reconstruction. One house was case of repair, one house has added 1 section in all the columns, and one house had jacketing of the column. One of the repaired houses by plastering in the walls. One house under-going reconstruction for Tie beam. As only two days were left for the recommendation and inspection for second tranche the tie-beam was constructed in rush and in lack of trained masons as a result it was non-compliant. The rebar of beam was running outside the column in beam-column joint section and the spacing of stirrups was not according to the minimum requirement.



- No. of HHs visited: 6
- No. of meetings/interaction with engineers: 1
- No. of engineers interacted with: 3
- No. of meetings/interaction with local officials: 1
- No. of local officials interacted with: 1

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Beneficiary had misconception of repair being considered as retrofit. The repaired house was found to be vulnerable.	The beneficiary was explained about the technical steps regarding retrofitting and how the structure would still be vulnerable with just few repairs.	Technical support to the beneficiaries regarding retrofitting	DLPIU-Building	ASAP
Lack of trained masons for retrofitting process	Mason training regarding retrofitting	Not yet	NRA, CLPIU-Building	ASAP
Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)				
Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)				
Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)				
Photos				



Ward no-4, Rupakot Municipality, Kaski
The beneficiary is enlisted under retrofit and have plastered the house and is currently living.
Housing Typology: Two Storey load bearing stone masonry in mud mortar.



Ward no-4, Rupakot Municipality, Kaski
The beneficiary has received the third tranche.
Housing Typology: Load Bearing Brick Masonry in cement mortar.

Field Visit Reports (kaski2)

Visit 1

Visit 1		
Date	Location	Participants
15-Nov, 2019	Ward no-1 and ward no-2, Annapurna Rural Municipality	• Biren Shah-HRRP • Rijan Gajurel-HRRP • Ganesh Thapa-DSE, NRA • Rajan Gautam-Engineer,DLPIU-Building • Kishor Yadav-Sub Er-DLPIU-Building • Hemanta Pradhan-Asst.Sub Er-DLPIU-building
Objective(s)	• To observe the retrofitted model house. • To interact with the beneficiaries under retrofit • To suggest corrections to the non-compliant houses.	
Why was the visit carried out in this location? Priority wise, Write any other reason		
To observe the retrofitted model house done by built change. During the first three day of the retrofitting process the technical of DLPIU along with DSE were involved but after that no any coordination was done. So, in order to observe the progress, technical aspects and beneficiary views the field visit was conducted.		
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.		
Previous Issues		Current Issues
Summary		

Field Visit:

- No. of HHs visited:1
- No. of meetings/interaction with engineers:1
- No. of engineers interacted with:4
- No. of meetings/interaction with local officials:1
- No. of local officials interacted with: 1

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Low interest in beneficiaries for retrofit.	Orientation, interaction and awareness program regarding simplified methodologies of retrofitting along with cost estimate sharing.	Interaction program with beneficiaries completed	DLPIU-Building	ASAP
Lack of masons to implement the retrofitting.	Retro-specified mason training.	Not yet	CLPIU-Building, DLPIU-Building	ASAP
New houses constructed attached with the old earthquake damaged house.	Dismantling the old house or retrofitting and making those earthquakes resilient.	Not yet	NRA, CLPIU-GMaLI, Palikas	ASAP

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

During the field visit one model house under retrofit was inspected by the Task-Force Kaski team at Annapurna RM. The model was load bearing stone masonry in mud mortar house. New houses constructed attached with the old earthquake damaged house. Proper monitoring on dismantling the old house or retrofitting and making those earthquakes resilient should be done.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

Photos



Ward No-2, Annapurna RM, Kaski Retrofit model house by Built Change
The beneficiary has received the first tranche of GON retrofitting grant.



Ward no-1, Annapurna RM, Kaski
New houses constructed attached with the old earthquake damaged house.

Field Visit Reports (Syangja 1)

Visit 1

Visit 1		
Date	Location	Participants
19-Nov,2019	Ward no-7 , Putalibazar Municipality , Syangja	Biren Shah-HRRP Rijan Gajurel – HRRP Nawaraj Sharma-DSE , NRA Samikshya Poudel-Focal Engineer-DLPIU-Building Dil Sagar-Sub Asst Er-DLPIU-Building
Objective(s)	• Interaction program with beneficiaries enlisted in retrofitting • Ward level meeting • The interaction program mainly focused on listing the technical feasibility ,Housing typology, interest of house owner on retrofit(if not then the reason why the beneficiary doesnot want to go for retrofit) in the presence of DLPIU-Technicals, DSE and HRRP Team.	
Why was the visit carried out in this location? Priority wise, Write any other reason		
Out of 44 benefeciaries under retrofit in the ward none of the beneficiaries has received the second tranche due to lack of knowledge of retrofit so the Interaction and Orientation program for the retrofitting benefeciaries was organized.		
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.		
Previous Issues		Current Issues
Summary		

Field Visit: During the field visit HRRP team along with DSE and DLPIU-Building technicals interacted with the retrofit beneficiaries. Altogether 44 beneficiaries were enlisted in the retrofit list of the ward out of which 44 has signed the PA agreement and received the first tranche but none have received the second tranche. The major housing typology of the houses to be retrofitted were two storey and two-storey plus attic load bearing stone masonry in mud mortar. During the interaction program some of the beneficiaries were not interested in retrofitting their houses due to various reasons and some of them were in a dilemma about the methods. During the program following observations and challenges were seen:-

- As per some of the beneficiaries after the earthquake some small hair line cracks formed in their houses and during the Damage Grade Assessment survey their houses were kept under retrofit. Now they have repaired those houses with plaster and feel safe to stay there and do not want to retrofit their houses.
- Some of the beneficiaries due to high vulnerability and risk of the catastrophe of the house with time have demolished their houses which were under retrofit and have constructed new house without technical assistance as per their need.
- Some of the beneficiaries after getting the first tranche coordinated at ward level and were said to repair houses as safe/resilient as possible and due to the absence of technical assistance during that time they have repaired/plastered their houses, dismantled the vulnerable parts with the first tranche they received and started living and now do not have proper finance to further retrofit their houses.
- No. of HHs visited:
- No. of meetings/interaction with engineers:1
- No. of engineers interacted with:3
- No. of meetings/interaction with local officials:1
- No. of local officials interacted with: 1

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Financial problem is the leading problem for retrofit startup as maximum beneficiaries have spent their first tranche in repairing their houses.	Provision of soft loans specially for retrofitting beneficiaries to initiate and boost up the process	Not any	NRA, Palika	ASAP
Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)				
Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)				
Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)				
Photos				



National Reconstruction Authority (NRA)
District Level Project Implementation Unit (DLPIU), Building
Syangja District

S.N.	Municipality/ Rural Municipality	Ward No.	House Owner Name	PAID	Building Typology	Technically Feasible (Yes/ No)	Financially Feasible (Yes/ No)	If feasible, Reason of technical infeasibility	House Owner interest on retrofitting (Yes/ No)	Reason for not interested on retrofitting	Remarks
9	Putalibazar Municipality	7	Prakash Khatiwada	8,39,50.0	2-story	Yes	Yes	—	Yes		
10	Putalibazar Municipality	7	Mr. Dev Karki	8,39,50.0	2-story	Yes	Yes	—	Yes		
11	Putalibazar Municipality	7	Yashwantrao Karki	8,39,50.0	2-story	Yes	Yes	—	Yes		
12	Putalibazar Municipality	7	Thapa	8,39,50.8	2-story	Yes	Yes	—	Yes		
13	Putalibazar Municipality	7	Mr. Khatiwada	8,39,50.8	2-story	Yes	Yes	—	Yes		
14	Putalibazar Municipality	7	Mr. Khatiwada	8,39,50.8	2-story	Yes	Yes	—	Yes		
15	Putalibazar Municipality	7	Mr. Khatiwada	8,39,50.8	2-story	Yes	Yes	—	Yes		
16	Putalibazar Municipality	7	Mr. Khatiwada	8,39,50.8	2-story	Yes	Yes	—	Yes		

Handwritten note: - Husband wife were from govt. old is financial support

Ward no-7, Putalibazar Municipality, Syangja District
Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Bisheshwor Prasad Regmi. The interaction and orientation program mainly focused on awareness on retrofitting, listing the technical feasibility, housing typology, interest of house owner on retrofit (if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU technical, DSE and HRRP Team.

Sample of listing form:

Field Visit Reports (Syangja 2)

Visit 1

Date		Location	Participants
20 Nov 2019		Ward no-13, Putalibazar Municipality , Syangja District	• Biren Shah-HRRP • Rijan Gajurel – HRRP • Nawaraj Sharma-DSE, NRA • Samikshya Poudel-Focal Engineer-DLPIU-Building •
Objective(s)	• Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Khyam Narayan Adhikari.The interaction and orientation program mainly focused on awareness on retrofitting , listing the technical feasibility , housing typology, interest of house owner on retrofit(if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU technical , DSE and HRRP Team.		
Why was the visit carried out in this location? Priority wise, Write any other reason			
The total number of retrofit beneficiaries in this ward is 112 out of which all have signed the PA agreement and received the first tranche of retrofit but haven't implemented the process to receive the second tranche for retrofit,as a result of which the second tranche is zero.			
If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.			
Previous Issues		Current Issues	
Summary			

Field Visit: During the field visit HRRP team along with DSE and DLPIU-Building technicals interacted with the retrofit beneficiaries. Altogether 112 beneficiaries were enlisted in the retrofit list of the ward out of which 112 has signed the PA agreement and received the first tranche but none have received the second tranche. The major housing typology of the houses to be retrofitted were two storey and two-storey plus attic load bearing stone masonry in mud mortar. During the interaction program some of the beneficiaries were not interested in retrofitting their houses due to various reasons and some of them were in a dilemma about the methods. During the program following observations and challenges were seen:-

- As per some of the beneficiaries after the earthquake some small hair line cracks formed in their houses and during the Damage Grade Assessment survey their houses were kept under retrofit. Now they have repaired those houses with plaster and feel safe to stay there and do not want to retrofit their houses.
- Some of the beneficiaries due to high vulnerability and risk of the catastrophe of the house with time have demolished their houses which were under retrofit and have constructed new house without technical assistance as per their need.
- Some of the beneficiaries after getting the first tranche coordinated at ward level and were said to repair houses as safe/resilient as possible and due to the absence of technical assistance during that time they have repaired/plastered their houses, dismantled the vulnerable parts with the first tranche they received and started living and now do not have proper finance to further retrofit their houses.
- No. of HHs visited: 0
- No. of meetings/interaction with engineers: 1
- No. of engineers interacted with: 1
- No. of meetings/interaction with local officials: 1
- No. of local officials interacted with: 1

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Financial problem is the leading problem for retrofit startup as maximum beneficiaries have spent their first tranche in repairing their houses.	Provision of soft loans specially for retrofitting beneficiaries to initiate and boost up the process	Not any	NRA, Palika	ASAP
Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)				
Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)				
Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)				
Photos				



Ward no-13, Putalibazar Municipality , Syangja District
Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Bisheshwor Prasad Regmi. The interaction and orientation program mainly focused on awareness on retrofitting, listing the technical feasibility, housing typology, interest of house owner on retrofit (if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU technical, DSE and HRRP Team.

- As per some of the beneficiaries after the earthquake some small hair line cracks formed in their houses and during the Damage Grade Assessment survey their houses were kept under retrofit. Now they have repaired those houses with plaster and feel safe to stay there and do not want to retrofit their houses.
- Some of the beneficiaries due to high vulnerability and risk of the catastrophe of the house with time have demolished their houses which were under retrofit and have constructed new house without technical assistance as per their need.
- Some of the beneficiaries after getting the first tranche coordinated at ward level and were said to repair houses as safe/resilient as possible and due to the absence of technical assistance during that time they have repaired/plastered their houses, dismantled the vulnerable parts with the first tranche they received and started living and now do not have proper finance to further retrofit their houses.

Field Visit Reports (Syangja 3)

Visit 1

Date	Location	Participants
21 Nov 2019	Ward no-13, Galyang Municipality, Syangja District	• Biren Shah-HRRP • Rijan Gajurel – HRRP • Nawaraj Sharma-DSE, NRA • Samikshya Poudel-Focal Engineer-DLPIU-Building • Dipendra Kumar Yadav-DLPIU Er • Lal Bahadur Aslani-DLPIU-Sub Er

Objective(s)	Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Netra Prasad Pandey. The interaction and orientation program mainly focused on awareness on retrofitting , listing the technical feasibility , housing typology, interest of house owner on retrofit(if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU technical , DSE and HRRP Team.			
Why was the visit carried out in this location? Priority wise, Write any other reason				
The total number of retrofit beneficiaries in this ward is 112 out of which all have signed the PA agreement and received the first tranche of retrofit but haven't implemented the process to receive the second tranche for retrofit, as a result of which the second tranche is zero therefore for Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Netra Prasad Pandey				
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.				
Previous Issues		Current Issues		
Summary				
Field Visit: During the field visit HRRP team along with DSE and DLPIU-Building technicals interacted with the retrofit beneficiaries. Altogether 77 beneficiaries were enlisted in the retrofit list of the ward out of which 77 has signed the PA agreement and received the first tranche but none have received the second tranche. The major housing typology of the houses to be retrofitted were two storey and two-storey plus attic load bearing stone masonry in mud mortar. During the interaction program some of the beneficiaries were not interested in retrofitting their houses due to various reasons and some of them were in a dilemma about the methods. During the program following observations and challenges were seen:- - As per some of the beneficiaries after the earthquake some small hair line cracks formed in their houses and during the Damage Grade Assessment survey their houses were kept under retrofit. Now they have repaired those houses with plaster and feel safe to stay there and do not want to retrofit their houses. - Some of the beneficiaries due to high vulnerability and risk of the catastrophe of the house with time have demolished their houses which were under retrofit and have constructed new house without technical assistance as per their need. - Some of the beneficiaries after getting the first tranche coordinated at ward level and were said to repair houses as safe/resilient as possible and due to the absence of technical assistance during that time they have repaired/plastered their houses , dismantled the vulnerable parts with the first tranche they received and started living and now do not have proper finance to further retrofit their houses. - No. of HHs visited: 0 - No. of meetings/interaction with engineers: 1 - No. of engineers interacted with: 2 - No. of meetings/interaction with local officials: 1 - No. of local officials interacted with: 1				
Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)

Financial problem is the leading problem for retrofit startup as maximum beneficiaries have spent their first tranche in repairing their houses.	Provision of soft loans specially for retrofitting beneficiaries to initiate and boost up the process	Not any	NRA,Palika	ASAP
Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)				
Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)				
Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)				
Photos				
				
Ward no-13, Galyang Municipality ,Syangja District Interaction and orientation Program with beneficiaries enlisted in retrofitting and ward level meeting in the chairmanship of Mr. Netra Prasad Pandey.The interaction and orientation program mainly focused on awareness on retrofitting , listing the technical feasibility , housing typology, interest of house owner on retrofit(if not then the reason why the beneficiary does not want to go for retrofit) in the presence of DLPIU technical , DSE and HRRP Team.				

Housing Typology Report (Max 4 Photos, Select best photos from each district)

Photo



Caption: Ward no-4, Rupakot Municipality, Kaski
The beneficiary has received the third tranche.
Housing Typology: Load Bearing Brick Masonry in cement mortar.

Photo



Caption: ward no-6, Besisahar Municipality, Lamjung District
Housing Typology: Two rooms Load bearing brick masonry in cement mortar.
The beneficiary has not received the third tranche as the house is missing the gable band and recommended for corrections.

Photo



Caption:
Ward No-2, Annapurna RM, Kaski Retrofit model house by Built Change
The beneficiary has received the first tranche of GON retrofitting grant.

Photo



Caption:
Ward no-4, Rupakot Municipality, Kaski
The beneficiary is enlisted under retrofit and have plastered the house and is currently living.
Housing Typology: Two Storey load bearing stone masonry in mud mortar.

