

District Report

Rasuwa

15 March – 11 April 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Transportation rate of various construction materials were updated: Transportation rate from the nearest market (Bidur Nuwakot) to different rural municipalities was updated at national level. During survey, we found the easiest and fast means of transportation for construction materials is Eicher. Sub way linked most of the communities of district and on the other side most them are just grabbed and has narrow width. So, people prefer to transport materials in Eicher by which it delivers materials near to their construction site. Cost of construction is high due to lack of road accessibility.	9 April 2019			lm.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Report on Training of Trainers Nuwakot was updated: Two parallel “7 Days Training of Trainers (ToT) on earthquake resistant building construction” started from March 11, 2019 at Sukhad Pahuna Ghar Hotel and Hotel Saptarangi, Bidur-4, Metropolitan City, Nuwakot for newly recruited NRA engineers. The training is organized by CLPIU- building with Technical support from HRRP and NSET. There are 74 engineers including 3 females from Dhading and Nuwakot districts.	14 March 2019	71	3	lm.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	

Summary of events during this period

The topic of the training includes earthquake basics, earthquake resistant design and construction philosophy, NBC, inspection process of reconstructed building typologies, retrofitting etc. Sessions Taken By DTC Rasuwa(Biren Shah) and DTC Dhading (Sachin Sapkota) : Light timber/steel frame structure manual ,Hybrid structure manual , Bracing calculations and Hollow concrete block manual					
Hollow concrete block manual orientation was successfully completed in Rasuwa District.	18 March 2019	20		Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Featured technical focal engineer report was prepared.	5 April 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Preparation of Hollow concrete block orientation report	31 March 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Housing Typology upload in excel format	1 April 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Update of housing typologies of Rasuwa district in Flickr	April 2019			Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Report of TOT held in Nuwakot was prepared and shared with the team.				Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	
Ward level meeting: Ward level meeting was conducted on Naukunda RM -3. Ward chairperson together with others technical person and visited team discusses some raising issues of ward. Discussed Issue: In completion certificate distribution process, around 80%				Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	


Summary of events during this period

households already received third tranche after completion of house construction but certificate distribution process seems slow and late. Distribution should start as soon as possible which we made the decision at meeting. • Information collection about house sizes and number of rooms, HRRP district coordinator first illustrate the importance of collection of this information and handover the data collection templet to ward technical person. • Other technical issues and challenges in ward level. Some of them are: Maximum BMC ,RCC structure housing typology • High rate of construction material and price inflation. • This results in the gap of information and interaction between the beneficiaries and the technical manpower.					
Rural municipality Action Plan Update and website uploading process: All five rural municipalities action plan was updated and uploaded on respective palikas websites. The signed copy of action plan is ongoing. However, two palikas signed copy is received and others is not signed yet.				lm.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	


Tranche Status

Rural /Municipality	Gosaikunda RM	Kalika RM	Naukunda RM	Aamo Chhindigmo RM	Uttargaya RM
Total HHs Surveyed	1979	2569	3349	1964	2631
Total HHs Eligible	1979	2569	3349	1964	2631
Total HHs Enrolled	1836	2456	3291	1802	2274
First Tranche	1836	2456	3291	1802	2274
Second Tranche	1649	2308	3038	1560	1958
Third Tranche	1248	2121	2758	1273	1725
Total HH Constructed	1248	2121	2758	1273	1725
Grievance Registered					
Grievance Addressed	257	277	246	237	239
RF HH Eligible	84	11	59	32	25
RF HH Enrolled	60	10	2	10	11
RF 1 st Tranche	60	10	2	10	11
RF 2 nd Tranche	0	0	0	0	0
Non-Compliance Registered	89	48	54	101	124
Non-Compliance Addressed	69	36	40	70	86


Graph of Tranche Status:

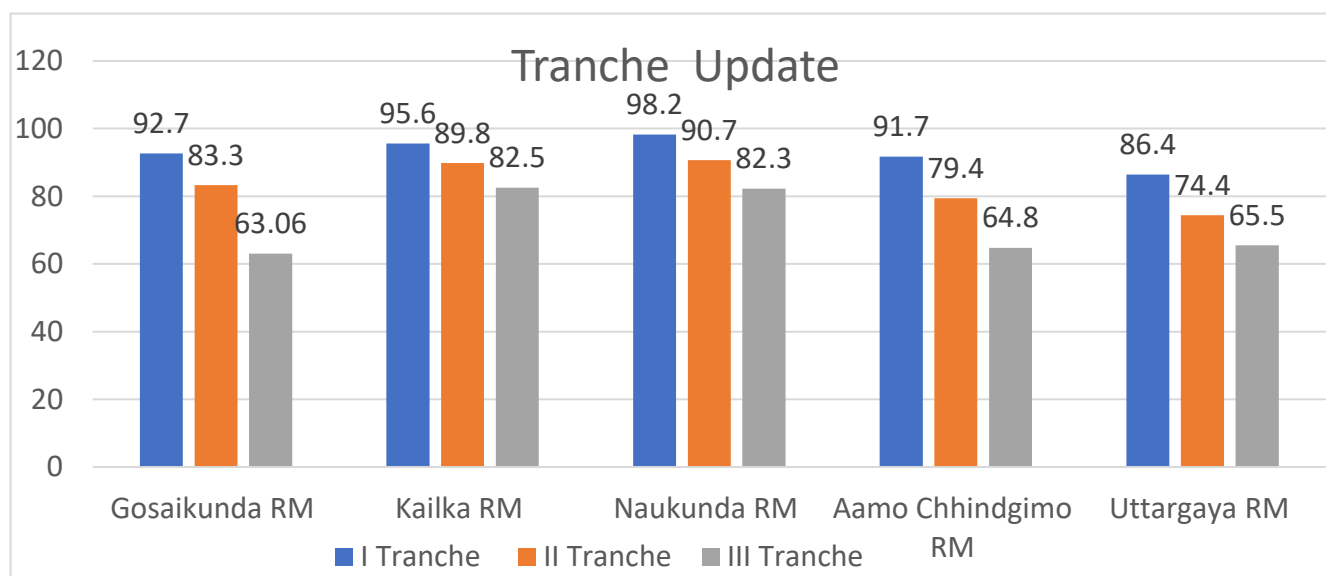

Graph for Retrofitting Status:

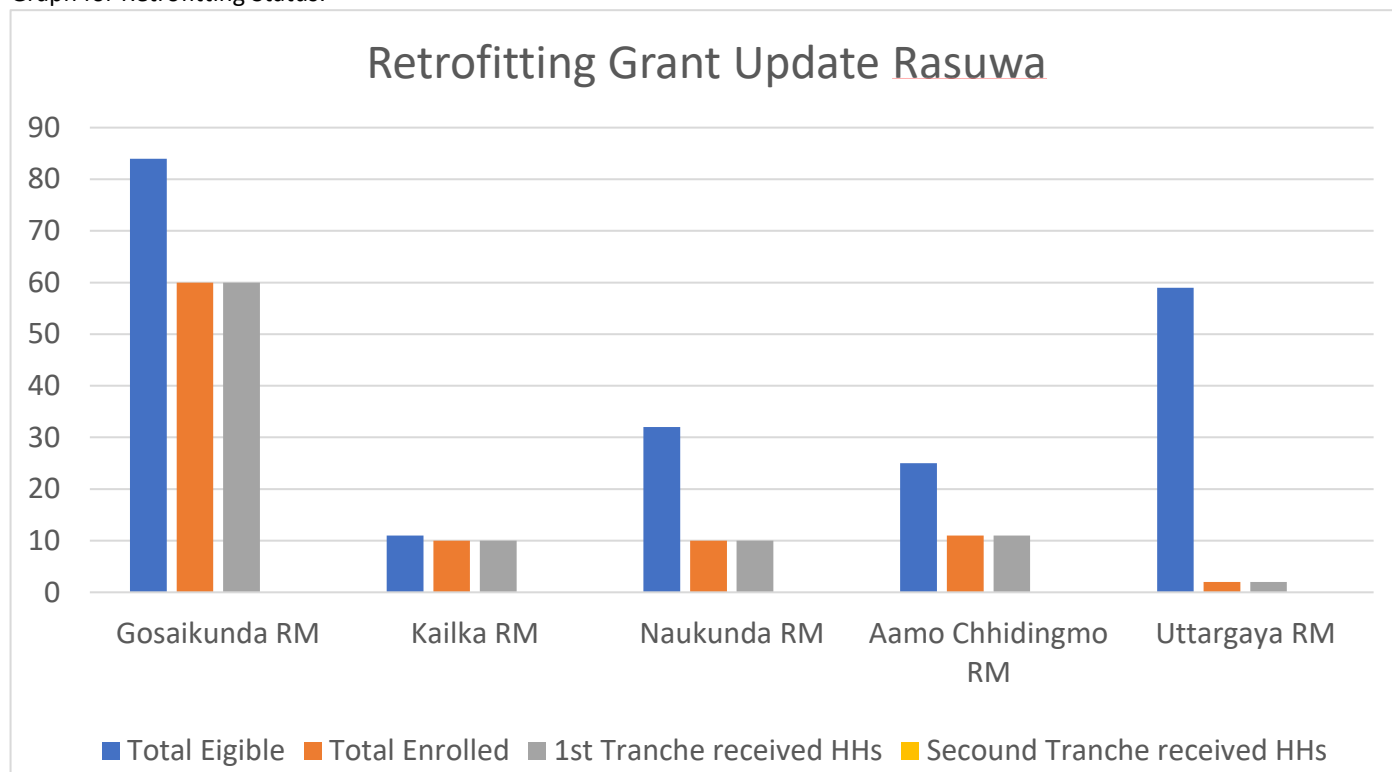

Graph for Grievance Status:



Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders			
27 th March,2019	Naukunda RM ward number 3 and ward no-1	Rijan Gajurel – HRRP Biren Shah – HRRP Saroj Kumar Yadav – Building Prajwal KC – DSE			
Objective(s)	- Discussion about the status and challenges of reconstruction at ward level. - Discuss about the gap between the technical and ward representatives. - Discuss about the reasons beneficiaries who has not taken the first tranche. - To discuss the issues of high rate of non-compliance, low mobilization of engineers. - Disseminate information on Reverification and Resurvey guidelines and policies on ward level.				
•					
Summary	HRRP team together with building district focal person Mr. Saroj Kumar Yadav and district support engineer visited Naukunda RM ward number 3 and 1 (Parchang and Aru Kharka). Team conducted ward level meeting and field monitoring at ward number-3. Ward chairperson Mr Membar Thi Tamang.				
	Tranche update record of Naukunda ward number 3 ,Parchyang				
	Total Eligible HHs	First Tranche Received HHs	Second Tranche Received HHs	Third Tranche Received HHs	Construction Completed HHs
	555	548	528	490	490
	Key points of discussion:				
	In completion certificate distribution process, around 88% households already received third tranche after completion of house construction, but certificate distribution process seems slow and late. Distribution should start as soon as possible which we made the decision at meeting. - Discussion on the beneficiaries who are not enrolled yet although listed and those who have not taken the second tranche. - Discussion on the Guidelines and policies on Resurvey and Reverification-Handover the Resurvey and Reverification manual to the ward chairperson.				
	Key finding of field visit:				
	a) Maximum Load bearing Brick Masonary in Cement Mortar and Reinforced frame Cement Concrete (RCC) structure housing typology. b) High rate of construction material and price inflation. c) This results in the gap of information and interaction between the beneficiaries and the technical manpower. d) One of the major challenges of this ward is that the beneficiaries are not willing now to take the second tranche although they have constructed the house. This is because they are likely to expect bank loans and are known that if they receive the second tranche they will not be able to receive the bank loan according to the Guidelines made by NRA. e) Mostly One room house are constructed in this ward and still the beneficiaries are living in the earthquake affected vulnerable houses. f) Lack of road accessibility. g) No net facility in the ward office has been a major problem.				

After the completion of field visit at ward number 3 we went towards ward number 1(Aru Kharka). After, walking nearly 2.5 hours from the road we reached the village. There is no ward office in this village. The ward office is located in Langbu village of this ward. So, after interaction with beneficiaries we moved to the field.

Tranche update record of ward number 1

Total Eligible HHs	First Tranche Received HHs	Second Tranche Received HHs	Third Tranche Received HHs	Construction Completed HHs
619	611	573	529	529

Key points of discussion:

- **In completion certificate distribution process**, around 85% households already received third tranche after completion of house construction, but certificate distribution process seems slow and late. Distribution should start as soon as possible which we made the decision at meeting.
- Interaction with the beneficiaries on the technical support from ward engineers/sub engineers and sub-assistant engineers.
- The beneficiaries are still living in the earthquake affected house.

Key finding from field monitoring

- High rate of construction material and price inflation is a major problem.
- Variation in housing typologies can be seen ranging from Load bearing SMC structure , Hybrid and RCC structures.
- Although the beneficiaries have constructed new earthquake resilient houses but they are still living in the old earthquake affected vulnerable houses which is one of the main problem in this ward.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
There is gap of information and interaction between the beneficiaries and the technical manpower.	Coordination among the technical and beneficiaries	Ward representatives, Ward technical , DLPIU Building	ASAP
The beneficiaries are still living in the earthquake affected house although they have constructed new houses.	Awareness programs	DLPIU GMaLI , DLPIU Building , Rural Municipality , ward level	ASAP
Photos			



Naukunda Rural Municipality, Ward no-3, Rasuwa

Name of Beneficiary: Mr. Bru Rana Neki Tamangi

Tranche update: Third received

Housing Typology: Reinforced cement concrete framed building(RCC)

The house is a four rooms structure with columns of size 12"x 12". The structure consists of all the bands at different levels and the house is under construction. The total cost of construction is nearly 18 lakhs. The owner are temporarily living in the earthquake affected house until the new house is constructed completely.

Naukunda Rural Municipality, Ward no-3, Rasuwa

Name of Beneficiary: Mr. Tulu Sarki Tamangi


Tranche Update: Third tranche received

Housing Typology: Reinforced cement concrete framed building(RCC)

The house is a two rooms structure with 6 columns of size 12"x 12". The structure consists of all the bands at different levels and the construction of the house is completed. The total cost of construction is nearly 10 lakhs

Housing Typology Report

Photo

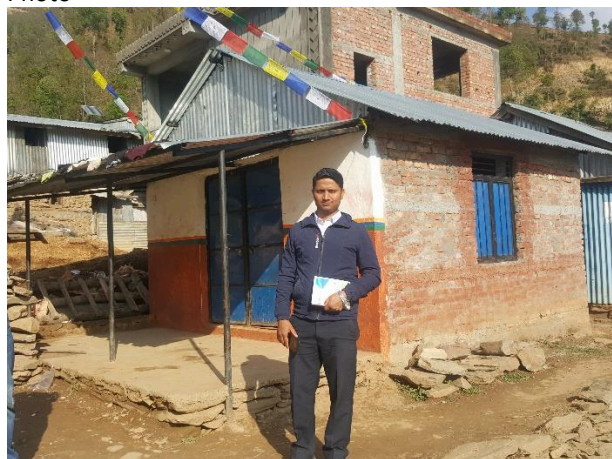

Naukunda Rural Municipality, Ward no-3, Rasuwa

Name of Beneficiary: Mr. Basanta Ghale

Tranche Update: Third Received

Housing Typology: Load bearing Brick Masonary and cement mortar Masonary

It is a one room house with room size 10'x12'. There are five members in family.

Photo



Name of Beneficiary: Mr.Kam GhyaTamang(Father) and Jitman Tamang (son)

Tranche Update: Third Received

Housing Typology: Load bearing stone Masonary and mud mortar Masonary

They have received all the third tranches of the GON housing grant. It is a two one- rooms SMM house with RCC band .There is a gap in between the house but the house has common roofing. The construction of the house is completed.

Photo



Naukunda Rural Municipality, Ward no-3 , Rasuwa
Name of Beneficiary: Yo Nurpu Lopchan Tamang.
Tranche Update: Third Received
Housing Typology: Load bearing Brick Masonary and cement mortar Masonary
It is a two room BMC house with RCC band .The construction of the house is completed.

Photo



Naukunda Rural Municipality , Ward no-3 , Rasuwa
Name of Beneficiary: Mr. Chiring Ghale
Tranche Update: Third Received
Housing Typology: Reinforced cement concrete framed building
The house is with columns of size 12"x 12". The structure consists of all the bands at different levels and the construction of the house is completed.



Naukunda Rural Municipality, Ward no-1 , Rasuwa
Name of Beneficiary: Nur Chuwang Lama
Tranche Update: second Received
Housing Typology: Load bearing stone Masonary and mud mortar Masonary(planned)
It is a one room house and has planned to use RCC band and light CGI roofing. The cost of construction till date is NRs 40000.



Naukunda Rural Municipality, Ward no-1 , Rasuwa
Name of Beneficiary: Tasi Memba Lopchan
Tranche Update: Third Received
Housing Typology: Hybrid structure
It is a two room hybrid structure with lower load bearing brick Masonary in cement mortar and upper CGI sheet structure.



Naukunda Rural Municipality, Ward no-1 , Rasuwa
Name of Beneficiary: Suk Bahadur Lopchan
Tranche Update: Third Received
Housing Typology: Reinforced cement concrete framed
structure (RCC).

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will the construction completion certificate be given?	Beneficiaries	(The distribution of completion certificate is started in other wards AND has been send in the ward level. The process has started already and now the technicals are also working on that
What is the deadline of the first tranche?	Beneficiaries	The deadline has been extended till Ashar 2076
Will there be additional top-up for us??	Beneficiaries	There is top up only for of 50k Rs for people who have been listed in vulnerable groups.

Challenges and Way Forward

Challenge	Way Forward
Lack of awareness in the beneficiaries about compliant RCC construction.	Effective mason training and awareness programs must be conducted.
Some of the beneficiaries have constructed one room up to DPC level and are not looking up for further construction.	Follow up from DLPIU-Building, DLPIU -GMAI about the deadline and blacklist process.
