


FACTS AND FIGURES

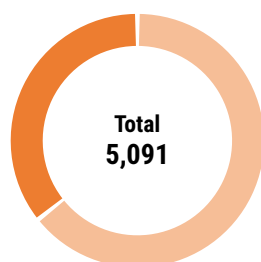

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	72.50%	44.19%
Timber Frame Structure	23.85%	16.91%
Brick and Cement Mortar Masonry	2.36%	26.60%
Stone and Cement Mortar Masonry	0.84%	1.32%
Others	0.46%	10.97%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	1,710
PA Agreement	1,541 169
I st Tranche received	1,541 169
II nd Tranche received	1,429 281
III rd Tranche received	986 724

Houses

Under Construction: 1,489

Completed: 800

Retrofitting Status

Total Eligible HHs	564
PA Agreement	415 149
I st Tranche received	415 149
II nd Tranche received	564

Grievances

Registered: 1,224

Addressed: 1,224

Non-compliances

Registered: 54

Addressed: 54

Data Updated on: 2019-04-22 00:00:00

P0 Presence

Active: PIN (Shelter)

Phased Out: BNMT (Health), EBMF (Education), HELVETAS (Shelter), NRCS (Agriculture), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), PIN (Shelter)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	25,080	-	-
Aggregate	m ³	26,173	-	-
Sand	m ³	2,682	-	-
Timber	cu. ft.	3,110	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	86,558	-	-
Rebars	kgs.	271,079	-	-
Tin	bundle	3,538	-	-
Bricks	pcs.	201,044	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

OTHER SECTORS



Schools

Damaged: 44
Under Construction: 22
Construction Completed: 22



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

KEY CONTACTS

Municipal Office

Raj Kumar Malla
Chairman
9855069405

Municipal Office

Er. Ram k.c.
Focal Person
9846606447

Municipal Office

Nirmala Himdung
Deputy Chairman
9845599541

GMaLI/NRA

Som Raj Timilsena
NRA Chief-District
9855030632

Municipal Office

Ram Kumar Pudasaini
Chief Administration Officer
9845502695

DLPIU-Building

Sudip Acharya
DUDBC.DLPIU Chief
9851153206

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING

Trainings (# out of total required)

7 days Training



50 days Vocational Training




Reached

Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

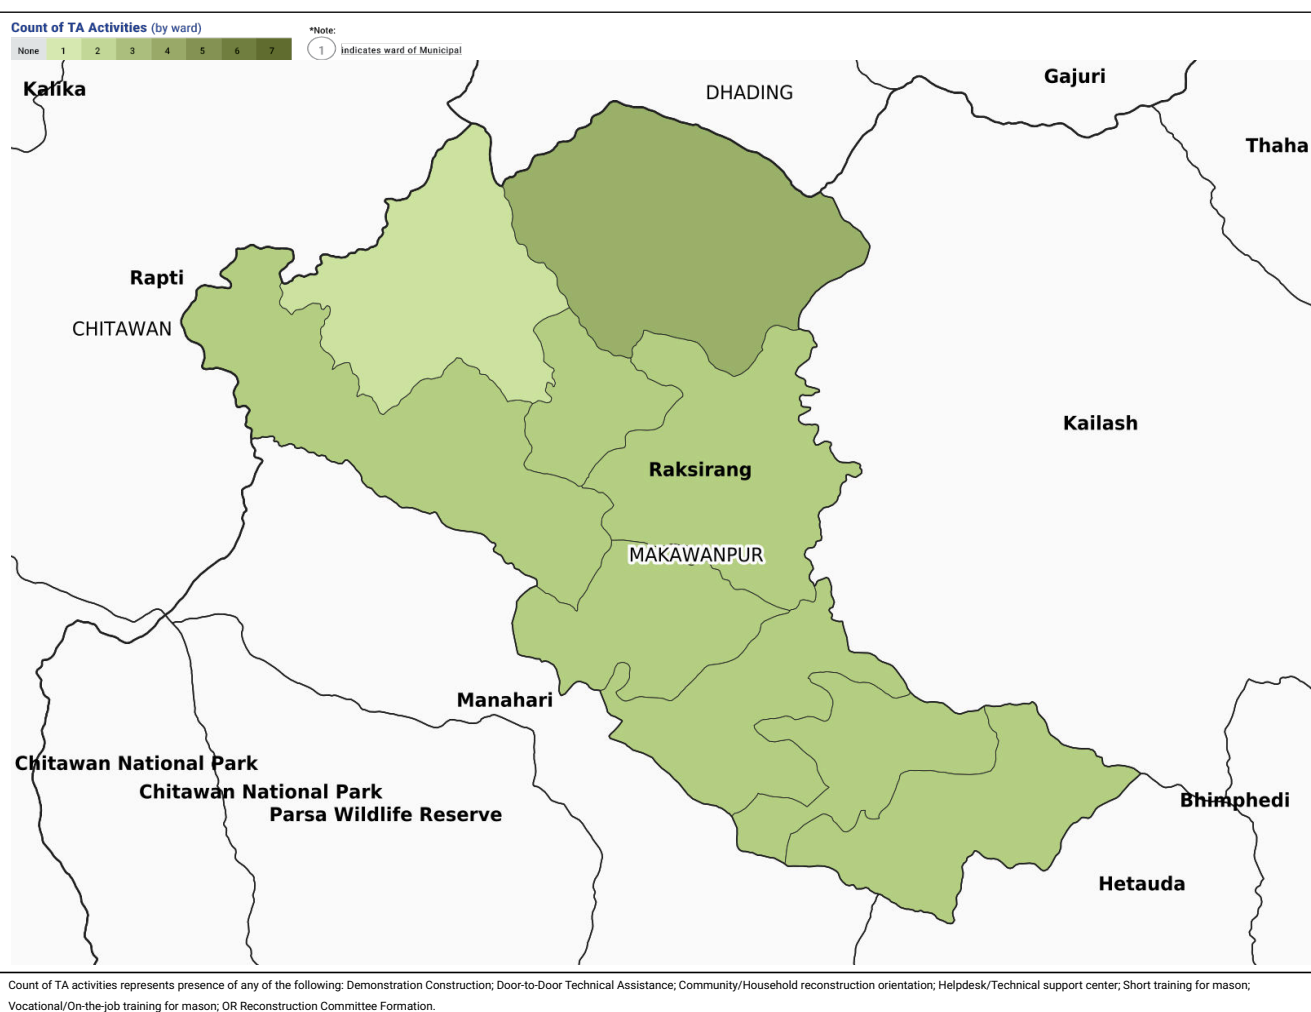

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. (District Coordinator) 2. Kausal Bist (District Technical Officer) 3. Sachin Malego (District Information Management Officer)
9849787273 984166793
