

Monthly District Report

Solukhumbu, Okhaldhunga, Khotang

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Solukhumbu	Ward level Meeting	11 th June 2019	Solukhumbu, Thulung Dodhkoshi Rural Municipality ward no 1	Ghana Raj Rai	Click here for minutes
	Field Visit / Housing typology Collection	12 th June 2019	Ward no 1 and 2 of Thulung Dodhkoshi Rural Municipality	Raman Rai	
	Informal Meeting with Acting GMaLI Chief	10 th June 2019	Office room of his own	Buddhi Kumar Shrestha	
Okhaldhunga	District Coordination Meeting	7 th June 2019	GMaLI Meeting hall Okhaldhunga	Yubraj Kharel	CLICK here for meeting Minutes
	Field Visit /Housing Typology Collection	13 th June 2019	Chisankhugadi Rural Municipality	Bibek Basnet	
Khotang	Follow up with Stakeholders	Regular	GMaLI, DLPIU and Partners		

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
One Day orientation at Solukhumbu		HRRP	Prakash Basnet, Birodh Kattel
One Day Orientation at Khotang		HRRP	Prakash Basnet, Birodh Kattel
Field Visit	Halesi Tuwachung Rural Municipality		

Tranche Status (Solukhumbu)


Tranche Status Table:

Rural /Municipality	Dhudhkoshi	Khumbupasang	Likhupike	Mahakhulung	Nechasalyan	Solududhkunda	Sotang	Thulung Dudhkausika
Total HHs Surveyed	Total:- 17460							
Total HHs Eligible	1007	793	1186	596	1166	1910	551	2738
Total HHs Enrolled	1007	793	1186	596	1166	1910	551	2738
First Tranche	1005	793	1186	596	1166	1910	551	2738
Second Tranche	785	691	857	259	570	1097	290	1442
Third Tranche	158	103	285	221	560	765	244	1199
Total HH Constructed	158	103	285	221	560	765	244	1199
Grievance Registered	Total:- 283							
Grievance Addressed	Total:-463							
RF HH Eligible	Total:- 2382							
RF HH Enrolled	38		37	66	19	7	9	68
RF 1st Tranche	36		37	66	19	7	9	68
RF 2nd								

Graph of Tranche Status:

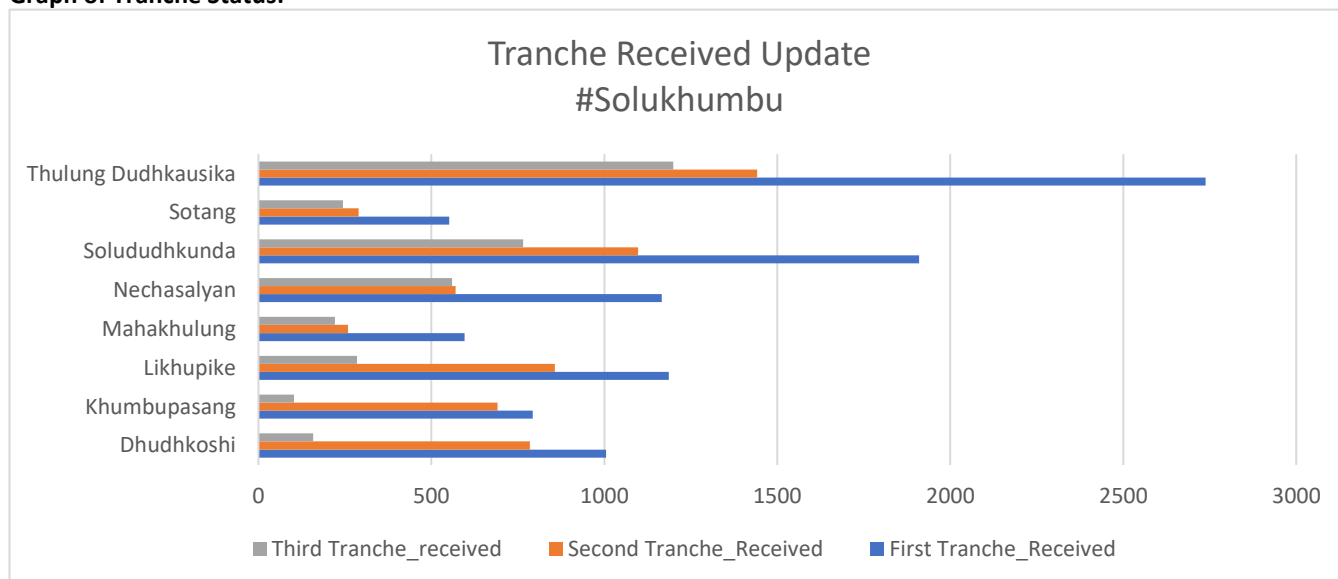

Graph for Retrofitting Status:

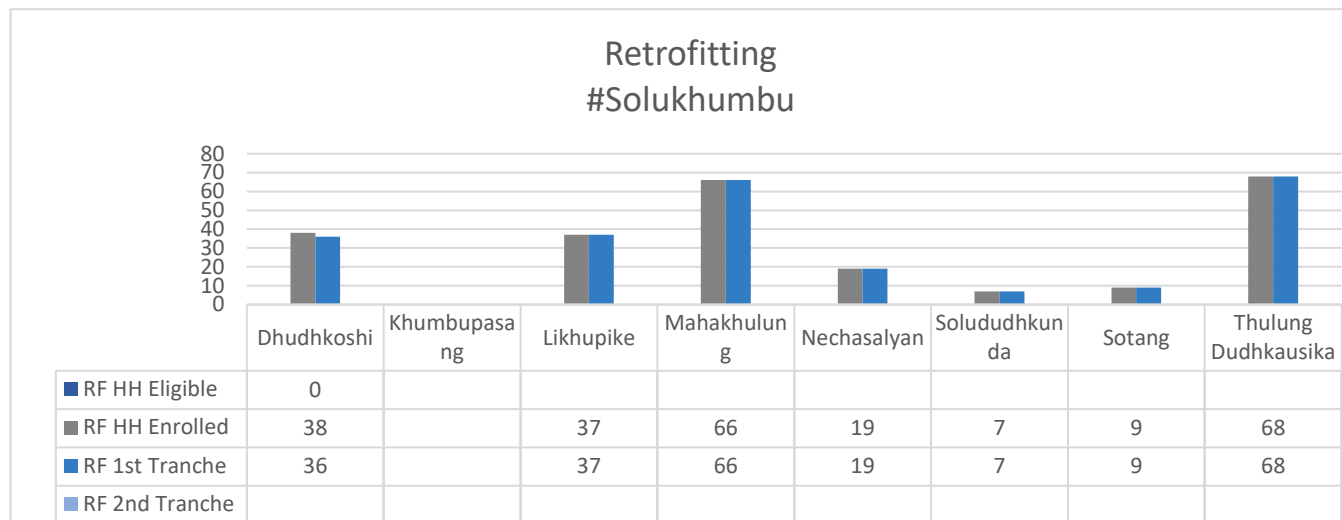


Tranche Status (Okhaldhunga)

Graph of Tranche Status:

Tranche Status Table:


Rural /Municipality	Siddicharan	Manebhanjyang	Molung	Likhu	Sunkoshi	Khijidemba	Champadevi	Chishankhugadi
Total HHs Surveyed	3898	2978	5191	4441	5538	3902	6057	1917
Total HHs Eligible	2707	1679	2997	3261	3304	2928	3395	1067
Total HHs Enrolled	2468	1544	2891	3212	3206	2808	3291	1007
First Tranche	2468	1544	2891	3212	3206	2808	3291	1007
Second Tranche	2040	1298	2562	3006	3002	2674	3010	887
Third Tranche	1680	1054	2310	2741	2671	2522	2740	820
Total HH Constructed	1680	1054	2310	2741	2671	2522	2740	820
Grievance Registered	1336	1361	2462	1394	2523	1083	3040	904
Grievance Addressed	1336	1361	2462	1394	2523	1083	3040	904
RF HH Eligible	870	597	494	248	567	259	753	276
RF HH Enrolled	451	410	250	169	97	201	471	174
RF 1st Tranche	450	410	250	169	97	201	471	174
RF 2nd Tranche								

Tranche Received Update #Okhaldhunga

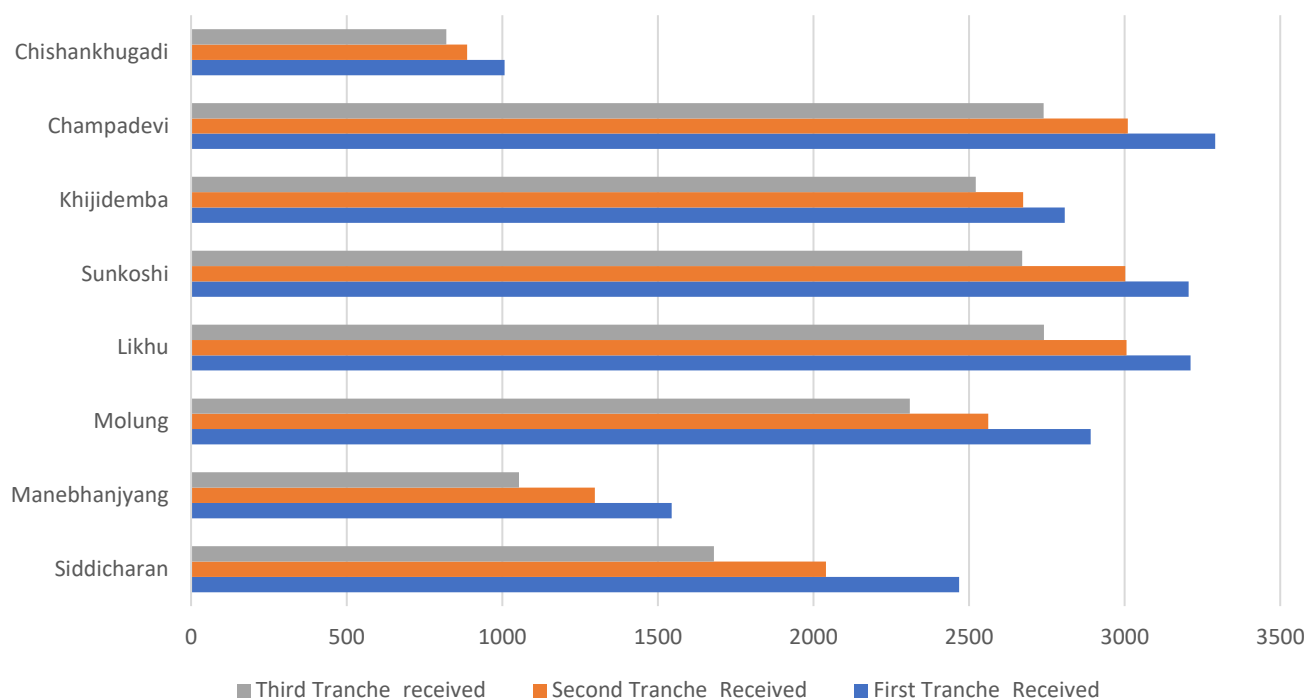

Graph for Retrofitting Status:

Retrofitting #Okhaldhunga

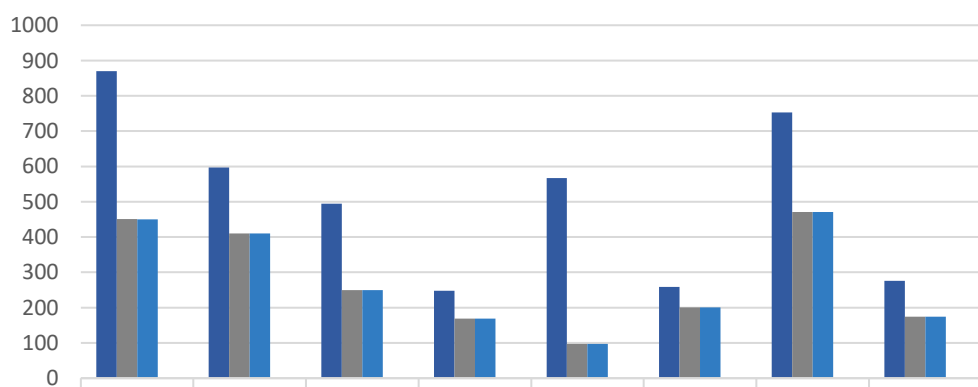

	Siddicharan	Manebhanjyang	Molung	Likhu	Sunkoshi	Khijidemba	Champadevi	Chishankhugadi
RF HH Eligible	870	597	494	248	567	259	753	276
RF HH Enrolled	451	410	250	169	97	201	471	174
RF 1st Tranche	450	410	250	169	97	201	471	174
RF 2nd Tranche								

Tranche Status (Khotang)

Tranche Status Table:

Total Survey: - 12899
Total Eligible: - 8574

Retrofitting Numbers: - 2367
PA Agreement: - 8331
First Tranche Released: - 8328
Second Tranche Released: - 5796
Third Tranche Released: - 4972
Grievance Registered: - 268
Grievance Addressed: - 3287

Field Visit Reports (Solukhumbu)

Visit 1

Visit 1		
Date	Location	Participants
11 th June 2019	Thulung Dodhkoshi Rural Municipality ward no 1 nele	HRRP Team, Focal Engineers, ward Level engineers and local representative
Objective(s)	• To collect the housing Typology and conduct ward level meeting with the ward leader and local representative. • To get the burning issues of reconstruction in this ward and to provide the possible solutions and to know the status of resurvey and reverification. • Ward Chief Mr Dhanaraj Sunuwar explained about the reconstruction status and issue of Thulung Dudhkoshi Rural municipality ward no 1. As per him no skilled masons are available into the Ward to complete the reconstruction on time. The previous trained masons have been moved to another districts. • Also discussed regarding the resurvey and reverification, Ward engineers explained about the progress of resurvey. As per them the reverification and resurvey has been completed. • Ward Chief Mr Sunuwar concerned about the houses which are constructed before the NRA engineer's recruitment. The beneficiaries constructed their houses as per their interest, but engineers are pointing these houses as a noncompliance. He suggested to make flexibility after some correction done for the tranche release.	
Why was the visit carried out in this location?		
This ward is one of the ward with the Largest numbers of beneficiary and it was in the priority one for our field visit plan and as per the request of the District support engineer and		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
This ward was no visited previously, and this was the first time		
Summary		

Field Visit: joint monitoring was conducted with focal engineers Raman Bantawa and Subash Jha at Thulung Doodhkoshi Rural Municipality ward no 1 Meeting was conducted with the Engineers before selecting the ward for the visit. During the Visit about 10 houses were observed which were of different typology as listed below in the typology report. aslo the meeting was conducted at ward level under the chairmanship of ward leader Ghana Raj Sunuwar some of the key points during the meeting were as follows

- During the meeting it was discussed that due to lack of trained mason it is difficult to complete the reconstruction in time so to complete the reconstruction in time trained mason should be produced in the ward level so, ward leader requested HRRP to manage training by facilitating with the NRA and DLPIU.
- As per the Ward leader resurvey and re verification is going in the ward level smoothly and he also said that all the work of resurvey and re verification will be completed in time provided by the NRA.
- As per the Ward leader there are various houses which were built before the arrival of NRA Technician and are non-compliance and are to be corrected so, ward leader made sure that ward representative will suggest all such beneficiary to make correction of those houses and help NRA to complete reconstruction in

Meeting minutes: <https://drive.google.com/open?id=1hdNzNSySill0sOoFingpsjYFi-RJgOU1>

Photos



Solu Dudhkunda Municipality ward-6, Dorpu Solukhumbu : Chabinarayan Rajbhandari he has built this two roomed single storey house immediately after the earth quake the house is built providing foundation of stone in mud mortar and walls of wooden planks with column of wood and the design has been approved by the Municipality asper house owner. No any horizontal bands have been provided the beneficiary has already received all three tranche of government and waiting for the completion certificate. As per the engineer of NRA most of the houses are of same typology in that area.




Thulung Doodhkoshi RM ward no 1 Nele Solukhumbu :Bhesh Bahadur Karki house under construction with RCC band at the plinth level and wooden bands at the wall and the vertical bar used is of 12 mm only due to lack of technical assistance.evethough the engineer has visited that house twice till now The Beneficiary has received first and second tranches.



Thulung Doodhkoshi Rural Municipality ward no 1 Nele Solukhumbu: Lalit Bahadu rai: Non-compliance two storey house constructed on stone mud mortar typology and corrections to be made based on correction/exception manual. Beneficiaries are not interested to do correction as they have finished their construction and blaming government for not providing technical assistance during construction period. The beneficiary has already received his first tranche from the government.

Thulung Doodhkoshi RM ward no 1 Nele Solukhumbu: Gyan Bahadur Khadka: Under construction This stone mud-mortar house is about to complete without any inspection and is noncompliance due to more attic height. There was no any inspection and the beneficiary built the house as per his own knowledge learned from the radio program. He has no idea about the engineers it is clear that the house is noncompliance due to lack of technical assistance. Beneficiary has received first tranche.

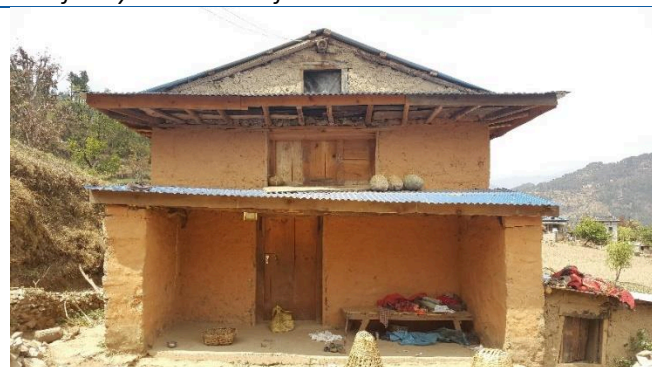

Thulung Doodhkoshi RM ward no 1 nele Solukhumbu:Kirti Bahadur Thapa : this house has been completed about 3 month ago without any technical assistance from the government. The house is noncompliance due to higher percentage of opening. Beneficiary has received first tranche and waiting for the second and has no idea about this second tranches. Suggestion from the beneficiary was if government cannot send the technical person in the village to prevent other houses form being noncompliance please provide one model house in each ward which will be compliance so that other beneficiary themselves can learn from that house and could built compliance house learning from that even without technical support.

Thulung Doodhkoshi RM ward no 1 Nele Solukhumbu :Rajendra tamang: Build this house one after the earthquake he waited for the government for one year leaving in tent house since his house was completely collapsed after the earthquake of 2015. House is built with stone in mud mortar and is noncompliance since the attic height and the opening in the first floor is not appropriate. The beneficiary has already received first trance and waiting for the second hoping that for those house which were build already will receive other tranches without any correction. As per the Beneficiary the cost of construction of this house was 5 lakhs.

Field Visit Reports (Okhaldhunga)

Visit 1

Date	Location	Participants
13 th June 2019	Chisankhugadi Rural Municipality ward no 3 Diyale	HRRP Team and District Support Engineer of Okhaldhunga
Objective(s)	- To monitor the house which were complained as noncompliance by World bank - To collect housing typology and conduct ward level meeting	
Why was the visit carried out in this location?		
Some of the houses in this ward were reported as non-compliance from the Central level and the world bank so to verify that actually they were compliance or non-compliance monitoring was done by DSE along with HRRP team.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
This ward was not visited previously		
Summary		
Field Visit: - About five to six houses were visited and monitored by the DSE specially those houses which were reported as noncompliance were monitored by the district support engineers. - Meeting was conducted with the ward Engineers and necessary suggestion were provided by the district support engineers regarding the re survey and reverification.		
Meeting: not held		

Housing Typology Report (Max 4 Photos, Select best photos from each district)

Photo



Figure 1 House of Bir Bahadur dahal Chisankhugadi ward no 3 diyale



Figure 2 House of Chandra Bahadur Sunuwar Thulung Doodhkoshi Rural municipality ward no 1 Nele



Figure 3 House of Surya prashad giri Chisankhugadi RM Ward No 3 Diyale



Figure 4 House of Dendi dawa sherpa Thulung Doodhkoshi RM 1 Nele
