

District Report

Makwanpur

11 to 24 May 2018

Summary of Activities		
Activity	Contact Person	Reference Document
<u>Technical Coordination Meeting and Joint(GMLI/HRRP) Field Monitoring Visit:</u> Date: 17th May, 2018 Time: 7:00AM onwards Location: Kailash Rural Municipality (Previous Gogane VDC), Makwanpur Participants: GMLI Makwanpur, HRRP DTC, local bodies, NRA technicians & Beneficiaries. Date: 18th May, 2018 Time: 7:00AM onwards Location: Thaha Municipality -7 & 8 (Previous Agra VDC), Makwanpur Participants: GMLI Makwanpur, HRRP DTC, local bodies, NRA technicians & Beneficiaries.	techcord.makwanpur@hrrpnepal.org	Field report and photo
<u>Joint Monitoring Visit of GMaLI, HRRP and CSRC:</u> Date: 17th May, 2018 Time: Whole days Location: Bakaiya 4, Chhatiwan and Bakaiya 2, Dhiyal Participants: <u>Bakaiya 4, Chhatiwan</u> - Bakaiya R. Municipality: Vice-chair, CAO & 13 Engineers - GMaLI: M&E Specialist & Engineer - HRRP: District Coordinator - CHRC: Project Coordinator Key issues discussed: - Discussion on overall reconstruction progress, issues, challenges - Issues of landless beneficiaries, houses build on Ailani lands, etc. - Options to expedite grants delivery process. Participants: <u>Bakaiya 2, Dhiyal</u> - GMaLI: M&E Specialist & Engineer - HRRP: District Coordinator - CHRC: Project Coordinator - Beneficiaries Key issues discussed: - Criteria and process for purchase of land with additional grant (2 Lac) - Plan of action for completion of land purchase process of the 31 landless applicants from Dhiyal, Bakaiya.	dc.makwanpur@hrrpnepal.org	Photos attached, attendance sheet annexed
Date: 18th May, 2018 Time: Whole day Location: Bagmati-2, Raigaun & Bagmati-4, Faparbari Participants: - GMaLI: M&E Specialist, Engineer & field technicians - HRRP: District Coordinator		

• CHRC: Project Coordinator • Beneficiaries Key tasks accomplished: • On-site inspection/monitoring of houses under construction at Raigaun, Bagmati Rural Municipality. • Special attention given to find out if any houses constructed on Ailani Land would have been approved for tranches. • GMaLI Engineer also inspected the Ward Office Building being constructed at Faparbari of Bagmati Rural Municipality.		
<u>"Financial Management Risk Mitigation" Training: A national level event of CLPIU (GMaLI)</u> Date: 21 and 22 May, 2018 Time: 10:30am to 1:30pm Venue: Noble Hotel, Hetauda, Makwanpur HRRP Contribution: • Logistic, Coordination and Communication Support Participants: Day 1 (21st May, 2018) • Representatives of 25 local banks • GMaLI: CLPIU and DLPIU Team • Chief of District Financial Comptroller's Office • HRRP Team Subject matter: • Financial management risk mitigation • Prompt and efficient flow of tranches/grants Participants: Day 1 (22nd May, 2018) • GMaLI: CLPIU and DLPIU Team • DCC: Social Development Officer • POs: NRCS, RADO Nepal, Lumanti, CSRC/PIN and TI Nepal • HRRP Team Subject matter: • Reconstruction updates from POs supporting to housing reconstruction • Issues, challenges, good practices and lessons learnt	dc.makwanpur@hrrpnepal.org	Scanned copy of minute annexed.
<u>Meeting with DFID Team:</u> Date: 23th May, 2018 Time: 3:30pm onwards Location: GMaLI DLPIU Office, Makwanpur Participants: • GMaLI: District chief, M&E Specialist • DFID: 1. Ishwar Pudasaini, 2. Sampad Jamarkattel • HRRP: Whole team Key issues discussed: • Major gaps of EQ Housing Reconstruction • Durable Solution-III, DFID-WASH and Retrofitting Support programs	dc.makwanpur@hrrpnepal.org	
<u>Meeting with DFID and Durable Solution/PIN Team:</u> Date: 24th May, 2018 Time: 4:00pm onwards Location: Durable Solution/PIN/CSRC Office, Makwanpur Participants: • DFID: Ishwar Pudasaini and Sampad Jamarkattel • HRRP: District Coordinator and District IM Officer • PIN: Bijaya jee, Upahar Jee and Ran Subba Gurung Jee Key issues discussed: • Ways to accelerate the land purchase and relocation issues. • Requirement of Geologist support for the Geo-hazard-prone areas.	dc.makwanpur@hrrpnepal.org	

Upcoming Events

Event	Date, Time and Venue	Contact Person
Meeting of District Reconstruction Facilitation Committee, Makwanpur	30 th May, 2018; 11:00am onwards DCC, Makwanpur	dc.makwanpur@hrrpnepal.org

Field Visit Reports

Date	Location	Participants						
17 th May, 2018	Technical Coordination Meeting with Joint Field Visit in Kailash Rural Municipality (Previous Gogane VDC)	GMLI, NRCS, Build Change, HRRP DTC, Local Bodies, NRA Technicians and Beneficiaries. (Total 11 participants)						
Objective (s)	- Observed the construction houses in Gogane VDC and Agra VDC of NRCS grant and Government grant. - Conduct technical coordination meeting in local level, overall reconstruction status in housing reconstruction. - Separate interaction with NRA local based technicians and beneficiaries. - To find out the key issues and challenges for delay in reconstruction at local level. If any major issues include in district level general coordination meeting otherwise solve in local level.							
Summary	NRCS/Build Change has been working for 3years in Kailash Rural Municipality (Previous Gogane VDC) for contribution of reconstruction. Whole beneficiaries enrolled with grant supported by NRCS, absent of government grant in this VDC and Technical supported by Build Change Nepal. Till to the date around 50% houses have been completed and 85% beneficiaries received 2 nd tranches.							
	Latest Construction rate of Kailash Rural Municipality:							
	SN	RM/M/SM Name	Previous VDCs	1st tranche received	Construction Started	Verified for 2nd tranche	Verified for third tranche	Completed HHs
	1	Kailash Rural Municipality	Namtar 2,5,6,7,8 &9	586	305	290	80	87
			Kalikatar	194	132	127	66	60
			Bhartta	157	151	120	26	31
			Gogane	646	598	524	305	315
			Dadakharka	355	327	302	131	124
	We have conducted technical coordination meeting with participate of NRCS/Build Change/ local Government and separate interaction with NRA field base technicians and also beneficiaries.							
	Key Points of Meeting:							
We briefed discussed about the agendas of overall reconstruction status, major key issues and challenges, POs activities, coordination between beneficiaries and technicians, role of ward members in their locally level.								
Conclusion:								
- We concluded in Gogagne meeting with participate of local government/NRCS/Build Change, all enrolled HHs complete for DPC level and verify for second tranche and meet to government time line of Ashad Masant. - Speed up reconstruction, motivate to beneficiaries for reconstruct their houses, carry out the survey for beneficiaries and find out the fake beneficiaries.								
Date	Location	Participants						
18 th May, 2018	Technical Coordination Meeting with Joint Field Visit in Thaha Municipality-7 &8 (Previous Agra VDC)	GMLI, HRRP DTC, Local Bodies, NRA Technicians and Beneficiaries. (Total 15 participants)						

Objective (s)	• Observed the current reconstruction status. • Conduct technical coordination meeting in local level, overall reconstruction status in housing reconstruction. • Separate interaction with NRA local based technicians and beneficiaries. • To find out the key issues and challenges for delay in reconstruction at local level. If any major issues include in district level general coordination meeting otherwise solve in local level.																																		
Summary	Similarly in Thaha Municipality-7 & 8 (Previous Agra VDC), RADO Nepal has been completed around 300HHs with funding supported by TEAR fund and handover the program. From government side, there is ongoing reconstruction with rapidly but slow in received 3rd tranches. During the visit, we found, there are some issues like as didn't carry out supervision on time, didn't inspection and file submit to DLPIU on time etc. So, we concluded in meeting early arrange the office for engineers in ward office. We found different typologies of housing, almost stone in mud mortar with RCC band. This is most important factors for reconstruction due to uses local material and to make earthquake resilient structures. Latest Construction rate of Thaha Municipality: <table><tr><th>SN</th><th>RM/M/SM Name</th><th>Previous VDCs</th><th>1st tranche received</th><th>Construction Started</th><th>Verified for 2nd tranche</th><th>Verified for third tranche</th><th>Completed HHs</th></tr><tr><td rowspan="4">1</td><td rowspan="4">Thaha Municipality</td><td>Thaha Nagarpalika</td><td>2769</td><td>1215</td><td>1210</td><td>44</td><td>113</td></tr><tr><td>Agra</td><td>1688</td><td>1300</td><td>1288</td><td>678</td><td>652</td></tr><tr><td>Tistung</td><td>619</td><td>674</td><td>668</td><td>402</td><td>401</td></tr><tr><td>Chitalng</td><td>292</td><td>201</td><td>195</td><td>156</td><td>148</td></tr></table> We have conducted technical coordination meeting with participate of NRCS/Build Change/ local Government and separate interaction with NRA field base technicians and also beneficiaries. Key Points of Meeting: We briefed discussed about the agendas of overall reconstruction status, major key issues and challenges, POs activities, coordination between beneficiaries and technicians, role of ward members in their locally level. Conclusion: • If beneficiaries completed to DPC level for 2nd tranche and roof band with toilet constructed for third tranche till to meeting date of Agra VDC, all houses inspection and submit to DLPIU within 7days. • Regular supervision, inspection and engineers working station early arrange in ward office. (Agra VDC) current Thaha Municipality-7, 8.	SN	RM/M/SM Name	Previous VDCs	1st tranche received	Construction Started	Verified for 2nd tranche	Verified for third tranche	Completed HHs	1	Thaha Municipality	Thaha Nagarpalika	2769	1215	1210	44	113	Agra	1688	1300	1288	678	652	Tistung	619	674	668	402	401	Chitalng	292	201	195	156	148
SN	RM/M/SM Name	Previous VDCs	1st tranche received	Construction Started	Verified for 2nd tranche	Verified for third tranche	Completed HHs																												
1	Thaha Municipality	Thaha Nagarpalika	2769	1215	1210	44	113																												
		Agra	1688	1300	1288	678	652																												
		Tistung	619	674	668	402	401																												
		Chitalng	292	201	195	156	148																												
Challenges / Issues Identified	Action Required	Responsible			Timeframe																														
Government dateline Ashad masant for 2 nd and Push masant for 3 rd tranche.	We concluded in Gogagne meeting with participate of local government/NRCS/Build Change, till to the Ashad masant all enrolled HHs complete for DPC level and verify for second tranche.	Government engineer/NRCS/Build Change/			Ashad Masant.																														
Gap between tranches distribution	After meeting, we concluded if beneficiaries completed to DPC band level for second tranche and to roof band level, toilet constructed for third tranche till to meeting date, still technician inspection and submit file to DLPIU in the district with in 7days.	NRA technicians, Local Government			7days for Agra VDC																														

Mobilization of technicians	It should be very necessary for mobilization of technicians in timely for inspection and submit inspection file with in time frame. We all are aware about mobilization of technicians under local government.	Local Government NRA Makwanpur	
-----------------------------	--	-----------------------------------	--



Figure1: Technical Coordination Meeting in VDC level Kailash Rural Municipality (Previous Gogane VDC). There were 11 participants from local government bodies, GMLI Makwanpur, NRCS/Build Change, HRRP-DTC & NRA Technicians.



Figure 2: Technical Coordination Meeting in VDC level Thaha Municipality-7 & 8 (Previous Agra VDC). There were 15 participants from local government bodies, GMLI Makwanpur, HRRP-DTC & NRA Technicians.



Figure3: Kailash Rural Municipality (previous Gogane VDC), Sher Bahadur Gurung. He has received all tranches of NRCS grants. Technical supported by Build Change Nepal and inspected by government engineer. Stone in mud mortar with all earthquake resilient elements provided. The total construction cost is around 5.5lakh.



Figure4: Kailash Rural Municipality (previous Gogane VDC), Brick in cement mortar with RCC band and flexible roof, one room with one story. He has received all tranches of NRCS grants. Technical supported by Build Change Nepal and inspected by government engineer. The construction cost of this house is around 2.5lakh.



Figure 5: Thaha Municipality- 7 (previous Agra VDC), Rup Bahadur Ghalang. He received all tranches of TEAR Fund and technical supported by RADO Nepal for this house. Stone in mud mortar with RCC band, two rooms with two story an attic. Total construction cost is around 6lakh.


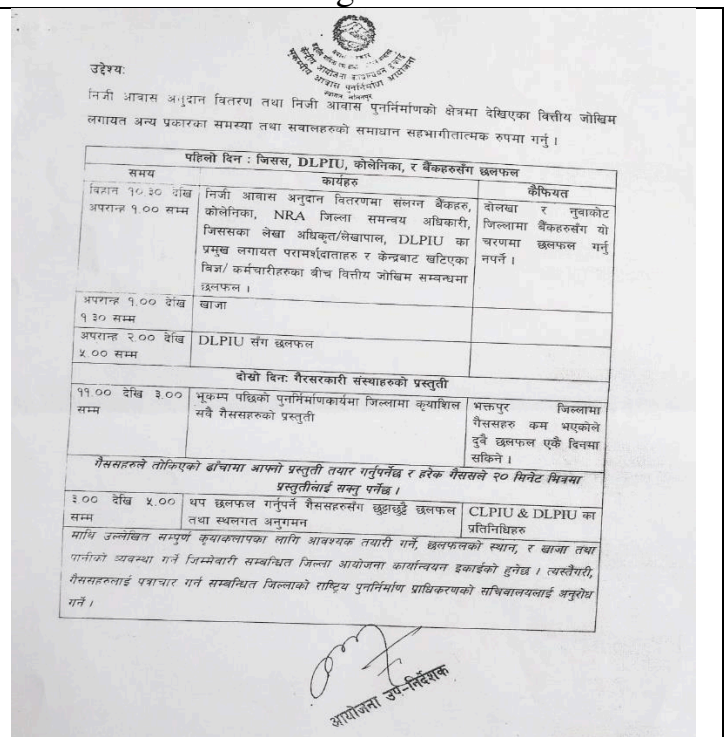


Figure 6: Thaha Municipality-07. House owner Sanu Kanxi Syantan, she has received second tranche and verified for third tranche by government engineer. Brick in cement mortar with RCC band.

Questions Collected

Question of the week	Who Asked the Question?	Response Provided (By Whom)
Why doesn't implement the retrofitting issue for second tranche.	Ward member	We have completed the 2batch retrofitting training for engineers. According to the beneficiary application, engineer guided for construction with retrofitting methodology and after completed engineer inspected for second tranche.
Why doesn't the engineer inspection for all tranches in one instalment?	Ward President-7	The grant is provided in three tranches to allow for compliance checks like as plinth band for 2 nd tranche, roof band as with toilet for 3 rd tranche. if house owner their house constructed with compliance and meet all requirement, follow building code of Nepal, the engineer inspection for in one instalment (second and Third) in field level.

Photos of two-day training on "Financial Risk Mitigation"



Official Invitation Letter from NRA CLPIU (GMAI) for the two-day training on "Financial Management Risk Mitigation"

Itinerary of two-day training on "Financial Management Risk Mitigation"



Mr. Yogendraraj Rijal, M&E Specialist, CLPIU facilitating the training; participants are from local banks.



Representatives from different POs, SDO of DCC and other participants of the training on second day.

Photos of visit to Bakaiya and Bagmati Rural Municipalities



Mr. Vibek Gautam (white shirt, Nepali cap), M&E Specialist, DLPIU GMaLI Makwanpur, facilitating the meeting at Bakaiya Rural Municipality meeting hall



Participants of meeting, local Engineers, Sub-Engineers feeling up monitoring checklist distributed by M&E specialist.



Dhiyal Meeting; participants introducing themselves (Among the participants, one is land-seller who has committed to provide his registered land to 31 landless beneficiaries; the others are from among 31 applicants who have planned to purchase land with additional grant of Rs. 200,000 and build a composite settlement.)



Dhiyal Meeting; participants in group discussion (Among the participants, one is land-seller who has committed to provide his registered land to 31 landless beneficiaries; the others are from among 31 applicants who have planned to purchase land with additional grant of Rs. 200,000 and build a composite settlement.)
