


## FACTS AND FIGURES

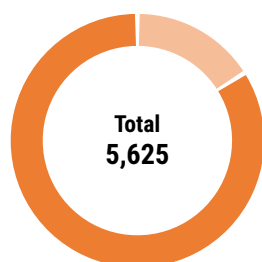

Damage Status - Private Structures

## MAJOR HOUSING TYPOLOGIES

| Typology                        | Municipal | District |
|---------------------------------|-----------|----------|
| Stone and Mud Mortar Masonry    | 99.02%    | 97.73%   |
| Adobe Structures                | 0.41%     | 0.44%    |
| Dry Stone Masonry               | 0.21%     | 0.11%    |
| Stone and Cement Mortar Masonry | 0.14%     | 0.46%    |
| Others                          | 0.22%     | 1.27%    |

CBS damage assessment survey, 2015

## HOUSING RECONSTRUCTION & RETROFIT UPDATES

### Reconstruction Status

|                                    |       |
|------------------------------------|-------|
| Total Eligible HHs                 | 3,671 |
| PA Agreement                       | 3,555 |
| I <sup>st</sup> Tranche received   | 3,550 |
| II <sup>nd</sup> Tranche received  | 3,148 |
| III <sup>rd</sup> Tranche received | 2,240 |

### Houses

Under Construction: -

Completed: -

### Retrofitting Status

|                                   |     |
|-----------------------------------|-----|
| Total Eligible HHs                | 821 |
| PA Agreement                      | 20  |
| I <sup>st</sup> Tranche received  | 20  |
| II <sup>nd</sup> Tranche received | 821 |

### Grievances

Registered: 1,392

Addressed: 1,392

### Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-29 00:00:00

## P0 Presence

Active: No POs Reported

Phased Out: CSIDB (Shelter), GON - DUDBC (Shelter), GON-PAF (Shelter), HELVETAS (Shelter), NDBS (Education), SABAL (Shelter), SCI (Education), SCI (Shelter), SCI (Social Protection)

## OTHER SECTORS



### Schools

Damaged: 43  
Under Construction: 32  
Construction Completed: 32



### Health Posts

Damaged: -  
Under Construction: -  
Construction Completed: -

## STATUS OF CONSTRUCTION MATERIALS

| Materials    | Unit           | Req. Quantity* | Ava. | Cost (NRs.)** |
|--------------|----------------|----------------|------|---------------|
| Stone        | m <sup>3</sup> | 87,654         | Y    | -             |
| Aggregate    | m <sup>3</sup> | 90,490         | Y    | -             |
| Sand         | m <sup>3</sup> | 9,366          | Y    | -             |
| Timber       | cu. ft.        | 10,831         | Y    | -             |
| Cement (PPC) | Sack           | -              | -    | -             |
| Cement (OPC) | Sack           | 300,487        | Y    | -             |
| Rebars       | kgs.           | 950,315        | -    | -             |
| Tin          | bundle         | 12,286         | -    | -             |
| Bricks       | pcs.           | 938,462        | Y    | -             |

### Types of Workers

1. Skilled mason
2. Labourer

### Avg. daily wage (NRs.)

-/-  
-/-

## KEY CONTACTS

### Municipal Office

Dhawa Lama  
Chairman  
9854040040

### Municipal Office

Raj Kishor Jaiswal  
Focal Person  
9843905584

### Municipal Office

Gita Bista  
Deputy Chairman  
9849346863

### GMaLI/NRA

NRA Chief-District  
0

### Municipal Office

Sunil Niraula  
Chief Administration Officer  
9851144835

### DLPIU-Building

Prabhakar Lal Karna  
DUDBC.DLPIU Chief  
9854041543

## HHs WITH LAND ISSUES

No Reported Land Issues

## STATUS OF TECHNICAL STAFF


| Staff               | Available Nos.            | Additional Req. Nos.      |
|---------------------|---------------------------|---------------------------|
| Engineers           | -                         | -                         |
| Sub-Engineers       | -                         | -                         |
| Asst. Sub-Engineers | -                         | -                         |
| Masons              | - (7 days)<br>- (50 days) | - (7 days)<br>- (50 days) |

Source: Municipal survey

## MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

## TA ACTIVITIES MAP

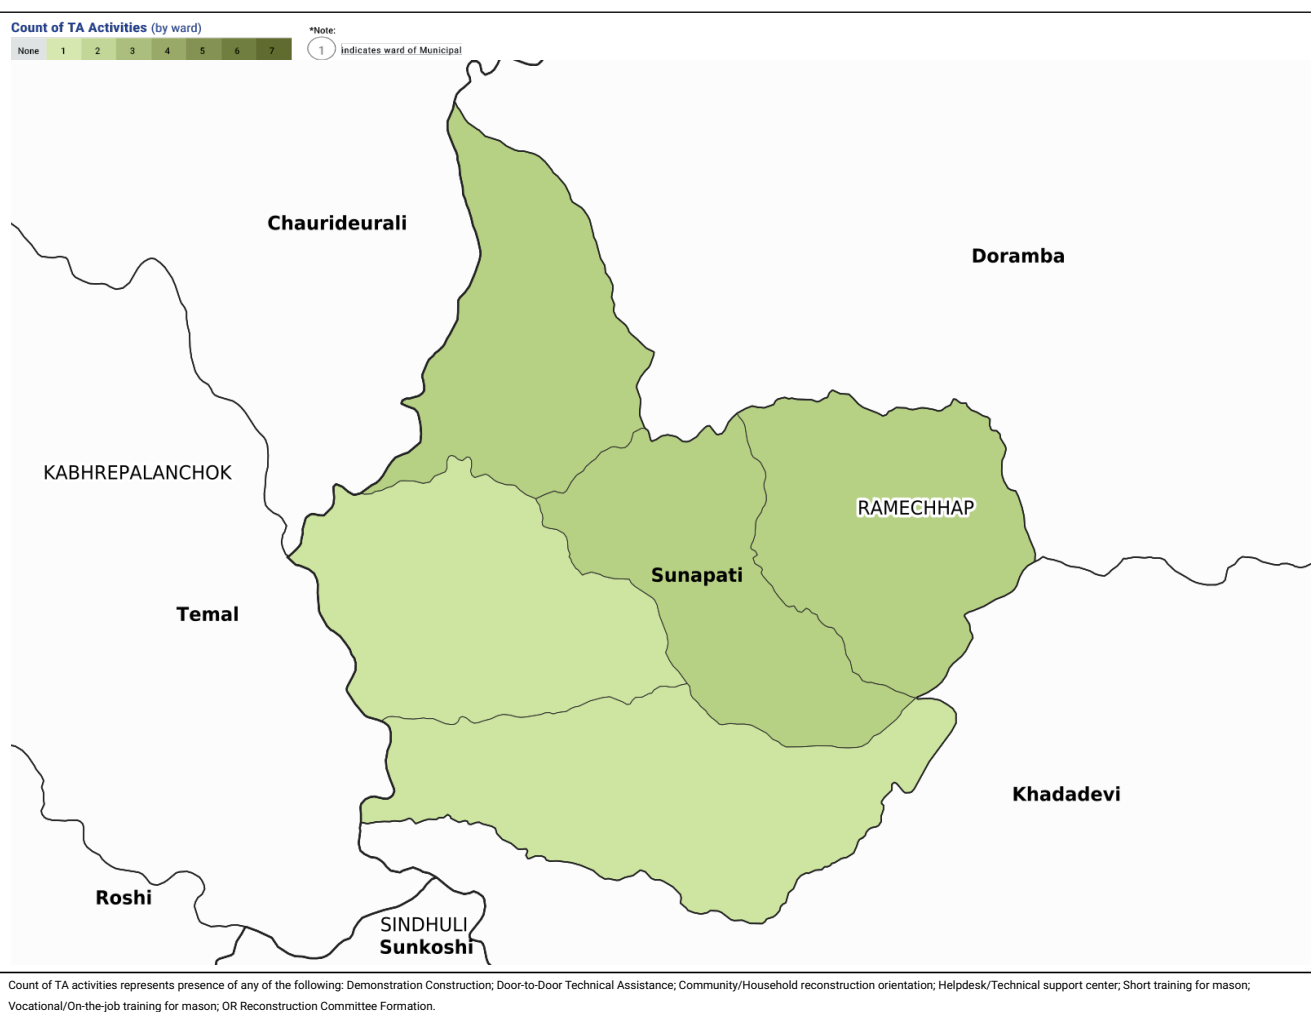

## FAQs

**Q: What documents are required for enrolment in the GoN housing reconstruction programme?**

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

**Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?**

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Prabin Gautam (District Coordinator)  
9860687776

2. Tulasi Ram Lamichhane (District Technical Officer)  
9851213610

3. Pranjal Bhandari (District Information Management Officer)  
9840057752
